



Dekalb County School System

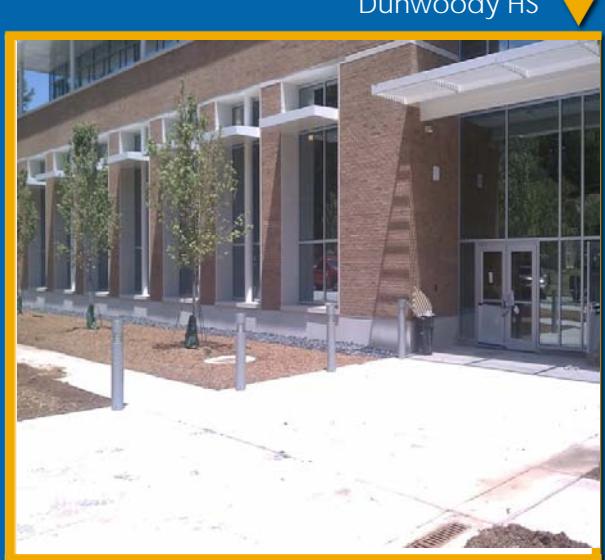

Capital Improvements Team Progress & Status Report

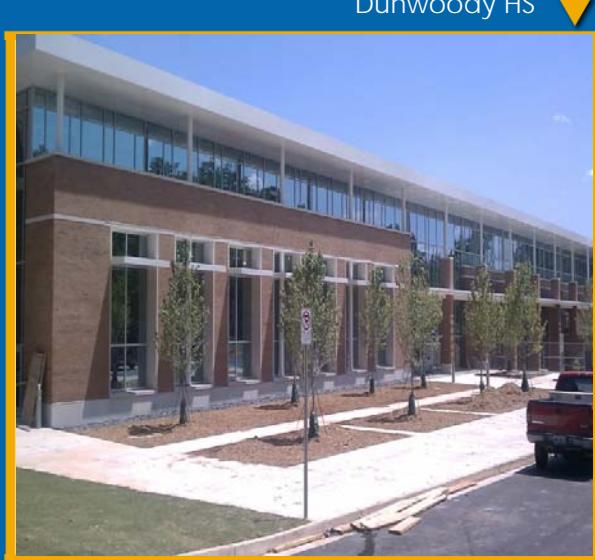

Monthly Status Report

SPLOST III Capital Improvement Program

April 2011



Table of Contents

1. Executive Summary
2. SPLOST III Funding
3. Program Financial Summary
4. Project Financial Summary
5. Project Status by Phase
6. Program Change Order Details
7. Local School Priority Request Projects
8. Site Improvement Projects
9. Program Master Schedule
10. Project Detail Status
11. Project Bid List
12. Budget Reallocations Approved This Period

SPLOST III Capital Improvement Program

Monthly Status Report

Glossary of Construction and CIP Terms

This glossary lists some of the terms used throughout construction and the capital improvement program.

ADA	The Americans with Disabilities Act gives civil rights protection to individuals with disabilities similar to those provided to individuals on the basis of race, color, sex, national origin, age, and religion. It guarantees equal opportunity for individuals with disabilities in public accommodations, employment, transportation, state and local government services, and telecommunications.
Addendum	(Addenda) Written information adding to, clarifying or modifying the bidding documents. An addendum is generally issued by the owner to the contractor during the bidding process and as such, addenda are intended to become part of the contract documents when the construction contract is executed.
Alternate Bid	Amount stated in the bid to be added or deducted from the base bid amount proposed for alternate materials and/or methods of construction.
Application for Payment	Contractor's written request for payment for completed portions of the work and, for materials delivered or stored and properly labeled for the respective project.
BAFO	Best And Final Offer. During contract negotiations, this is a term used to describe quote submissions from vendors to the project owner.
Bid	An offer or proposal of a price, including the amount offered or proposed.
Bid Form	A standard written form furnished to all bidders for the purpose of obtaining the requested information and required signatures from the authorized bidding representatives.
Bid Opening	The actual process of opening and tabulating bids submitted within the prescribed bid date/time and conforming with the bid procedures. A Bid Opening can be open (where the bidders are permitted to attend) or closed (where the bidders are not permitted to attend).
Bid Price	The stipulated sum stated in the bidder's bid.
Bidding Documents	The published advertisement or written invitation to bid , instructions to bidders, the bid form and the proposed contract documents including any acknowledged addenda issued prior to receipt of bids.
Building Process	A term used to express every step of a construction project from the conception to final acceptance and occupancy.
Change Order	A written document authorizing a change in the work or an adjustment in the contract sum or the contract time. A change order may be signed by the architect or engineer, provided they have written authority from the owner for such procedure and that a copy of such written authority is furnished to the contractor upon request. The contract sum and the contract time may be changed only by change order. A change order may be in the form of additional compensation or time; or less compensation or time known as a Deduction (from the contract) the amount deducted from the contract sum by change order.
Facility or Site Analysis	A visual inspection of a building and on-site improvements for functional or physical deterioration; prepare optional Replacement Cost Estimate for making recommendations to improve functional and physical deficiencies to increase market value; AND/OR prepare a Reserve Study over five (5) years to increase Net Operating Income (NOI) for the facility.
General Conditions	A written portion of the contract documents set forth by the owner stipulating the contractor's minimum acceptable performance requirements including the rights, responsibilities and relationships of the parties involved in the performance of the contract. General conditions are usually included in the book of specifications but are sometimes found in the architectural drawings.
Indirect Cost (or expense)	A contractor's or consultant's overhead expense; expenses indirectly incurred and not chargeable to a specific project or task. The terms indirect costs and soft costs are synonymous.
Lump Sum Contract	A written contract between the owner and contractor wherein the owner agrees the pay the contractor a specified sum of money for completing a scope of work consisting of a variety of unspecified items or work.
Plans	A term used to represent all drawings including sections and details; and any supplemental drawings for complete execution of a specific project.
Preliminary Drawings	The drawings that precede the final approved drawings. Usually these drawings are stamped or titled "PRELIMINARY"; and the "PRELIMINARY" is removed from the drawings upon being reviewed and approved by the owner.
Pre-qualification of prospective bidders	A screening process wherein the owner or his/her appointed representative gathers background information from a contractor or construction professional for selection purposes. Qualifying considerations include competence, integrity, dependability, responsiveness, bonding rate, bonding capacity, work on hand, similar project experience, and other specific owner requirements

SPLOST III Capital Improvement Program

Monthly Status Report

Glossary of Construction and CIP Terms

R.F.I.	An abbreviation for Request for Information. A written request from a contractor to the owner or architect for clarification or information about the contract documents following a contract award.
RFP	<ul style="list-style-type: none"> 1. An abbreviation for Request for Proposal. 2. A written request from the requestor (usually the owner or a contractor) to a contractor, design professional or subcontractor for an estimate or cost proposal. The RFP usually contains a specific scope of work.
Safety Report	The Occupational Safety and Health Act of 1970 clearly states the common goal of safe and healthful working conditions. A Safety Report is prepared following a regularly scheduled project safety inspection of the specific project.
Schedule of Values	A statement furnished by the contractor to the architect or engineer reflecting the portions of the contract sum allotted for the various parts of the work and used as the basis for reviewing the contractor's applications for progress payments.
Schematic	A preliminary sketch or diagram representing the proposed intent of the designer.
Schematic Design Phase	The first phase of the architect's basic services in which the architect consults with the owner to ascertain the requirements of the project and prepares schematic design studies consisting of drawings and other documents showing the scale and project components for the owner's approval.
Scheme	A chart, a diagram, or an outline of a system being proposed.. An orderly combination of related construction systems and components for a specific project or purpose.
Scope of Work	A written range of view or action; outlook; hence, room for the exercise of faculties or function; capacity for achievement; all in connection with a designated project.
Special Conditions	A section of the conditions of the contract, other than the General Conditions and Supplementary Conditions, which may be prepared for a particular project. Specific clauses setting forth conditions or requirements peculiar to the project under consideration, and covering work or materials involved in the proposal and estimate, but not satisfactorily covered by the General Conditions. (See General Conditions)
Structural Design	A term used to represent the proportioning of structural members to carry loads in a building structure.
Subb	An abbreviation for Subcontractor.
Subcontract	A written form of agreement between the prime or main contractor and another contractor or supplier for the satisfactory performance of services or delivery or material as set forth in the plans and specifications for a specific project.
Subcontractor	A qualified subordinate contractor to the prime or main contractor.
TM	An abbreviation for a contracting method called Time and Materials. A written agreement between the owner and the contractor wherein payment is based on the contractor's actual cost for labor, equipment, materials, and services plus a fixed add-on amount to cover the contractor's overhead and profit.
Unit Price Contract	A written contract wherein the owner agrees to pay the contractor a specified amount of money for each unit of work successfully completed as set forth in the contract.
Variance	This report uses the term variance to indicate the calculation of the current budget less the forecasted cost at completion. A positive variance amount does not indicate that funds are available for use on additional projects. The original scope of work must be completed before funds can be reallocated.
Zoning	Restrictions of areas or regions of land within specific geographical areas based on permitted building size, character, and uses as established by governing urban authorities.
Zoning Permit	A document issued by a governing urban authority permitting land to be used for a specific purpose.

SPLOST III Capital Improvement Program

Monthly Status Report

Glossary of Construction and CIP Terms

Construction Delivery Methods

Design/Bid/Build

Under this traditional method, an architectural firm is hired and serves as the owner's agent. Although the firm may have numerous responsibilities, including the selection of consultants, its primary responsibility is to provide and oversee the design and construction documents for the project. As the design progresses, cost estimates are periodically prepared by the architectural firm and external cost estimators. Once the construction documents and specifications are completely finished, and other requirements of the owner have been met, the project is bid and subsequently awarded to the Bidder whose bid is the lowest responsive responsible bid.

Design/Propose/Build

Under this traditional method, an architectural firm is hired and serves as the owner's agent. Although the firm may have numerous responsibilities, including the selection of consultants, its primary responsibility is to provide and oversee the design and construction documents for the project. As the design progresses, cost estimates are periodically prepared by the architectural firm and external cost estimators. Once the construction documents and specifications are completely finished, and other requirements of the owner have been met, the project is solicited as a Request for Proposals and subsequently awarded to the Offeror whose proposal is most advantageous to the Board of Education.

Construction Manager at Risk

This system of delivery is similar to that of Design/Bid/Build with three key differences. First, a construction manager is hired during the preconstruction phase to manage the construction process, including the selection of subcontractors. Second, through coordination between the architect and construction manager, the design and construction phases can be overlapped thereby expediting the delivery process. Third, the construction manager, who is responsible for quality control, scheduling and the estimate of construction costs, provides a guaranteed maximum price for the project.

Design/Build

Rather than hiring an architect, under Design/Build the owner enters into a contract with a single firm with design and building capabilities or a construction entity that employs the architect as a consultant. As with the aforementioned delivery system, a guaranteed maximum price for the entire project may be provided, construction management techniques to overlap design and construction phases are utilized, and the overall project delivery is expedited.

CIP Project Phase Descriptions

Planning/Programming

The research and decision-making process that identifies the scope of work to be designed.

Design

This phase consists of the development. Detail scope, program requirements, budgets, and schedules are developed.

Procurement

This is the phase where architectural and/or general contractor services are procured for a project. It may involve the RFP, bidding, award, contract review, and contract execution activities.

Construction

Construction begins once the project has been awarded to the contractor.

Close-out

The final inspection, submission of necessary documentation, acceptance, and concluding payment on a construction project, as required by the contract documents.

Completed

All design, construction, and close-out requirements for the project have been completed and accepted by the owner.

On-Going SPLOST Activity

This phase relates to activities within the CIP that are on-going throughout the length of the program. These projects are generally supporting activities.

On Hold

A project is placed on hold when the detailed scope, budget, or necessity may need to be further defined.

Deemed Unnecessary

A project within the CIP may be deemed unnecessary in situations where the project may have already been completed using other funds, the project may have been incorporated into larger construction projects, or the project may no longer be required due to current applicability

SPLCOT III Capital Improvement Program

Monthly Status Report

Executive Summary April 2011




This report summarizes the DeKalb County School System's SPLOST III Capital Improvement Program through April 2011. Sales tax revenue collections are ahead of the estimated schedule. Over 74% of the total projects within the program are under construction, in close-out, or completed. Several projects are on hold and deemed unnecessary pending the project's current applicability and necessity.

School Design Highlights

For Chamblee HS, the BOE approved the award of the CM/GC at Risk Contract to Turner Construction Company on April 18, 2011. The Preliminary Design and Estimate from the A/E is due on May 2, 2011. HVAC projects at Hambrick ES, Indian Creek ES, Montgomery ES, Rockbridge ES, Stone Mill ES, Stone Mtn ES, and Warran Tech are under design.

School Construction Highlights

Construction at Lakeside HS includes installation of footings for the Fine Arts and Auditorium addition, and CMU walls in the lower level classrooms and the new main electrical room. The Auditorium addition at Dunwoody HS is approximately 99% complete with an anticipated completion of end of May. Interior trim out is in progress.

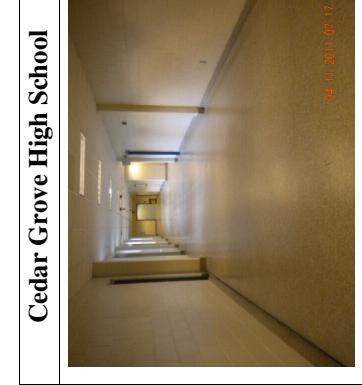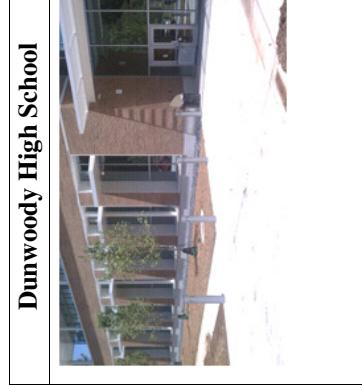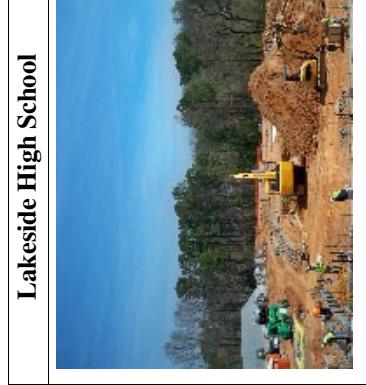

4/1/2011 01:17

Program Status		No. of Projects	Current Budget	% Budget
Planning & Programming	4	\$2,172,372	0%	
Design	14	\$54,654,542	11%	
Procurement	7	\$10,344,608	2%	
Construction	27	\$78,811,127	15%	
Close-out	21	\$181,724,943	35%	
Completed	100	\$26,909,611	5%	
On-Going SPLCOT Activity	10	\$146,022,519	28%	
On Hold	10	\$12,300,862	2%	
Deemed Unnecessary	6	\$529,379	0%	
Total Projects:	199	\$513,469,963	100%	

Revenue Status	
Sales tax receipts are 13% ahead of schedule. This has allowed projects to start on time, and some projects have been moved ahead of schedule.	
Budgeted Receipts:	\$328,264,121
Actual Receipts:	\$361,164,248
Percent Collected:	110%

Expenditures Status	
The Monthly CIP expenditures are anticipated at \$9.5 million per month for the 2011 calendar year. This will have the CIP anticipated total expenditures at 75% complete by the end of 2011 calendar year.	
CIP Current Budget:	\$513,469,963
Committed Costs:	\$389,993,847
Expenditures:	\$294,050,851
	76% of Budget
	75% of Committed



SPLIST III Funding

The sales tax collections through April 2011 are:	\$361,164,248
Expenditures through this time period are:	\$294,050,851

Planned SPLOST III			Budgeted SPLOST III			Actual SPLOST III			% Collected	
Month	Month	Total	Month	Total	Month	Month	Total	Month	Total	Month
Sep-2007	\$7,812,349	\$7,812,349	\$7,252,445	\$7,252,445	\$9,677,573	\$9,677,573	\$133%	133%	133%	133%
Oct-2007	\$7,272,688	\$15,085,037	\$6,751,460	\$14,003,905	\$8,864,435	\$18,542,008	131%	131%	132%	132%
Nov-2007	\$8,281,590	\$23,366,627	\$7,688,056	\$21,691,961	\$9,320,988	\$27,862,996	121%	121%	128%	128%
Dec-2007	\$7,607,096	\$30,973,723	\$7,061,901	\$28,753,862	\$8,718,808	\$36,581,804	123%	123%	127%	127%
Jan-2008	\$7,330,325	\$38,304,048	\$6,804,966	\$35,558,828	\$7,890,547	\$44,472,351	116%	116%	125%	125%
Feb-2008	\$8,373,407	\$46,677,455	\$7,773,293	\$43,332,121	\$9,359,571	\$53,831,921	120%	120%	124%	124%
Mar-2008	\$7,132,517	\$53,809,972	\$6,621,335	\$49,953,456	\$7,257,907	\$61,089,829	110%	110%	122%	122%
Apr-2008	\$7,258,039	\$61,068,011	\$6,737,870	\$56,691,326	\$8,353,056	\$69,442,885	124%	124%	122%	122%
May-2008	\$7,613,063	\$68,681,074	\$7,067,450	\$63,758,776	\$9,267,949	\$78,710,834	131%	131%	123%	123%
Jun-2008	\$7,008,504	\$75,689,577	\$6,506,218	\$70,264,994	\$8,234,794	\$86,945,628	127%	127%	124%	124%
Jul-2008	\$7,598,540	\$83,288,117	\$7,053,968	\$77,318,961	\$8,672,457	\$95,618,085	123%	123%	124%	124%
Aug-2008	\$7,491,002	\$90,779,119	\$6,954,137	\$84,273,098	\$8,948,874	\$104,566,960	129%	129%	124%	124%
Sep-2008	\$7,098,858	\$97,877,977	\$6,590,097	\$90,863,195	\$8,386,971	\$112,953,930	127%	127%	124%	124%
Oct-2008	\$7,848,961	\$105,726,938	\$7,286,441	\$98,149,637	\$7,867,280	\$120,821,210	108%	108%	123%	123%
Nov-2008	\$8,347,491	\$114,074,429	\$7,749,243	\$105,898,880	\$8,715,533	\$129,536,743	112%	112%	122%	122%
Dec-2008	\$7,384,236	\$121,458,665	\$6,855,022	\$112,753,902	\$7,334,293	\$136,871,036	107%	107%	121%	121%
Jan-2009	\$6,724,043	\$128,182,708	\$6,242,145	\$118,996,047	\$7,081,202	\$143,952,238	113%	113%	121%	121%
Feb-2009	\$7,898,155	\$136,080,863	\$7,332,110	\$126,328,157	\$9,615,637	\$153,567,875	131%	131%	122%	122%
Mar-2009	\$8,171,613	\$144,252,476	\$7,585,969	\$133,914,126	\$7,626,335	\$161,194,210	101%	101%	120%	120%
Apr-2009	\$7,588,292	\$151,840,768	\$7,044,455	\$140,958,581	\$6,301,644	\$167,495,854	89%	89%	119%	119%
May-2009	\$7,836,977	\$159,677,745	\$7,275,316	\$148,233,897	\$10,522,040	\$178,017,894	145%	145%	120%	120%
Jun-2009	\$8,222,776	\$167,900,521	\$7,633,466	\$155,867,363	\$6,920,940	\$184,938,834	91%	91%	119%	119%
Jul-2009	\$8,566,685	\$176,467,206	\$7,952,728	\$163,820,091	\$7,767,185	\$192,706,019	98%	98%	118%	118%
Aug-2009	\$7,688,824	\$184,156,030	\$7,137,782	\$170,957,873	\$7,765,507	\$200,471,526	109%	109%	117%	117%
Sep-2009	\$8,162,173	\$192,318,203	\$7,577,206	\$178,535,079	\$8,737,095	\$209,208,621	115%	115%	117%	117%
Oct-2009	\$8,113,089	\$200,431,292	\$7,531,640	\$186,066,719	\$7,606,358	\$216,814,979	101%	101%	117%	117%
Nov-2009	\$8,069,241	\$208,500,533	\$7,490,934	\$193,557,654	\$7,596,451	\$224,411,430	101%	101%	116%	116%
Dec-2009	\$7,495,031	\$215,995,563	\$6,957,877	\$200,515,530	\$7,279,638	\$231,691,068	105%	105%	116%	116%
Jan-2010	\$7,616,512	\$223,612,076	\$7,070,652	\$207,586,183	\$8,386,392	\$240,077,460	119%	119%	116%	116%
Feb-2010	\$8,871,402	\$232,483,478	\$8,235,606	\$215,821,789	\$8,398,966	\$248,476,426	102%	102%	115%	115%
Mar-2010	\$8,045,821	\$240,529,298	\$7,469,193	\$223,290,982	\$7,992,823	\$256,469,250	107%	107%	115%	115%
Apr-2010	\$8,282,658	\$248,811,956	\$7,689,057	\$230,980,038	\$8,281,221	\$264,750,471	108%	108%		

Monthly Status Report

SPLOST II Actual Expenditures		
Month	Total	
\$1,903,425	\$1,903,425	
\$1,538,795	\$3,442,220	
\$3,245,292	\$6,687,512	
\$0	\$6,687,512	
\$146,651	\$6,834,163	
\$1,017,361	\$7,851,524	
\$7,995,081	\$15,846,605	
\$1,757,340	\$17,603,945	
\$1,699,434	\$19,303,379	
\$2,409,549	\$21,712,928	
\$1,931,931	\$23,644,859	
\$1,299,062	\$24,943,921	
\$4,134,080	\$29,078,002	
\$8,752,959	\$37,830,961	
\$3,725,225	\$41,556,186	
\$3,611,719	\$45,167,905	
\$10,521,547	\$55,689,451	
\$11,813,289	\$67,502,741	
\$5,930,732	\$73,433,472	
\$5,137,218	\$78,570,690	
\$6,423,112	\$84,993,802	
\$18,363,813	\$103,357,615	
\$4,705,022	\$108,062,637	
\$3,667,502	\$111,730,139	
\$11,876,071	\$123,606,210	
\$11,302,080	\$134,908,290	
\$10,050,977	\$144,959,267	
\$8,609,631	\$153,568,898	
\$7,351,970	\$160,920,868	
\$1,085,734	\$162,006,602	
\$6,083,347	\$168,089,948	
\$9,365,229	\$177,455,178	



SPLIST III Funding

The sales tax collections through April 2011 are:	\$361,164,248
Expenditures through this time period are:	\$294,050,851

Planned SPLOST III			Budgeted SPLOST III			Actual SPLOST III			% Collected	
Month	Month	Total	Month	Total	Month	Month	Total	Month	Total	
May-2010	\$8,269,952	\$257,081,908	\$7,677,261	\$238,657,299	\$7,655,002	\$272,400,473		100%	114%	
Jun-2010	\$8,661,111	\$265,743,019	\$8,040,386	\$246,697,685	\$8,389,540	\$280,790,013		104%	114%	
Jul-2010	\$8,255,996	\$273,999,014	\$7,664,305	\$254,361,990	\$7,643,256	\$288,433,269		100%	113%	
Aug-2010	\$8,240,993	\$282,240,007	\$7,650,377	\$262,012,368	\$7,976,221	\$296,409,490		104%	113%	
Sep-2010	\$8,342,170	\$290,582,178	\$7,744,304	\$269,756,671	\$8,546,697	\$304,956,187		110%	113%	
Oct-2010	\$9,322,599	\$299,904,777	\$8,654,467	\$278,411,138	\$7,871,571	\$312,827,758		91%	112%	
Nov-2010	\$8,644,081	\$308,548,858	\$8,024,577	\$286,435,715	\$7,884,395	\$320,712,153		98%	112%	
Dec-2010	\$7,834,072	\$316,382,930	\$7,272,620	\$293,708,335	\$7,397,636	\$328,109,789		102%	112%	
Jan-2011	\$8,345,683	\$324,728,613	\$7,747,565	\$301,455,900	\$9,428,375	\$337,538,164		122%	112%	
Feb-2011	\$10,134,573	\$334,863,186	\$9,408,249	\$310,864,149	\$7,474,784	\$345,012,947		79%	111%	
Mar-2011	\$9,366,493	\$344,229,679	\$8,695,215	\$319,559,364	\$8,020,271	\$353,033,218		92%	110%	
Apr-2011	\$9,377,000	\$353,606,679	\$8,704,969	\$328,264,332	\$8,131,029	\$361,164,248		93%	110%	
May-2011	\$9,031,024	\$362,637,703	\$8,383,788	\$336,648,121						
Jun-2011	\$8,351,729	\$370,989,431	\$7,753,177	\$344,401,298						
Jul-2011	\$8,874,946	\$379,864,377	\$8,238,896	\$352,640,194						
Aug-2011	\$9,591,730	\$389,456,107	\$8,904,310	\$361,544,504						
Sep-2011	\$10,029,208	\$399,485,315	\$9,310,435	\$370,854,939						
Oct-2011	\$9,879,504	\$409,364,820	\$9,171,460	\$380,026,399						
Nov-2011	\$11,373,160	\$420,737,980	\$10,558,069	\$390,584,468						
Dec-2011	\$6,909,225	\$427,647,205	\$6,414,054	\$396,998,522						
Jan-2012	\$8,372,755	\$436,019,960	\$7,772,696	\$404,771,218						
Feb-2012	\$10,052,757	\$446,072,717	\$9,332,296	\$414,103,514						
Mar-2012	\$9,109,914	\$455,182,631	\$8,457,025	\$422,560,539						
Apr-2012	\$8,948,472	\$464,131,103	\$8,307,153	\$430,867,692						
May-2012	\$8,672,337	\$472,803,440	\$8,050,808	\$438,918,500						
Jun-2012	\$10,361,622	\$483,165,062	\$9,619,025	\$448,537,525						
Jul-2012	\$10,037,552	\$493,202,614	\$9,318,181	\$457,855,706						
Aug-2012	\$8,773,040	\$501,975,654	\$8,144,294	\$466,000,000						

Monthly Status Report

SPL OST III Capital Improvement Program

Program Financial Summary

Monthly Status Report

Capital Improvement Program

Budget Category	Current Budget	Original Contract	Executed Change Orders	Current Contract	Paid To Date	Contract Balance	Approved CORs	Current Contract Plus CORs	Uncommitted
-----------------	----------------	-------------------	------------------------	------------------	--------------	------------------	---------------	----------------------------	-------------

CIT Managed									
Architect/Engineer	\$16,650,325	\$13,101,543		\$1,726,170	\$14,827,713	\$9,161,914	\$5,665,799	\$12,170	\$14,839,883
Surveying	\$774,771	\$443,043			\$443,043	\$413,480	\$29,563		\$217,318
Construction Testing	\$1,760,087	\$907,902		\$24,554	\$932,456	\$830,258	\$102,198		\$50,353
Abatement	\$1,571,211	\$994,832			\$994,832	\$923,621	\$71,211		\$156,420
Other Consultants	\$2,915,839	\$2,216,043		\$2,477	\$2,218,520	\$910,798	\$1,307,722	\$1,500	\$372,829
Management Fees	\$15,374,724	\$15,374,724			\$15,374,724	\$13,142,009	\$2,232,715		\$118,369
Construction	\$293,746,181	\$201,663,475		\$29,495,816	\$231,159,291	\$186,683,116	\$44,476,175	\$1,085,009	\$232,244,300
Construction Infrastructure	\$1,38,200	\$62,345			\$62,345	\$0	\$62,345		\$5,301,513
Miscellaneous	\$59,172,827	\$56,154,464			\$56,154,464	\$570,467	\$55,583,997		\$178,713
Security	\$1,725,991	\$1,033,850			\$1,033,850	\$885,374	\$148,476		\$450,215
Utilities	\$1,603,510	\$137,389			\$137,389	\$42,556	\$94,833		\$31,915
Moving / Relocation	\$3,014,105	\$1,454,107			\$1,454,107	\$1,381,198	\$72,909		\$98,826
Trailers	\$832,756	\$285,481			\$285,481	\$246,880	\$38,601		\$71,259
Contingency	\$38,399,207	\$10,640,000			\$10,640,000	\$0	\$10,640,000		\$86,165
CIT Managed	\$438,922,734	\$304,469,198		\$31,249,017	\$335,718,215	\$215,191,671	\$120,526,544	\$1,103,992	\$23,616,953
DOSS Managed									
Land	\$2,785,085	\$285,084			\$285,084	\$285,084	\$0		\$2
FF&E	\$13,640,138	\$8,573,328			\$8,573,328	\$8,443,232	\$130,096		\$341,786
Technology	\$46,122,006	\$32,324,997			\$32,324,997	\$32,086,014	\$238,983		\$8,744,505
Transportation	\$12,000,000	\$11,988,231			\$11,988,231	\$11,988,231	\$0		\$11,769
DOSS Managed	\$74,547,229	\$53,171,640			\$53,171,640	\$52,802,561	\$369,079		\$9,098,062
Grand Total	\$513,469,263	\$357,640,838		\$31,249,017	\$388,889,855	\$267,994,232	\$120,895,623	\$1,103,992	\$39,848,910

SPL OST III Capital Improvement Program

Project Financial Summary

Monthly Status Report

Budget Category

Budget Category	Project Number	Current Budget	Original Contract	Executed Change Orders	Current Contract	Paid To Date	Contract Balance	Approved CORs	Current Contract Plus CORs	Uncommitted
ADA Group A- Main Project	421-301	\$81,808	\$91,389	\$0	\$91,389	\$90,692	\$697	\$0	\$91,389	(\$9,581)
ADA Group A-2A	421-301-021	\$56,574	\$533,490	\$23,284	\$556,774	\$256,774	\$0	\$0	\$556,774	\$4,800
ADA Group A-2B	421-301-022	\$678,336	\$650,000	\$28,336	\$678,336	\$414,115	\$264,221	\$0	\$678,336	\$0
ADA Group B- Main Project	421-302	\$510,448	\$1,935	\$0	\$1,935	\$1,935	\$0	\$0	\$1,935	\$508,513
ADA Group B-1	421-302-001	\$496,000	\$495,645	\$0	\$495,645	\$311,539	\$184,106	\$2,604	\$498,249	(\$2,249)
ADA Group B-2	421-302-002	\$407,299	\$388,199	(\$23,231)	\$364,968	\$62,443	\$302,525	\$38,396	\$403,364	\$3,935
ADA Group B-3	421-302-003	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
ADA Group C- Main Project	421-303	\$1,023,071	\$59,864	\$0	\$59,864	\$56,701	\$3,163	\$0	\$59,864	\$963,207
ADA Group D	421-304	\$337,051	\$2,343	\$0	\$2,343	\$0	\$0	\$2,343	\$0	\$2,343
ADA Group E	421-305	\$427,202	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$396,272
Administrative & Instructional Complex (AIC)	421-124	\$31,824,966	\$26,954,467	\$4,098,276	\$31,052,743	\$30,914,264	\$138,479	\$47,661	\$31,100,404	\$11,309
Allgood ES - ADA	421-301-010	\$32,556	\$32,556	\$0	\$32,556	\$32,556	\$0	\$0	\$32,556	\$0
Allgood ES - Roof	421-217	\$585,240	\$448,759	\$597	\$449,356	\$405,739	\$43,617	\$24,706	\$474,062	\$0
Allgood ES- Kitchen	421-341-043	\$400,000	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$400,000
Ashford Park ES- ADA	421-301-007	\$54,200	\$44,924	\$0	\$44,924	\$0	\$44,924	\$0	\$44,924	\$9,276
Atherton ES- Chiller Replacement	421-341-022	\$123,176	\$118,336	\$4,840	\$123,176	\$123,176	\$0	\$0	\$123,176	\$0
Avondale ES - ADA	421-301-005	\$22,406	\$22,406	\$0	\$22,406	\$22,406	\$0	\$0	\$22,406	\$0
Avondale ES - Roof	421-209	\$578,746	\$596,221	(\$17,475)	\$578,746	\$578,379	\$367	\$0	\$578,746	\$0
Avondale HS- Renovations	421-1123-002	\$4,480,700	\$255,042	\$49,566	\$304,608	\$101,278	\$203,330	\$0	\$304,608	\$1,075
Basin Heaters	421-321-014	\$345,500	\$345,500	\$0	\$345,500	\$345,500	\$0	\$0	\$345,500	\$0
Bob Mathis ES - ADA	421-301-001	\$22,299	\$22,299	\$0	\$22,299	\$22,299	\$0	\$0	\$22,299	\$0
Brockett ES - Make-up Air Units	421-320-001	\$94,030	\$94,030	\$0	\$94,030	\$94,030	\$0	\$0	\$94,030	\$0
Bulk Purchase - Plumbing Fixtures	421-322-001	\$2,043,950	\$836,289	\$40,625	\$876,914	\$390,493	\$486,421	\$0	\$876,914	\$0
Bulk Purchase- Ceiling Tile and Grid	421-600-002	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Bulk Purchase- Fixed Audience Seating	421-600-006	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Bulk Purchase- Metal Lockers	421-600-003	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Bulk Purchase- Theatrical Lighting & Sound Syst	421-600-004	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Bulk Purchasing- Lighting	421-600-005	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Buses 1	421-401	\$3,479,453	\$3,479,453	\$0	\$3,479,453	\$3,479,453	\$0	\$0	\$3,479,453	\$0
Buses 2	421-402	\$4,520,547	\$4,524,398	\$0	\$4,524,398	\$4,524,398	\$0	\$0	\$4,524,398	(\$3,851)
Buses 3	421-403	\$4,000,000	\$3,984,380	\$0	\$3,984,380	\$3,984,380	\$0	\$0	\$3,984,380	\$15,620
Capital Improvement Team Compensation	421-650	\$15,374,724	\$15,374,724	\$0	\$15,374,724	\$13,142,009	\$2,232,715	\$0	\$15,374,724	\$0

SPL OST III Capital Improvement Program

Project Financial Summary

Monthly Status Report

Budget Category

Number

Project Budget

Current Budget

Original Contract

Executed Change Orders

Current Contract

Paid To Date

Contract Balance

Approved CORs

Current Contract Plus CORs

Uncommitted

Carpet Replacement - Multiple Schools (LSPR 1	421-341-031	\$10,237	\$10,237	\$0	\$10,237	\$0	\$10,237	\$0	\$10,237	\$0
Carpet Replacement - Multiple Schools (LSPR 2	421-341-040	\$30,667	\$29,836	\$0	\$29,836	\$9,885	\$19,951	\$0	\$29,836	\$831
Cedar Grove HS - HVAC, Lighting, Ceiling & Ro	421-115	\$6,211,315	\$4,826,612	\$327,310	\$5,153,921	\$4,167,258	\$986,663	\$0	\$5,153,921	\$712,394
Chamblee Charter HS - Lockers	421-341-014	\$50,000	\$43,457	\$0	\$43,457	\$0	\$43,457	\$0	\$43,457	\$6,543
Chamblee HS - New Replacement High School	421-117	\$11,152,507	\$2,981,623	\$0	\$2,981,623	\$74,841	\$2,906,782	\$1,500	\$2,983,123	(\$1)
Chamblee MS - Roof	421-226	\$83,683	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$83,683
Chamblee MS - Sound Panels	421-341-050	\$27,500	\$38,900	\$0	\$38,900	\$38,900	\$0	\$0	\$38,900	(\$11,400)
Chamblee MS- Mirror	421-341-049	\$960	\$960	\$0	\$960	\$960	\$0	\$0	\$960	\$0
Chamblee MS- Painting	421-341-042	\$145,000	\$9,135	\$0	\$9,135	\$0	\$9,135	\$0	\$9,135	\$35,865
Champion MS - ADA	421-301-020	\$15,362	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$15,362
Champion Theme MS - Roof	421-208	\$382,342	\$382,342	\$0	\$382,342	\$210,394	\$171,948	\$0	\$382,342	\$0
Champion Theme MS- Chiller Replacement	421-341-010	\$47,539	\$38,464	\$9,075	\$47,539	\$47,539	\$0	\$0	\$47,539	\$0
Chapel Hill ES- Chiller Replacement	421-341-009	\$69,964	\$69,964	\$0	\$69,964	\$69,964	\$0	\$0	\$69,964	\$0
Chapel Hill MS- Ceiling Tiles & Site Work	421-341-028	\$240,275	\$275	\$0	\$275	\$262	\$13	\$0	\$275	\$240,000
Chapel Hill MS- Track & Tennis Court	421-341-051	\$243,956	\$237,142	\$18,380	\$255,522	\$255,522	\$0	\$0	\$255,522	(\$11,566)
Chestnut Charter ES - ADA	421-303-002	\$448,179	\$417,642	\$26,137	\$443,779	\$442,329	\$1,450	\$0	\$443,779	\$4,400
Chestnut Charter ES- Basketball Court Replaceeme	421-322-004	\$52,957	\$52,957	\$0	\$52,957	\$4,980	\$47,977	\$0	\$52,957	\$0
Clarkston Center- Roof	421-207	\$0	\$0	\$0	\$0	\$6,333	(\$6,333)	\$0	\$0	\$0
Clarkston HS- Renovation & Addition	421-118	\$12,275,194	\$9,608,658	\$669,672	\$10,278,330	\$35,23,493	\$6,754,837	\$348,387	\$10,626,717	\$114,606
CLEA 2008- Comprehensive Lighting Energy Au	421-600-001	\$98,032	\$98,032	\$0	\$98,032	\$98,032	\$0	\$0	\$98,032	\$0
Clifton ES - HVAC	421-114	\$172,792	\$172,792	\$0	\$172,792	\$172,792	\$0	\$0	\$172,792	\$0
Clifton ES- Ceiling Tiles	421-341-039	\$110,000	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$110,000
Columbia HS - SPL OST II Deferred	421-104	\$11,452,000	\$10,441,256	\$830,413	\$11,271,669	\$12,414,811	(\$1,143,142)	\$0	\$11,271,669	\$180,331
CCPS Debt Reduction	421-001	\$66,000,000	\$66,000,000	\$0	\$66,000,000	\$0	\$66,000,000	\$0	\$66,000,000	\$0
Coralwood Diagnostic Ctr. - Renovation & Additi	421-213	\$423,427	\$365,263	\$0	\$365,263	\$149,263	\$216,000	\$0	\$365,263	\$58,164
Cross Keys HS - Renovation & Addition	421-106	\$18,612,631	\$2,530,512	\$14,699,928	\$17,230,440	\$15,909,429	\$1,321,011	\$104,803	\$17,335,243	\$1,205,509
DeKalb HS of Tech North - Roof	421-221	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
DeKalb HS of Tech South - Roof	421-215	\$352,288	\$351,428	\$0	\$351,428	\$340,818	\$10,610	\$0	\$351,428	\$860
DeKalb International Student Center- Canopy	421-341-047	\$2,000	\$9,340	\$0	\$9,340	\$1,000	\$8,340	\$0	\$9,340	(\$7,340)
Druid Hills HS - Renovation & Addition	421-119	\$18,633,137	\$18,243,673	(\$36,854)	\$18,206,819	\$16,876,266	\$1,330,553	\$0	\$18,206,819	\$221,068
DSA Relocation to Avondale HS	421-123	\$5,348,715	\$4,635,500	\$118,869	\$4,754,369	\$4,622,506	\$131,863	\$47,317	\$4,801,686	(\$971)
Dunwoody HS - Renovation & Addition	421-120	\$20,530,480	\$15,855,086	\$1,941,365	\$17,796,451	\$15,112,257	\$2,684,194	\$471,825	\$18,268,276	\$39,707

SPL OST III Capital Improvement Program

Project Financial Summary

Monthly Status Report

Budget Category

Budget Category	Project Number	Current Budget	Original Contract	Executed Change Orders	Current Contract	Paid To Date	Contract Balance	Approved CORs	Current Contract Plus CORs	Uncommitted
-----------------	----------------	----------------	-------------------	------------------------	------------------	--------------	------------------	---------------	----------------------------	-------------

Eagle Wood Academy- Replace Windows & Repa	421-321-011	\$55,435	\$55,435	\$0	\$55,435	\$55,435	\$0	\$0	\$55,435	\$0
East Campus - APHONE	421-341-026	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Eldridge L. Miller ES - Roof	421-216	\$452,953	\$477,453	(\$24,500)	\$452,953	\$452,953	\$0	\$0	\$452,953	\$0
Emergency Generators	421-321-015	\$3,800,000	\$115,994	\$0	\$115,994	\$36,626	\$79,368	\$0	\$115,994	\$0
Emergency HVAC Work	421-101	\$4,636,397	\$4,508,266	\$26,478	\$4,534,744	\$4,474,415	\$60,329	\$0	\$4,534,744	\$653
Energy Management System Update	421-322-002	\$948,000	\$948,000	\$0	\$948,000	\$948,000	\$0	\$0	\$948,000	\$0
Evansdale ES - Roof	421-218	\$647,608	\$520,953	\$0	\$520,953	\$6,142	\$514,811	\$0	\$520,953	\$0
Facilities Assessment	421-700	\$1,770,367	\$1,770,367	\$0	\$1,770,367	\$501,571	\$1,268,796	\$0	\$1,770,367	\$0
Fairlington ES- HVAC, Ceilings & Lighting	421-121	\$1,977,131	\$1,901,978	\$48,380	\$1,950,358	\$1,923,678	\$26,680	\$0	\$1,950,358	\$3,605
FF&E- LS PR 1 Q09	421-341-033	\$44,379	\$44,379	\$0	\$44,379	\$44,379	\$0	\$0	\$44,379	\$0
FF&E- LS PR 2Q09	421-341-048	\$21,100	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$21,100
Flat Shoals ES - Roof	421-219	\$764,826	\$539,871	\$0	\$539,871	\$7,000	\$532,871	\$0	\$539,871	\$0
Forrest Hills ES - HVAC	421-137	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
General Services Main Project	421-600	\$302,149	\$193,991	\$0	\$193,991	\$187,349	\$6,642	\$0	\$193,991	\$108,158
Glen Haven ES - ADA	421-301-016	\$93,771	\$93,771	\$0	\$93,771	\$93,771	\$0	\$0	\$93,771	\$0
Glen Haven ES - Roof	421-225	\$990,000	\$629,027	\$0	\$629,027	\$361,599	\$267,428	\$0	\$629,027	\$0
Glen Haven ES - Widen Drive	421-341-032	\$131,200	\$129,802	\$0	\$129,802	\$15,670	\$114,132	\$0	\$129,802	\$1,398
Glen Haven ES- Replace Toilet Fixtures & Carpet	421-321-004	\$94,950	\$94,950	\$0	\$94,950	\$94,950	\$0	\$0	\$94,950	\$0
Gresham Park ES - ADA	421-301-017	\$80,516	\$75,886	\$4,631	\$80,517	\$80,517	\$0	\$0	\$80,517	(\$1)
Gresham Park ES- Replace carpet in Media Cente	421-320-008	\$16,947	\$16,947	\$0	\$16,947	\$8,287	\$8,660	\$0	\$16,947	\$0
Hambrick ES - HVAC	421-136	\$1,871,891	\$72,500	\$0	\$72,500	\$5,438	\$67,062	\$0	\$72,500	\$0
Hambrick ES - Roof	421-223	\$1,090,000	\$8,470	\$0	\$8,470	\$8,122	\$348	\$0	\$8,470	\$0
Hawthorne ES - ADA	421-303-011	\$13,750	\$13,750	\$0	\$13,750	\$0	\$13,750	\$0	\$13,750	\$0
Hawthorne ES - Roof	421-224	\$1,100,000	\$8,470	\$0	\$8,470	\$8,122	\$348	\$0	\$8,470	\$0
Henderson Mill ES - Chiller Replacement	421-341-008	\$69,228	\$69,228	\$0	\$69,228	\$69,228	\$0	\$0	\$69,228	\$0
Henderson Mill ES - New Door	421-341-034	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Henderson Mill ES- Ceiling Tiles	421-341-046	\$3,911	\$3,911	\$0	\$3,911	\$3,911	\$0	\$0	\$3,911	\$0
Henderson MS- Classroom & Restroom Upgrades	421-320-002	\$128,052	\$164,715	\$0	\$164,715	\$164,715	\$0	\$0	\$164,715	(\$36,663)
Henderson MS- Gym Light Switches	421-341-013	\$6,670	\$6,670	\$0	\$6,670	\$6,670	\$0	\$0	\$6,670	\$0
Henderson MS- Hold-Opens & Toilets	421-341-052	\$75,278	\$74,800	\$0	\$74,800	\$0	\$74,800	\$0	\$74,800	\$478
Henderson MS- Repair/Replace uneven tile near r	421-320-007	\$2,985	\$2,985	\$0	\$2,985	\$2,985	\$0	\$0	\$2,985	\$0
Heritage Center - Roof	421-204	\$351,097	\$349,597	\$0	\$349,597	\$350,288	(\$691)	\$0	\$349,597	\$1,500

SPL OST III Capital Improvement Program

Project Financial Summary

Monthly Status Report

Budget Category

Budget Category	Project Number	Current Budget	Original Contract	Executed Change Orders	Current Contract	Paid To Date	Contract Balance	Approved CORs	Current Contract Plus CORs	Uncommitted
Hooper Alexander ES - HVAC & ADA	421-134	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Huntley Hills ES - Roof	421-220	\$0	\$0	\$0	\$0	\$2,380	(\$2,380)	\$0	\$0	\$0
Huntley Hills ES - Restroom Renovations	421-321-006	\$66,767	\$66,767	\$0	\$66,767	\$66,767	\$0	\$0	\$0	\$66,767
Idlewood ES - ADA	421-301-003	\$9,611	\$9,611	\$0	\$9,611	\$9,611	\$0	\$0	\$0	\$9,611
Idlewood ES- Carpet Replacement	421-341-001	\$1,325	\$1,325	\$0	\$1,325	\$1,325	\$0	\$0	\$0	\$1,325
Idlewood ES- Parking Lots	421-321-010	\$237,201	\$237,202	\$0	\$237,202	\$237,202	\$0	\$0	\$0	\$237,202
Indian Creek ES - ADA	421-301-013	\$23,948	\$23,948	\$0	\$23,948	\$23,948	\$0	\$0	\$0	\$23,948
Indian Creek ES - HVAC	421-139	\$1,164,368	\$50,150	\$0	\$50,150	\$0	\$50,150	\$0	\$0	\$50,150
Kelley Lake ES - Courtyard	421-341-041	\$10,000	\$12,800	\$0	\$12,800	\$12,800	\$0	\$0	\$0	\$12,800
Kingsley Charter ES- Media Center Furniture	421-341-003	\$18,194	\$18,194	\$0	\$18,194	\$18,194	\$0	\$0	\$0	\$18,194
Kingsley ES - ADA	421-301-004	\$8,600	\$13,927	(\$5,327)	\$8,600	\$8,600	\$0	\$0	\$0	\$8,600
Kittredge Magnet ES- Chiller Replacement	421-341-020	\$99,202	\$99,202	\$0	\$99,202	\$99,202	\$0	\$0	\$0	\$99,202
Knollwood ES - HVAC & ADA	421-132	\$1,662,372	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Lakeside HS - Career Tech, ADA	421-125	\$24,289,410	\$20,832,696	\$760,090	\$21,592,786	\$2,949,005	\$18,643,781	\$11,841	\$21,604,627	(\$44,120)
Lakeside HS - Natatorium	421-341-012	\$293,903	\$274,511	\$13,995	\$288,506	\$271,394	\$17,112	\$0	\$288,506	\$5,397
Land	421-107	\$11,350	\$20,350	\$0	\$20,350	\$20,350	\$0	\$0	\$0	\$20,350
Laurel Ridge ES - ADA	421-301-006	\$67,396	\$67,396	\$0	\$67,396	\$67,396	\$0	\$0	\$0	\$67,396
Laurel Ridge- Replace Parking Lot & Tennis Cou	421-321-012	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Lithonia HS - Addition	421-126	\$0	\$25,488	\$0	\$25,488	\$25,488	\$0	\$0	\$0	\$25,488
Lithonia MS - Renovations	421-341-044	\$207,000	\$2,790	\$0	\$2,790	\$0	\$2,790	\$0	\$0	\$204,210
Lithonia MS - Security Cameras	421-341-045	\$85,982	\$85,982	\$0	\$85,982	\$100,398	(\$14,416)	\$0	\$85,982	\$0
Lithonia MS- Band Room Carpet	421-341-004	\$6,028	\$6,028	\$0	\$6,028	\$6,028	\$0	\$0	\$0	\$6,028
LSPR 1- Main Project	421-320	\$163,176	\$165,862	\$0	\$165,862	\$165,862	\$0	\$0	\$0	\$165,862
LSPR 2- Main Project	421-341	\$643,871	\$108,848	\$0	\$108,848	\$88,875	\$19,973	\$0	\$108,848	\$535,023
Marbut/Bouie ES- New Multi-purpose Bldg. Restr	421-321-003	\$239,039	\$232,941	\$6,098	\$239,039	\$239,039	\$0	\$0	\$0	\$239,039
Margaret Harris Center- Paving	421-321-007	\$31,232	\$31,232	\$0	\$31,232	\$31,232	\$0	\$0	\$0	\$31,232
Margaret Harris Center- Washing Machines	421-321-007D	\$9,050	\$9,050	\$0	\$9,050	\$9,050	\$0	\$0	\$0	\$9,050
Margaret Harris- Dryers	421-321-007E	\$704	\$704	\$0	\$704	\$704	\$0	\$0	\$0	\$704
Margaret Harris ES- Door Release System	421-341-005	\$6,748	\$6,748	\$0	\$6,748	\$6,748	\$0	\$0	\$0	\$6,748
Margaret Harris- Exterior Facade & RR Renovati	421-321-007B	\$326,943	\$320,440	\$6,503	\$326,943	\$326,943	\$0	\$0	\$0	\$326,943
Martin Luther King, Jr. HS - Addition	421-127	\$9,889,279	\$465,639	\$0	\$465,639	\$113,112	\$352,527	\$0	\$465,639	\$0
McLendon ES - HVAC & ADA	421-130	\$2,098,390	\$1,887,320	\$164,673	\$2,051,993	\$1,910,159	\$141,834	\$964	\$2,052,957	\$2,333

SPL OST III Capital Improvement Program

Project Financial Summary

Monthly Status Report

Budget Category

Number

Project Budget

Current Budget

Original Contract

Executed Change Orders

Current Contract

Paid To Date

Contract Balance

Approved CORs

Current Contract Plus CORs

Uncommitted

McLendon ES- Basketball Court, Paint & Blinds	421-341-030	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
McNair HS - SPLOST II Deferred	421-105	\$869,475	\$844,547	\$0	\$844,547	\$844,323	\$224	\$0	\$844,547	\$0	\$24,928
McNair MS- Ceiling Tile Replacement	421-341-015	\$49,058	\$49,058	\$0	\$49,058	\$49,058	\$0	\$0	\$0	\$49,058	\$0
McNair MS- Chiller Replacement	421-341-023	\$192,000	\$192,000	\$0	\$192,000	\$192,000	\$0	\$0	\$0	\$192,000	\$0
Middle School- Additional Parking Lot Lighting	421-341-038	\$200,382	\$200,382	\$0	\$200,382	\$200,382	\$0	\$0	\$0	\$200,382	\$0
Midvale ES - HVAC, Roof, ADA	421-112	\$3,070,205	\$2,935,201	\$71,919	\$3,007,120	\$2,818,426	\$188,694	\$0	\$3,007,120	\$0	\$4,102
Midway ES- Roof	421-214	\$547,056	\$556,661	(\$9,605)	\$547,056	\$547,056	\$0	\$0	\$547,056	\$0	\$0
Miller Grove HS - Addition	421-128	\$5,792,887	\$242,163	\$0	\$242,163	\$50,055	\$192,108	\$0	\$242,163	\$0	\$0
Modular Ramps ADA	421-303-001	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Montclair ES - Chiller Replacement	421-341-021	\$170,000	\$119,602	\$1,823	\$121,425	\$121,425	\$0	\$0	\$0	\$121,425	\$0
Montgomery ES - HVAC	421-138	\$1,599,826	\$69,000	\$0	\$69,000	\$0	\$69,000	\$0	\$0	\$69,000	\$0
Monggomery ES - Parking Lot, underground detent	421-320-005	\$234,448	\$217,000	\$12,530	\$229,530	\$209,147	\$20,383	\$4,917	\$234,447	\$0	\$1
Murphy Candler ES - Roof	421-202	\$654,341	\$645,446	\$8,895	\$654,341	\$654,341	\$0	\$0	\$654,341	\$0	\$0
Murphy Candler ES- Carpet Replacement	421-341-002	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Nancy Creek (Kittridge) ES - Roof	421-212	\$515,440	\$515,115	(\$1,875)	\$513,240	\$512,964	\$276	\$0	\$513,240	\$0	\$0
Nancy Creek ES - Parking Lot & bus loop	421-320-004	\$365,425	\$365,425	\$0	\$365,425	\$365,425	\$0	\$0	\$365,425	\$0	\$0
Narvie J Harris ES- Carpet Replacement	421-341-016	\$17,705	\$17,705	\$0	\$17,705	\$17,705	\$0	\$0	\$0	\$17,705	\$0
Oak Grove ES- Classroom Lighting	421-341-035	\$85,000	\$81,400	\$0	\$81,400	\$0	\$81,400	\$0	\$0	\$81,400	\$3,600
Oak Grove ES- Downspouts	421-321-013	\$43,331	\$43,331	\$0	\$43,331	\$43,331	\$0	\$0	\$43,331	\$0	\$0
Oak Grove ES- Exterior Lighting	421-341-029	\$75,000	\$8,925	\$0	\$8,925	\$0	\$8,925	\$0	\$0	\$8,925	\$66,075
Oak Grove ES- Paving	421-341-036	\$100,225	\$92,562	\$2,900	\$95,462	\$0	\$95,462	\$0	\$0	\$95,462	\$4,763
Panola Way ES - ADA	421-301-009	\$11,464	\$11,464	\$0	\$11,464	\$11,464	\$0	\$0	\$0	\$11,464	\$0
Program Contingency	421-900	\$22,716,950	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$22,716,950
Rainbow ES - Roof	421-203	\$370,791	\$325,178	\$46,022	\$371,200	\$371,200	\$0	\$0	\$371,200	\$0	(\$409)
Rainbow ES- Chiller Replacement	421-341-011	\$69,964	\$69,964	\$0	\$69,964	\$69,964	\$0	\$0	\$69,964	\$0	\$0
Redan HS - Roof, HVAC, Cancer Tech, ADA	421-111	\$11,343,479	\$8,342,946	\$251,910	\$8,594,857	\$7,407,454	\$1,187,403	(\$73,786)	\$8,521,071	\$0	\$73,013
Rockbridge ES - HVAC & ADA	421-133	\$1,671,149	\$75,229	\$0	\$75,229	\$0	\$75,229	\$0	\$0	\$75,229	\$0
Sagamore Hills ES - Roof	421-222	\$659,638	\$610,089	(\$7,731)	\$602,358	\$602,358	\$0	\$0	\$602,358	\$0	\$57,280
Sagamore Hills ES- Media Center Carpet Replace	421-341-017	\$7,142	\$7,142	\$0	\$7,142	\$7,142	\$0	\$0	\$7,142	\$0	\$0
Salem MS - Replace chalk boards w/white boards	421-320-010	\$24,406	\$24,406	\$0	\$24,406	\$24,406	\$0	\$0	\$24,406	\$0	\$0
Sam Moss Center - Paint and Carpet	421-341-019	\$67,700	\$41,904	\$0	\$41,904	\$35,486	\$6,418	\$0	\$41,904	\$0	\$25,796
Sam Moss Center- Paving Repair and Replaceme	421-341-037	\$474,855	\$402,265	\$72,590	\$474,855	\$474,855	\$0	\$0	\$474,855	\$0	\$0

SPL OST III Capital Improvement Program

Project Financial Summary

Monthly Status Report

Budget Category

Budget Category	Project Number	Current Budget	Original Contract	Executed Change Orders	Current Contract	Paid To Date	Contract Balance	Approved CORs	Current Contract Plus CORs	Uncommitted
Sam Moss Service Center - HVAC and Roof	421-131	\$1,706,432	\$1,609,580	(\$9,186)	\$1,600,393	\$1,472,456	\$127,937	\$21,336	\$1,621,729	\$69,637
School Choice/Relocation	421-320-003	\$271,205	\$226,861	\$0	\$226,861	\$213,812	\$13,049	\$0	\$226,861	\$44,344
Security Equipment	421-341-018	\$103,978	\$207,956	\$0	\$207,956	\$103,978	\$0	\$0	\$207,956	(\$103,978)
Security Lighting	421-321-009	\$506,540	\$506,540	\$0	\$506,540	\$506,540	\$0	\$0	\$506,540	\$0
Security Upgrade Systems	421-341-025	\$550,000	\$550,000	\$0	\$550,000	\$535,775	\$14,225	\$0	\$550,000	\$0
Sequoayah MS - Roof	421-205	\$1,958,812	\$1,665,152	\$34,485	\$1,699,637	\$1,504,463	\$195,174	\$0	\$1,699,637	\$4,179
Site Improvements 1- Main Project	421-321	\$42,891	\$15,071	\$0	\$15,071	\$15,071	\$0	\$0	\$15,071	\$27,820
Site Improvements 2- Main Project	421-322	\$62,534	\$536	\$0	\$536	\$536	\$0	\$0	\$536	\$62,018
Sky Haven ES - Roof	421-201	\$767,601	\$751,098	(\$22,701)	\$728,397	\$724,097	\$4,300	\$0	\$728,397	\$25,204
Sky Haven ES- Window Replacement	421-341-006	\$384,379	\$373,499	\$0	\$373,499	\$6,510	\$366,989	\$0	\$373,499	\$10,880
Smoke Rise ES - 20 classroom dry eraser boards	421-320-009	\$13,848	\$13,848	\$0	\$13,848	\$13,848	\$0	\$0	\$13,848	\$0
Snappinger ES - Roof	421-210	\$732,621	\$646,718	\$0	\$646,718	\$437,922	\$208,796	\$0	\$646,718	\$0
SPL OST Audit	421-000	\$30,000	\$47,880	\$0	\$47,880	\$47,880	\$0	\$0	\$47,880	(\$17,880)
Stephenson HS-Triack Field Improvements	421-321-001	\$259,658	\$259,658	\$0	\$259,658	\$259,658	\$0	\$0	\$259,658	\$0
Stephenson MS - HVAC	421-113	\$35,120	\$35,120	\$0	\$35,120	\$35,120	\$0	\$0	\$35,120	\$0
Stone Mill ES - HVAC	421-140	\$1,396,903	\$52,500	\$0	\$52,500	\$0	\$52,500	\$0	\$52,500	\$0
Stone Mountain ES - HVAC & ADA	421-135	\$1,731,048	\$116,240	\$0	\$116,240	\$0	\$116,240	\$0	\$116,240	\$0
Stone Mountain HS - HVAC, Roof	421-110	\$6,596,254	\$5,557,744	\$408,501	\$5,966,245	\$4,898,971	\$1,067,274	\$0	\$5,966,245	\$0
Stonemill ES- Parking Lot Repair	421-321-001A	\$53,373	\$53,373	\$0	\$53,373	\$53,373	\$0	\$0	\$53,373	\$0
Stoneview ES- Chiller Replacement	421-341-024	\$94,180	\$91,420	\$0	\$91,420	\$94,180	(\$2,760)	\$2,760	\$94,180	\$0
Stoneview ES- Kitchen Equipment	421-341-007	\$162,907	\$164,952	\$5,018	\$169,970	\$145,706	\$24,264	\$0	\$169,970	(\$7,063)
SW DeKalb HS - SPLOST II Deferred, ADA	421-102	\$22,310,250	\$2,443,172	\$184,785	\$2,627,957	\$1,976,429	\$651,528	\$0	\$2,627,957	\$0
Technology	421-503	\$6,000,000	\$24,065	\$0	\$24,065	\$24,065	\$0	\$0	\$24,065	\$5,975,935
Technology - Media Center Upgrades	421-502	\$10,000,000	\$9,250,856	\$0	\$9,250,856	\$9,250,856	\$0	\$0	\$9,250,856	\$749,144
Technology - Refresh Cycle for all Schools and Ct	421-501	\$19,598,581	\$18,340,164	\$0	\$18,340,164	\$18,340,164	(\$33,158)	\$0	\$18,340,164	\$1,258,417
Terry Mill ES - Parking Lot Paving	421-320-011	\$339,297	\$328,509	\$11,279	\$339,788	\$339,788	\$0	\$0	\$339,788	(\$491)
Terry Mill ES - Reloc Hooper Alex DESA, renova	421-320-006	\$536,460	\$512,217	\$27,184	\$539,401	\$566,563	(\$27,162)	\$0	\$539,401	(\$2,941)
Terry Mill ES (DESA) - Roof	421-211	\$610,187	\$612,687	(\$2,500)	\$610,187	\$610,187	\$0	\$0	\$610,187	\$0
Towers HS - SPLOST II Deferred	421-103	\$3,046,400	\$2,744,902	\$102,723	\$2,847,625	\$2,693,229	\$154,396	(\$1,060)	\$2,846,565	\$111,028
Tucker HS - New Replacement High School	421-108	\$61,365,016	\$53,463,133	\$6,409,499	\$59,872,632	\$53,849,654	\$6,022,978	(\$35,05)	\$59,837,127	\$2,209
Vanderlyn ES - HVAC, Roof, ADA	421-116	\$2,308,591	\$1,893,457	\$129,933	\$2,023,390	\$1,986,539	\$36,851	\$0	\$2,023,390	(\$150)
Vanderlyn ES- Replace Toilet Fixtures	421-321-005	\$71,116	\$0	\$71,116	\$71,116	\$71,116	\$0	\$0	\$71,116	\$0

SPL OST III Capital Improvement Program

Project Financial Summary

Monthly Status Report

Budget Category

	Project Number	Current Budget	Original Contract	Executed Change Orders	Current Contract	Paid To Date	Contract Balance	Approved CORs	Current Contract Plus CORs	Uncommitted
Wadsworth ES - Roof	421-206	\$638,290	\$638,919	(\$629)	\$638,290	\$638,290	\$0	\$0	\$638,290	\$0
Wadsworth ES- Band Lockers	421-320-003D	\$24,000	\$24,000	\$0	\$24,000	\$24,000	\$0	\$0	\$24,000	\$0
Wadsworth Magnet- HVAC & Lighting	421-341-027	\$400,000	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$400,000
Warren Tech - HVAC	421-129	\$1,130,212	\$46,863	\$0	\$46,863	\$0	\$46,863	\$0	\$46,863	\$0
William Bradley Bryant Center	421-228	\$3,500,000	\$10,519	\$0	\$10,519	\$7,956	\$2,563	\$0	\$10,519	\$0
Woodridge ES - Roof	421-227	\$990,000	\$593,822	\$0	\$593,822	\$483,727	\$110,095	\$0	\$593,822	\$0
Woodward ES - HVAC, Roof	421-109	\$2,201,816	\$2,008,231	\$143,219	\$2,151,450	\$2,151,450	\$0	\$0	\$2,151,450	\$50,366
Grand Total		\$513,469,963	\$357,640,838	\$31,249,017	\$388,889,854	\$267,994,232	\$120,895,623	\$1,103,992	\$389,993,847	\$39,848,910

SPLOST III Capital Improvement Program

Projects Status by Phase

Monthly Status Report

Project Name	Project Number	Delivery Method	Current Budget	Current Contract
1. Planning & Programming				
1 Bulk Purchasing- Lighting	421-600-005	Fixed Price	\$0	\$0
2 Clifton ES- Ceiling Tiles	421-341-039	Fixed Price	\$110,000	\$0
3 Knollwood ES - HVAC & ADA	421-132	Design / Bid / Build	\$1,662,372	\$0
4 Wadsworth Magnet- HVAC & Lighting	421-341-027	Design / Build	\$400,000	\$0
1. Planning & Programming Subtotal:			\$2,172,372	\$0
2. Design				
1 ADA Group D	421-304	Design / Bid / Build	\$337,051	\$2,343
2 Avondale HS- Renovations	421-123-002	Design / Bid / Build	\$4,480,700	\$304,608
3 Chamblee HS- New Replacement High School	421-117	CM @ Risk	\$11,152,507	\$2,981,623
4 DeKalb International Student Center- Canopy	421-341-047	Fixed Price	\$2,000	\$9,340
5 Hambrick ES - HVAC	421-136	Design / Bid / Build	\$1,871,891	\$72,500
6 Hawthorne ES - ADA	421-303-011	Design / Bid / Build	\$13,750	\$13,750
7 Indian Creek ES - HVAC	421-139	Design / Bid / Build	\$1,164,368	\$50,150
8 Miller Grove HS - Addition	421-128	Design / Bid / Build	\$5,792,887	\$242,163
9 Montgomery ES - HVAC	421-138	Design / Bid / Build	\$1,599,826	\$69,000
10 Rockbridge ES - HVAC & ADA	421-133	Design / Bid / Build	\$1,671,149	\$75,229
11 Stone Mill ES - HVAC	421-140	Design / Bid / Build	\$1,396,903	\$52,500
12 Stone Mountain ES - HVAC & ADA	421-135	Design / Bid / Build	\$1,731,048	\$116,240
13 SW DeKalb HS - SPLOST II Deferred, ADA	421-102	Design / Bid / Build	\$22,310,250	\$2,627,957
14 Warren Tech - HVAC	421-129	Design / Bid / Build	\$1,130,212	\$46,863
2. Design Subtotal:			\$54,654,542	\$6,664,266
3. Procurement				
1 Bulk Purchase- Ceiling Tile and Grid	421-600-002	Fixed Price	\$0	\$0
2 Emergency Generators	421-321-015	Design / Bid / Build	\$3,800,000	\$115,994
3 Evansdale ES - Roof	421-218	Design / Bid / Build	\$647,608	\$520,953
4 Hambrick ES - Roof	421-223	Design / Bid / Build	\$1,090,000	\$8,470
5 Hawthorne ES - Roof	421-224	Design / Bid / Build	\$1,100,000	\$8,470
6 Lithonia MS - Renovations	421-341-044	Fixed Price	\$207,000	\$2,790
7 William Bradley Bryant Center	421-228	Design / Bid / Build	\$3,500,000	\$10,519
3. Procurement Subtotal:			\$10,344,608	\$667,196

SPLOST III Capital Improvement Program

Projects Status by Phase

Monthly Status Report

Project Name	Project Number	Delivery Method	Current Budget	Current Contract
4. Construction				
1 ADA Group A- Main Project	421-301	Fixed Price	\$81,808	\$91,389
2 ADA Group B- Main Project	421-302	Design / Build	\$510,448	\$1,935
3 ADA Group B-1	421-302-001	Design / Build	\$496,000	\$495,645
4 ADA Group B-2	421-302-002	Design / Build	\$407,299	\$364,968
5 Allgood ES- Roof	421-217	Design / Bid / Build	\$585,240	\$449,356
6 Bulk Purchase - Plumbing Fixtures	421-322-001	Fixed Price	\$2,043,950	\$876,914
7 Bulk Purchase- Fixed Audience Seating	421-600-006	Fixed Price	\$0	\$0
8 Bulk Purchase- Metal Lockers	421-600-003	Fixed Price	\$0	\$0
9 Carpet Replacement- Multiple Schools (LSPR 2Q09)	421-341-040	Fixed Price	\$30,667	\$29,836
10 Cedar Grove HS - HVAC, Lighting, Ceiling & Roof	421-115	Fixed Price	\$6,211,315	\$5,153,921
11 Chapel Hill MS- Ceiling Tiles & Site Work	421-341-028	Fixed Price	\$240,275	\$275
12 Clarkston HS -Renovation & Addition	421-118	Design / Bid / Build	\$12,275,194	\$10,278,330
13 Dunwoody HS - Renovation & Addition	421-120	Design / Bid / Build	\$20,530,480	\$17,796,451
14 Emergency HVAC Work	421-101	Fixed Price	\$4,636,397	\$4,534,744
15 FF&E- LSPR 2Q09	421-341-048	Fixed Price	\$21,100	\$0
16 Flat Shoals ES - Roof	421-219	Design / Bid / Build	\$764,826	\$539,871
17 General Services Main Project	421-600	Fixed Price	\$302,149	\$193,991
18 Glen Haven ES - Roof	421-225	Design / Bid / Build	\$990,000	\$629,027
19 Glen Haven ES - Widen Drive	421-341-032	Design / Build	\$1,311,200	\$129,802
20 Lakeside HS - Career Tech, ADA	421-125	Guaranteed Maximum Price	\$24,289,410	\$21,592,786
21 LSPR 2- Main Project	421-341	Design / Bid / Build	\$643,871	\$108,848
22 Oak Grove ES- Classroom Lighting	421-341-035	Fixed Price	\$85,000	\$81,400
23 Sam Moss Service Center - HVAC and Roof	421-131	Design / Build	\$1,706,432	\$1,600,393
24 Site Improvements 1- Main Project	421-321		\$42,891	\$15,071
25 Site Improvements 2- Main Project	421-322		\$62,554	\$536
26 Snapfinger ES - Roof	421-210	Design / Bid / Build	\$732,621	\$646,718
27 Woodridge ES - Roof	421-227	Design / Bid / Build	\$990,000	\$593,822
4. Construction Subtotal:				\$66,206,029
5. Close-out				
1 ADA Group A-2A	421-301-021	Design / Build	\$561,574	\$556,774
2 ADA Group A-2B	421-301-022	Design / Build	\$678,336	\$678,336
3 Administrative & Instructional Complex (AIC)	421-124	Design / Build	\$31,824,966	\$31,052,743

SPL OST III Capital Improvement Program

Projects Status by Phase

Monthly Status Report

Project Name	Project Number	Delivery Method	Current Budget	Current Contract
5. Close-out				
4 Chesnut Charter ES- Basketball Court Replacement	421-322-004	Design / Bid / Build	\$52,957	\$52,957
5 Columbia HS - SPLOST II Deferred	421-104	CM @ Risk	\$11,452,000	\$11,271,669
6 Cross Keys HS - Renovation & Addition	421-106	CM @ Risk	\$18,612,631	\$17,230,440
7 Druid Hills HS - Renovation & Addition	421-119	CM @ Risk	\$18,633,137	\$18,206,819
8 DSA Relocation to Avondale HS	421-123	Design / Bid / Build	\$5,348,715	\$4,754,369
9 Fairington ES- HVAC, Ceilings & Lighting	421-121	Design / Bid / Build	\$1,977,131	\$1,950,358
10 Henderson MS- Hold-Opens & Toilets	421-341-052	Design / Bid / Build	\$75,278	\$74,800
11 Lakeside HS - Natatorium	421-341-012	Fixed Price	\$293,903	\$288,506
12 Margaret Harris- Exterior Facade & RR Renovation	421-321-007B	Fixed Price	\$326,943	\$326,943
13 McLendon ES - HVAC & ADA	421-130	Design / Bid / Build	\$2,098,390	\$2,051,993
14 Midvale ES - HVAC, Roof, ADA	421-112	Design / Bid / Build	\$3,070,205	\$3,007,120
15 Oak Grove ES- Paving	421-341-036	Design / Bid / Build	\$100,225	\$95,462
16 Redan HS - Roof, HVAC, Career Tech, ADA	421-111	Design / Bid / Build	\$11,343,479	\$8,594,857
17 Sequoyah MS - Roof	421-205	Design / Bid / Build	\$1,958,812	\$1,699,637
18 Stone Mountain HS - HVAC, Roof	421-110	Design / Bid / Build	\$6,596,254	\$5,966,245
19 Towers HS - SPLOST II Deferred	421-103	Design / Bid / Build	\$3,046,400	\$2,847,625
20 Tucker HS - New Replacement High School	421-108	CM @ Risk	\$61,365,016	\$59,872,632
21 Vanderlyn ES - HVAC, Roof, ADA	421-116	Design / Bid / Build	\$2,308,591	\$2,023,390
5. Close-out Subtotal:			\$181,724,943	\$172,603,675
6. Completed				
1 Allgood ES - ADA	421-301-010	Fixed Price	\$32,556	\$32,556
2 Atherton ES- Chiller Replacement	421-341-022	Fixed Price	\$123,176	\$123,176
3 Avondale ES - ADA	421-301-005	Fixed Price	\$22,406	\$22,406
4 Avondale ES - Roof	421-209	Design / Bid / Build	\$578,746	\$578,746
5 Baisin Heaters	421-321-014	Fixed Price	\$345,500	\$345,500
6 Bob Mathis ES - ADA	421-301-001	Fixed Price	\$22,299	\$22,299
7 Brockett ES - Make-up Air Units	421-320-001	Fixed Price	\$94,030	\$94,030
8 Buses 1	421-401		\$3,479,453	\$3,479,453
9 Buses 3	421-403		\$4,000,000	\$3,984,380
10 Carpet Replacement - Multiple Schools (LSPR 1Q09)	421-341-031	Fixed Price	\$10,237	\$10,237
11 Chamblee Charter HS - Lockers	421-341-014	Fixed Price	\$50,000	\$43,457
12 Chamblee MS - Sound Panels	421-341-050	Fixed Price	\$27,500	\$38,900

SPL OST III Capital Improvement Program

Projects Status by Phase

Monthly Status Report

Project Name	Project Number	Delivery Method	Current Budget	Current Contract
6. Completed				
13 Chamblee MS- Mirror	421-341-049	Fixed Price	\$960	\$960
14 Champion MS - ADA	421-301-020	Fixed Price	\$15,362	\$0
15 Champion Theme MS - Roof	421-208	Design / Bid / Build	\$382,342	\$382,342
16 Champion Theme MS- Chiller Replacement	421-341-010	Fixed Price	\$47,539	\$47,539
17 Chapel Hill ES- Chiller Replacement	421-341-009	Fixed Price	\$69,964	\$69,964
18 Chapel Hill MS- Track & Tennis Court	421-341-051	Fixed Price	\$243,956	\$255,522
19 Chesnut Charter ES - ADA	421-303-002	Design / Build	\$448,179	\$443,779
20 CLEA 2008- Comprehensive Lighting Energy Audit	421-600-001	Fixed Price	\$98,032	\$98,032
21 Clifton ES - HVAC	421-114		\$172,792	\$172,792
22 DeKalb HS of Tech North - Roof	421-221		\$0	\$0
23 DeKalb HS of Tech South - Roof	421-215	Design / Bid / Build	\$352,288	\$351,428
24 Eagle Wood Academy- Replace Windows & Repair Doors	421-321-011	Fixed Price	\$55,435	\$55,435
25 East Campus - APHONE	421-341-026		\$0	\$0
26 Eldridge L. Miller ES - Roof	421-216	Design / Bid / Build	\$452,953	\$452,953
27 Energy Management System Update	421-322-002	Fixed Price	\$948,000	\$948,000
28 FF&E- LS PR 1Q09	421-341-033	Fixed Price	\$44,379	\$44,379
29 Glen Haven ES - ADA	421-301-016	Design / Build	\$93,771	\$93,771
30 Glen Haven ES- Replace Toilet Fixtures & Carpet	421-321-004	Fixed Price	\$94,950	\$94,950
31 Gresham Park ES - ADA	421-301-017	Fixed Price	\$80,516	\$80,517
32 Gresham Park ES- Replace carpet in Media Center	421-320-008	Fixed Price	\$16,947	\$16,947
33 Henderson Mill ES - Chiller Replacement	421-341-008	Fixed Price	\$69,228	\$69,228
34 Henderson Mill ES- Ceiling Tiles	421-341-046	Fixed Price	\$3,911	\$3,911
35 Henderson MS- Classroom & Restroom Upgrades	421-320-002	Fixed Price	\$128,052	\$164,715
36 Henderson MS- Gym Light Switches	421-341-013	Fixed Price	\$6,670	\$6,670
37 Henderson MS- Repair/Replace uneven tile near ref	421-320-007	Fixed Price	\$2,985	\$2,985
38 Heritage Center - Roof	421-204	Design / Bid / Build	\$351,097	\$349,597
39 Hooper Alexander ES - HVAC & ADA	421-134		\$0	\$0
40 Huntley Hills ES- Restroom Renovations	421-321-006	Fixed Price	\$66,767	\$66,767
41 Idlewood ES - ADA	421-301-003	Fixed Price	\$9,611	\$9,611
42 Idlewood ES- Carpet Replacement	421-341-001	Fixed Price	\$1,325	\$1,325
43 Idlewood ES- Parking Lots	421-321-010	Design / Build	\$237,201	\$237,202
44 Indian Creek ES - ADA	421-301-013	Fixed Price	\$23,948	\$23,948
45 Kelley Lake ES - Courtyard	421-341-041		\$10,000	\$12,800

SPL OST III Capital Improvement Program

Projects Status by Phase

Monthly Status Report

Project Name	Project Number	Delivery Method	Current Budget	Current Contract
6. Completed				
46 Kingsley Charter ES- Media Center Furniture	421-341-003	Fixed Price	\$18,194	\$18,194
47 Kingsley ES - ADA	421-301-004	Fixed Price	\$8,600	\$8,600
48 Kittridge Magnet ES- Chiller Replacement	421-341-020	Fixed Price	\$99,202	\$99,202
49 Laurel Ridge ES - ADA	421-301-006	Design / Build	\$67,396	\$67,396
50 Laurel Ridge- Replace Parking Lot & Tennis Court	421-321-012		\$0	\$0
51 Lithonia MS - Security Cameras	421-341-045	Fixed Price	\$85,982	\$85,982
52 Lithonia MS- Band Room Carpet	421-341-004	Fixed Price	\$6,028	\$6,028
53 LSPR 1- Main Project	421-320		\$163,176	\$165,862
54 Marbut/Bouie ES- New Multi-purpose Bldg. Restrooms	421-321-003	Design / Build	\$239,039	\$239,039
55 Margaret Harris Center- Paving	421-321-007	Fixed Price	\$31,232	\$31,232
56 Margaret Harris Center- Washing Machines	421-321-007D	Fixed Price	\$9,050	\$9,050
57 Margaret Harris-Dryers	421-321-007E	Fixed Price	\$704	\$704
58 Margaret Harris ES- Door Release System	421-341-005	Fixed Price	\$6,748	\$6,748
59 McLendon ES- Basketball Court, Paint & Blinds	421-341-030		\$0	\$0
60 McNair HS - SPLOST II Deferred	421-105	Design / Bid / Build	\$869,475	\$844,547
61 McNair MS- Ceiling Tile Replacement	421-341-015	Fixed Price	\$49,058	\$49,058
62 McNair MS- Chiller Replacement	421-341-023	Fixed Price	\$192,000	\$192,000
63 Middle School- Additional Parking Lot Lighting	421-341-038	Design / Build	\$200,382	\$200,382
64 Midway ES - Roof	421-214	Design / Bid / Build	\$547,056	\$547,056
65 Modular Ramps ADA	421-303-001		\$0	\$0
66 Monclair ES - Chiller Replacement	421-341-021	Fixed Price	\$170,000	\$121,425
67 Montgomery ES - Parking Lot, undergroud detention	421-320-005	Design / Build	\$234,448	\$229,530
68 Murphy Candler ES - Roof	421-202	Design / Bid / Build	\$654,341	\$654,341
69 Murphy Candler ES- Carpet Replacement	421-341-002	Fixed Price	\$0	\$0
70 Nancy Creek (Kittridge) ES - Roof	421-212	Design / Bid / Build	\$515,440	\$513,240
71 Nancy Creek ES- Parking Lot & bus loop	421-320-004	Design / Build	\$365,425	\$365,425
72 Narvie J Harris ES- Carpet Replacement	421-341-016	Fixed Price	\$17,705	\$17,705
73 Oak Grove ES- Downspouts	421-321-013	Design / Build	\$43,331	\$43,331
74 Oak Grove ES- Exterior Lighting	421-341-029	Fixed Price	\$75,000	\$8,925
75 Panola Way ES - ADA	421-301-009	Fixed Price	\$11,464	\$11,464
76 Rainbow ES - Roof	421-203		\$370,791	\$371,200
77 Rainbow ES- Chiller Replacement	421-341-011	Fixed Price	\$69,964	\$69,964
78 Saganore Hills ES - Roof	421-222	Design / Bid / Build	\$659,638	\$602,358

SPL OST III Capital Improvement Program

Projects Status by Phase

Monthly Status Report

Project Name	Project Number	Delivery Method	Current Budget	Current Contract
6. Completed				
79 Sagamore Hills ES- Media Center Carpet Replacement	421-341-017	Fixed Price	\$7,142	\$7,142
80 Salem MS - Replace chalk boards w/white boards	421-320-010	Fixed Price	\$24,406	\$24,406
81 Sam Moss Center - Paint and Carpet	421-341-019	Fixed Price	\$67,700	\$41,904
82 Sam Moss Center- Paving Repair and Replacement	421-341-037	Design / Build	\$474,855	\$474,855
83 School Choice/Relocation	421-320-003		\$271,205	\$226,861
84 Security Equipment	421-341-018		\$103,978	\$207,956
85 Security Lighting	421-321-009	Design / Build	\$506,540	\$506,540
86 Security Upgrade Systems	421-341-025	Fixed Price	\$550,000	\$550,000
87 Sky Haven ES - Roof	421-201	Design / Bid / Build	\$767,601	\$728,397
88 Smoke Rise ES - 20 classroom dry eraser boards	421-320-009	Fixed Price	\$13,848	\$13,848
89 Stephenson HS- Track Field Improvements	421-321-001	Design / Build	\$259,658	\$259,658
90 Stephenson MS -HVAC	421-113		\$35,120	\$35,120
91 Stonemill ES- Parking Lot Repair	421-321-001A	Fixed Price	\$53,373	\$53,373
92 Stoneview ES- Chiller Replacement	421-341-024	Fixed Price	\$94,180	\$91,420
93 Stoneview ES- Kitchen Equipment	421-341-007	Fixed Price	\$162,907	\$169,970
94 Terry Mill ES - Parking Lot Paving	421-320-011	Fixed Price	\$339,297	\$339,788
95 Terry Mill ES - Reloc Hooper Alex DESA, renovation	421-320-006	Design / Bid / Build	\$536,460	\$539,401
96 Terry Mill ES (DESA) - Roof	421-211	Design / Bid / Build	\$610,187	\$610,187
97 Vanderlyn ES- Replace Toilet Fixtures	421-321-005	Fixed Price	\$71,116	\$71,116
98 Wadsworth ES- Roof	421-206	Design / Bid / Build	\$638,290	\$638,290
99 Wadsworth ES- Band Lockers	421-320-003D	Fixed Price	\$24,000	\$24,000
100 Woodward ES - HVAC, Roof	421-109	Design / Bid / Build	\$2,201,816	\$2,151,450
6. Completed Subtotal:			\$26,909,611	\$26,678,879
7. On-Going SPL OST Activity				
1 Buses 2	421-402		\$4,520,547	\$4,524,398
2 Capital Improvement Team Compensation	421-650		\$15,374,724	\$15,374,724
3 COPS Debt Reduction	421-001		\$66,000,000	\$66,000,000
4 Facilities Assessment	421-700	Fixed Price	\$1,770,367	\$1,770,367
5 Land	421-107		\$11,350	\$20,350
6 Program Contingency	421-900		\$22,716,950	\$0
7 SPLOST Audit	421-000		\$30,000	\$47,880
8 Technology	421-503		\$6,000,000	\$24,065

SPLCOST III Capital Improvement Program

Projects Status by Phase

Monthly Status Report

Project Name	Project Number	Delivery Method	Current Budget	Current Contract
--------------	----------------	-----------------	----------------	------------------

7. On-Going SPLOST Activity

9 Technology - Media Center Upgrades	421-502		\$10,000,000	\$9,250,856
10 Technology - Refresh Cycle for all Schools and Ctr	421-501		\$19,598,581	\$18,340,164

7. On-Going SPLOST Activity Subtotal

\$146,022,519

\$115,352,804

8. On Hold

1 ADA Group B-3	421-302-003	Design / Bid / Build	\$0	\$0
2 ADA Group C- Main Project	421-303	Design / Bid / Build	\$1,023,071	\$59,864
3 ADA Group E	421-305	Design / Bid / Build	\$427,202	\$0
4 Allgood ES- Kitchen	421-341-043	Fixed Price	\$40,000	\$0
5 Ashford Park ES - ADA	421-301-007	Fixed Price	\$54,200	\$44,924
6 Chamblee MS - Roof	421-226		\$83,683	\$0
7 Coralwood Diagnostic Ctr. - Renovation & Addition	421-213	Design / Bid / Build	\$423,427	\$365,263
8 Huntley Hills ES - Roof	421-220		\$0	\$0
9 Lithonia HS - Addition	421-126		\$0	\$25,488
10 Martin Luther King, Jr. HS - Addition	421-127	Design / Bid / Build	\$9,889,279	\$465,639

8. On Hold Subtotal:

\$12,300,862

9. Deemed Unnecessary

1 Bulk Purchase- Theatrical Lighting & Sound System	421-600-004	Fixed Price	\$0	\$0
2 Chamblee MS- Painting	421-341-042	Fixed Price	\$145,000	\$9,135
3 Clarkston Center - Roof	421-207		\$0	\$0
4 Forrest Hills ES - HVAC	421-137		\$0	\$0
5 Henderson Mill ES - New Door	421-341-034		\$0	\$0
6 Sky Haven ES- Window Replacement	421-341-006	Fixed Price	\$384,379	\$373,499

9. Deemed Unnecessary Subtotal:

\$529,379

\$382,634

SPL OST III Capital Improvement Program

Projects Status by Phase

Monthly Status Report

Project Name

Project Number

Delivery Method

Current Budget

Current Contract

Program Totals: \$513,469,963

\$388,889,854

Project Budgets by Phase

Close-out, \$181,724,943

Procurement, \$10,344,608

Planning & Programming, \$2,172,372

On-Going SPLOST Activity, \$146,022,519

Design, \$54,654,542

On Hold, \$12,300,862

Completed, \$26,909,611

On-Going SPLOST Activity

Construction, \$78,811,127

Deemed Unnecessary, \$529,379

Planning & Programming

Procurement

Close-out

Completed

Construction

Deemed Unnecessary

Design

On Hold

Planning & Programming

Procurement

SPLOST III Capital Improvement Program

Monthly Status Report

Change Order Details for the Month of April 2011

Project Name: Bulk Purchase - Plumbing Fixtures

Project No. / Vendor Name	CO No.	CO Date	CO Amount	COR No.	COR Date	COR Amount	COR Description
421-322-001 Continental Eng	2	4/5/2011	\$5,270	2	3/23/2011	\$5,270	Saw cut concrete/glazed blocks in both Pre-K and Gang Bathrooms and change out copper piping to meet new elevations. One additional toilet was installed that was not in original contract.

Project Name: Clarkston HS - Renovation & Addition

Project No. / Vendor Name	CO No.	CO Date	CO Amount	COR No.	COR Date	COR Amount	COR Description
421-118 Hogan Construction	14	4/13/2011	\$48,928	21	3/24/2011	\$3,397	Plenum in bathroom

421-118 Hogan Construction	43	3/24/2011	\$4,733				Remove existing chalkboards Phase 5
	44	3/24/2011	\$3,248				Install door closers in phase 5 and 6
	61	4/4/2011	\$3,309				Install new AHU to replace existing unit in Phase 2 West. New duct was installed to feed four small rooms in the area.
	62	3/24/2011	\$17,940				New parapet Wall to be added to match elevation height on drawings-Phase 1
	63	3/24/2011	\$5,097				Phase 6-Re-wire existing HVAC units Phase 5-Added 25 GFI receptacles Phase 2-Added 20 GFI receptables
	66	3/24/2011	\$1,432				Broom sweeps/Fire dampers/Paintgrip locker covers
	68	3/24/2011	\$1,065				Additional fire dampers in Phase 2
	69	3/24/2011	\$802				Paint grip covers for lockers.
	7	3/24/2011	\$7,905				Demo Chalkboard (Phase 9 & 4)



SPLOST III Capital Improvement Program

Monthly Status Report

Change Order Details for the Month of April 2011

Project Name: Cross Keys HS - Renovation & Addition						
Project No. / Vendor Name	CO No.	CO Date	CO Amount	COR No.	COR Date	COR Amount
421-106 Evergreen Construction	26	4/6/2011	\$43,069	5contingenc	3/3/2011	\$0
						RFI-102 Piping Connections from Sand Filter to Cooling Tower
	26savings	2/2/2011	\$0			Conduit for AT&T Fiber Optic
	26savings	3/31/2011	\$0			Raise Light Fixtures in Construction Technology
	26savings	1/25/2011	\$0			Door Frame and Door modifications to existing frames (Area 7, band, music, and gym)
	26savings	1/25/2011	\$0			Door, Frame and hardware
	26savings	1/25/2011	\$0			RFI#34 - Door, hardware and frame questions.
	26savings	1/25/2011	\$0			Wing 2 Door and Frame Revisions
	26savings	2/10/2011	\$0			Relocate Hood fan from Home economics classroom to the Health science lab
	26savings	2/16/2011	\$0			RFI 206-HVAC and electrical revisions rooms 100.7 and 100.8
	26savings	3/24/2011	\$0			RFI 147-Issued Women's Locker Room Sketch
	26savings	3/31/2011	\$0			RFI 170-Equipment Yard Fencing
	26savings	2/28/2011	\$0			Flooring and Other miscellaneous Changes-No Cost
	26scope	3/15/2011	\$2,232			RFI #201-Electrical for Equipment in Wing 1 and Wing 2
	26scope	2/10/2011	\$1,622			Relocate Security Monitors from main office to 301.2
	26scope	2/10/2011	\$4,191			Tie in trailer intercom speakers to new head end unit
	26scope	2/28/2011	\$2,923			Noise at gym return air grilles
	26scope	2/28/2011	\$1,928			Rewire existing compressors for science labs in wings 2 and 3
	26scope	3/3/2011	\$12,975			Add power to existing exterior lighting g
	26scope	3/3/2011	\$17,198			RFI 156-HVAC Work at Admin Area
421-106 Evergreen Construction	27	4/20/2011	\$23,967	7contingenc	3/31/2011	\$0
						RFI #225-Wash Sink at Kitchen Restrooms
	7contingenc	3/31/2011	\$0			Paint Walls at Automotive Labs
	7contingenc	3/31/2011	\$0			Home Economics Hood Fan Ansul System Power Requirements-- shunt trip breakers
	7contingenc	3/31/2011	\$0			Fire marshal revisions per 100% Fire marshal walk thru on 7/27/10 for gym and 80% walk thru on 7/27/10 for wing 3.
	27scope	3/31/2011	\$15,232			RFI #178. Soffit Details at Science Lab
	27scope	3/31/2011	\$2,558			Notes from Pre Fire Marshal Walk through-electrical revisions
	27scope	3/31/2011	\$2,052			Notes from 12/13/10 50/80% Pre-Fire marshal walk thru
	27scope	3/31/2011	\$4,125			Leak under door 350d

Project Name: DSA Relocation to Avondale HS

Project No. / Vendor Name	CO No.	CO Date	CO Amount	COR No.	COR Date	COR Amount	COR Description
422-123 Warren Epstein	2	4/27/2011	\$2,500	2	4/22/2011	\$2,500	Additional reimbursables for blueprinting, copies, phone & postage to complete project

SPL OST III Capital Improvement Program

Monthly Status Report

Change Order Details for the Month of April 2011

Project Name: Dunwoody HS - Renovation & Addition

Project No. / Vendor Name	CO No.	CO Date	CO Amount	COR No.	COR Date	COR Amount	COR Description
421-120 Doster Construction C	16	4/13/2011	\$41,691	103	3/31/2011	\$17,500	Auditorium Mechanical Revisions
				111	3/24/2011	\$17,270	11 Additional Science Lab Tables
				114	2/28/2011	\$835	Extending the existing dryer vent in the Consumer Science Lab (Room 2704)
				115	3/18/2011	\$1,799	Fire Dampers at auditorium
				117	3/31/2011	\$1,509	Replace panic devices with Von Duprin
				75	3/18/2011	\$4,013	Demo Existing Brick and Replace with CMU @ North stair
				98	3/29/2011	(\$1,235)	Credit for not installing turn downs on sidewalk.
							Smoke rate existing storage rooms, mech/electrooms, stairwells.

Project Name: Lakeside HS - Career Tech, ADA

Project No. / Vendor Name	CO No.	CO Date	CO Amount	COR No.	COR Date	COR Amount	COR Description
421-120 Perkins and Will	2	4/13/2011	\$8,700	2		\$8,700	

Project Name: Oak Grove ES- Paving

Project No. / Vendor Name	CO No.	CO Date	CO Amount	COR No.	COR Date	COR Amount	COR Description
421-341-036 ShepCo Paving	1 - FINAL	4/1/2011	\$2,900		1/26/2011	\$2,900	Fire lane signs, speed bumps, ramp

Project Name: Sequoyah MS - Roof

Project No. / Vendor Name	CO No.	CO Date	CO Amount	COR No.	COR Date	COR Amount	COR Description
421-205 Woodall Roofing Com	2	4/1/2011	(\$1,995)	1	7/30/2010	\$2,440	Cost Adjustment for Structural Repair
				2	7/30/2010	\$0	The covering of existing skylights to provide a fire rated corridor to obtain a certificate of occupancy on the HVAC project.
				3	8/13/2010	\$13,865	The concrete repair of a perimeter beam.
				8	11/29/2010	\$1,734	Repair of Parapet Wall
				9	12/28/2010	\$7,966	The testing and adjustment of the gas piping on the roof.
						(\$28,000)	The deletion of unused allowances

SPL OST III Capital Improvement Program

Monthly Status Report

Change Order Details for the Month of April 2011

Project Name: Stone Mountain HS - HVAC, Roof

Project No. / Vendor Name	CO No.	CO Date	CO Amount	COR No.	COR Date	COR Amount	COR Description
421-110 Merit Construction	14	4/27/2011	\$23,736	58	8/30/2010	\$0	Additional time to the construction schedule due to a delay in getting the Fire Marshal approval for building evacuation and assembly plans and approval for temporary classroom plan, requiring numerous revisions and re-submittals over a substantial period of time. Revisions were made to contract drawings to satisfy changes required by the Fire Marshal.
				68	10/5/2010	\$4,007	Provide new exhaust for Kilns to exhaust heat produced by operation of the kilns.
				80	4/5/2011	\$1,290	Add a comminicator and cabling to the new fire alarm system to make the new fire alarm system compatible with the new DCSS monitoring.
				87	4/6/2011	\$7,330	Provide 11 additional strobes, 2 additional smoke detectors and new power supply/battery to the fire alarm system.
				90	3/21/2011	\$6,375	Provide a 100-watt voice evacuation system panel expander and two (2) speakers for the Commons Area fire alarm system to attain the required sound level.
				91	3/24/2011	\$2,005	Provide additional emergency lighting in the kitchen and two (2) practice rooms.
				93	4/11/2011	\$2,412	Repair of damages to trailer used for temporary classrooms. It is necessary to repair damages as they are considered to be other than normal wear and tear to leased trailers.
				94	4/11/2011	\$317	Repair leak over Child Development Room which involves clearing an obstructed drain receiving condensate from a new rooftop air conditioning unit.
				95	4/20/2011	\$0	Additional 66 days to construction schedule, extending the contract completion date from February 1, 2011 to April 4, 2011.

SPLIST III Capital Improvement Program

Monthly Status Report

Change Order Details for the Month of April 2011

Project Name: Towers HS - SPLOST II Deferred

Project No. / Vendor Name	CO No.	CO Date	CO Amount	COR No.	COR Date	COR Amount	COR Description
421-103 YLH Construction 09-	4	4/19/2011	\$28,179	12	10/28/2010	\$307	Install underground raceway for the Cable TV provider to install their cable.
				13	10/26/2010	\$6,370	Repair existing fence & add new fence
				14	4/1/2011	\$8,457	Provide a more permanent solution to the wood ramp installed on the outside of the cafeteria to provide access to the dumpster. The wood ramp will remain and will be stained with a stain/waterproofing application. The existing wood wall will be replaced with an EIFS finish over drywall with insulation in the wall cavity. The drywall on the inside will be prepped for paint and painted. The existing door will be replaced with an exterior grade hollow metal door with matching hardware as the exist doors for new addition and will be painted to match all other school doors.
				15	11/1/2010	\$2,550	Provide tree removal and trimming services along the fence line of the back parking lot of the school adjacent to the new addition and remove the dead sycamore tree next to the sidewalk along West Austin Drive. The sycamore presents a danger to students as limbs are falling. The tree trimming along the parking lot fence line will provide for better lighting of lots and property at night since the existing lights are now covered by the growth of these trees.
				17	10/27/2010	\$290	Sales tax for Owner provided plumbing fixtures.
				18	11/1/2010	\$2,289	Provide appliances for the Health Occupation Lab including washer, dryer, refrigerator and range. All appliances have been spec'd by Paul Canick.
				20R	1/10/2011	(\$19,073)	Reconciliation of allowances to the contract.
				21	11/29/2010	\$3,507	Provide and install Cyclorama Curtain in Studio on three walls per Paul Canick.
				22	12/17/2010	\$0	Contractual Schedule delay due to Fire Marshal 100% inspection being postponed until the existing school generator and transfer switch could be repaired.
				23	2/2/2011	\$2,618	Door Modifications made to allow the school to lock Door 1101a from the Exit Corridor side keeping students from the classrooms during non-school hours.
				24	2/2/2011	\$351	Fire Alarm Subcontractor called out to school due to fire alarm for entire school being set off by student. School maintenance personnel did not properly reset the pull station that a student had activated.
				25	1/10/2011	\$3,612	Misc. changes per the Fire Marshal inspection including additional strobes, horns, emergency lights, heat sensors and door closers.
				26	2/9/2011	\$5,313	Design fees associated with the Fire Marshal required exiting plans for the entire existing school.
				8a	10/25/2010	\$11,588	Fire marshal requests to accommodate summer activities and fall semester activities listed below: 1. Build temporary partitions to segregate portions of the building during the summer and the removal of partitions at the end of summer. 2. Electrical contractor cost to relocate exit signs. 3. Fence contractor to cut existing baseball field fence and install new openings for student evacuation. 4. YLH cost to install crushed stone ramps to access the baseball field for emergencies and build wood ramp from cafeteria to loading/dock dumpster area.



Project Name	Project Number	Current Budget	Encumbered	Balance
Planning & Programming				
Clifton ES- Ceiling Tiles	421-341-039	\$110,000	\$0	\$110,000
Wadsworth Magnet- HVAC & Lighting	421-341-027	\$400,000	\$0	\$400,000
Planning & Programming Subtotal:				
Design				
DeKalb International Student Center- Canopy	421-341-047	\$2,000	\$9,340	(\$7,340)
Design Subtotal:				
Procurement				
Lithonia MS - Renovations	421-341-044	\$207,000	\$2,790	\$204,210
Procurement Subtotal:				
Construction				
Carpet Replacement - Multiple Schools (LSPR 2Q09)	421-341-040	\$30,667	\$29,836	\$831
Chamblee MS- Painting	421-341-042	\$145,000	\$9,135	\$135,865
Chapel Hill MS- Ceiling Tiles & Site Work	421-341-028	\$240,275	\$275	\$240,000
FF&E- LSPR 2Q09	421-341-048	\$21,100	\$0	\$21,100
Glen Haven ES - Widén Drive	421-341-032	\$131,200	\$129,802	\$1,398
LSPR 2- Main Project	421-341	\$643,871	\$108,848	\$535,023
Oak Grove ES- Classroom Lighting	421-341-035	\$85,000	\$0	\$85,000
Construction Subtotal:				
Close-out				
Henderson MS- Hold-Opens & Toilets	421-341-052	\$75,278	\$74,800	\$478
Lakeside HS - Natatorium	421-341-012	\$293,903	\$288,506	\$5,397
Oak Grove ES- Paving	421-341-036	\$100,125	\$95,462	\$4,763
Close-out Subtotal:				
Completed				
Atherton ES- Chiller Replacement	421-341-022	\$123,176	\$123,176	\$0
Brockett ES - Make-up Air Units	421-320-001	\$94,030	\$94,030	\$0
Carpet Replacement - Multiple Schools (LSPR 1Q09)	421-341-031	\$10,237	\$10,237	\$0
Chamblee Charter HS - Lockers	421-341-014	\$50,000	\$43,457	\$6,543
Chamblee MS - Sound Panels	421-341-050	\$27,500	\$38,900	(\$11,400)
Chamblee MS- Mirror	421-341-049	\$960	\$960	\$0



SPLIST III Capital Improvement Program

Local School Priority Requests

Monthly Status Report

Project Name	Project Number	Current Budget	Encumbered	Balance
Completed				
Champion Theme MS- Chiller Replacement	421-341-010	\$47,539	\$47,539	\$0
Chapel Hill ES- Chiller Replacement	421-341-009	\$69,964	\$69,964	\$0
Chapel Hill MS- Track & Tennis Court	421-341-051	\$243,956	\$255,522	(\$11,566)
East Campus - AIPHONE ONE	421-341-026	\$0	\$0	\$0
FF&E- LSPR 1Q09	421-341-033	\$44,379	\$44,379	\$0
Gresham Park ES- Replace carpet in Media Center	421-320-008	\$16,947	\$16,947	\$0
Henderson Mill ES - Chiller Replacement	421-341-008	\$69,228	\$69,228	\$0
Henderson Mill ES- Ceiling Tiles	421-341-046	\$3,911	\$3,911	\$0
Henderson MS- Classroom & Restroom Upgrades	421-320-002	\$128,052	\$164,716	(\$36,663)
Henderson MS- Gym Light Switches	421-341-013	\$6,670	\$6,670	\$0
Henderson MS- Repair/Replace uneven tile near ref	421-320-007	\$2,985	\$2,985	\$0
Idlewood ES- Carpet Replacement	421-341-001	\$1,325	\$1,325	\$0
Kelley Lake ES - Courtyard	421-341-041	\$10,000	\$12,800	(\$2,800)
Kingsley Charter ES- Media Center Furniture	421-341-003	\$18,194	\$18,194	\$0
Kittredge Magnet ES- Chiller Replacement	421-341-020	\$99,202	\$99,202	\$0
Lithonia MS - Security Cameras	421-341-045	\$85,982	\$85,981	\$0
Lithonia MS- Band Room Carpet	421-341-004	\$6,028	\$6,028	\$0
LSPR 1- Main Project	421-320	\$163,176	\$165,862	(\$2,686)
Margaret Harris ES- Door Release System	421-341-005	\$6,748	\$6,748	\$0
McLendon ES- Basketball Court, Paint & Blinds	421-341-030	\$0	\$0	\$0
McNair MS- Ceiling Tile Replacement	421-341-015	\$49,058	\$49,058	\$0
McNair MS- Chiller Replacement	421-341-023	\$192,000	\$192,000	\$0
Middle School- Additional Parking Lot Lighting	421-341-038	\$200,382	\$200,382	\$0
Montclair ES - Chiller Replacement	421-341-021	\$170,000	\$121,425	\$48,575
Montgomery ES - Parking Lot, undergroud detention	421-320-005	\$234,448	\$229,530	\$4,918
Murphy Candler ES- Carpet Replacement	421-341-002	\$0	\$0	\$0
Nancy Creek ES - Parking Lot & bus loop	421-320-004	\$365,425	\$365,425	\$0
Narvie J Harris ES- Carpet Replacement	421-341-016	\$17,705	\$17,705	\$0
Oak Grove ES- Exterior Lighting	421-341-029	\$75,000	\$8,925	\$66,075
Rainbow ES- Chiller Replacement	421-341-011	\$69,964	\$69,964	\$0
Sagamore Hills ES- Media Center Carpet Replacement	421-341-017	\$71,142	\$71,142	\$0
Salem MS - Replace chalk boards w/white boards	421-320-010	\$24,406	\$24,406	\$0



SPOLOST III Capital Improvement Program

Local School Priority Requests

Monthly Status Report

Local School Priority Requests

Project Name	Project Number	Current Budget	Encumbered	Balance
Completed				
Sam Moss Center - Paint and Carpet	421-341-019	\$67,700	\$41,904	\$25,796
Sam Moss Center- Paving Repair and Replacement	421-341-037	\$474,855	\$474,855	\$0
School Choice/Relocation	421-320-003	\$271,205	\$226,861	\$44,344
Security Equipment	421-341-018	\$103,978	\$207,956	(\$103,978)
Security Upgrade Systems	421-341-025	\$550,000	\$550,000	\$0
Smoke Rise ES - 20 Classroom dry eraser boards	421-320-009	\$13,848	\$13,848	\$0
Stoneview ES- Chiller Replacement	421-341-024	\$94,180	\$91,420	\$2,760
Stoneview ES- Kitchen Equipment	421-341-007	\$162,907	\$169,970	(\$7,063)
Terry Mill ES - Parking Lot Paving	421-320-011	\$339,297	\$339,788	(\$491)
Terry Mill ES - Reloc Hooper Alex DESA, renovation	421-320-006	\$536,460	\$539,402	(\$2,942)
Wadsworth ES- Band Lockers	421-320-003D	\$24,000	\$24,000	\$0
Completed Subtotal:		\$5,374,149	\$5,354,727	\$19,422
On Hold				
Allgood ES- Kitchen	421-341-043	\$400,000	\$0	\$400,000
On Hold Subtotal:		\$400,000	\$0	\$400,000
Deemed Unnecessary				
Henderson Mill ES - New Door	421-341-034	\$0	\$0	\$0
Sky Haven ES- Window Replacement	421-341-006	\$384,379	\$373,499	\$10,880
Deemed Unnecessary Subtotal:		\$384,379	\$373,499	\$10,880
LSPR Program Totals:		\$8,644,047	\$6,477,020	\$2,167,027



Overview:


Project Name	Project Number	Current Budget	Encumbered	Balance
--------------	----------------	----------------	------------	---------

Project Name

Stage	Current Budget	Encumbered	Balance
Planning & Programming	\$510,000	\$0	\$510,000
Design	\$2,000	\$9,340	(\$7,340)
Procurement	\$207,000	\$2,790	\$204,210
Construction	\$1,297,113	\$277,896	\$1,019,217
Close-out	\$469,406	\$458,768	\$10,638
Completed	\$5,374,149	\$5,354,727	\$19,422
On Hold	\$400,000	\$0	\$400,000
Deemed Unnecessary	\$384,379	\$373,499	\$10,880
LSPR Program Totals:	\$8,644,047	\$6,477,020	\$2,167,027

Project Name

Current Budget by Phase

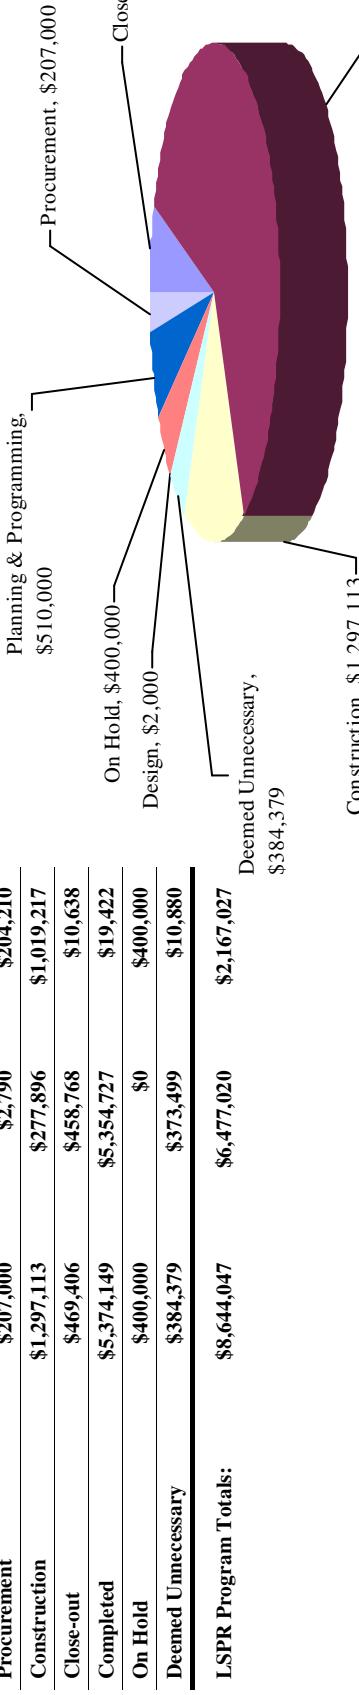

Completed, \$5,374,149

Construction, \$1,297,113

Deemed Unnecessary,
\$384,379

Close-out, \$469,406

Planning & Programming,
\$510,000

Procurement, \$207,000



Project Name	Project Number	Current Budget	Encumbered	Balance
Procurement				
Emergency Generators	421-321-015	\$3,800,000	\$115,994	\$3,684,006
				\$3,684,006
Construction				
Bulk Purchase - Plumbing Fixtures	421-322-001	\$2,043,950	\$876,914	\$1,167,036
Site Improvements 1- Main Project	421-321	\$42,891	\$15,071	\$27,820
Site Improvements 2- Main Project	421-322	\$62,554	\$536	\$62,018
				\$1,256,874
Close-out				
Chesnut Charter ES- Basketball Court Replacement	421-322-004	\$52,957	\$52,957	\$0
Margaret Harris- Exterior Facade & RR Renovation	421-321-007B	\$326,943	\$326,943	\$1
				\$1
				\$379,900
Completed				
Basin Heaters	421-321-014	\$345,500	\$345,500	\$0
Eagle Wood Academy- Replace Windows & Repair Doors	421-321-011	\$55,435	\$55,435	\$0
Energy Management System Update	421-322-002	\$948,000	\$948,000	\$0
Glen Haven ES- Replace Toilet Fixtures & Carpet	421-321-004	\$94,950	\$94,950	\$0
Huntley Hills ES- Restroom Renovations	421-321-006	\$66,767	\$66,767	\$0
Idlewood ES- Parking Lots	421-321-010	\$237,201	\$237,201	(\$1)
Laurel Ridge- Replace Parking Lot & Tennis Court	421-321-012	\$0	\$0	\$0
Marbut/Bouie ES- New Multi-purpose Bldg. Restrooms	421-321-003	\$239,039	\$239,039	\$0
Margaret Harris Center- Paving	421-321-007	\$31,232	\$31,232	\$0
Margaret Harris Center- Washing Machines	421-321-007D	\$9,050	\$9,050	\$0
Margaret Harris- Dryers	421-321-007E	\$704	\$704	\$0
Oak Grove ES- Downspouts	421-321-013	\$43,331	\$43,331	\$0
Security Lighting	421-321-009	\$506,540	\$506,540	\$0
Stephenson HS- Track Field Improvements	421-321-001	\$259,658	\$259,658	\$0
Stonemill ES- Parking Lot Repair	421-321-001A	\$53,373	\$53,373	\$0

SPLOST III Capital Improvement Program

Site Improvement Projects

Monthly Status Report

Project Name

Project Name	Project Number	Current Budget	Encumbered	Balance
--------------	----------------	----------------	------------	---------

Completed

Vanderlyn ES- Replace Toilet Fixtures	421-321-005	\$71,116	\$71,116	\$0
Completed Subtotal:		\$2,961,896	\$2,961,897	(\$1)
Site Improvements Program Totals:		\$9,291,191	\$4,350,312	\$4,940,880

Overview:

Stage

Stage	Current Budget	Encumbered	Balance
-------	----------------	------------	---------

Procurement \$3,800,000 \$115,994 \$3,684,006

Construction \$2,149,395 \$892,521 \$1,256,874


Close-out \$379,900 \$379,900 \$1

Completed \$2,961,896 \$2,961,897 (\$1)

SI Program Totals: \$9,291,191 \$4,350,312 \$4,940,880

Current Budget by Phase

Close-out, \$379,900




Completed, \$2,961,896
Construction, \$2,149,395

SPLCOT III CIP Master Program Schedule

D	Project/WBS Code	Project Name	Start	Finish	Duration	2007				2008				2009				2010				2011					
						Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4		
1	421-101	Emergency HVAC Work	Mon 10/1/07	Tue 5/31/11	957 days																						
2	421-102	Southwest DeKalb HS-Deferred Work	Thu 11/23/06	Fri 8/2/13	1747 days																						
12	421-103	Towers High School	Tue 5/12/09	Tue 1/4/11	431 days																						
16	421-104	Columbia High School	Mon 1/1/07	Fri 9/11/09	705 days																						
21	421-105	McNair High School	Mon 12/17/07	Wed 10/28/09	488 days																						
26	421-106	Cross Keys High School	Tue 6/12/07	Wed 8/31/11	1102 days																						
31	421-107	Land	Wed 1/13/10	Thu 5/3/12	602 days																						
32	421-108	Tucker High School	Mon 5/14/07	Tue 11/16/10	917 days																						
37	421-109	Woodward Elementary School	Wed 8/29/07	Fri 1/29/10	633 days																						
42	421-110	Stone Mountain High School	Mon 6/2/08	Thu 11/18/10	644 days																						
47	421-111	Redan High School	Mon 4/14/08	Fri 9/24/10	640 days																						
52	421-112	Midvale Elementary School	Fri 5/1/09	Fri 9/3/10	351 days																						
56	421-113	Stephenson Middle School	Fri 11/17/06	Mon 9/8/08	472 days																						
60	421-114	Clifton Elementary School	Fri 11/17/06	Mon 9/8/08	472 days																						
64	421-115	Cedar Grove High School	Mon 6/23/08	Fri 12/17/10	650 days																						
68	421-116	Vanderlyn Elementary School	Mon 5/25/09	Fri 3/4/11	465 days																						
73	421-117	Chamblee High School	Wed 4/8/09	Tue 12/11/12	960 days																						
78	421-118	Clarkston High School	Mon 2/25/08	Fri 12/30/11	1005 days																						
83	421-119	Druid Hills High School	Mon 5/14/07	Thu 7/29/10	839 days																						
88	421-120	Dunwoody High School	Tue 4/29/08	Mon 3/26/12	1020 days																						
93	421-121	Fairington Elementary School	Mon 6/1/09	Thu 9/23/10	344 days																						
97	421-123	DeKalb School of Arts Relocation	Mon 4/14/08	Thu 5/31/12	1079 days																						
103	421-124	Mountain Industrial Center	Tue 5/22/07	Fri 4/30/10	769 days?																						
112	421-125	Lakeside High School	Mon 3/2/09	Thu 5/10/12	834 days																						
117	421-127	MLK Jr. High School	Mon 4/4/10	Mon 4/1/13	846 days																						
122	421-128	Miller Grove High School	Mon 1/4/10	Mon 4/1/13	846 days																						
127	421-129	Warren Tech	Thu 7/1/10	Mon 7/18/11	273 days																						
132	421-130	McLendon Elementary School	Fri 7/31/09	Tue 3/1/11	413 days																						
136	421-131	Sam Moss Center	Mon 6/30/08	Thu 10/14/10	599 days?																						
138	421-132	Knollwood Elementary School	Thu 7/1/10	Mon 8/15/11	293 days																						
143	421-133	Rockbridge Elementary School	Thu 7/1/10	Mon 8/15/11	293 days																						
148	421-135	Stone Mountain Elementary School	Thu 7/1/10	Mon 8/15/11	293 days																						
153	421-136	Hambrick Elementary School - HVAC	Thu 7/1/10	Mon 8/15/11	293 days																						
158	421-138	Montgomery Elementary School	Thu 7/1/10	Mon 8/15/11	293 days																						
163	421-139	Indian Creek Elementary School	Thu 7/1/10	Mon 8/15/11	293 days																						
168	421-140	Stone Mill Elementary School	Thu 7/1/10	Mon 8/15/11	293 days																						
172	421-201	Sky Haven Elementary School	Thu 7/1/10	Mon 8/15/11	293 days																						
177	421-202	Murphy Candler Elementary School	Thu 7/1/10	Mon 8/15/11	293 days																						
182	421-203	Rainbow Elementary School	Thu 7/1/10	Mon 8/15/11	293 days																						
187	421-205	Sequoyah Middle School - Roof Replacement	Mon 5/4/09	Mon 9/13/10	356 days																						
192	421-206	Wedsworth Elementary School	Wed 10/1/08	Tue 8/25/09	235 days																						
197	421-208	Champion Middle School	Mon 4/16/07	Mon 5/24/10	811 days																						
202	421-209	Avondale Elementary School	Wed 10/1/08	Tue 9/15/09	240 days																						
207	421-210	Snappinger Elementary School - Roof	Mon 6/1/09	Wed 9/15/10	338 days																						

SPLCOT III CIP Master Program Schedule

SPLCOT III CIP Master Program Schedule

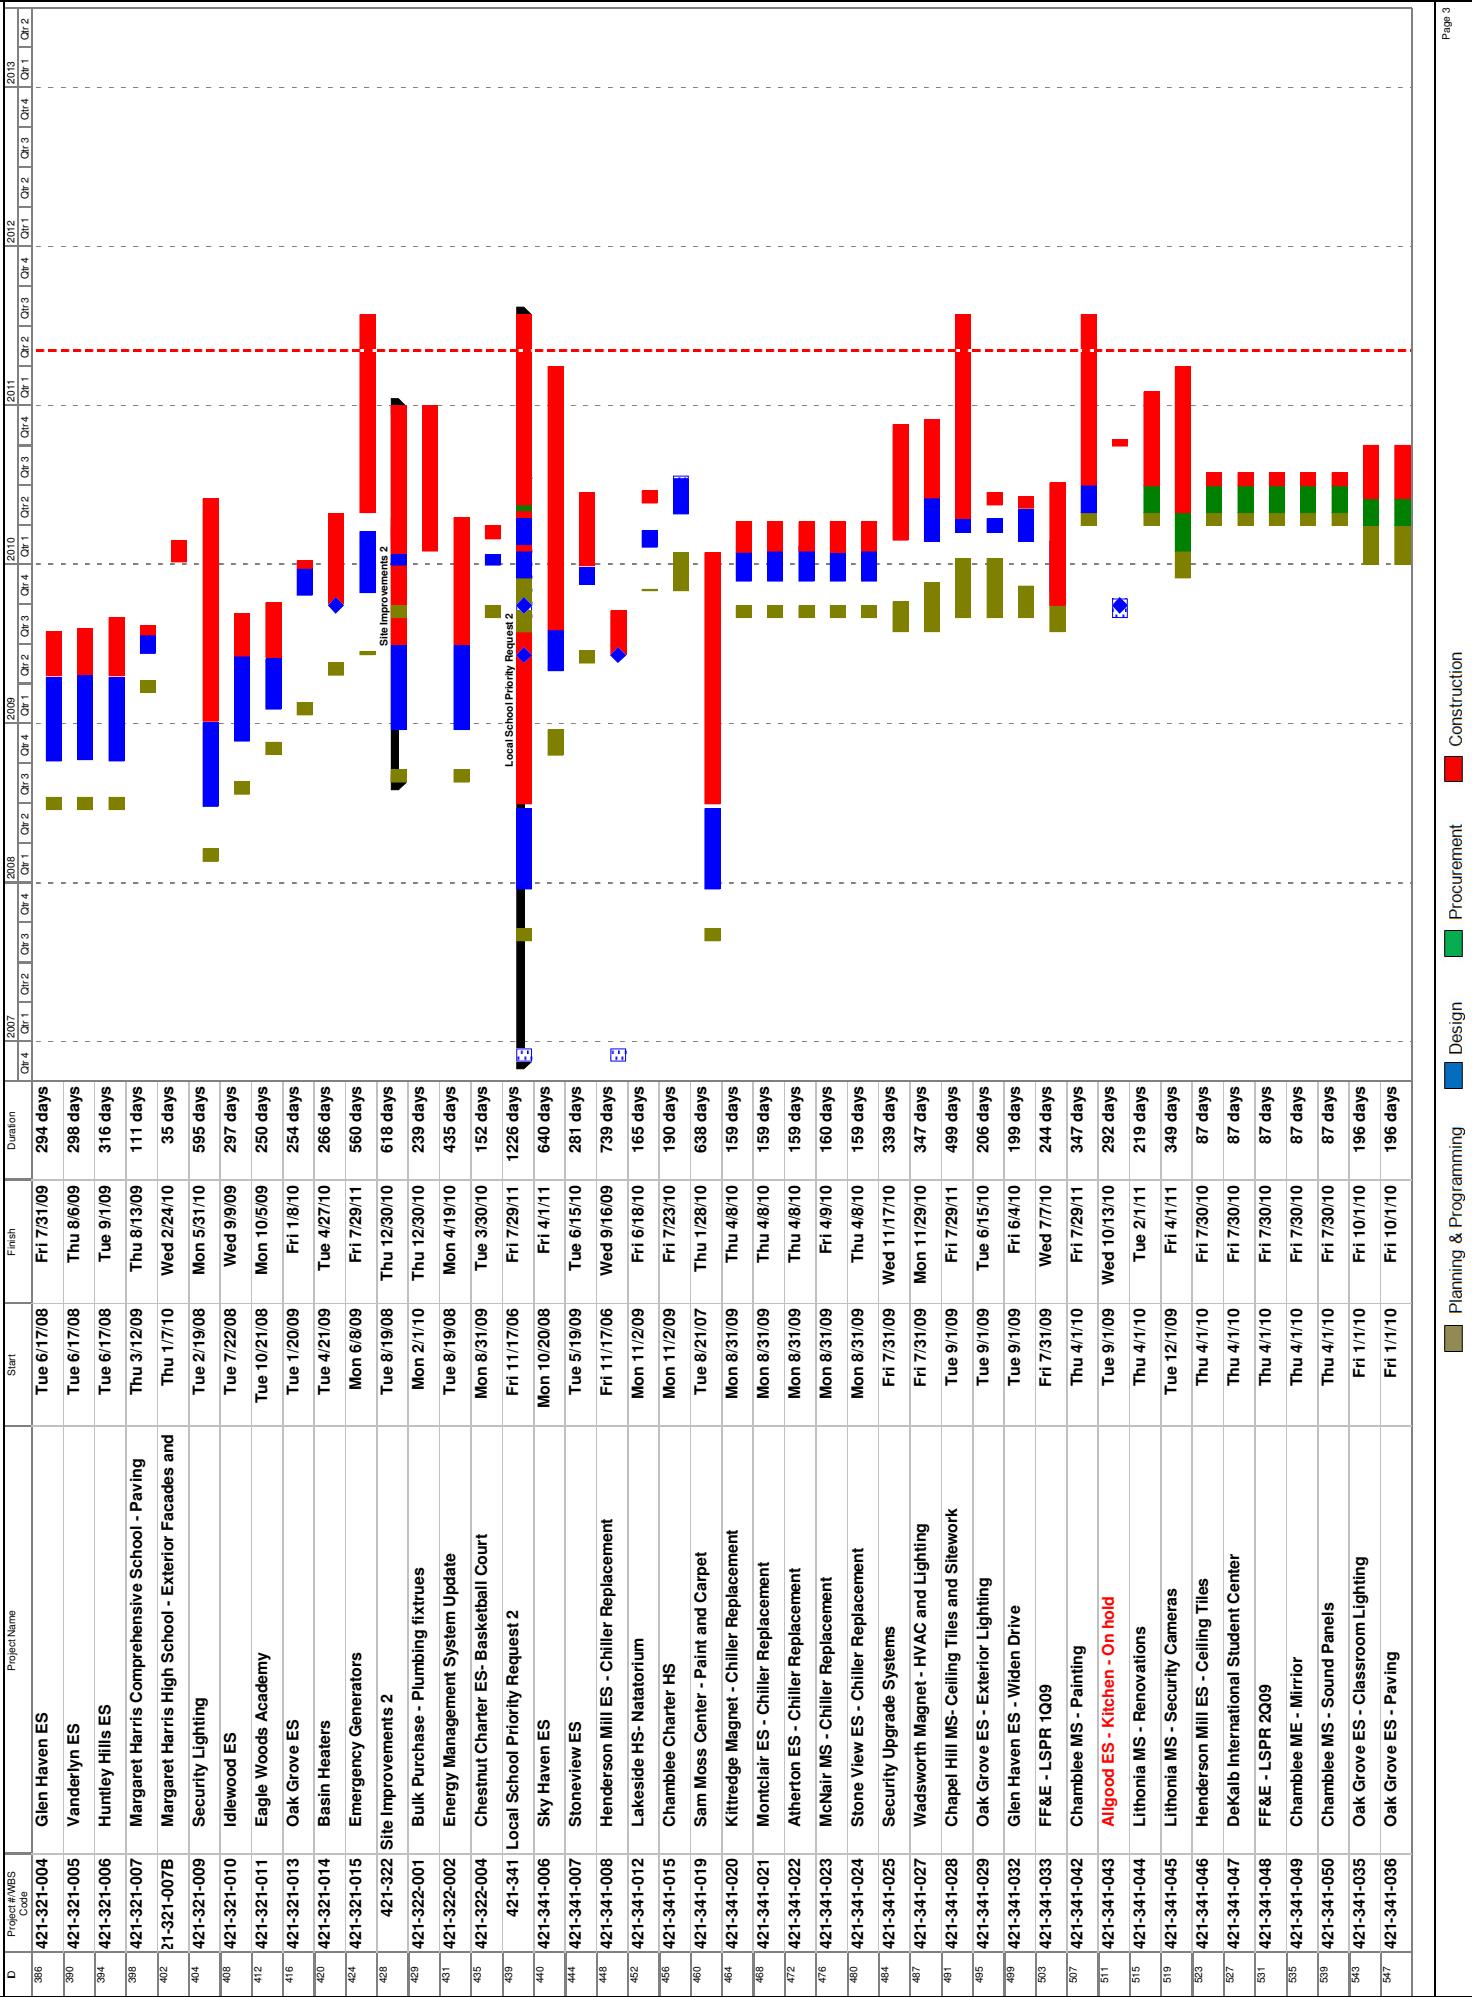

SPLOST III CIP Master Program Schedule


D Project#WBS Code	Project Name	Start	Finish	Duration	2007				2008				2009				2010				2011				2012					
					Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4		
55_1 421-341-038	MS Additional Parking Lot Lighting	Fri 1/1/10	Fri 4/30/10	86 days																										
55_5 421-341-039	Clifton ES - Ceiling Tiles - On hold	Tue 9/1/09	Wed 10/13/10	292 days																										
55_9 421-341-040	Carpet Replacement	Thu 10/1/09	Mon 2/1/10	88 days																										
56_3 421-341-041	Kelley Lakes ES - Courtyard - On hold	Tue 9/1/09	Wed 10/13/10	292 days																										
56_7 421-341-037	Sam Moss Center Paving Repair and Replacement	Thu 10/1/09	Fri 4/30/10	152 days																										
57_1 421-341-051	Chapel Hill MS - Track and Tennis Court	Mon 8/3/09	Mon 8/16/10	271 days																										
57_5 421-401	Buses 1	Thu 1/1/09	Wed 12/30/09	52 wks																										
57_6 421-402	Buses 2	Fri 1/1/10	Thu 12/30/10	52 wks?																										
57_7 421-403	Buses 3	Thu 1/1/09	Wed 12/30/09	52 wks																										
57_8 421-501	Technology Refresh	Thu 1/1/09	Wed 12/30/09	52 wks																										
57_9 421-502	Technology - Media Centers	Fri 1/1/10	Thu 12/30/10	52 wks																										
58_0 421-503	Technology	Fri 1/1/10	Thu 12/30/10	52 wks																										
58_1 421-600	General Services	Mon 2/15/10	Thu 11/3/11	449 days																										
58_2 421-600-002	Bulk Purchase - Ceiling Tile and Grid	Tue 6/1/10	Mon 5/30/11	52 wks																										
58_3 421-600-003	Bulk Purchase - Metal Lockers	Mon 2/15/10	Fri 2/11/11	52 wks																										
58_4 421-600-004	Bulk Purchases - Theatrical Lighting and Sound Sys	Fri 11/5/10	Thu 11/3/11	52 wks																										
58_5 421-600-005	Bulk Purchase - Lighting	Fri 11/5/10	Thu 11/3/11	52 wks																										
58_6 421-600-006	Bulk Purchase - Fixed Audience Seating	Tue 3/9/10	Mon 3/7/11	52 wks																										

General Services



 Planning & Programming
  Design
  Procurement
  Construction

Program\DeKalb County\421 SPLOST III\Other Facilities\Administrative & Instructional Complex (AIC)

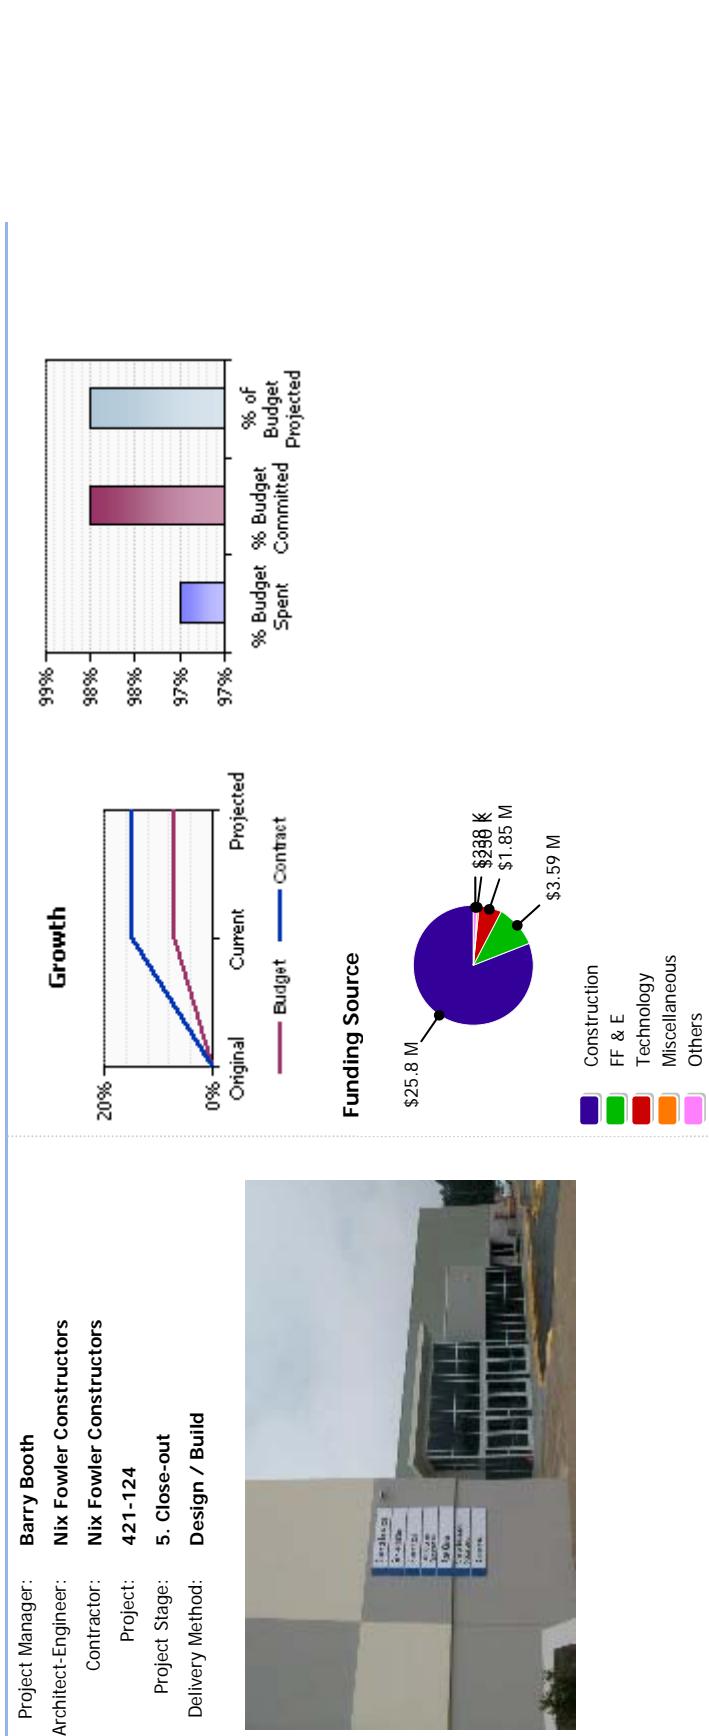

Remarks:


- Phase I (DECA, with Hogan Construction as Design/Builder) was completed in 2008.
- Phase II (all other areas, with Nix-Fowler Constructors as Design/Builder) received the final Certificate of Occupancy on 7/22/10. Project is in the closeout phase.

Cost Status by Budget Category:

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	ETC Completion	Estimate At Completion	Uncommitted
CIT Managed													
Architect/Engineer: 7100-7101	\$1,000,000	(\$964,905)	\$35,095	\$35,095		\$35,095	\$35,095				\$35,095		
Surveying: 7100-7102	\$23,037	\$23,037	\$23,037								\$23,037	\$23,037	
Construction Testing: 7100-7103	\$232,898	(\$200,000)	\$32,898	\$8,804		\$8,804	\$8,804				\$24,094	\$32,898	
Abatement: 7100-7104	\$70,000	(\$70,000)										(\$0)	
Other Consultants: 7100-7105	\$307,115	\$47,115	\$13,250			\$13,250	\$7,500	\$5,750					
Management Fees: 7200-7201	\$1,909,417	(\$1,909,417)											
Construction: 7300-7301	\$20,783,949	\$5,018,741	\$25,802,690	\$21,624,605	\$4,098,276	\$25,722,881	\$25,645,254	\$73,860	\$47,661	\$32,148	\$25,802,690	\$0	


Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
Miscellaneous: 7300-7302	\$472,839	(\$222,839)	\$250,000	\$7,920		\$7,920	\$6,971			\$242,080	\$250,000	(\$0)
Security: 7400-7401	\$100,000	(\$100,000)										
Utilities: 7500-7501	\$150,000	(\$150,000)										
Moving / Relocation: 7500-7502	\$500,000	(\$300,000)	\$200,000	\$124,257		\$124,257				\$75,743	\$200,000	(\$0)
Contingency: 9999-9999	\$1,491,815	(\$1,491,815)										
CIT Managed Subtotal	\$27,041,070	(\$650,235)	\$26,390,835	\$21,813,932	\$4,098,276	\$25,912,208	\$25,827,881	\$79,610	\$47,661	\$430,967	\$26,390,836	(\$1)
DCSS Managed												
FF&E: 7700-7504	\$2,045,226	\$1,539,905	\$3,585,131	\$3,573,821		\$3,573,826	\$36,524			\$3,573,821	\$11,310	
Technology: 7800-7801	\$750,000	\$1,099,000	\$1,849,000	\$1,566,714		\$1,566,714	\$1,549,087	\$17,402		\$282,286	\$1,849,000	(\$0)
DCSS Managed Subtotal	\$2,795,226	\$2,638,905	\$5,334,131	\$5,140,535		\$5,140,535	\$5,086,383	\$53,927		\$282,286	\$5,422,821	\$11,310
Project Total	\$29,836,296	\$1,988,670	\$31,824,966	\$26,954,467	\$4,098,276	\$31,052,743	\$30,914,264	\$133,537	\$47,661	\$713,253	\$31,813,657	\$11,309

Program\DeKalb County\421 SPLOST III\Elementary Schools\Allgood ES - Roof

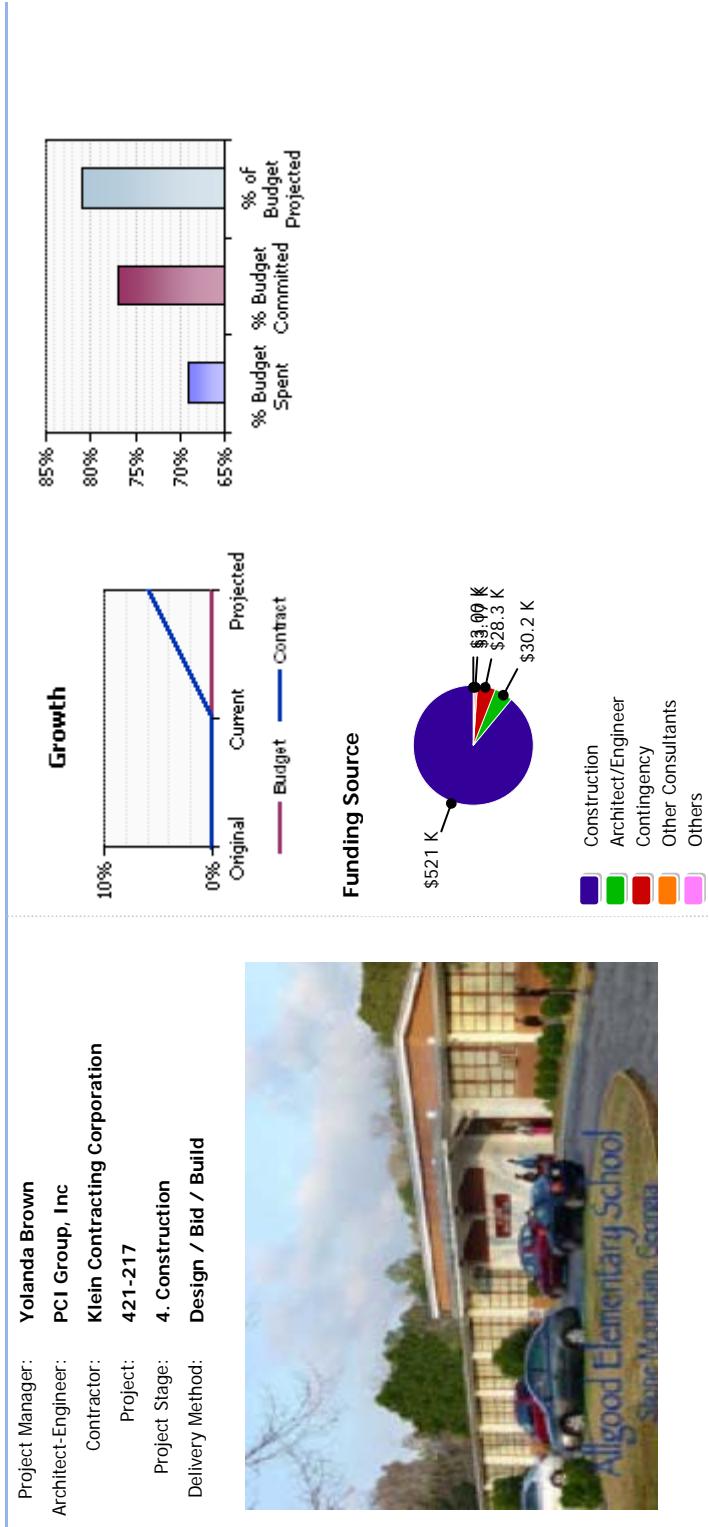


- In Construction Phase - Klein Contracting Corporation is the GC on the project. The cap sheet has been installed in all areas except in the immediate area of the Cafeteria. The work will resume around this area when the replacement of unknown deteriorated or abated material is complete by a change in scope.

Program\DeKalb County\421 SPLOST III\Elementary Schools\Avondale ES - Roof

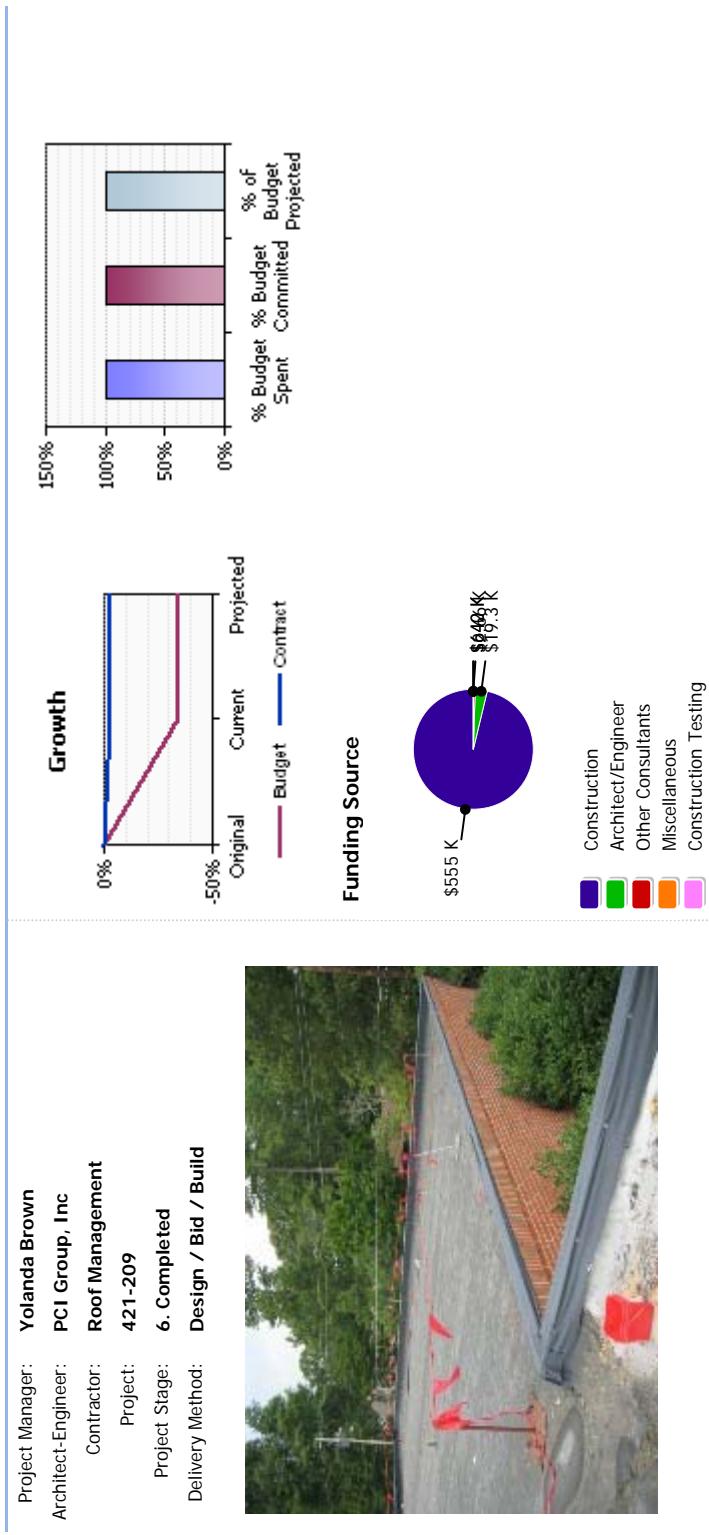


Program\DeKalb County\421 SPLOST III\High Schools\DSA\Avondale HS\Avondale HS- Renovations

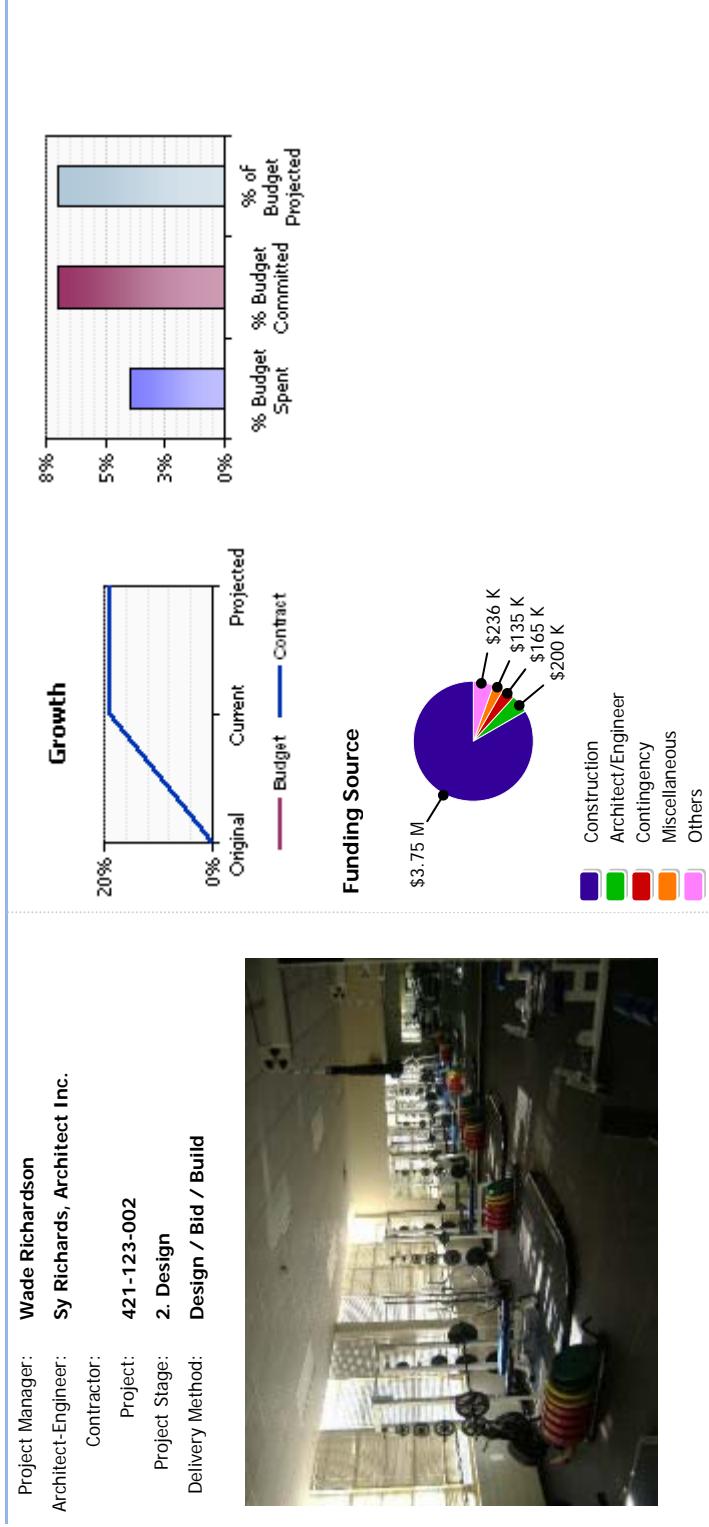

- Redesign of the existing locker rooms and adjacent spaces, window replacement, weight room, dumpster pad, roof replacement, renovation of four existing science labs, site modifications - damaged sidewalks, ROTC drill pad, and parking lot repair (if allowed within the budget)
- 100% Design documents for AHS/DSA Roof replacement has been submitted and under review. The roof replacement is projected to be ready for bid in April. DSA is reviewing proposed A/V system program prepared by Larry Steele.

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORS	ETC Forecast	Estimate At Completion	Uncommitted
Contingency: 9999-9999												
Contingency: 9999-9999	\$165,000	\$165,000	\$165,000	\$165,000						\$165,000	\$165,000	
CLT Managed Subtotal	\$4,475,700	\$4,475,700	\$251,042	\$49,566	\$300,608	\$97,278	\$121,627			\$4,174,017	\$4,474,625	\$1,075
DCSS Managed												
FF&E: 7700-7504	\$5,000	\$5,000	\$4,000			\$4,000				\$1,000	\$5,000	
DCSS Managed Subtotal	\$5,000	\$5,000	\$4,000	\$4,000	\$4,000	\$4,000				\$1,000	\$5,000	
Project Total	\$4,480,700	\$4,480,700	\$255,042	\$49,566	\$304,608	\$101,278	\$121,627			\$4,175,017	\$4,479,625	\$1,075


Program\DeKalb County\421 SPLOST III\Site Improvements\Site Improvements 2 (322)\Bulk Purchase - Plumbing Fixtures

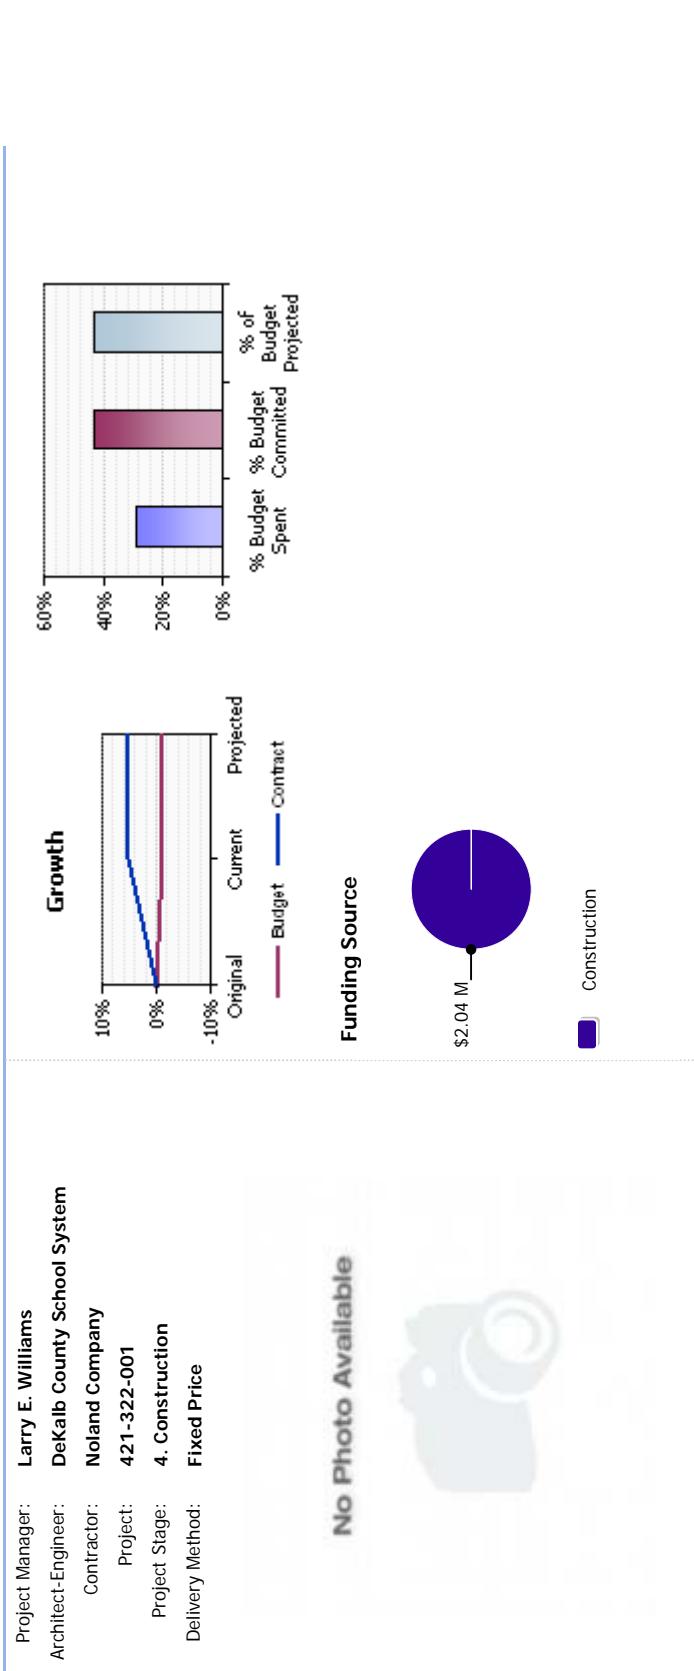

Cost Status by Budget Category:


Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CCRs	ETC Forecast	ETC At Completion	Estimate At Completion	Uncommitted
CIT Managed	\$2,069,950	(\$26,000)	\$2,043,950	\$836,289	\$40,625	\$876,914	\$390,493	\$444,055		\$1,167,036	\$2,043,950	\$0	
Construction: 7300-7301	\$2,069,950	(\$26,000)	\$2,043,950	\$836,289	\$40,625	\$876,914	\$390,493	\$444,055		\$1,167,036	\$2,043,950	\$0	
CIT Managed Subtotal	\$2,069,950	(\$26,000)	\$2,043,950	\$836,289	\$40,625	\$876,914	\$390,493	\$444,055		\$1,167,036	\$2,043,950	\$0	
Project Total	\$2,069,950	(\$26,000)	\$2,043,950	\$836,289	\$40,625	\$876,914	\$390,493	\$444,055		\$1,167,036	\$2,043,950	\$0	

Program\DeKalb County\421 SPLOST III\High Schools\Cedar Grove HS - HVAC, Ceiling, Lighting & Roof

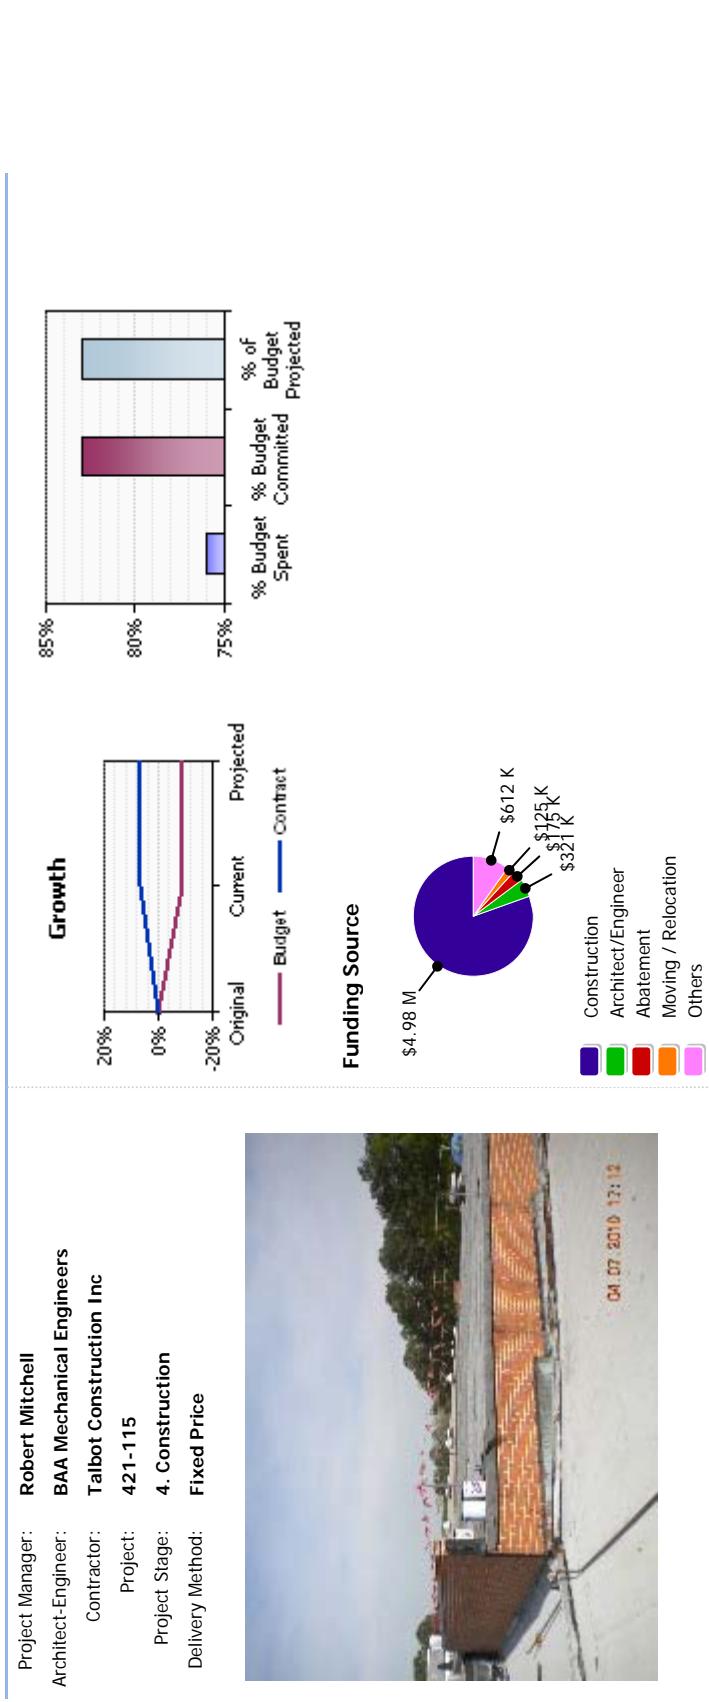

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORS	ETC Forecast	Estimate At Completion	Uncommitted
Security: 7400-7401	\$30,000	\$40,000	\$70,000	\$27,425		\$27,425	\$27,030	\$395	\$40,000	\$67,425	\$2,575	
Utilities: 7500-7501	\$75,000		\$75,000								\$75,000	
Moving / Relocation: 7500-7502	\$125,000		\$125,000	\$100,843		\$100,843	\$76,120	\$24,723	\$20,000	\$120,843	\$4,157	
Trailers: 7600-7503	\$250,000	(\$199,999)	\$50,001								\$50,001	
Contingency: 9999-9999	\$342,850	(\$278,000)	\$6,850						\$10,000	\$10,000	\$54,850	
CIT Managed Subtotal	\$6,856,998	(\$760,682)	\$6,096,316	\$4,754,629	\$327,310	\$5,081,938	\$4,142,312	\$896,172	\$305,000	\$5,386,938	\$709,318	
DCSS Managed												
Technology: 7800-7801	\$114,999	\$114,999	\$71,983			\$71,983	\$24,947	\$46,209	\$40,000	\$111,983	\$3,016	
DCSS Managed Subtotal	\$114,999	\$114,999	\$71,983			\$71,983	\$24,947	\$46,209	\$40,000	\$111,983	\$3,016	
Project Total	\$6,856,998	(\$645,683)	\$6,211,315	\$4,826,612	\$327,310	\$5,153,921	\$4,167,258	\$942,382	\$345,000	\$5,498,921	\$712,394	

Program\DeKalb County\421 SPLOST III\High Schools\Chamblee HS- New Replacement High School

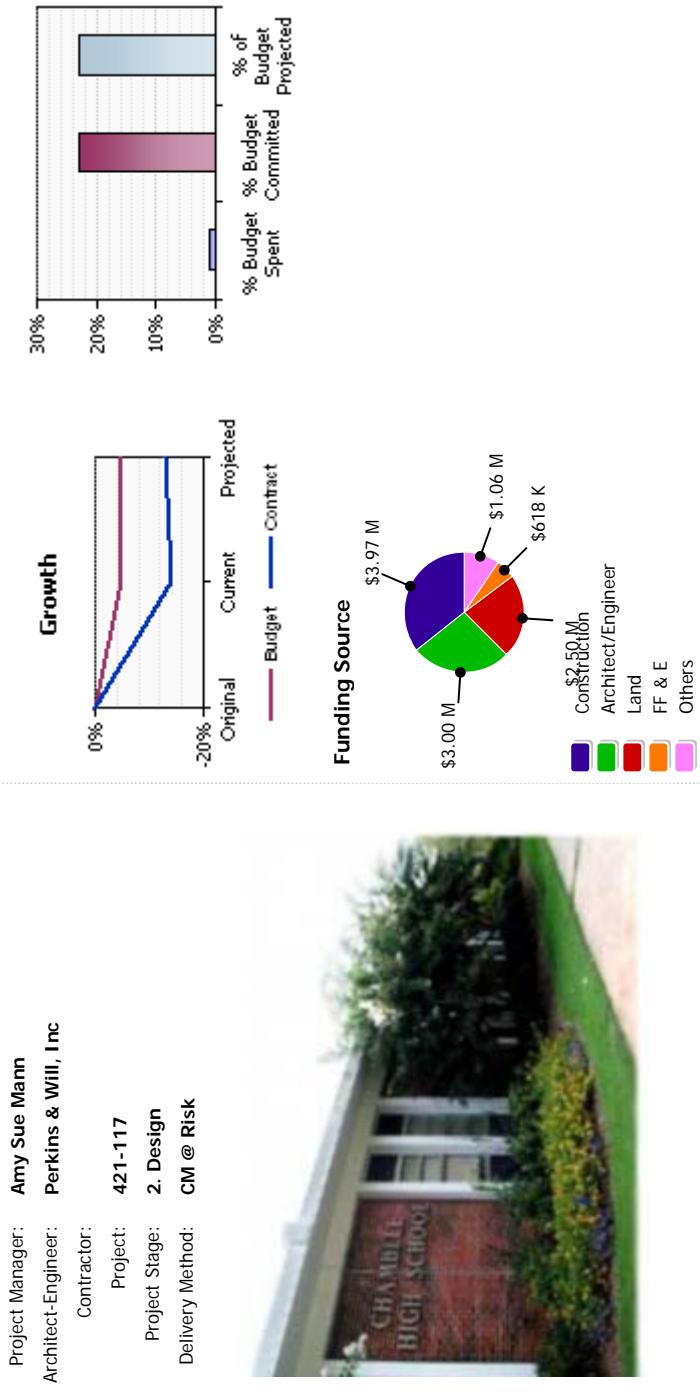


Cost Status by Budget Category:

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
CIT Managed												
Architect/Engineer: 7100-7101	\$540,126	\$2,459,874	\$3,000,000	\$2,905,051		\$2,905,051	\$31,301	\$2,873,750		\$94,949	\$3,000,000	(\$0)
Surveying: 7100-7102	\$20,000		\$20,000	\$13,495		\$13,495				\$6,505	\$20,000	(\$0)
Construction Testing: 7100-7103	\$78,500		\$78,500	\$22,910		\$12,420				\$55,591	\$78,500	(\$0)
Other Consultants: 7100-7105	\$67,300	\$2,500	\$69,800	\$36,242		\$36,242	\$15,232	(\$1,526)	\$1,500	\$32,058	\$69,800	
Management Fees: 7200-7201	\$572,800	(\$572,800)										
Construction: 7300-7301	\$8,932,106	(\$4,959,874)	\$3,972,232							\$3,972,232	\$3,972,232	
Construction Technology: 7300-7301.22		\$94,000								\$94,000	\$94,000	
Miscellaneous: 7300-7302	\$183,436	(\$2,500)	\$180,936	\$1,425		\$1,425	\$960			\$179,511	\$180,936	
Security: 7400-7401	\$50,000		\$50,000							\$50,000	\$50,000	

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
Utilities: 7500-7501	\$100,000		\$100,000							\$100,000	\$100,000	
Moving / Relocation: 7500-7502	\$75,000		\$75,000	\$2,500			\$2,500	\$1,433		\$72,500	\$75,000	
Contingency: 9999-9999	\$338,450	(\$94,000)	\$244,450							\$244,450	\$244,450	
CIT Managed Subtotal	\$10,957,718	(\$3,072,800)	\$7,884,918	\$2,981,623			\$2,981,623	\$74,841	\$2,876,577	\$1,500	\$4,901,796	\$7,884,918
DCSS Managed												
Land: 7100-7150	\$2,500,000	\$2,500,000								\$2,500,000	\$2,500,000	
FF & E: 7700-7504	\$617,589		\$617,589							\$617,589	\$617,589	
Technology: 7800-7801	\$150,000		\$150,000							\$150,000	\$150,000	
DCSS Managed Subtotal	\$767,589	\$2,500,000	\$3,267,589							\$3,267,589	\$3,267,589	
Project Total	\$11,725,307	\$572,800	\$11,152,507	\$2,981,623			\$2,981,623	\$74,841	\$2,876,577	\$1,500	\$8,169,385	\$11,152,507

Program\DeKalb County\421 SPLOST III\High Schools\Clarkston HS - Renovation & Addition

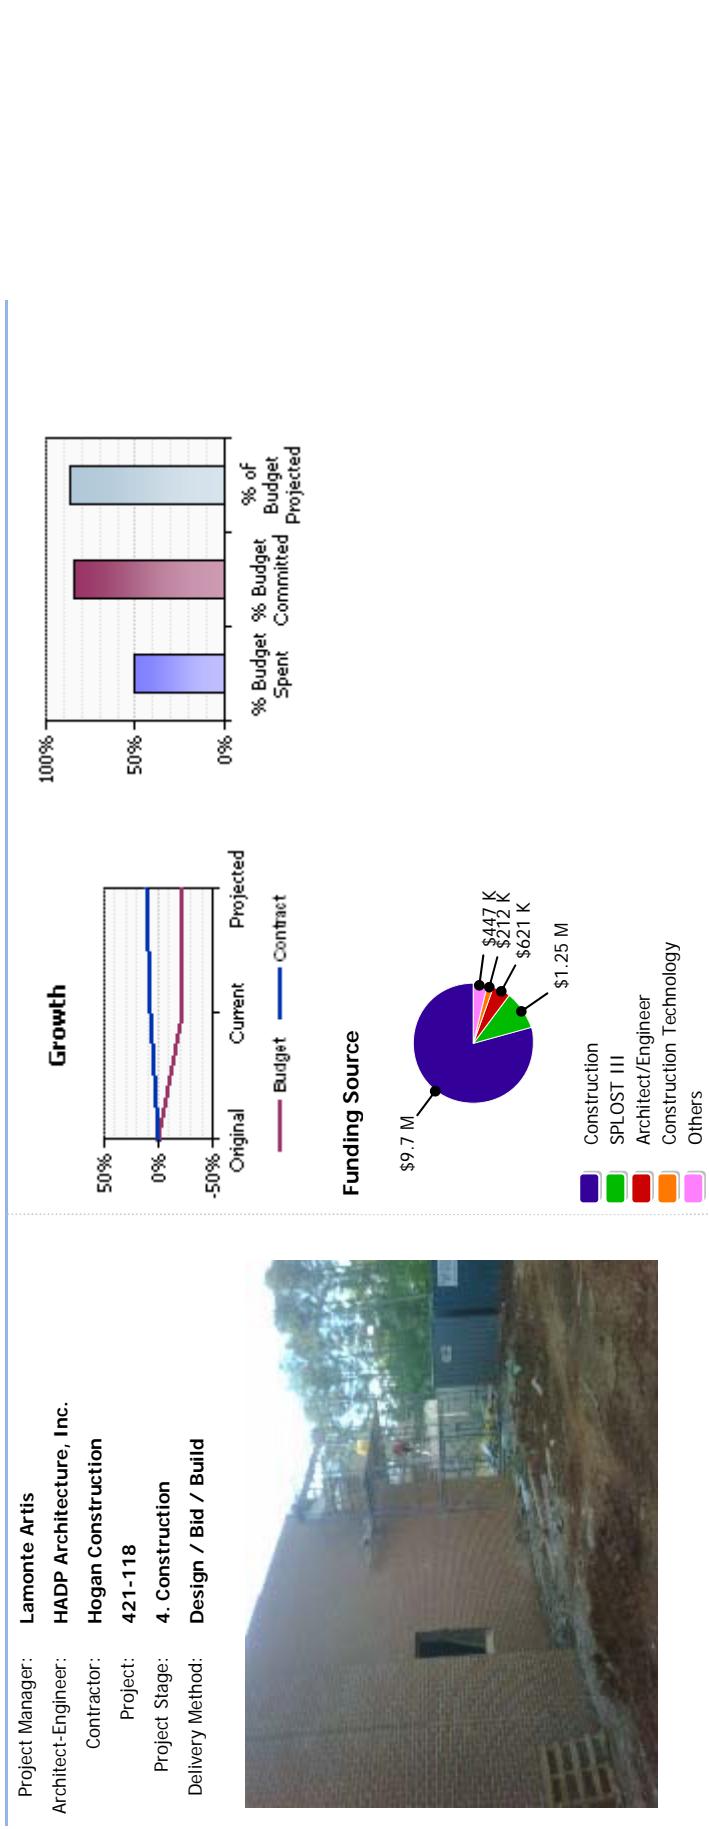

Scope of Work:

- A building addition of 32,000 SF that includes Career Technology space and a new auditorium. Also included is replacement of HVAC, ceiling and lighting systems in the existing building as well as other facility improvements.
- Construction and renovation activities are currently taking place in Phases 7 and 13. The new exhaust hood for the professional food service program has been installed in phase 7. The roof structure for the new addition is 80% complete. New emergency generator has been tested and passed for proper sequencing. Construction started on June 2, 2010, anticipated completion date 3rd quarter 2011.

Remarks:


- Construction and renovation activities are currently taking place in Phases 7 and 13. The new exhaust hood for the professional food service program has been installed in phase 7. The roof structure for the new addition is 80% complete. New emergency generator has been tested and passed for proper sequencing. Construction started on June 2, 2010, anticipated completion date 3rd quarter 2011.

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
CIT Managed												
Architect/Engineer: 7100-7101	\$721,378	(\$100,000)	\$621,378	\$588,101	\$17,340	\$605,441	\$541,394	\$55,611		\$15,937	\$621,378	
Surveying: 7100-7102	\$20,000	\$19,000	\$39,000	\$32,030		\$32,030	\$30,250			\$6,970	\$39,000	
Construction Testing: 7100-7103	\$100,000		\$100,000	\$34,979		\$35,933	(\$2,269)			\$65,021	\$100,000	
Abatement: 7100-7104	\$20,000			\$17,640		\$17,640	\$6,155			\$15,503	\$33,143	
Other Consultants: 7100-7105	\$57,672		\$57,672	\$4,843		\$4,843	\$4,843			\$52,829	\$57,672	
Management Fees: 7200-7201	\$419,488	(\$419,488)										
Construction: 7300-7301	\$12,002,960	(\$2,255,000)	\$9,747,960	\$8,824,039	\$652,332	\$9,476,371	\$2,834,395	\$3,961,940	\$342,005	(\$188,094)	\$9,630,282	\$117,676
Construction Technology: 7300-7301-22		\$212,000		\$11,451		\$11,451				\$200,549	\$212,000	
Miscellaneous: 7300-7302	\$270,126	(\$213,143)	\$56,983	\$557		\$557				\$56,426	\$56,983	

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
Security: 7400-7401	\$75,000	<u>(\$50,000)</u>	\$25,000							\$25,000	\$25,000	
Utilities: 7500-7501	\$165,000	<u>(\$125,000)</u>	\$40,000							\$40,000	\$40,000	
Moving / Relocation: 7500-7502	\$100,000	<u>(\$45,000)</u>	\$55,000	\$58,415		\$58,415	\$53,945	<u>(\$31)</u>		\$58,415	<u>(\$3,415)</u>	
Contingency: 9999-9999	\$536,325	<u>(\$456,000)</u>	\$80,325							\$73,600	\$73,600	<u>\$6,725</u>
CIT Managed Subtotal	\$14,487,949	<u>(\$3,419,488)</u>	\$11,068,461	<u>\$9,572,054</u>	<u>\$669,672</u>	<u>\$10,241,726</u>	<u>\$3,507,473</u>	<u>\$4,031,791</u>	<u>\$342,005</u>	<u>\$363,741</u>	<u>\$10,947,472</u>	<u>\$120,985</u>
DCSS Managed												
FF & E: 7700-7504	\$718,733		\$718,733	\$27,144		\$27,144	\$16,020	\$11,124		\$691,589	\$718,733	<u>(\$0)</u>
Technology: 7800-7801	\$488,000		\$488,000	\$9,459		\$9,459	\$4,890	\$4,890		\$478,541	\$488,000	<u>(\$0)</u>
DCSS Managed Subtotal	\$1,206,733		<u>\$1,206,733</u>	<u>\$36,604</u>	<u>\$36,604</u>	<u>\$36,604</u>	<u>\$16,020</u>	<u>\$16,015</u>	<u>\$1,170,130</u>	<u>\$1,206,734</u>	<u>(\$1)</u>	
Project Total	\$15,694,682	<u>(\$3,419,488)</u>	\$12,275,194	\$9,608,658	<u>\$669,672</u>	<u>\$10,278,330</u>	<u>\$3,523,493</u>	<u>\$4,047,805</u>	<u>\$342,005</u>	<u>\$1,533,871</u>	<u>\$12,154,206</u>	<u>\$120,988</u>

Program\DeKalb County\421 SPLOST III\High Schools\Columbia HS - SPLOST II Deferred

Project Manager:	Vincent Pope and Associates
Architect-Engineer:	Merit Construction Company
Contractor:	Project: 421-104
	Project Stage: 5. Close-out
	Delivery Method: CM @ Risk

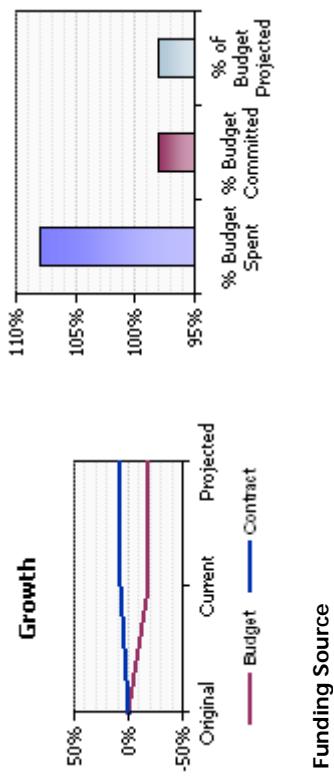

Scope of Work:

- Scope includes a Fine Arts building addition, resurfacing of the track, restoring the baseball dugouts, reggrading the football field and miscellaneous renovations inside the existing buildings, which includes HVAC, ceiling and lighting improvements.

Cost Status by Product Category

Cost Status by Budget Category:								
Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance
CIT Managed								
Architect/Engineer: 7100-7101	\$660,137	\$16,863	\$677,000	\$625,000	\$52,000	\$677,000	\$655,419	\$21,581
Surveying: 7100-7102	\$30,000	(\$15,300)	\$14,700	\$14,700		\$14,700	\$14,700	\$0
Construction Testing: 7100-7103	\$45,022	(\$21,664)	\$23,358	\$23,358		\$23,358	\$23,358	\$0
Abatement: 7100-7104	\$70,000	(\$36,400)	\$13,600	\$13,600		\$13,600	\$13,600	\$0
Other Consultants: 7100-7105	\$115,022	(\$87,773)	\$27,249	\$27,249		\$27,249	\$27,249	\$0
Management Fees: 7200-7201	\$230,045	(\$230,045)						
Construction: 7300-7301	\$10,255,916	(\$1,110,731)	\$9,145,185	\$8,194,812	\$778,413	\$8,973,225	\$10,137,948	(\$1,164,723)
Miscellaneous: 7300-7302	\$556,364	(\$239,108)	\$317,256	\$317,256		\$317,256	\$317,256	\$0
Security: 7400-7401	\$25,000	(\$24,459)	\$541	\$541		\$541	\$541	\$0
Utilities: 7500-7501	\$75,000	(\$75,000)	\$57,970	\$17,030	\$1,998	\$1,998	\$1,998	\$1,998
Moving / Relocation: 7500-7502	\$75,000							

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
Trailers: 7600-7503	\$200,000	<u>(\$179,058)</u>	\$20,942	\$20,942		\$20,942	\$20,942				\$20,942	
Contingency: 9999-9999	\$575,114	<u>(\$575,114)</u>										
CLT Managed Subtotal	\$12,912,620	<u>(\$2,655,759)</u>	\$10,256,861	<u>\$9,239,455</u>	<u>\$830,413</u>	<u>\$10,069,868</u>	<u>\$11,213,010</u>	<u>(\$1,143,142)</u>			<u>\$10,069,868</u>	
DCSS Managed											\$186,993	
FF&E: 7700-7504	\$750,000	<u>\$115,000</u>	\$865,000	<u>\$934,276</u>		\$934,276	<u>\$934,276</u>	<u>(\$0)</u>				
Technology: 7800-7801	\$255,139	<u>\$75,000</u>	\$330,139	<u>\$267,525</u>		\$267,525	<u>\$267,525</u>	<u>(\$0)</u>				
DCSS Managed Subtotal	\$1,005,139	<u>\$190,000</u>	\$1,195,139	<u>\$1,201,800</u>		\$1,201,801	<u>\$1,201,801</u>	<u>(\$0)</u>				
Project Total	\$13,917,759	<u>(\$2,465,759)</u>	\$11,452,000	\$10,441,256	<u>\$830,413</u>	\$11,271,669	<u>\$12,414,811</u>	<u>(\$1,143,142)</u>			<u>\$11,271,669</u>	
											<u>\$180,331</u>	

Program\DeKalb County\421 SPLOST III\High Schools\Cross Keys HS - Renovation & Addition

Project Manager: Janene Glasman
Architect-Engineer: Richard Wittsiebe Hand
Contractor: Evergreen Construction
Project: 421-106
Project Stage: 5. Close-out
Delivery Method: CM @ Risk

Growth

Original Current Projected

— Budget — Contract

Funding Source

\$14.6 M \$1.14 M \$1.18 M
\$792 K Construction
FF & E FF & E
Architect/Engineer Architect/Engineer
Technology Technology
Others Others

Financials

Category	Value
Budget Committed	\$14.6 M
Budget Spent	\$1.14 M
Budget Projected	\$1.18 M
Remaining Budget	\$792 K

Site Photograph

Evergreen Construction
421-106
Project Status - 5. Close-out
2024-08-28



Scope of Work:

- This project includes renovation and upgrades to HVAC, ceilings, lighting, and electrical systems. Also included is a 15,000 SF expansion to a classroom wing to accommodate the relocation of DeKalb High School of Technology North and re-roofing of the existing building.



Cost Status by Budget Category:									
Budget Category		Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance
CIT Managed	Architect/Engineer: 7100-7101	\$708,1178	\$218,000	\$926,178	\$646,877	\$260,421	\$907,298	\$888,914	\$14,432
	Surveying: 7100-7102	\$25,000	\$22,000	\$47,000	\$26,121	\$26,121	\$26,121	\$26,121	\$0
	Construction Testing: 7100-7103	\$45,000		\$45,000	\$12,257	\$19,580	\$31,837	\$31,837	(\$214)
	Abatement: 7100-7104	\$70,000	\$56,000	\$126,000	\$109,870		\$109,870	\$109,870	\$0
	Other Consultants: 7100-7105	\$20,000		\$20,000	\$6,615		\$6,615	\$6,615	\$0
	Management Fees: 7200-7201	\$449,717	(\$449,717)						
	Construction Technology: 7300-7301	\$11,777,973	\$2,800,000	\$14,577,973	\$475,113	\$14,419,927	\$14,895,040	\$13,635,053	\$804,662
	Miscellaneous: 7300-7301.22	\$195,000	\$195,000	\$26,692	\$26,692	\$26,692	\$26,692	\$26,692	\$0
	Security: 7400-7401	\$240,846	(\$134,500)	\$106,346	\$1,412	\$1,412	\$1,412	\$1,412	\$0
	Security: 7300-7302	\$150,000	(\$110,000)	\$40,000					

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORS	ETC Forecast	Estimate At Completion	Uncommitted
Utilities: 7500-7501	\$100,000	(\$35,000)	\$45,000				\$142,705	\$129,260	\$13,445		\$3,000	\$42,000
Moving / Relocation: 7500-7502	\$125,000	\$25,000	\$150,000	\$142,705			\$64,955	\$62,453	\$2,502		\$5,000	\$147,705
Trailers: 7600-7503	\$1,000,000	(\$850,000)	\$150,000	\$64,955							\$35,000	\$99,955
Contingency: 9999-9999	\$549,222	(\$336,000)	\$213,222									\$50,045
CIT Managed Subtotal	\$15,260,936	\$1,380,783	\$16,641,719	\$1,512,617	\$14,699,928	\$16,212,545	\$14,891,535	\$861,520	\$104,803	\$71,879	\$16,389,227	\$213,222
DCSS Managed												\$252,492
FF & E: 7700-7504	\$916,412	\$262,500	\$1,178,912				\$885,700	\$885,700				\$293,212
Technology: 7800-7801	\$750,000	\$42,000	\$792,000	\$132,195				\$132,195				\$659,805
DCSS Managed Subtotal	\$1,666,412	\$304,500	\$1,910,912	\$1,017,895				\$1,017,895				\$933,017
Project Total	\$16,927,348	\$1,685,283	\$18,612,631	\$2,530,512	\$14,699,928	\$17,230,440	\$15,909,429	\$861,520	\$104,803	\$71,879	\$17,407,122	\$1,205,509

Program\DeKalb County\421 SPLOST III\High Schools\DeKalb HS of Tech South - Roof

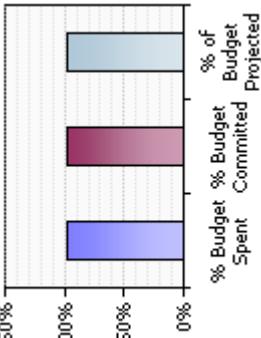
Project Manager:	Yolanda Brown	Growth	
Architect-Engineer:	PCI Group, Inc		
Contractor:	Roof Management		
Project:	421-215		
Project Stage:	6. Completed		
Delivery Method:	Design / Bid / Build		
No Photo Available			
Funding Source			
Cost Status by Budget Category:			
Scope of Work:			
	▪ Full roof replacement		
Remarks:			
	▪ Construction was completed May 1010.		

Program\DeKalb County\421 SPLOST III\High Schools\Druid Hills HS - Renovation & Addition
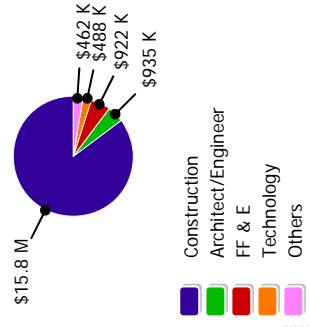
<p>Project Manager: Janene Glasman Architect-Engineer: Perkins & Will, Inc Contractor: Merit Construction Company Project: 421-119 Project Stage: 5. Close-out Delivery Method: CM @ Risk</p> 	<p>Growth</p> 	<p>Funding Source</p>  <table border="1"> <thead> <tr> <th>Funding Source</th> <th>Budget</th> <th>Contract</th> <th>Current</th> <th>Projected</th> </tr> </thead> <tbody> <tr> <td>Construction</td> <td>\$935 K</td> <td>\$922 K</td> <td>\$488 K</td> <td>\$462 K</td> </tr> <tr> <td>Architect/Engineer</td> <td></td> <td></td> <td></td> <td></td> </tr> <tr> <td>FF & E</td> <td></td> <td></td> <td></td> <td></td> </tr> <tr> <td>Technology</td> <td></td> <td></td> <td></td> <td></td> </tr> <tr> <td>Others</td> <td></td> <td></td> <td></td> <td></td> </tr> </tbody> </table>	Funding Source	Budget	Contract	Current	Projected	Construction	\$935 K	\$922 K	\$488 K	\$462 K	Architect/Engineer					FF & E					Technology					Others					<p>Scope of Work:</p> <ul style="list-style-type: none"> This project includes renovation and upgrades to HVAC, ceilings, lighting, and electrical systems. A 31,000 SF, two-story science classroom addition is also included. <p>Remarks:</p> <ul style="list-style-type: none"> This project is substantially complete. Punchlist work is ongoing. 	<p>Cost Status by Budget Category:</p> <table border="1"> <thead> <tr> <th>Budget Category</th> <th>Original Budget</th> <th>Budget Revision</th> <th>Current Budget</th> <th>Original Contract</th> <th>Executed Changes</th> <th>Current Contract</th> <th>Paid To Date</th> <th>Contract Balance</th> <th>CORs</th> <th>ETC Forecast</th> <th>ETC Completion</th> <th>Uncommitted</th> </tr> </thead> <tbody> <tr> <td>CIT Managed</td> <td></td> </tr> <tr> <td>Architect/Engineer: 7100-7101</td> <td>\$951,411</td> <td>(\$16,861)</td> <td>\$924,550</td> <td>\$924,550</td> <td></td> <td>\$922,322</td> <td>\$2,228</td> <td>\$2,000</td> <td>\$926,550</td> <td></td> <td>\$8,000</td> </tr> <tr> <td>Surveying: 7100-7102</td> <td>\$30,000</td> <td>(\$21,750)</td> <td>\$8,250</td> <td>\$8,250</td> <td></td> <td>\$8,250</td> <td></td> <td></td> <td></td> <td>\$8,250</td> <td></td> </tr> <tr> <td>Construction Testing: 7100-7103</td> <td>\$125,000</td> <td>(\$77,070)</td> <td>\$47,930</td> <td>\$44,664</td> <td></td> <td>\$41,340</td> <td>\$829</td> <td></td> <td>\$1,500</td> <td>\$46,164</td> <td>\$1,766</td> </tr> <tr> <td>Abatement: 7100-7104</td> <td>\$22,300</td> <td>\$54,457</td> <td>\$76,757</td> <td>\$65,311</td> <td></td> <td>\$64,953</td> <td>\$1</td> <td></td> <td>\$1,000</td> <td>\$66,311</td> <td>\$10,446</td> </tr> <tr> <td>Other Consultants: 7100-7105</td> <td>\$78,712</td> <td>(\$65,479)</td> <td>\$13,233</td> <td>\$3,233</td> <td></td> <td>\$3,233</td> <td></td> <td></td> <td>\$1,000</td> <td>\$4,233</td> <td>\$9,000</td> </tr> <tr> <td>Management Fees: 7200-7201</td> <td>\$1,235,912</td> <td>(\$1,235,912)</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> </tr> <tr> <td>Construction: 7300-7301</td> <td>\$15,826,842</td> <td>\$15,826,842</td> <td>\$15,728,822</td> <td>(\$36,854)</td> <td>\$15,691,968</td> <td>\$14,393,462</td> <td>\$409,104</td> <td></td> <td>\$122,006</td> <td>\$15,813,974</td> <td>\$12,868</td> </tr> <tr> <td>Miscellaneous: 7300-7302</td> <td>\$446,520</td> <td>(\$371,520)</td> <td>\$75,000</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>\$40,000</td> <td>\$40,000</td> <td>\$35,000</td> </tr> <tr> <td>Security: 7400-7401</td> <td>\$75,000</td> <td>(\$5,000)</td> <td>\$70,000</td> <td>\$65,868</td> <td></td> <td>\$65,868</td> <td></td> <td></td> <td></td> <td>\$65,868</td> <td>\$4,132</td> </tr> <tr> <td>Utilities: 7500-7501</td> <td>\$175,000</td> <td>(\$168,990)</td> <td>\$6,010</td> <td></td> <td></td> <td>\$6,010</td> <td></td> <td></td> <td></td> <td>\$6,010</td> <td></td> </tr> <tr> <td>Moving / Relocation: 7500-7502</td> <td>\$200,000</td> <td>(\$120,000)</td> <td>\$80,000</td> <td>\$65,763</td> <td></td> <td>\$65,763</td> <td>\$3,891</td> <td>\$500</td> <td>\$66,263</td> <td>\$13,738</td> <td></td> </tr> </tbody> </table>	Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	ETC Completion	Uncommitted	CIT Managed													Architect/Engineer: 7100-7101	\$951,411	(\$16,861)	\$924,550	\$924,550		\$922,322	\$2,228	\$2,000	\$926,550		\$8,000	Surveying: 7100-7102	\$30,000	(\$21,750)	\$8,250	\$8,250		\$8,250				\$8,250		Construction Testing: 7100-7103	\$125,000	(\$77,070)	\$47,930	\$44,664		\$41,340	\$829		\$1,500	\$46,164	\$1,766	Abatement: 7100-7104	\$22,300	\$54,457	\$76,757	\$65,311		\$64,953	\$1		\$1,000	\$66,311	\$10,446	Other Consultants: 7100-7105	\$78,712	(\$65,479)	\$13,233	\$3,233		\$3,233			\$1,000	\$4,233	\$9,000	Management Fees: 7200-7201	\$1,235,912	(\$1,235,912)										Construction: 7300-7301	\$15,826,842	\$15,826,842	\$15,728,822	(\$36,854)	\$15,691,968	\$14,393,462	\$409,104		\$122,006	\$15,813,974	\$12,868	Miscellaneous: 7300-7302	\$446,520	(\$371,520)	\$75,000						\$40,000	\$40,000	\$35,000	Security: 7400-7401	\$75,000	(\$5,000)	\$70,000	\$65,868		\$65,868				\$65,868	\$4,132	Utilities: 7500-7501	\$175,000	(\$168,990)	\$6,010			\$6,010				\$6,010		Moving / Relocation: 7500-7502	\$200,000	(\$120,000)	\$80,000	\$65,763		\$65,763	\$3,891	\$500	\$66,263	\$13,738	
Funding Source	Budget	Contract	Current	Projected																																																																																																																																																																																												
Construction	\$935 K	\$922 K	\$488 K	\$462 K																																																																																																																																																																																												
Architect/Engineer																																																																																																																																																																																																
FF & E																																																																																																																																																																																																
Technology																																																																																																																																																																																																
Others																																																																																																																																																																																																
Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	ETC Completion	Uncommitted																																																																																																																																																																																				
CIT Managed																																																																																																																																																																																																
Architect/Engineer: 7100-7101	\$951,411	(\$16,861)	\$924,550	\$924,550		\$922,322	\$2,228	\$2,000	\$926,550		\$8,000																																																																																																																																																																																					
Surveying: 7100-7102	\$30,000	(\$21,750)	\$8,250	\$8,250		\$8,250				\$8,250																																																																																																																																																																																						
Construction Testing: 7100-7103	\$125,000	(\$77,070)	\$47,930	\$44,664		\$41,340	\$829		\$1,500	\$46,164	\$1,766																																																																																																																																																																																					
Abatement: 7100-7104	\$22,300	\$54,457	\$76,757	\$65,311		\$64,953	\$1		\$1,000	\$66,311	\$10,446																																																																																																																																																																																					
Other Consultants: 7100-7105	\$78,712	(\$65,479)	\$13,233	\$3,233		\$3,233			\$1,000	\$4,233	\$9,000																																																																																																																																																																																					
Management Fees: 7200-7201	\$1,235,912	(\$1,235,912)																																																																																																																																																																																														
Construction: 7300-7301	\$15,826,842	\$15,826,842	\$15,728,822	(\$36,854)	\$15,691,968	\$14,393,462	\$409,104		\$122,006	\$15,813,974	\$12,868																																																																																																																																																																																					
Miscellaneous: 7300-7302	\$446,520	(\$371,520)	\$75,000						\$40,000	\$40,000	\$35,000																																																																																																																																																																																					
Security: 7400-7401	\$75,000	(\$5,000)	\$70,000	\$65,868		\$65,868				\$65,868	\$4,132																																																																																																																																																																																					
Utilities: 7500-7501	\$175,000	(\$168,990)	\$6,010			\$6,010				\$6,010																																																																																																																																																																																						
Moving / Relocation: 7500-7502	\$200,000	(\$120,000)	\$80,000	\$65,763		\$65,763	\$3,891	\$500	\$66,263	\$13,738																																																																																																																																																																																						


Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
Trailers: 7600-7503	\$156,532	(\$126,818)	\$29,814	\$29,959		\$29,959	\$26,143	\$3,816		(\$2,756)	\$27,203	\$2,611
Contingency: 9999-9999	\$856,915	(\$801,777)	\$55,138							\$40,000	\$40,000	\$15,138
CLT Managed Subtotal	\$20,180,244	(\$2,956,720)	\$17,223,524	\$16,942,430	(\$36,854)	\$16,905,576	\$15,587,186	\$419,869		\$205,250	\$17,110,826	\$112,698
DCSS Managed												
FF&E: 7700-7504	\$1,421,613	(\$500,000)	\$921,613	\$804,149		\$804,149	\$791,987	\$12,162			\$804,149	\$117,464
Technology: 7800-7801	\$488,000		\$488,000	\$497,094		\$497,094	\$497,093	\$1			\$497,094	(\$9,094)
DCSS Managed Subtotal	\$1,909,613	(\$500,000)	\$1,409,613	\$1,301,243		\$1,301,243	\$1,289,080	\$12,163		\$1,301,243	\$108,370	
Project Total:	\$22,089,857	(\$3,456,720)	\$18,633,137	\$18,243,673	(\$36,854)	\$18,206,819	\$16,876,266	\$432,033	\$205,250	\$18,412,069	\$221,068	

Program\DeKalb County\421 SPLOST III\High Schools\DSA\Avondale HS Relocation to Avondale HS

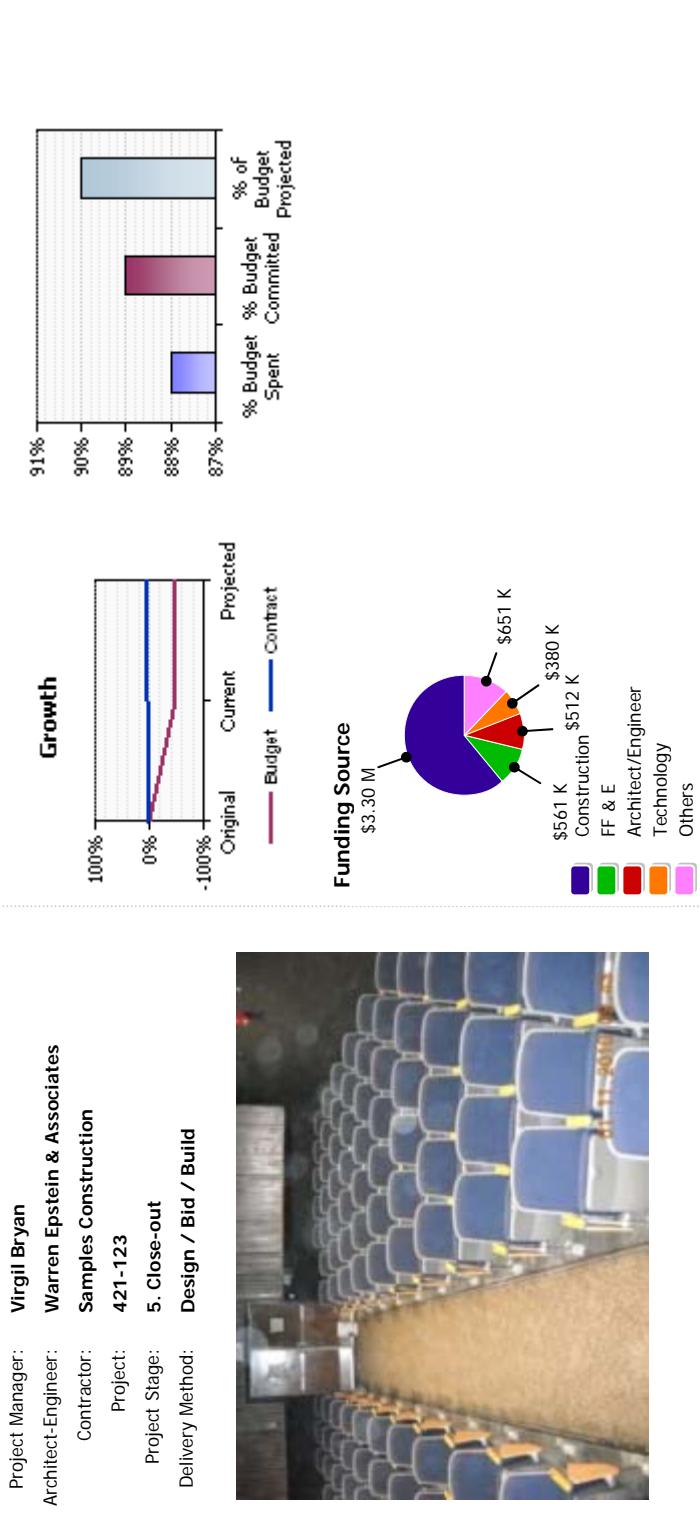

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
Security: 7400-7401	\$25,000	\$50,000	\$75,000	\$22,752		\$22,752	\$22,752			\$52,000	\$74,752	\$248
Utilities: 7500-7501	\$75,000	(\$50,000)	\$25,000							\$25,000	\$25,000	
Moving / Relocation: 7500-7502	\$125,000	\$5,000	\$130,000	\$93,094		\$93,094	(\$695)			\$36,000	\$129,094	\$906
Trailers: 7600-7503		\$54,999	\$54,999	\$13,045		\$13,045	\$9,897	\$2,259		\$43,000	\$56,045	(\$1,046)
Contingency: 9999-9999	\$500,000	(\$400,000)	\$100,000									\$100,000
CIT Managed Subtotal	\$9,239,250	(\$4,831,285)	\$4,407,965	\$3,920,080	\$118,869	\$4,038,949	\$3,930,168	\$38,777	\$47,317	\$323,000	\$4,409,266	(\$1,301)
DCSS Managed												
FF&E: 7700-7504	\$460,750	\$100,000	\$560,750	\$429,581		\$429,581	\$406,591	\$22,990		\$131,000	\$560,581	\$169
Technology: 7800-7801	\$300,000	\$80,000	\$380,000	\$285,839		\$285,839	\$285,746	\$93		\$94,000	\$379,839	\$161
DCSS Managed Subtotal	\$760,750	\$180,000	\$940,750	\$715,420		\$715,420	\$692,338	\$23,083		\$225,000	\$340,420	\$330
Project Total	\$10,000,000	(\$4,651,285)	\$5,348,715	\$4,635,500	\$118,869	\$4,754,369	\$4,622,506	\$61,860	\$47,317	\$548,000	\$5,349,686	(\$971)

Program\DeKalb County\421 SPLOST III\High Schools\HHS - Renovation & Addition

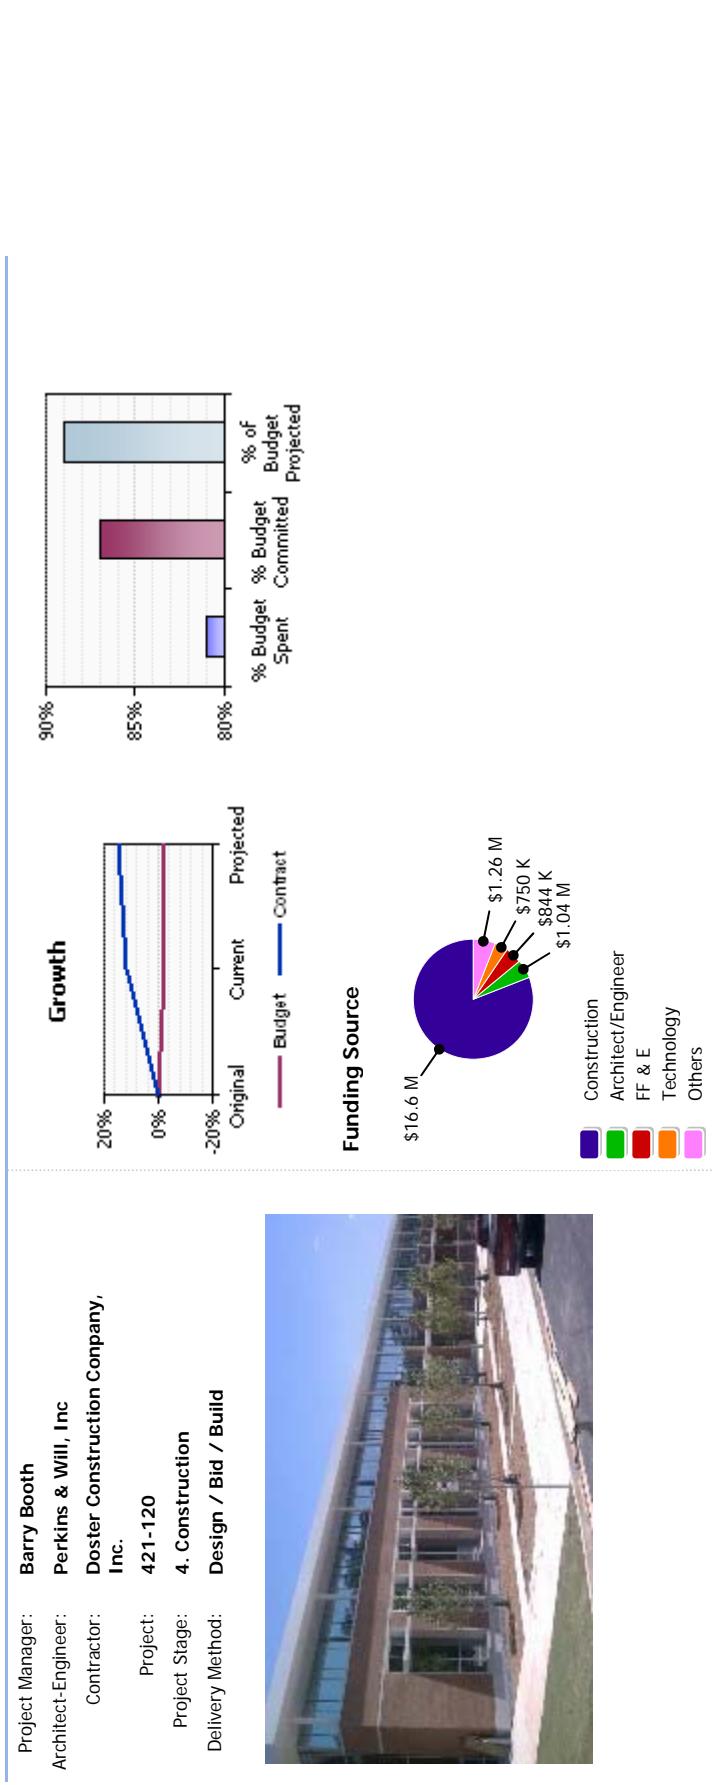

Scope of Work:


- The scope includes HVAC, Lighting and ADA upgrades, Career Technology Renovations and Classroom additions. The existing facility is approximately 170,030 sf and the planned additions are approximately 38,180 sf.

Remarks:


- The last phase, Auditorium addition is approximately 99% complete with an anticipated completion of end of May. Interior trim out in progress.

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
Trailers: 7600-7503	\$250,000	\$250,000	\$95,661			\$95,661	\$70,643	\$16,686		\$154,339	\$250,000	
Contingency: 9999-9999	\$700,866	(\$650,000)	\$50,866							\$50,000	\$50,000	\$866
CLT Managed Subtotal	\$19,184,661	(\$248,000)	\$18,936,661	\$15,651,832	\$1,941,365	\$17,593,197	\$14,918,109	\$1,246,834	\$471,825	\$831,931	\$18,896,953	\$39,708
DCSS Managed												
FF&E: 7700-7504	\$1,094,685	(\$250,866)	\$843,819	\$84,170		\$84,170	\$75,065	(\$0)		\$759,649	\$843,819	(\$0)
Technology: 7800-7801	\$750,000	\$750,000	\$119,083			\$119,083	\$119,083			\$630,917	\$750,000	(\$0)
DCSS Managed Subtotal	\$1,844,685	(\$250,866)	\$1,593,819	\$203,254		\$203,254	\$194,148	(\$0)		\$1,390,566	\$1,593,820	(\$1)
Project Total	\$21,029,346	(\$498,866)	\$20,530,480	\$15,855,086	\$1,941,365	\$17,796,451	\$15,112,257	\$1,246,833	\$471,825	\$2,222,497	\$20,490,773	\$39,707

Program\DeKalb County\421 SPLOST III\Elementary Schools\Eldridge L. Miller ES - Roof

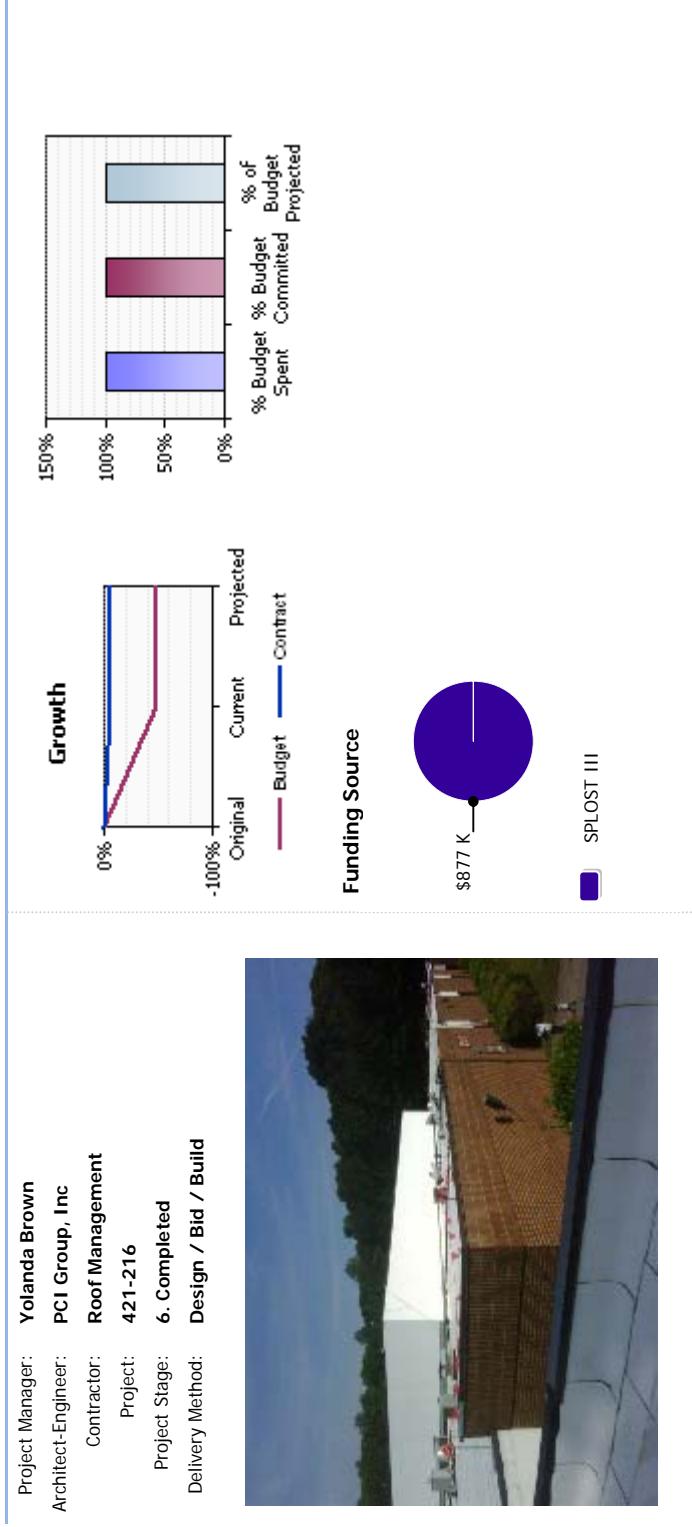


Program\DeKalb County\421 SPLOST III\Site Improvements\Site Improvements 1 (321)\Emergency Generators

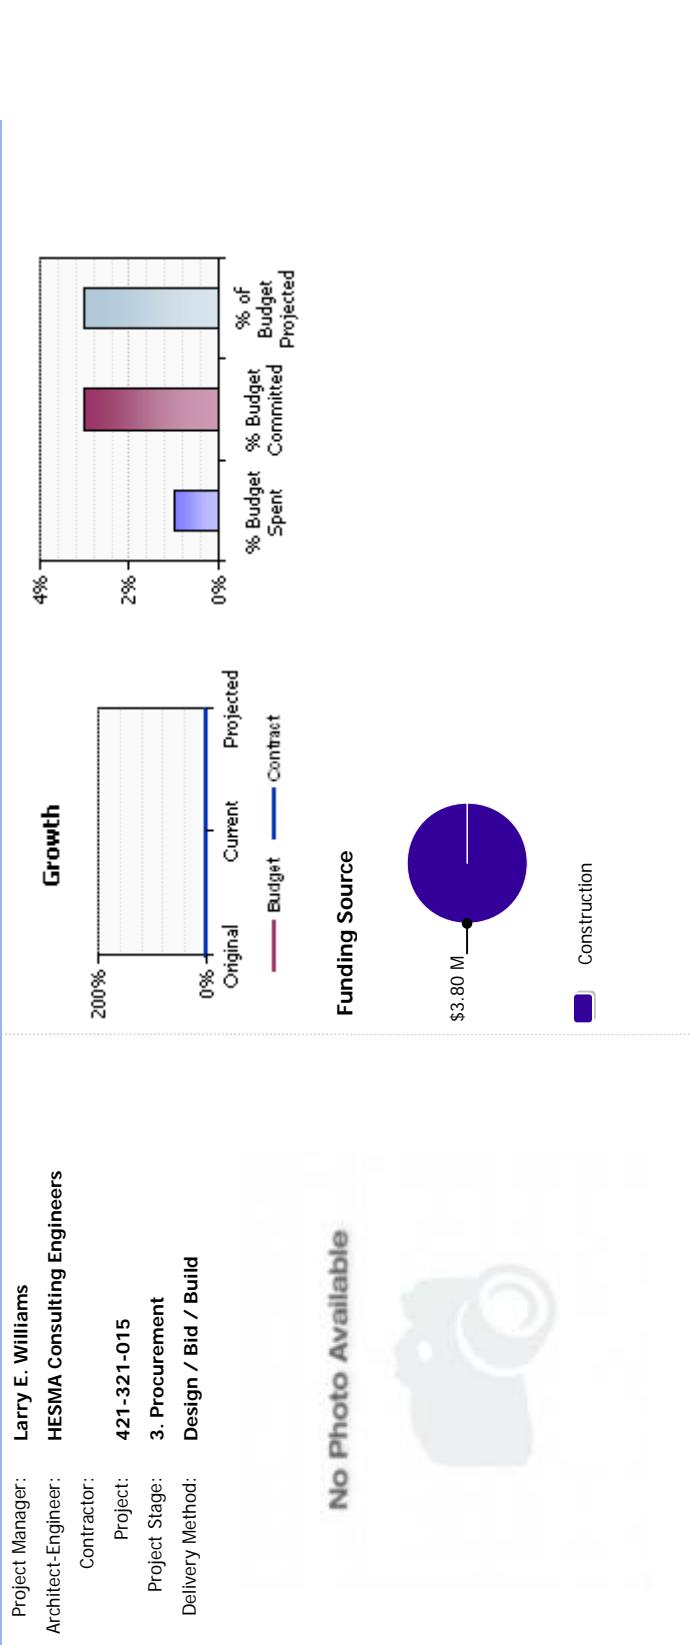

Cost Status by Budget Category:						
Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract
CIT Managed				\$115,994	\$36,626	\$79,368
Construction: 7300-7301	\$3,800,000	\$3,800,000	\$115,994	\$115,994		
CIT Managed Subtotal	\$3,800,000	\$3,800,000	\$115,994	\$36,626	\$79,368	
Project Total	\$3,800,000	\$3,800,000	\$115,994	\$115,994	\$36,626	\$79,368

Program\DeKalb County\421 SPLOST III\Emergency HVAC Work - SPLOST III\Emergency HVAC Work

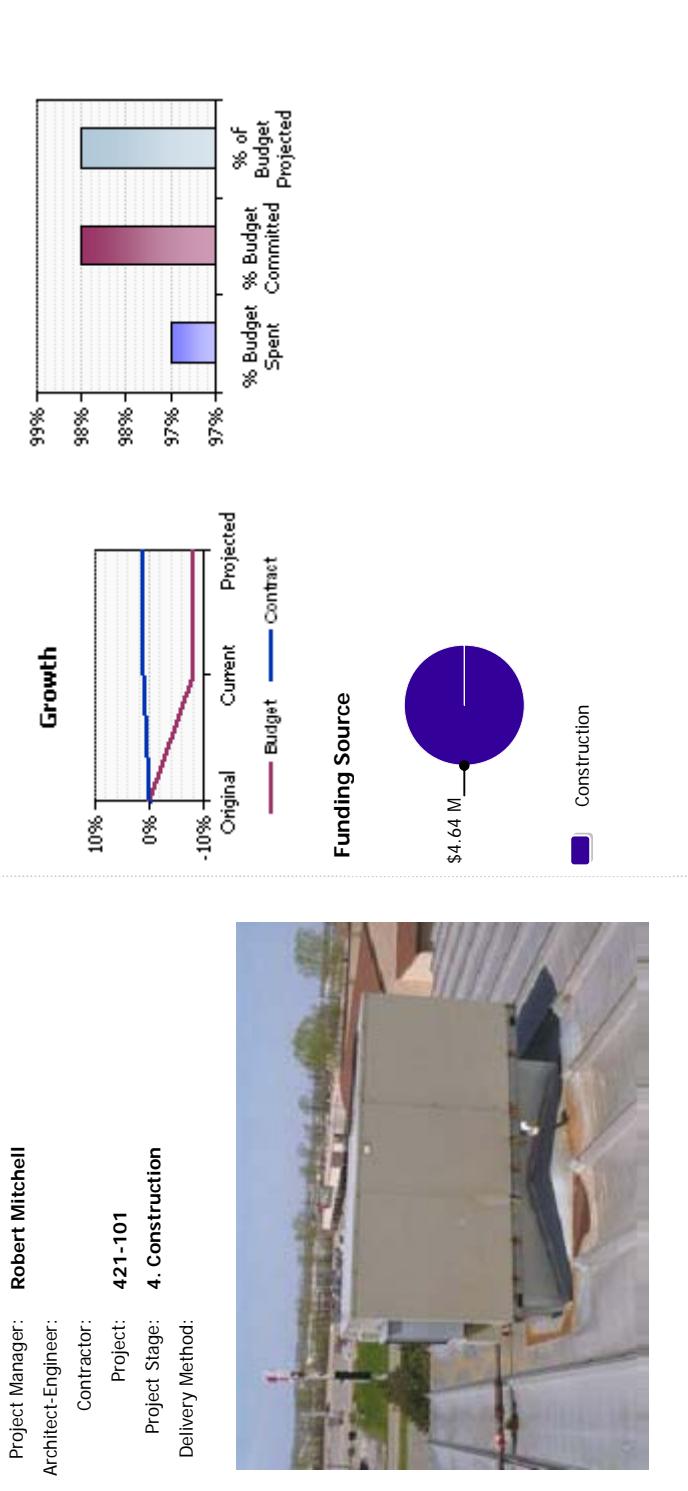

Scope of Work:

- The following are projects and their corresponding values which are funded from this project:
 - Sequoyah MS, 419-633 \$125,000
 - Margaret Harris HS, 419-652 \$349,282
 - Snapfinger ES, 419-660 \$3706,026
 - Avondale HS, 419-755 \$1,152,516
 - Redan ES, 419-763 \$402,800
 - Shamrock MS, 419-772 \$366,318


Remarks:

- Sequoyah MS - In Closeout and working on punchlist
- Margaret Harris HS - Completed
- Snapfinger ES - Completed - Closeout Documents Rec'd and punchlist done
- Avondale HS - Complete
- Redan ES - Complete
- Shamrock MS - Complete

Cost Status by Budget Category:

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
CIT Managed												
Construction: 7300-7301	\$5,026,397	(\$390,000)	\$4,636,397	\$4,508,266	\$26,478	\$4,534,744	\$4,474,415	\$60,329	\$101,000	\$4,635,744	\$653	
CIT Managed Subtotal	\$5,026,397	(\$390,000)	\$4,636,397	\$4,508,266	\$26,478	\$4,534,744	\$4,474,415	\$60,329	\$101,000	\$4,635,744	\$653	
Project Total	\$5,026,397	(\$390,000)	\$4,636,397	\$4,508,266	\$26,478	\$4,534,744	\$4,474,415	\$60,329	\$101,000	\$4,635,744	\$653	

Program\DeKalb County\421 SPLOST III\Site Improvements\Site Improvements 2 (322)\Energy Management System Update

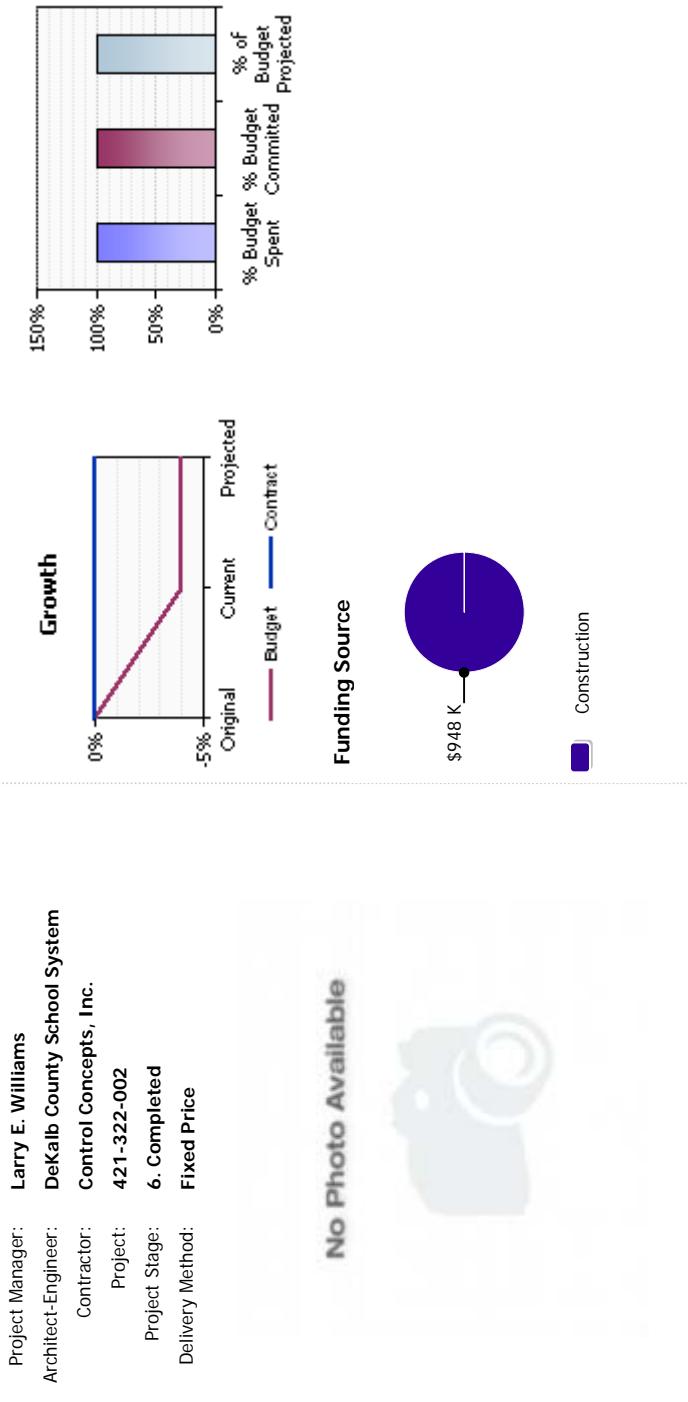

Scope of Work:

- Update the Energy Management System from Ergon to Staefa/Talon at 49 locations district-wide. This project allows Plant Services to monitor, schedule and control HVAC by zone at the following schools:
Elementary Schools - Kittredge Magnet, Livsey, Kingsley, Fernbank, Huntley Hills, McLendon, Henderson Mill, Idlewood, Knollwood, Wadsworth, Atherton, Murphy Candler, Rock Chapel, Stoneview, Robert Shaw, Rockbridge, Eldridge Miller, Clifton, Montclair, Pleasantdale, Rainbow, Smokerise, Indian Creek, Midway, Glen Haven, Toney, Kelley Lake, Laurel Ridge, Browns Mill, Shadow Rock, Shadow Rock Center, Hambrick, Stone Mill, Allgood, Pinecrest, Montgomery, Dresden, Sagamore Hills, Middle Schools - Ronald McNair, Sr., Chapel Hill, Miller Grove, Champion-Old St. Mt. Centers - Warren Tech, Rehoboth, International Student

Remarks:

- Phases 1 through 6 are complete. All documents have been completed to close this project out.


Cost Status by Budget Category:

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORS	ETC Forecast	ETC Completion	Estimate At Uncommitted
CIT Managed												
Construction: 7300-7301	\$988,000	(\$40,000)	\$948,000	\$948,000			\$948,000	\$948,000				\$948,000
CIT Managed Subtotal	\$988,000	(\$40,000)	\$948,000	\$948,000			\$948,000	\$948,000				\$948,000
Project Total	\$988,000	(\$40,000)	\$948,000	\$948,000			\$948,000	\$948,000				\$948,000

Program\DeKalb County\421 SPLOST III\Elementary Schools\Evansdale ES - Roof

Cost Status by Budget Category:												
Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
CIT Managed												
Architect/Engineer: 7100-7101	\$34,194	\$12,540										
Construction Testing: 7100-7103	\$1,500	\$1,500										
Other Consultants: 7100-7105	\$2,678	\$2,380										
Construction: 7300-7301	\$576,161	\$505,685										
Miscellaneous: 7300-7302	\$1,500	\$1,500										
Contingency: 9999-9999	\$31,575	\$31,575										
CIT Managed Subtotal	\$647,608		\$520,953			\$6,142	\$514,463		\$126,655	\$647,608	\$647,608	
Project Total	\$647,608					\$6,142	\$514,463		\$126,655	\$647,608	\$647,608	


Program\DeKalb County\421 SPLOST III\Elementary Schools\Fairington ES- HVAC, Ceilings & Lighting

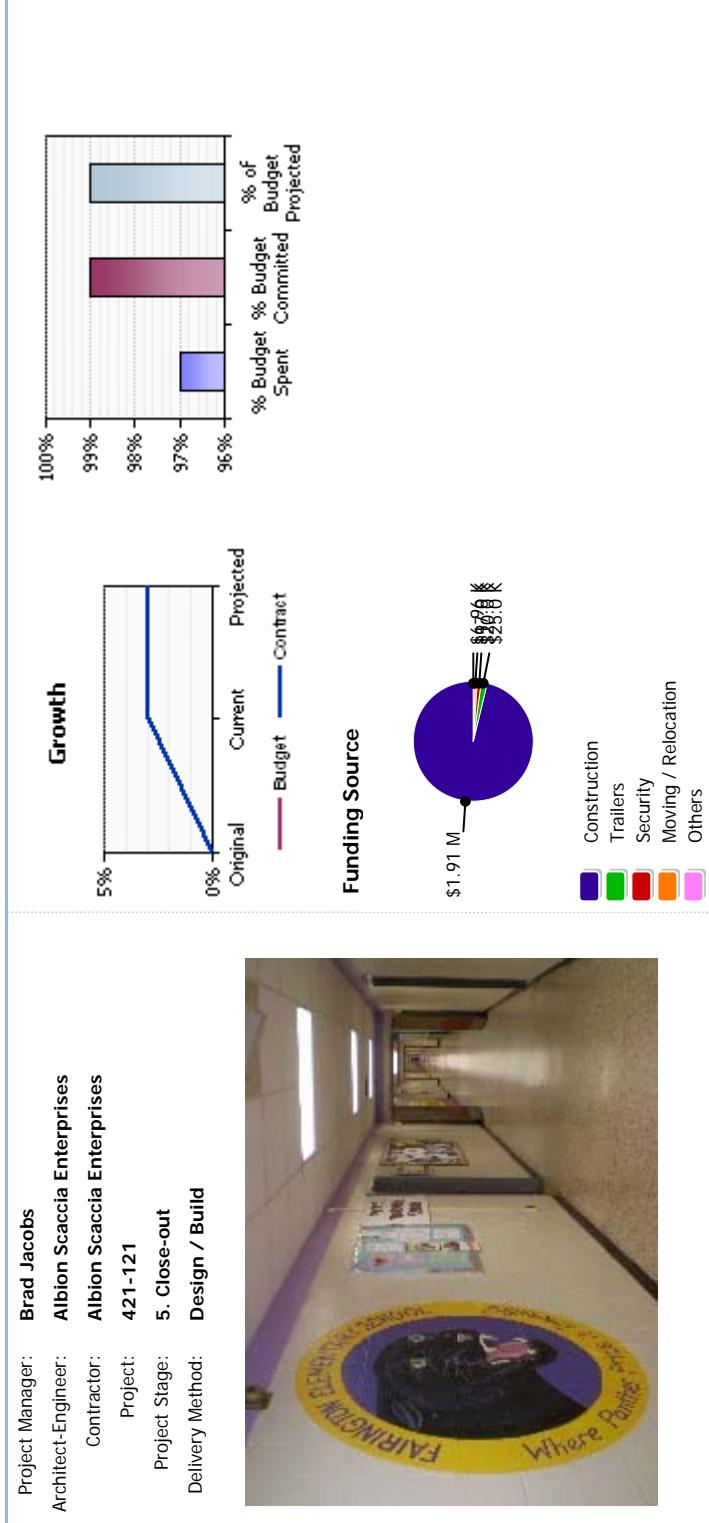

Cost Status by Budget Category:													
Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	ETC Completion	Estimate At Completion	Uncommitted
CIT Managed													
Architect/Engineer: 7100-7101	\$91,678	(\$91,678)											
Construction Testing: 7100-7103	\$16,684	(\$16,684)											
Abatement: 7100-7104	\$8,000	(\$2,713)	\$5,287	\$5,287									
Other Consultants: 7100-7105	\$15,590	(\$15,590)											
Management Fees: 7200-7201	\$34,316	(\$34,316)											
Construction: 7300-7301	\$1,488,974	\$419,196	\$1,908,170	\$1,846,223	\$48,380	\$1,894,603	\$1,871,184	\$23,418	\$13,568	\$1,908,171	\$174	\$16,411	(\$1)
Miscellaneous: 7300-7302	\$78,064	(\$77,890)	\$174	\$174									
Security: 7400-7401	\$10,000	\$10,000	\$20,000										
Utilities: 7500-7501	\$25,000	(\$25,000)											
Moving / Relocation: 7500-7502	\$50,000	(\$33,000)	\$17,000	\$10,383		\$10,383	(\$0)						

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	ETC Forecast	CORs Forecast	Estimate At Completion	Uncommitted
Trailers: 7600-7503	\$25,000	\$25,000	\$22,000	\$22,000		\$18,739	\$2,517		\$22,000		\$3,000	
Contingency: 99999-99999	\$98,825	(\$98,825)										
CIT Managed Subtotal	\$1,917,131	\$58,500	\$1,975,631	\$1,900,478	\$48,380	\$1,948,858	\$1,922,178	\$25,936	\$23,168	\$1,972,026	\$3,605	
DCSS Managed												
Technology: 7800-7801	\$1,500	\$1,500	\$1,500	\$1,500		\$1,500	\$1,500				\$1,500	
DCSS Managed Subtotal	\$1,500	\$1,500	\$1,500	\$1,500		\$1,500	\$1,500				\$1,500	
Project Total:	\$1,917,131	\$60,000	\$1,977,131	\$1,901,978	\$48,380	\$1,950,358	\$1,923,678	\$25,936	\$23,168	\$1,973,526	\$3,605	

Program\DeKalb County\421 SPLOST III\Elementary Schools\Flat Shoals ES - Roof

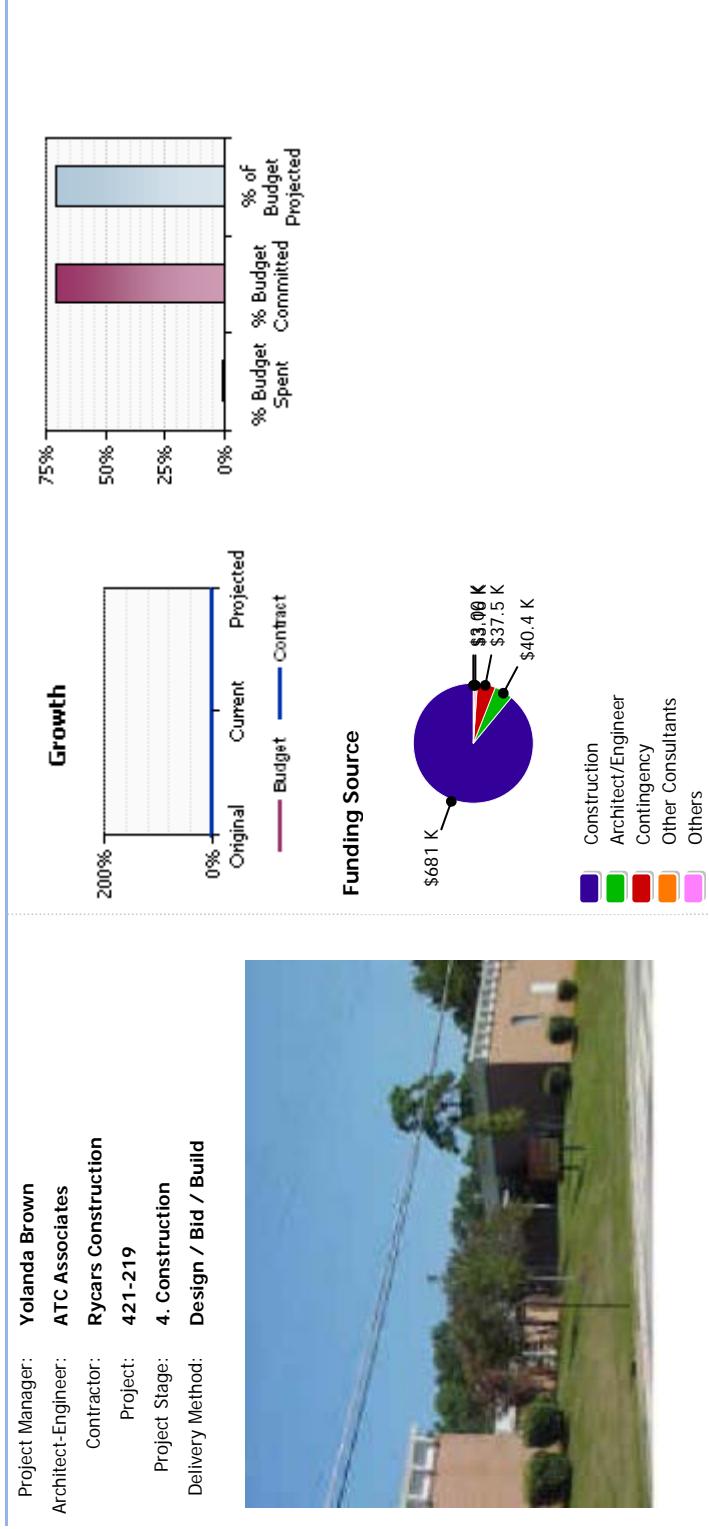

Budget Category	Original Budget	Budget Revision	Current Budget	Current Contract	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORS	ETC Forecast	Estimate At Completion	Uncommitted
CIT Managed													
Architect/Engineer: 7100-7101	\$40,396		\$40,396	\$11,830			\$11,830	\$3,549	\$8,281		\$28,566	\$40,396	
Construction Testing: 7100-7103	\$1,500		\$1,500								\$1,500	\$1,500	
Other Consultants: 7100-7105	\$3,155		\$3,103				\$3,103				\$52	\$3,155	(\$0)
Construction: 7300-7301	\$680,793		\$680,793	\$524,590			\$524,590				\$156,203	\$680,793	
Miscellaneous: 7300-7302	\$1,500		\$1,500	\$348			\$348				\$1,152	\$1,500	
Contingency: 9999-9999	\$37,482		\$37,482								\$37,482	\$37,482	
CIT Managed Subtotal	\$764,826		\$764,826	\$539,871			\$539,871	\$7,000	\$532,871		\$224,955	\$764,826	(-\$0)
Project Total	\$764,826		\$764,826	\$539,871			\$539,871	\$7,000	\$532,871		\$224,955	\$764,826	(-\$0)

PPProgram\DeKalb County\421 SPLOST II\Elementary Schools\Glen Haven ES - Roof

Project Manager: Yolanda Brown
Architect-Engineer: ATC Associates
Contractor: Klein Contracting Corporation
Project: 421-225
Project Stage: 4. Construction
Delivery Method: Design / Bid / Build

Growth

Original Current Projected

% Budget Spent % Budget Committed % Budget Projected

Funding Source


\$849 K \$2.00 K \$51.0 K \$84.1 K

Construction Contingency Architect/Engineer Other Consultants Others


Category	Budget	Actual
Construction	\$849 K	\$84.1 K
Contingency	\$2.00 K	\$51.0 K
Architect/Engineer	\$51.0 K	\$84.1 K
Other Consultants	\$84.1 K	\$84.1 K
Others	\$84.1 K	\$84.1 K

Photograph: A photograph of a modern house under construction, featuring a white frame and glass walls.

Program\DeKalb County\421 SPLIT III\Elementary Schools\Hambrick ES - HVAC

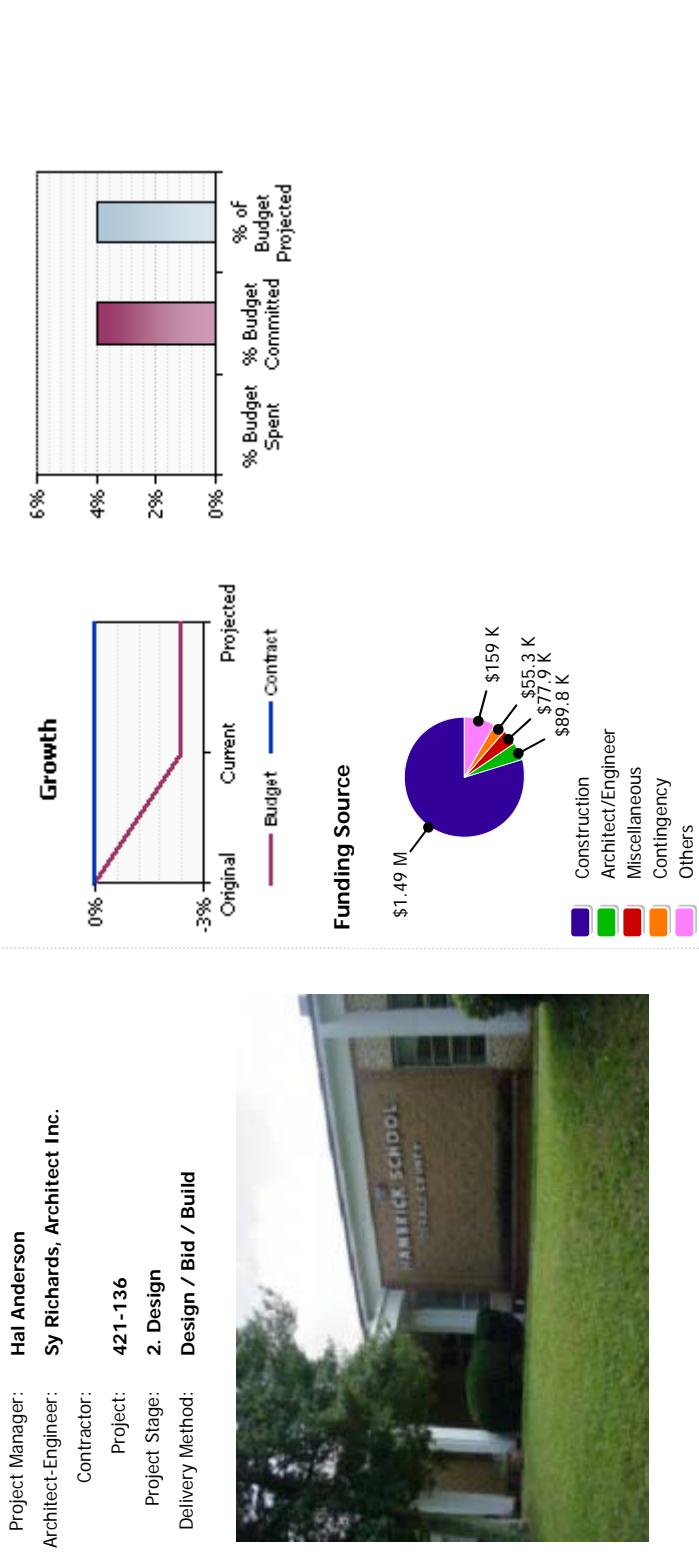


Program\DeKalb County\421 SPLOST III\Elementary Schools\Hambrick ES - Roof

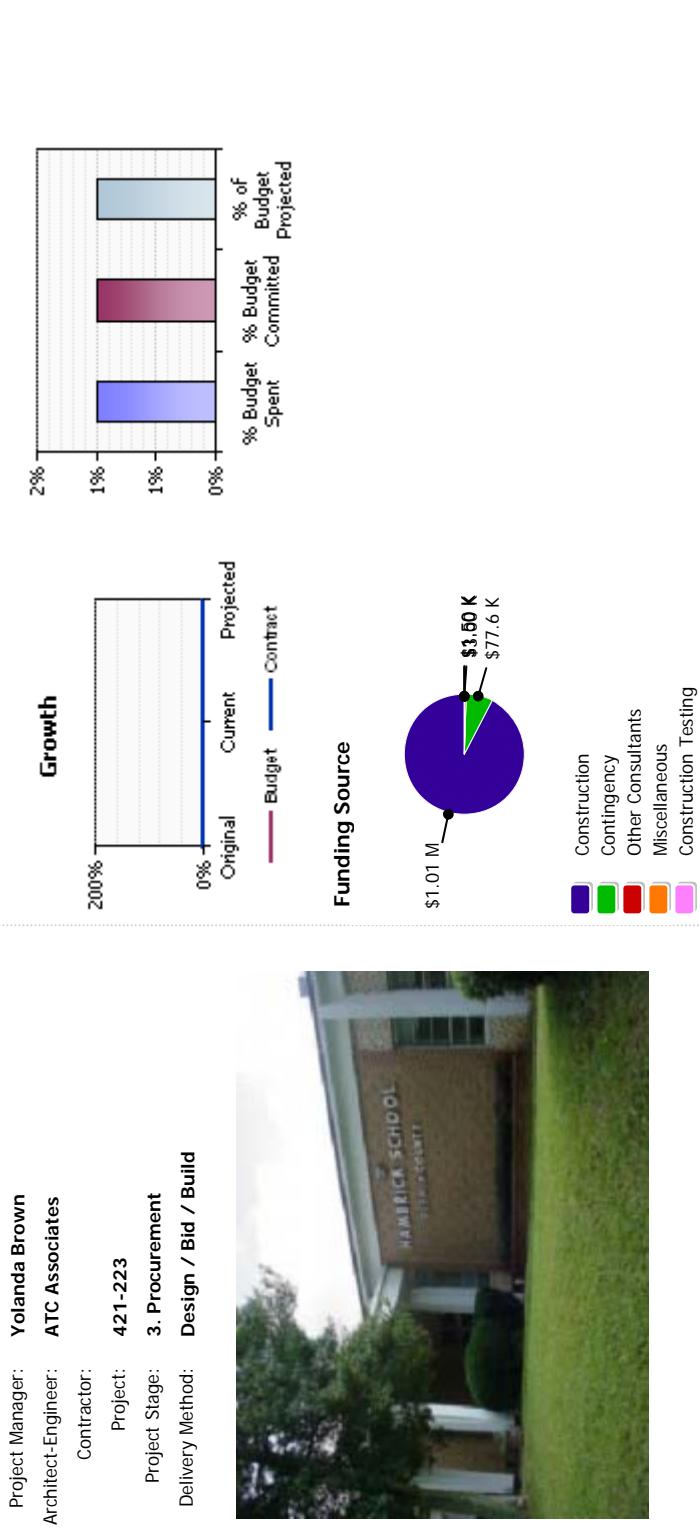



Cost Status by Budget Category:

Budget Category	Original Budget	Budget Revision	Current Budget	Current Contract	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	ccRs	ETC Forecast	ETC Completion	Estimate At Completion	Uncommitted
CIT Managed														
Architect/Engineer: 7100-7101	\$56,968	\$56,968	\$8,122					\$8,122	(\$0)		\$48,846	\$56,968		
Construction Testing: 7100-7103	\$1,500	\$1,500									\$1,500	\$1,500		
Other Consultants: 7100-7105	\$3,004	\$3,004									\$3,004	\$3,004		
Construction: 7300-7301	\$949,473	\$949,473									\$949,473	\$949,473		
Miscellaneous: 7300-7302	\$1,500	\$1,500	\$348								\$1,152	\$1,152		
Contingency: 9999-9999	\$77,555	\$77,555									\$77,555	\$77,555		
CIT Managed Subtotal	\$1,090,000	\$1,090,000	\$8,470					\$8,470	\$8,122	(\$0)	\$1,081,530	\$1,090,000		
Project Total	\$1,090,000		\$8,470					\$8,122	(\$0)		\$1,081,530	\$1,090,000		


Program\DeKalb County\421 SPLOST III\Elementary Schools\Hawthorne ES - Roof

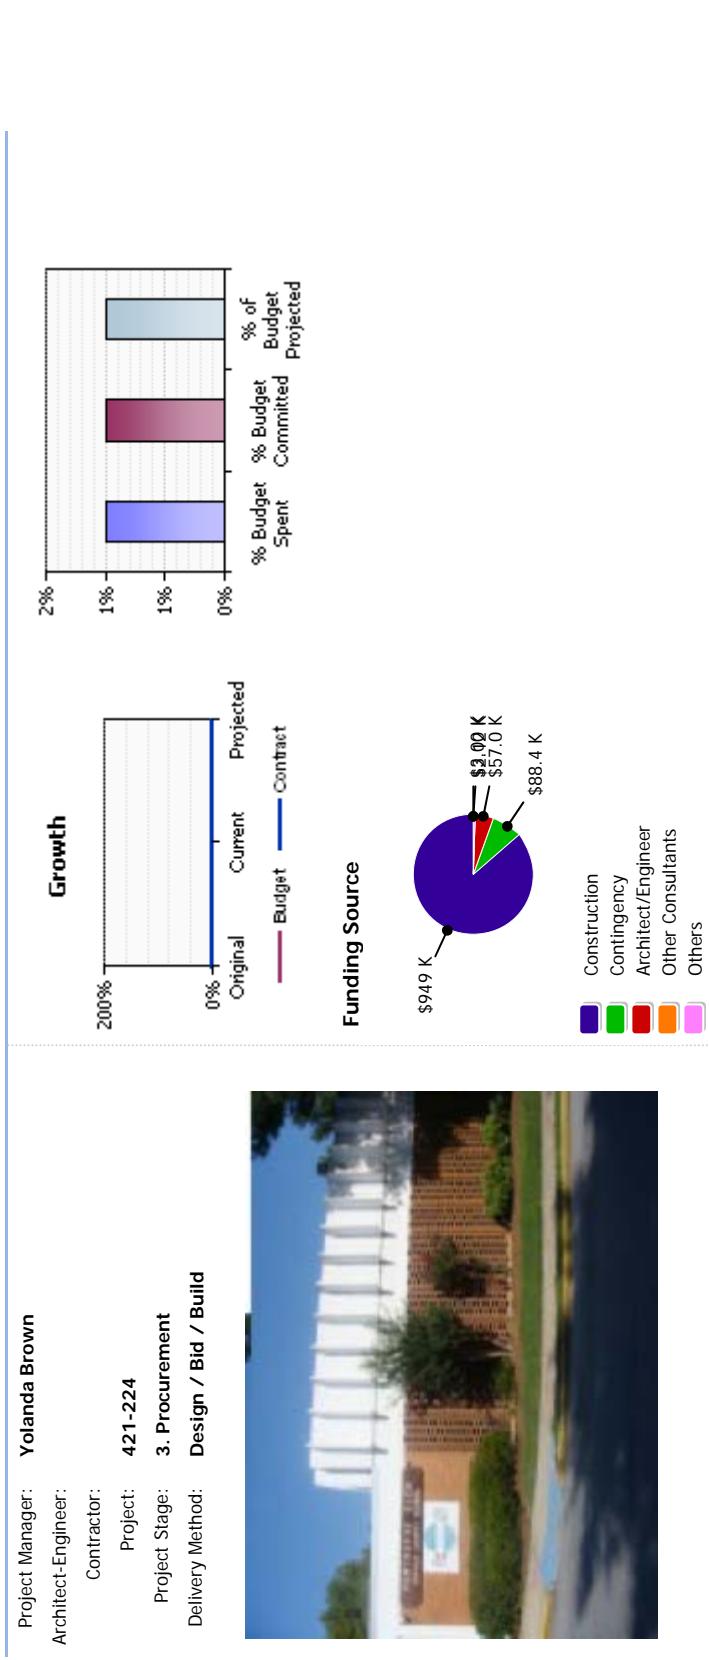

Program\DeKalb County\421 SPLOST III\Elementary Schools\Indian Creek ES - HVAC
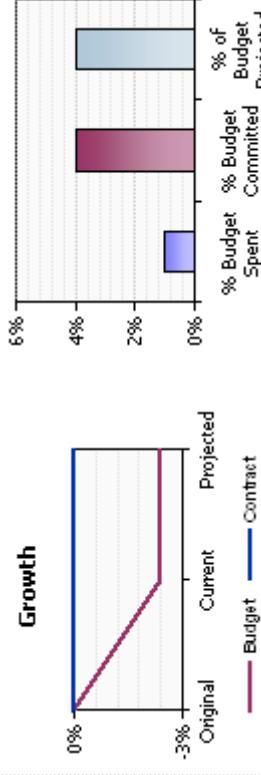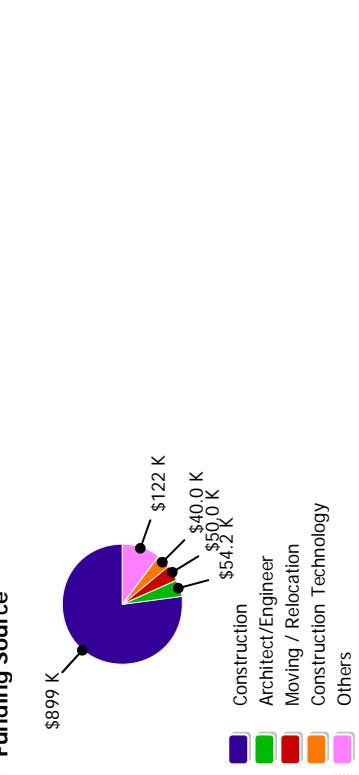
<p>Project Manager: Brad Jacobs Architect-Engineer: Epstein Group Contractor: Project: 421-139 Project Stage: 2. Design Delivery Method: Design / Bid / Build</p>	 <p>Growth</p> <table border="1"> <thead> <tr> <th>Stage</th> <th>Original</th> <th>Current</th> <th>Projected</th> </tr> </thead> <tbody> <tr> <td>% Budget Spent</td> <td>0%</td> <td>~4%</td> <td>~6%</td> </tr> <tr> <td>% Budget Committed</td> <td>0%</td> <td>~2%</td> <td>~4%</td> </tr> <tr> <td>% of Budget Projected</td> <td>0%</td> <td>~2%</td> <td>~4%</td> </tr> </tbody> </table>	Stage	Original	Current	Projected	% Budget Spent	0%	~4%	~6%	% Budget Committed	0%	~2%	~4%	% of Budget Projected	0%	~2%	~4%	 <p>Funding Source</p> <table border="1"> <thead> <tr> <th>Source</th> <th>Amount (\$K)</th> </tr> </thead> <tbody> <tr> <td>Construction</td> <td>\$399 K</td> </tr> <tr> <td>Architect/Engineer</td> <td>\$122 K</td> </tr> <tr> <td>Moving / Relocation</td> <td>\$40.0 K</td> </tr> <tr> <td>Construction Technology</td> <td>\$50.0 K</td> </tr> <tr> <td>Others</td> <td>\$54.2 K</td> </tr> </tbody> </table>	Source	Amount (\$K)	Construction	\$399 K	Architect/Engineer	\$122 K	Moving / Relocation	\$40.0 K	Construction Technology	\$50.0 K	Others	\$54.2 K	<p>Scope of Work:</p> <ul style="list-style-type: none"> HVAC, Ceiling and Lighting replacement and other improvements including new generator, parking lot lighting, grease trap, and cooler / freezer boxes. <p>Remarks:</p> <ul style="list-style-type: none"> Architect has completed their Preliminary Report, currently under review by DCSS. 	<p>Cost Status by Budget Category:</p> <table border="1"> <thead> <tr> <th>Budget Category</th> <th>Original Budget</th> <th>Budget Revision</th> <th>Current Budget</th> <th>Original Contract</th> <th>Executed Changes</th> <th>Current Contract</th> <th>Paid To Date</th> <th>Contract Balance</th> <th>CORs</th> <th>ETC Forecast</th> <th>ETC Completion</th> <th>Estimate At Completion</th> <th>Uncommitted</th> </tr> </thead> <tbody> <tr> <td>CIT Managed</td> <td></td> </tr> <tr> <td>Architect/Engineer: 7100-7101</td> <td>\$54,176</td> <td></td> <td>\$54,176</td> <td>\$50,150</td> <td></td> <td></td> <td>\$42,628</td> <td></td> <td></td> <td>\$4,026</td> <td>\$54,176</td> <td></td> <td></td> </tr> <tr> <td>Construction Testing: 7100-7103</td> <td>\$10,099</td> <td></td> <td>\$10,099</td> <td>\$10,201</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>\$10,099</td> <td>\$10,099</td> <td></td> <td></td> </tr> <tr> <td>Other Consultants: 7100-7105</td> <td>\$10,201</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>\$10,201</td> <td>\$10,201</td> <td></td> <td></td> </tr> <tr> <td>Management Fees: 7200-7201</td> <td>\$20,819</td> <td>(\$20,819)</td> <td></td> </tr> <tr> <td>Construction: 7300-7301</td> <td>\$898,642</td> <td></td> <td>\$898,642</td> <td></td> </tr> <tr> <td>Construction Technology: 7300-7301.22</td> <td>\$40,000</td> <td></td> <td>\$40,000</td> <td></td> </tr> <tr> <td>Miscellaneous: 7300-7302</td> <td>\$46,991</td> <td>(\$20,000)</td> <td>\$26,991</td> <td></td> </tr> <tr> <td>Security: 7400-7401</td> <td>\$10,000</td> <td></td> <td>\$10,000</td> <td></td> </tr> <tr> <td>Utilities: 7500-7501</td> <td>\$25,000</td> <td></td> <td>\$25,000</td> <td></td> </tr> <tr> <td>Moving / Relocation: 7500-7502</td> <td>\$50,000</td> <td></td> <td>\$50,000</td> <td></td> </tr> <tr> <td>Contingency: 9999-9999</td> <td>\$59,259</td> <td>(\$20,000)</td> <td>\$39,259</td> <td></td> </tr> <tr> <td></td> <td>\$39,259</td> <td>\$39,259</td> <td></td> <td></td> </tr> </tbody> </table>	Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	ETC Completion	Estimate At Completion	Uncommitted	CIT Managed														Architect/Engineer: 7100-7101	\$54,176		\$54,176	\$50,150			\$42,628			\$4,026	\$54,176			Construction Testing: 7100-7103	\$10,099		\$10,099	\$10,201						\$10,099	\$10,099			Other Consultants: 7100-7105	\$10,201									\$10,201	\$10,201			Management Fees: 7200-7201	\$20,819	(\$20,819)												Construction: 7300-7301	\$898,642		\$898,642											Construction Technology: 7300-7301.22	\$40,000		\$40,000											Miscellaneous: 7300-7302	\$46,991	(\$20,000)	\$26,991											Security: 7400-7401	\$10,000		\$10,000											Utilities: 7500-7501	\$25,000		\$25,000											Moving / Relocation: 7500-7502	\$50,000		\$50,000											Contingency: 9999-9999	\$59,259	(\$20,000)	\$39,259																					\$39,259	\$39,259		
Stage	Original	Current	Projected																																																																																																																																																																																																																																	
% Budget Spent	0%	~4%	~6%																																																																																																																																																																																																																																	
% Budget Committed	0%	~2%	~4%																																																																																																																																																																																																																																	
% of Budget Projected	0%	~2%	~4%																																																																																																																																																																																																																																	
Source	Amount (\$K)																																																																																																																																																																																																																																			
Construction	\$399 K																																																																																																																																																																																																																																			
Architect/Engineer	\$122 K																																																																																																																																																																																																																																			
Moving / Relocation	\$40.0 K																																																																																																																																																																																																																																			
Construction Technology	\$50.0 K																																																																																																																																																																																																																																			
Others	\$54.2 K																																																																																																																																																																																																																																			
Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	ETC Completion	Estimate At Completion	Uncommitted																																																																																																																																																																																																																							
CIT Managed																																																																																																																																																																																																																																				
Architect/Engineer: 7100-7101	\$54,176		\$54,176	\$50,150			\$42,628			\$4,026	\$54,176																																																																																																																																																																																																																									
Construction Testing: 7100-7103	\$10,099		\$10,099	\$10,201						\$10,099	\$10,099																																																																																																																																																																																																																									
Other Consultants: 7100-7105	\$10,201									\$10,201	\$10,201																																																																																																																																																																																																																									
Management Fees: 7200-7201	\$20,819	(\$20,819)																																																																																																																																																																																																																																		
Construction: 7300-7301	\$898,642		\$898,642																																																																																																																																																																																																																																	
Construction Technology: 7300-7301.22	\$40,000		\$40,000																																																																																																																																																																																																																																	
Miscellaneous: 7300-7302	\$46,991	(\$20,000)	\$26,991																																																																																																																																																																																																																																	
Security: 7400-7401	\$10,000		\$10,000																																																																																																																																																																																																																																	
Utilities: 7500-7501	\$25,000		\$25,000																																																																																																																																																																																																																																	
Moving / Relocation: 7500-7502	\$50,000		\$50,000																																																																																																																																																																																																																																	
Contingency: 9999-9999	\$59,259	(\$20,000)	\$39,259																																																																																																																																																																																																																																	
										\$39,259	\$39,259																																																																																																																																																																																																																									

Program\DeKalb County\421 SPLOST III\Elementary Schools\Knollwood ES - HVAC & ADA

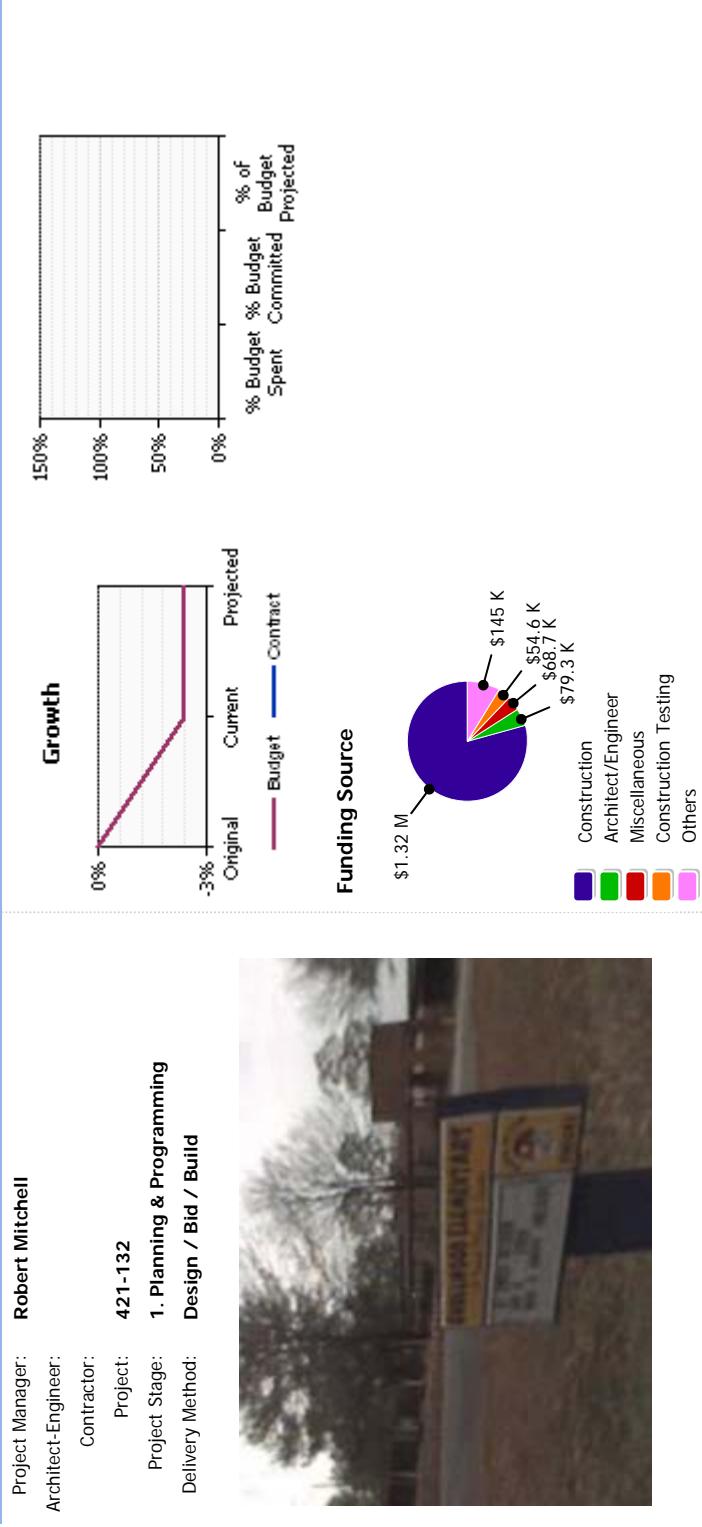




Scope of Work:

- ADA improvements for this school include interior and exterior accessibility upgrades. In addition, heat pumps will be replaced.

Remarks:



- March 2011: Design Review is underway.

Program\DeKalb County\421 SPLOST III\High Schools\Lakeside HS - Career Tech, ADA
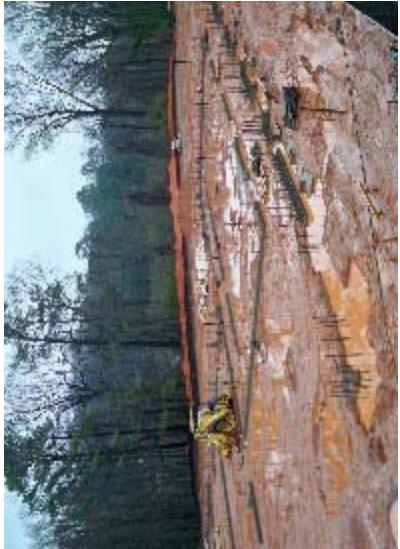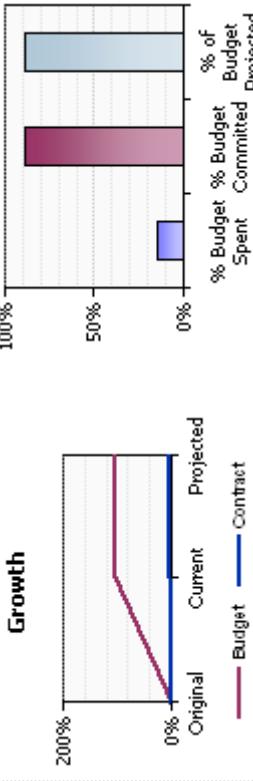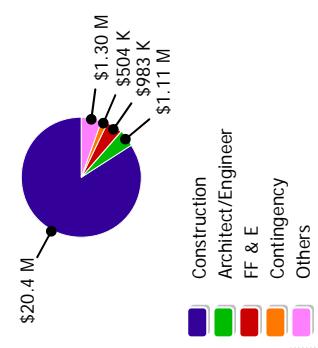
<p>Project Manager: Hal Anderson</p> <p>Architect-Engineer: Mangley, Spangler, & Smith Architects</p> <p>Contractor: Hogan Construction</p> <p>Project: 421-125</p> <p>Project Stage: 4. Construction</p> <p>Delivery Method: Guaranteed Maximum Price</p> 	<p>Growth</p>  <p>Funding Source</p>  <table border="1"> <thead> <tr> <th>Funding Source Category</th><th>Amount (\$)</th></tr> </thead> <tbody> <tr> <td>Construction</td><td>\$1.11 M</td></tr> <tr> <td>Architect/Engineer</td><td>\$1.30 M</td></tr> <tr> <td>FF & E</td><td>\$504 K</td></tr> <tr> <td>Contingency</td><td>\$983 K</td></tr> <tr> <td>Others</td><td>\$1.11 M</td></tr> <tr> <td>Total</td><td>\$20.4 M</td></tr> </tbody> </table>	Funding Source Category	Amount (\$)	Construction	\$1.11 M	Architect/Engineer	\$1.30 M	FF & E	\$504 K	Contingency	\$983 K	Others	\$1.11 M	Total	\$20.4 M																																																																																																																				
Funding Source Category	Amount (\$)																																																																																																																																		
Construction	\$1.11 M																																																																																																																																		
Architect/Engineer	\$1.30 M																																																																																																																																		
FF & E	\$504 K																																																																																																																																		
Contingency	\$983 K																																																																																																																																		
Others	\$1.11 M																																																																																																																																		
Total	\$20.4 M																																																																																																																																		
<p>Scope of Work:</p> <ul style="list-style-type: none"> The scope of work includes the design of a two-story Career-Tech building with various new classrooms, new auditorium with new fine arts classrooms, kitchen addition, ADA upgrades and various site improvements. In the existing building, new Boys and Girls athletic locker rooms, coaches offices, ROTC classrooms, and various new classrooms. The existing facility is approximately 164,600 sf and the planned addition is approximately 80,000 sf. 																																																																																																																																			
<p>Remarks:</p> <ul style="list-style-type: none"> Hogan Construction Group is installing footings for the Fine Arts and Auditorium addition. They are installing CMU walls in the lower level classrooms and the new main electrical room. The sanitary sewer and roof drainage are being installed in the slab. The underground detention pond in the practice field has been started. The rainy weather has impacted the site work. Budget reallocations pending. 																																																																																																																																			
<p>Cost Status by Budget Category:</p> <table border="1"> <thead> <tr> <th>Budget Category</th> <th>Original Budget</th> <th>Budget Revision</th> <th>Current Budget</th> <th>Original Contract</th> <th>Executed Changes</th> <th>Current Contract</th> <th>Paid To Date</th> <th>Contract Balance</th> <th>CORs</th> <th>ETC Forecast</th> <th>ETC Completion</th> <th>Uncommitted</th> </tr> </thead> <tbody> <tr> <td>CIT Managed</td> <td></td> </tr> <tr> <td>Architect/Engineer: 7100-7101</td> <td>\$544,026</td> <td>\$561,520</td> <td>\$1,105,546</td> <td>\$487,800</td> <td>\$661,866</td> <td>\$1,149,666</td> <td>\$675,110</td> <td>\$465,628</td> <td></td> <td></td> <td></td> <td>\$1,149,666</td> </tr> <tr> <td>Surveying: 7100-7102</td> <td>\$25,000</td> <td>\$2,338</td> <td>\$27,338</td> <td>\$27,338</td> <td></td> <td></td> <td>\$27,338</td> <td>\$27,338</td> <td></td> <td></td> <td></td> <td>\$27,338</td> </tr> <tr> <td>Construction Testing: 7100-7103</td> <td>\$78,500</td> <td>(\$28,500)</td> <td>\$50,000</td> <td>\$42,000</td> <td></td> <td></td> <td>\$42,000</td> <td>\$23,858</td> <td>\$2</td> <td></td> <td></td> <td>\$50,000</td> </tr> <tr> <td>Abatement: 7100-7104</td> <td></td> <td>\$40,000</td> <td>\$40,000</td> <td>\$18,358</td> <td></td> <td></td> <td>\$18,358</td> <td>\$5,973</td> <td>\$12,361</td> <td></td> <td></td> <td>\$21,642</td> </tr> <tr> <td>Other Consultants: 7100-7105</td> <td>\$50,000</td> <td>(\$20,000)</td> <td>\$30,000</td> <td>\$7,792</td> <td></td> <td></td> <td>\$7,792</td> <td>\$7,792</td> <td></td> <td></td> <td></td> <td>\$30,000</td> </tr> <tr> <td>Management Fees: 7200-7201</td> <td>\$475,100</td> <td>(\$475,100)</td> <td>\$1,359,065</td> <td>\$20,401,171</td> <td>\$19,953,751</td> <td>\$98,224</td> <td>\$20,051,975</td> <td>\$1,941,663</td> <td>\$17,552,893</td> <td>\$11,841</td> <td>\$337,355</td> <td>\$20,401,171</td> </tr> <tr> <td>Construction: 7300-7301</td> <td>\$9,042,106</td> <td>\$11,359,065</td> <td>\$265,000</td> <td>\$265,000</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>\$265,000</td> </tr> <tr> <td>Construction Technology: 7300-7301.22</td> <td></td> </tr> </tbody> </table>		Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	ETC Completion	Uncommitted	CIT Managed													Architect/Engineer: 7100-7101	\$544,026	\$561,520	\$1,105,546	\$487,800	\$661,866	\$1,149,666	\$675,110	\$465,628				\$1,149,666	Surveying: 7100-7102	\$25,000	\$2,338	\$27,338	\$27,338			\$27,338	\$27,338				\$27,338	Construction Testing: 7100-7103	\$78,500	(\$28,500)	\$50,000	\$42,000			\$42,000	\$23,858	\$2			\$50,000	Abatement: 7100-7104		\$40,000	\$40,000	\$18,358			\$18,358	\$5,973	\$12,361			\$21,642	Other Consultants: 7100-7105	\$50,000	(\$20,000)	\$30,000	\$7,792			\$7,792	\$7,792				\$30,000	Management Fees: 7200-7201	\$475,100	(\$475,100)	\$1,359,065	\$20,401,171	\$19,953,751	\$98,224	\$20,051,975	\$1,941,663	\$17,552,893	\$11,841	\$337,355	\$20,401,171	Construction: 7300-7301	\$9,042,106	\$11,359,065	\$265,000	\$265,000								\$265,000	Construction Technology: 7300-7301.22												
Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	ETC Completion	Uncommitted																																																																																																																							
CIT Managed																																																																																																																																			
Architect/Engineer: 7100-7101	\$544,026	\$561,520	\$1,105,546	\$487,800	\$661,866	\$1,149,666	\$675,110	\$465,628				\$1,149,666																																																																																																																							
Surveying: 7100-7102	\$25,000	\$2,338	\$27,338	\$27,338			\$27,338	\$27,338				\$27,338																																																																																																																							
Construction Testing: 7100-7103	\$78,500	(\$28,500)	\$50,000	\$42,000			\$42,000	\$23,858	\$2			\$50,000																																																																																																																							
Abatement: 7100-7104		\$40,000	\$40,000	\$18,358			\$18,358	\$5,973	\$12,361			\$21,642																																																																																																																							
Other Consultants: 7100-7105	\$50,000	(\$20,000)	\$30,000	\$7,792			\$7,792	\$7,792				\$30,000																																																																																																																							
Management Fees: 7200-7201	\$475,100	(\$475,100)	\$1,359,065	\$20,401,171	\$19,953,751	\$98,224	\$20,051,975	\$1,941,663	\$17,552,893	\$11,841	\$337,355	\$20,401,171																																																																																																																							
Construction: 7300-7301	\$9,042,106	\$11,359,065	\$265,000	\$265,000								\$265,000																																																																																																																							
Construction Technology: 7300-7301.22																																																																																																																																			

Program\DeKalb County\421 SPLOST III High Schools\Martin Luther King, Jr. HS - Addition

Project Manager:	Amy Sue Mann
Architect-Engineer:	RL Brown and Associates
Contractor:	
Project:	421-127
Project Stage:	8 On Hold
Delivery Method:	Design / Bid / Build

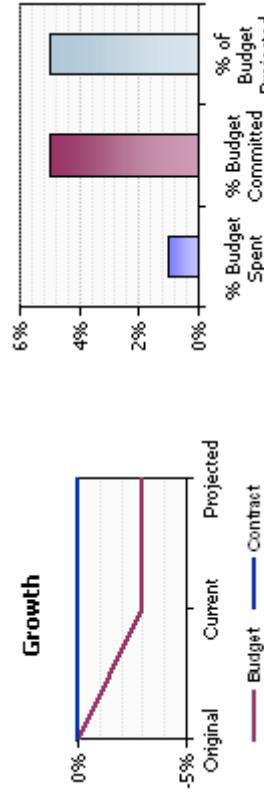

Scope of Work:

- The scope includes addition of 31 classrooms as well as sitework, furniture, fixture and equipment improvements.


Remarks:

- The current design is approximately \$5,000,000 over the Stated Cost Limitation for the project. This project has been placed on hold while DCSS reconciles the programmatic requirements with the currently established budget. In addition, the results of the District-wide Redistricting and Consolidation Plan and the 2020 Vision may result in a change of the programmatic needs for this facility. Once these evaluations are completed, this project will resume.

Cost Status by Budget Category:



Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
Construction Technology: 7300-7301.22			\$94,000	\$94,000						\$94,000	\$94,000	
Miscellaneous: 7300-7302	\$156,098		\$156,098							\$156,098	\$156,098	
Security: 7400-7401	\$75,000		\$75,000							\$75,000	\$75,000	
Utilities: 7500-7501	\$125,000		\$125,000							\$125,000	\$125,000	
Moving / Relocation: 7500-7502	\$100,000		\$100,000							\$100,000	\$100,000	
Contingency: 99999-9999	\$348,750	(\$162,850)	\$185,900							\$185,900	\$185,900	
CIT Managed Subtotal	\$9,301,129	(\$289,500)	\$9,011,629	\$448,005		\$448,005	\$95,478	\$321,703		\$8,563,624	\$9,011,629	
DCSS Managed												
FF & E: 7700-7504	\$277,650		\$277,650	\$17,634		\$17,634				\$260,016	\$277,650	(\$0)
Technology: 7800-7801	\$600,000		\$600,000							\$600,000	\$600,000	
DCSS Managed Subtotal	\$877,650		\$877,650	\$17,634		\$17,634				\$860,016	\$877,650	(\$0)
Project Total	\$10,118,779	(\$289,500)	\$9,889,279	\$465,639		\$465,639	\$113,112	\$321,703		\$9,423,640	\$9,889,279	(\$0)

Program\DeKalb County\421 SPLOST III\Elementary Schools\McLendon ES - HVAC & ADA

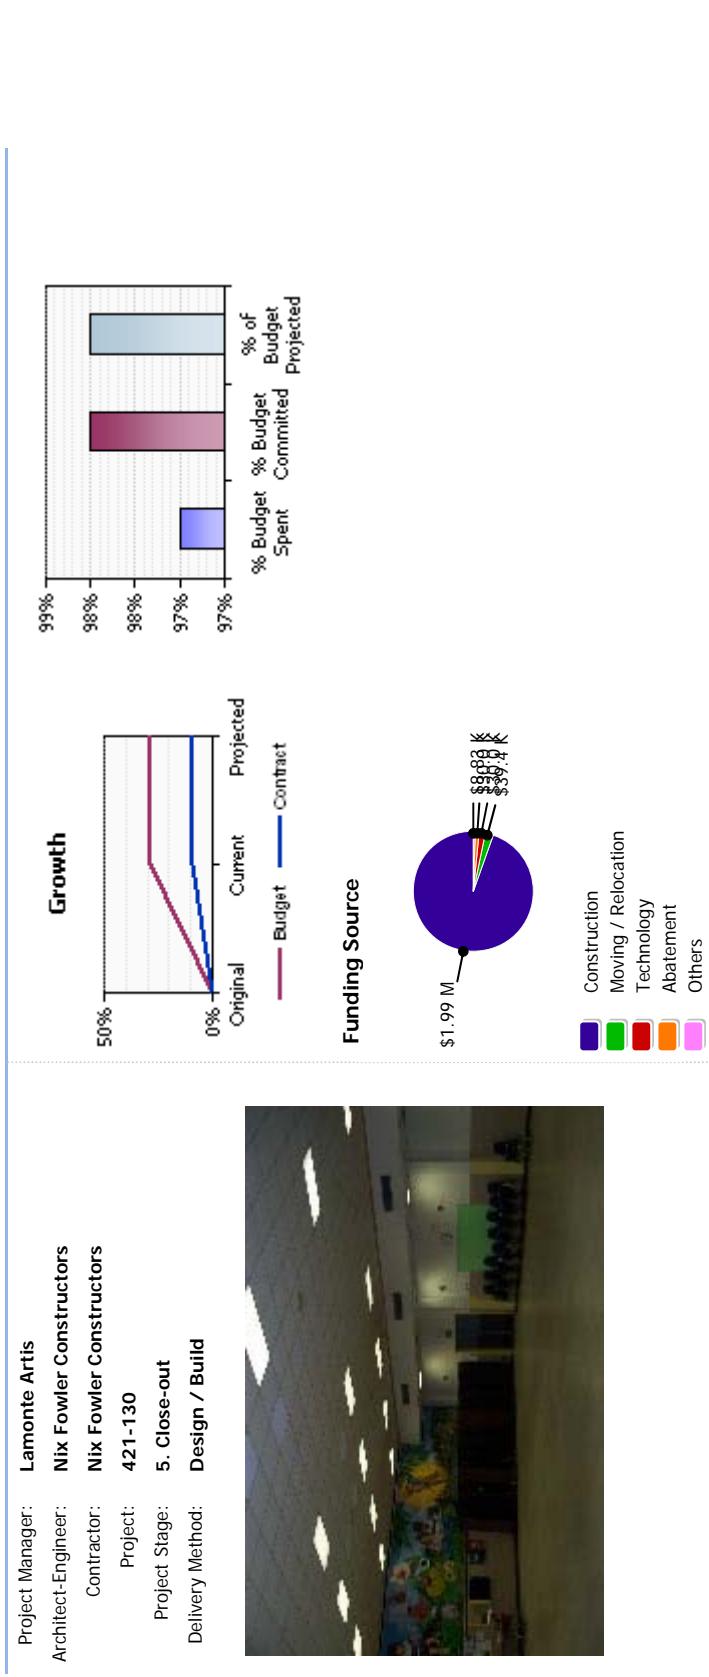


Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
CIT Managed Subtotal	\$1,627,626	\$437,764	\$2,065,390	\$1,862,306	\$164,673	\$2,026,979	\$1,889,282	(\$1,066)	\$964	\$35,500	\$2,063,443	\$1,947
DCSS Managed												
FF&E: 7700-7504	\$3,000	\$3,000	\$2,623			\$2,623	\$2,623	\$0			\$2,623	\$377
Technology: 7800-7801	\$30,000	\$30,000	\$22,391			\$22,391	\$18,255	\$4,136		\$7,600	\$29,991	\$9
DCSS Managed Subtotal	\$33,000	\$33,000	\$25,014			\$25,014	\$20,877	\$4,137		\$7,600	\$32,614	\$386
Project Total	\$1,627,626	\$470,764	\$2,098,390	\$1,887,320	\$164,673	\$2,051,993	\$1,910,159	\$3,070	\$964	\$43,100	\$2,096,057	\$2,333

Program\DeKalb County\421 SPLOST III\High Schools\McNair HS - SPLOST II Deferred
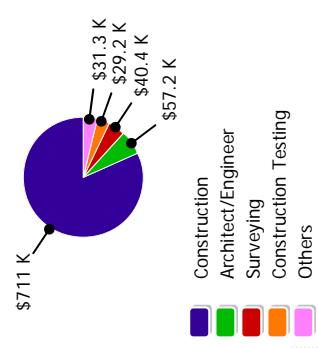
<p>Project Manager: Melissa Ryckley Architect-Engineer: CDH Partners Contractor: Merit Construction Company</p> <p>Project: 421-105 Project Stage: 6. Completed Delivery Method: Design / Bid / Build</p> 	<p>Growth</p>  <p>Funding Source</p>  <table border="1"> <thead> <tr> <th>Funding Source Category</th> <th>Amount (\$K)</th> </tr> </thead> <tbody> <tr> <td>Budget</td> <td>\$711 K</td> </tr> <tr> <td>Contract</td> <td>\$31.3 K</td> </tr> <tr> <td>Others</td> <td>\$29.2 K</td> </tr> <tr> <td>Architect/Engineer</td> <td>\$40.4 K</td> </tr> <tr> <td>Construction Testing</td> <td>\$57.2 K</td> </tr> <tr> <td>Surveying</td> <td>-\$5 K</td> </tr> </tbody> </table>	Funding Source Category	Amount (\$K)	Budget	\$711 K	Contract	\$31.3 K	Others	\$29.2 K	Architect/Engineer	\$40.4 K	Construction Testing	\$57.2 K	Surveying	-\$5 K	<p>Scope of Work:</p> <ul style="list-style-type: none"> The scope of work for this project includes a new handicapped ramp at the performing arts building and improvements at the sports fields, including goalposts and new dugouts at the baseball field and regarding re-sod the football field. The tennis courts will receive a new surface and new netting. New storage buildings for football and baseball will be constructed. Repaving, curb repair and new sidewalks, stairs, and ADA ramps will be installed. <p>Remarks:</p> <ul style="list-style-type: none"> This project was completed in May 2010. 	<p>Cost Status by Budget Category:</p> <table border="1"> <thead> <tr> <th>Budget Category</th> <th>Original Budget</th> <th>Budget Revision</th> <th>Current Budget</th> <th>Original Contract</th> <th>Executed Changes</th> <th>Current Contract</th> <th>Paid To Date</th> <th>Contract Balance</th> <th>CORs</th> <th>ETC Forecast</th> <th>Estimate At Completion</th> <th>Uncommitted</th> </tr> </thead> <tbody> <tr> <td>CIT Managed</td> <td></td> </tr> <tr> <td>Architect/Engineer: 7100-7101</td> <td>\$60,000</td> <td>(\$2,810)</td> <td>\$57,190</td> <td>\$57,190</td> <td></td> <td></td> <td>\$57,190</td> <td>\$56,966</td> <td></td> <td></td> <td>\$57,190</td> <td>(\$0)</td> </tr> <tr> <td>Surveying: 7100-7102</td> <td>\$7,488</td> <td>\$32,912</td> <td>\$40,400</td> <td>\$40,400</td> <td></td> <td></td> <td>\$40,400</td> <td>\$40,400</td> <td></td> <td></td> <td>\$40,400</td> <td></td> </tr> <tr> <td>Construction Testing: 7100-7103</td> <td>\$15,000</td> <td>\$14,239</td> <td>\$29,239</td> <td>\$29,239</td> <td></td> <td></td> <td>\$29,239</td> <td>\$29,239</td> <td></td> <td></td> <td>\$29,239</td> <td>(\$0)</td> </tr> <tr> <td>Other Consultants: 7100-7105</td> <td>\$7,488</td> <td>(\$1,432)</td> <td>\$6,056</td> <td>\$6,056</td> <td></td> <td></td> <td>\$6,056</td> <td>\$6,056</td> <td></td> <td></td> <td>\$6,056</td> <td></td> </tr> <tr> <td>Management Fees: 7200-7201</td> <td>\$14,977</td> <td>(\$4,977)</td> <td></td> </tr> <tr> <td>Construction: 7300-7301</td> <td>\$711,389</td> <td></td> <td>\$711,389</td> <td>\$711,389</td> <td></td> <td></td> <td>\$711,389</td> <td>\$711,389</td> <td></td> <td></td> <td>\$711,389</td> <td></td> </tr> <tr> <td>Miscellaneous: 7300-7302</td> <td>\$27,371</td> <td>(\$27,099)</td> <td>\$272</td> <td>\$272</td> <td></td> <td></td> <td>\$272</td> <td>\$272</td> <td></td> <td></td> <td>\$272</td> <td>(\$0)</td> </tr> <tr> <td>Contingency: 99999-99999</td> <td>\$37,442</td> <td>(\$37,442)</td> <td></td> </tr> <tr> <td>CIT Managed Subtotal</td> <td>\$881,155</td> <td>(\$36,609)</td> <td>\$844,546</td> <td>\$844,547</td> <td></td> <td></td> <td>\$844,547</td> <td>\$844,323</td> <td></td> <td></td> <td>\$844,547</td> <td>(\$1)</td> </tr> <tr> <td>DCSS Managed</td> <td></td> </tr> <tr> <td>FF&E: 7700-7504</td> <td>\$24,929</td> <td></td> <td>\$24,929</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> </tr> <tr> <td>DCSS Managed Subtotal</td> <td>\$24,929</td> <td></td> <td>\$24,929</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> </tr> <tr> <td>Project Total</td> <td>\$906,084</td> <td>(\$36,609)</td> <td>\$869,475</td> <td>\$844,547</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>\$844,547</td> <td>\$24,928</td> </tr> </tbody> </table>	Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted	CIT Managed													Architect/Engineer: 7100-7101	\$60,000	(\$2,810)	\$57,190	\$57,190			\$57,190	\$56,966			\$57,190	(\$0)	Surveying: 7100-7102	\$7,488	\$32,912	\$40,400	\$40,400			\$40,400	\$40,400			\$40,400		Construction Testing: 7100-7103	\$15,000	\$14,239	\$29,239	\$29,239			\$29,239	\$29,239			\$29,239	(\$0)	Other Consultants: 7100-7105	\$7,488	(\$1,432)	\$6,056	\$6,056			\$6,056	\$6,056			\$6,056		Management Fees: 7200-7201	\$14,977	(\$4,977)											Construction: 7300-7301	\$711,389		\$711,389	\$711,389			\$711,389	\$711,389			\$711,389		Miscellaneous: 7300-7302	\$27,371	(\$27,099)	\$272	\$272			\$272	\$272			\$272	(\$0)	Contingency: 99999-99999	\$37,442	(\$37,442)											CIT Managed Subtotal	\$881,155	(\$36,609)	\$844,546	\$844,547			\$844,547	\$844,323			\$844,547	(\$1)	DCSS Managed													FF&E: 7700-7504	\$24,929		\$24,929										DCSS Managed Subtotal	\$24,929		\$24,929										Project Total	\$906,084	(\$36,609)	\$869,475	\$844,547							\$844,547	\$24,928
Funding Source Category	Amount (\$K)																																																																																																																																																																																																																			
Budget	\$711 K																																																																																																																																																																																																																			
Contract	\$31.3 K																																																																																																																																																																																																																			
Others	\$29.2 K																																																																																																																																																																																																																			
Architect/Engineer	\$40.4 K																																																																																																																																																																																																																			
Construction Testing	\$57.2 K																																																																																																																																																																																																																			
Surveying	-\$5 K																																																																																																																																																																																																																			
Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted																																																																																																																																																																																																								
CIT Managed																																																																																																																																																																																																																				
Architect/Engineer: 7100-7101	\$60,000	(\$2,810)	\$57,190	\$57,190			\$57,190	\$56,966			\$57,190	(\$0)																																																																																																																																																																																																								
Surveying: 7100-7102	\$7,488	\$32,912	\$40,400	\$40,400			\$40,400	\$40,400			\$40,400																																																																																																																																																																																																									
Construction Testing: 7100-7103	\$15,000	\$14,239	\$29,239	\$29,239			\$29,239	\$29,239			\$29,239	(\$0)																																																																																																																																																																																																								
Other Consultants: 7100-7105	\$7,488	(\$1,432)	\$6,056	\$6,056			\$6,056	\$6,056			\$6,056																																																																																																																																																																																																									
Management Fees: 7200-7201	\$14,977	(\$4,977)																																																																																																																																																																																																																		
Construction: 7300-7301	\$711,389		\$711,389	\$711,389			\$711,389	\$711,389			\$711,389																																																																																																																																																																																																									
Miscellaneous: 7300-7302	\$27,371	(\$27,099)	\$272	\$272			\$272	\$272			\$272	(\$0)																																																																																																																																																																																																								
Contingency: 99999-99999	\$37,442	(\$37,442)																																																																																																																																																																																																																		
CIT Managed Subtotal	\$881,155	(\$36,609)	\$844,546	\$844,547			\$844,547	\$844,323			\$844,547	(\$1)																																																																																																																																																																																																								
DCSS Managed																																																																																																																																																																																																																				
FF&E: 7700-7504	\$24,929		\$24,929																																																																																																																																																																																																																	
DCSS Managed Subtotal	\$24,929		\$24,929																																																																																																																																																																																																																	
Project Total	\$906,084	(\$36,609)	\$869,475	\$844,547							\$844,547	\$24,928																																																																																																																																																																																																								


Program\DeKalb County\421 SPLOST III\Elementary Schools\Midvale ES - HVAC, Roof, ADA

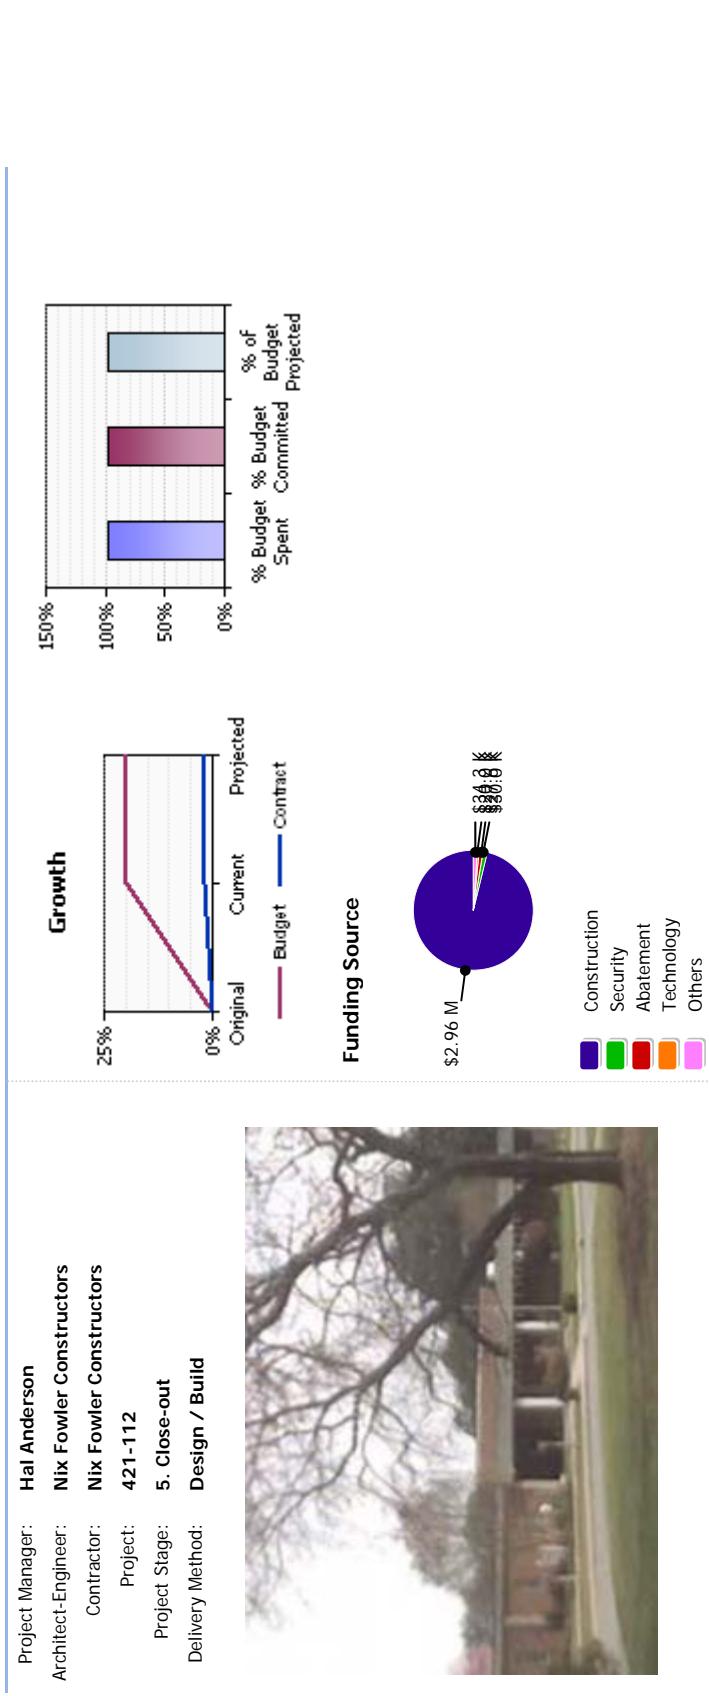


- Scope of Work:**
- The scope consists of HVAC, ceiling and lighting replacement as well as roof replacement for the 60,855 sf building.
- Remarks:**
- The project is in closeout. The contractor is taking care of some HVAC and electrical design issues that were listed in the program narrative and bid documents. These issues are being taken care of ASAP.

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
Moving / Relocation: 7500-7502	\$50,000	(\$36,700)	\$13,300	\$16,557		\$16,557	\$16,557	\$0		\$16,557		(\$3,257)
Contingency: 9999-9999	\$131,070	(\$131,070)										
CIT Managed Subtotal	\$2,564,393	\$485,812	\$3,050,205	\$2,918,564	\$71,919	\$2,990,482	\$2,810,159	\$71,592	\$58,983	\$3,049,465		\$740
DCSS Managed												
Technology: 7800-7801	\$20,000	\$20,000	\$16,637		\$16,637	\$8,267	\$8,371			\$16,637		\$3,363
DCSS Managed Subtotal	\$20,000	\$20,000	\$16,637		\$16,637	\$8,267	\$8,371			\$16,637		\$3,363
Project Total	\$2,564,393	\$505,812	\$3,070,205	\$2,935,201	\$71,919	\$3,007,120	\$2,818,426	\$79,962	\$58,983	\$3,066,103	\$4,102	

Program\DeKalb County\421 SPLOST III\Elementary Schools\Midway ES - Roof

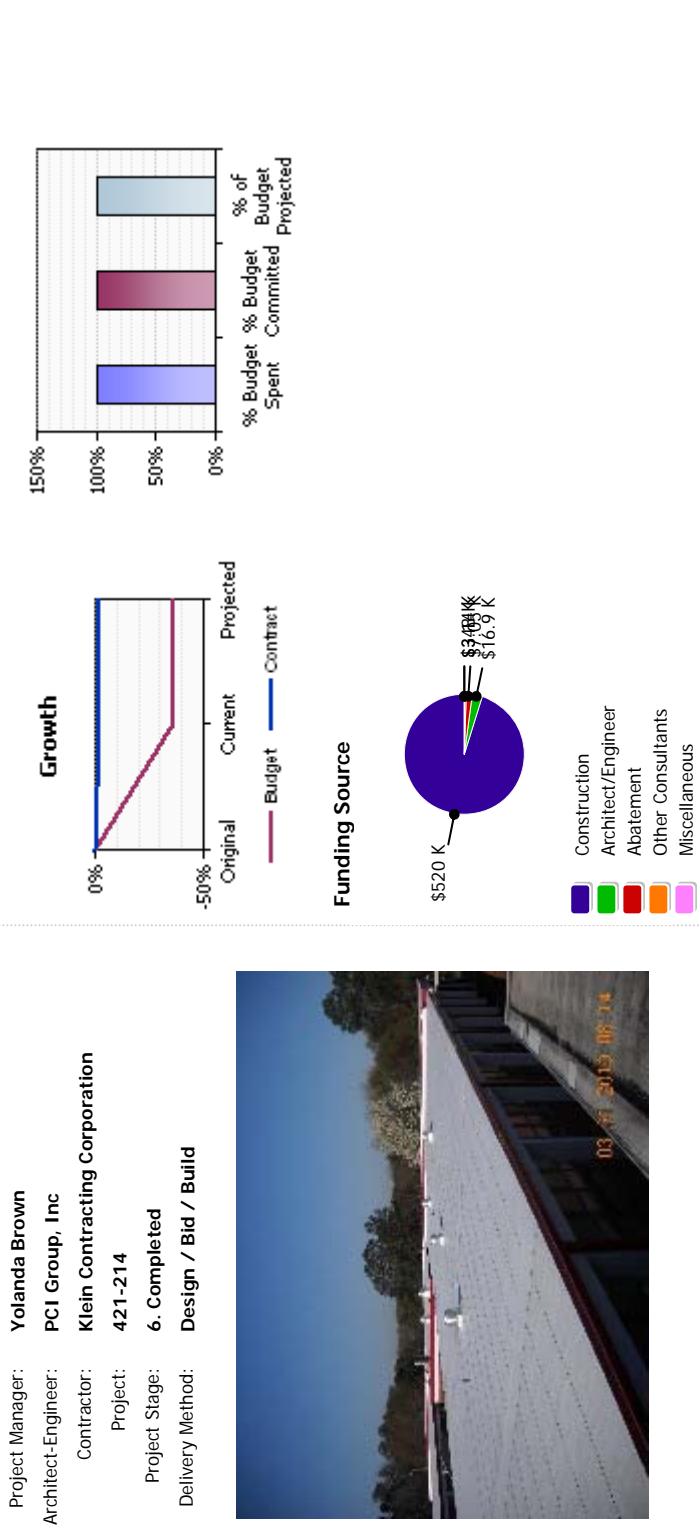


Program\DeKalb County\421 SPLOST III\High Schools\Miller Grove HS - Addition

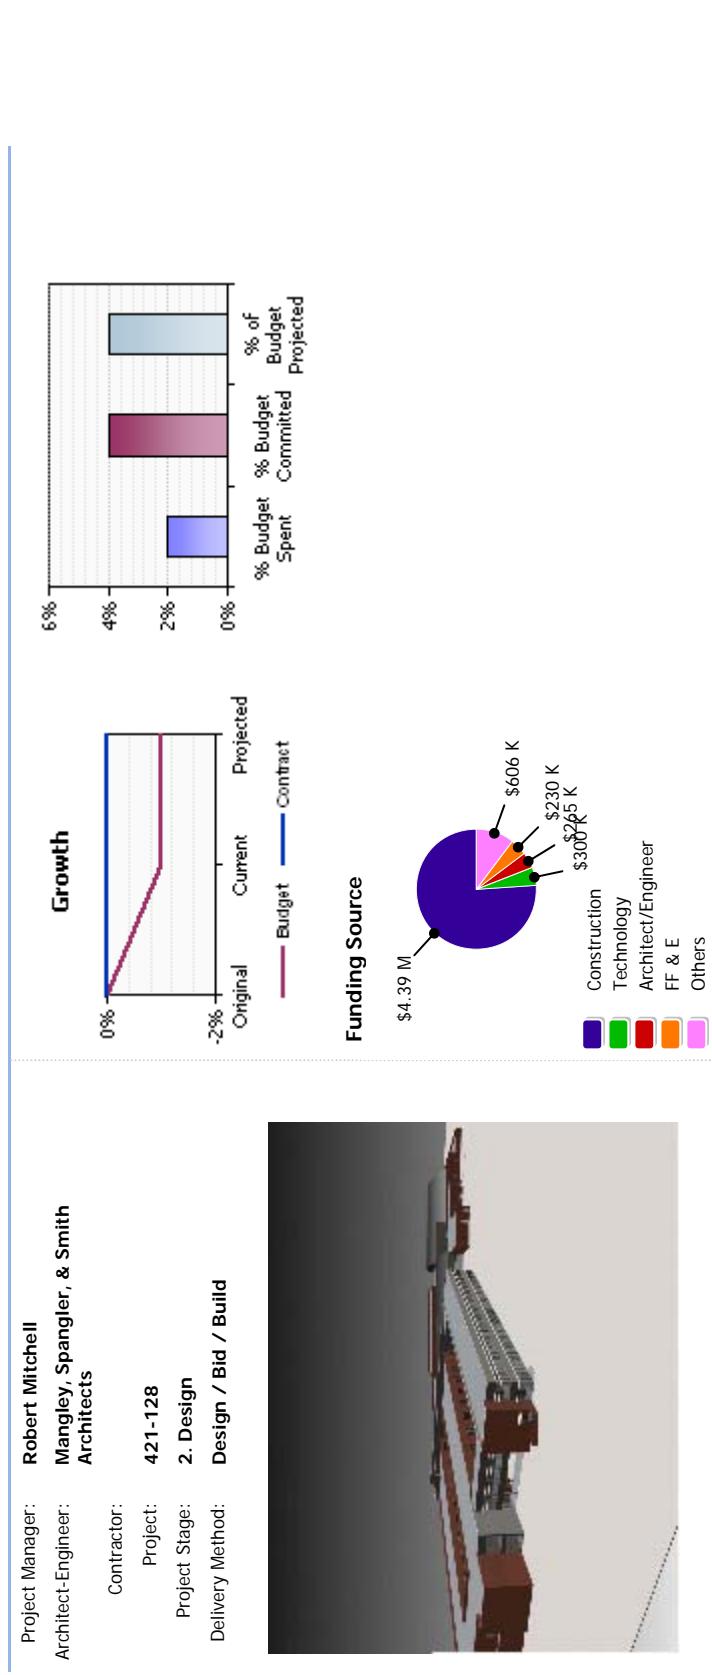

- Remarks:**
- 4/29/11 Met with the Architect and the school user group concerning the design and budget review; the Architect is to revise the floor plan for science labs, math classrooms etc. The next meeting should be scheduled mid May 2011.

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORS	ETC Forecast	Estimate At Completion	Uncommitted
Moving / Relocation: 7500-7502	\$75,000	\$75,000								\$75,000	\$75,000	
Contingency: 9999-9999	\$204,000	(\$71,600)	\$132,400							\$132,400	\$132,400	
CIT Managed Subtotal	\$5,344,087	(\$81,600)	\$5,262,487	\$242,163		\$242,163	\$50,055	\$189,066		\$5,020,324	\$5,262,487	
DCSS Managed												
FF&E: 7700-7504	\$230,400		\$230,400							\$230,400	\$230,400	
Technology: 7800-7801	\$300,000		\$300,000							\$300,000	\$300,000	
DCSS Managed Subtotal	\$530,400		\$530,400							\$530,400	\$530,400	
Project Total	\$5,874,487	(\$81,600)	\$5,792,887	\$242,163		\$242,163	\$50,055	\$189,066		\$5,550,724	\$5,792,887	


Program\DeKalb County\421 SPLOST III\Elementary Schools\Montgomery ES - HVAC

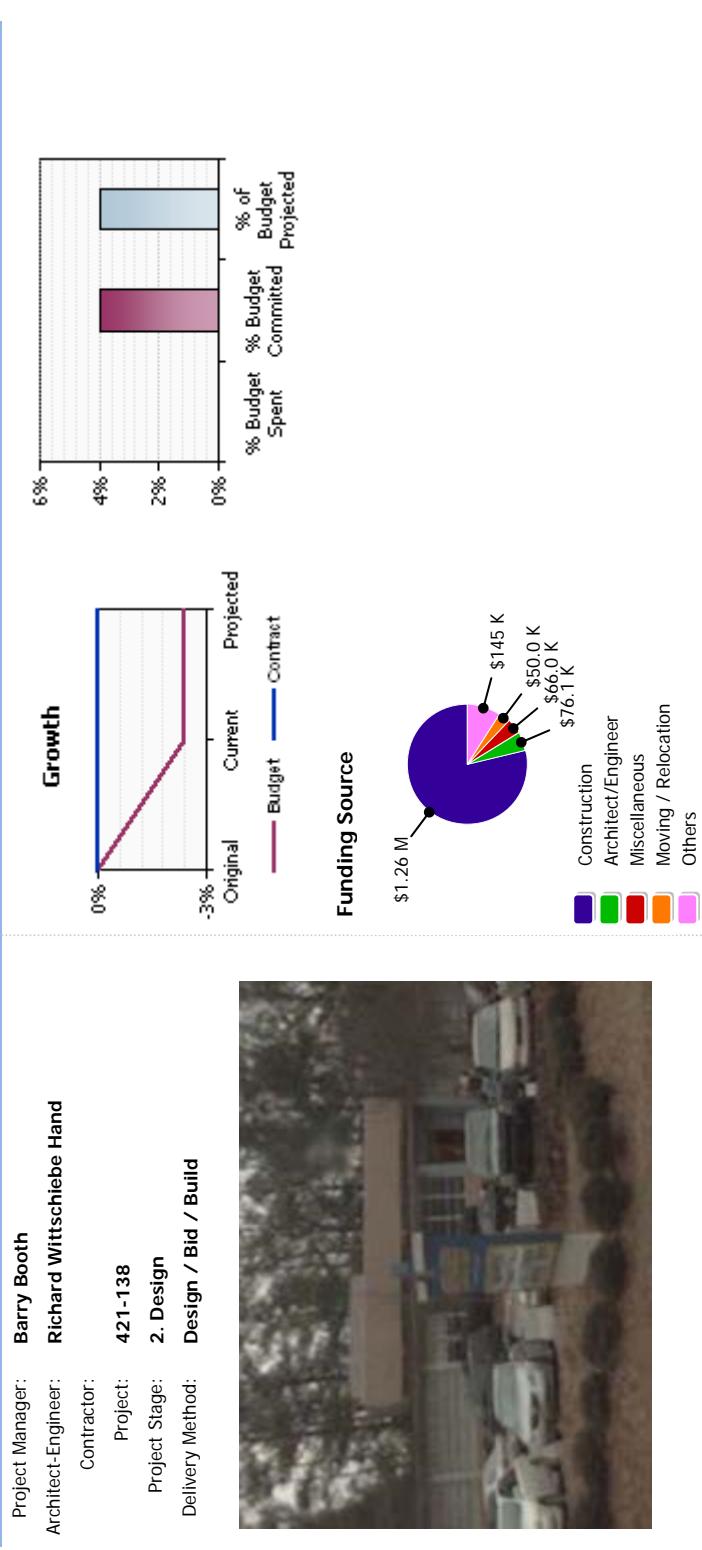

- The design kick off meeting was held on March 23, 2011. A walk through with the architect will take place at the school on March 29, 2011 to gather information for Finding of Fact and the Preliminary Report.

Program\DeKalb County\421 SPL0ST III Elementary Schools\Murphrey Candler ES - Roof

Program\DeKalb County\421 SPLOST III\Elementary Schools\Nancy Creek (Kittridge) ES - Roof

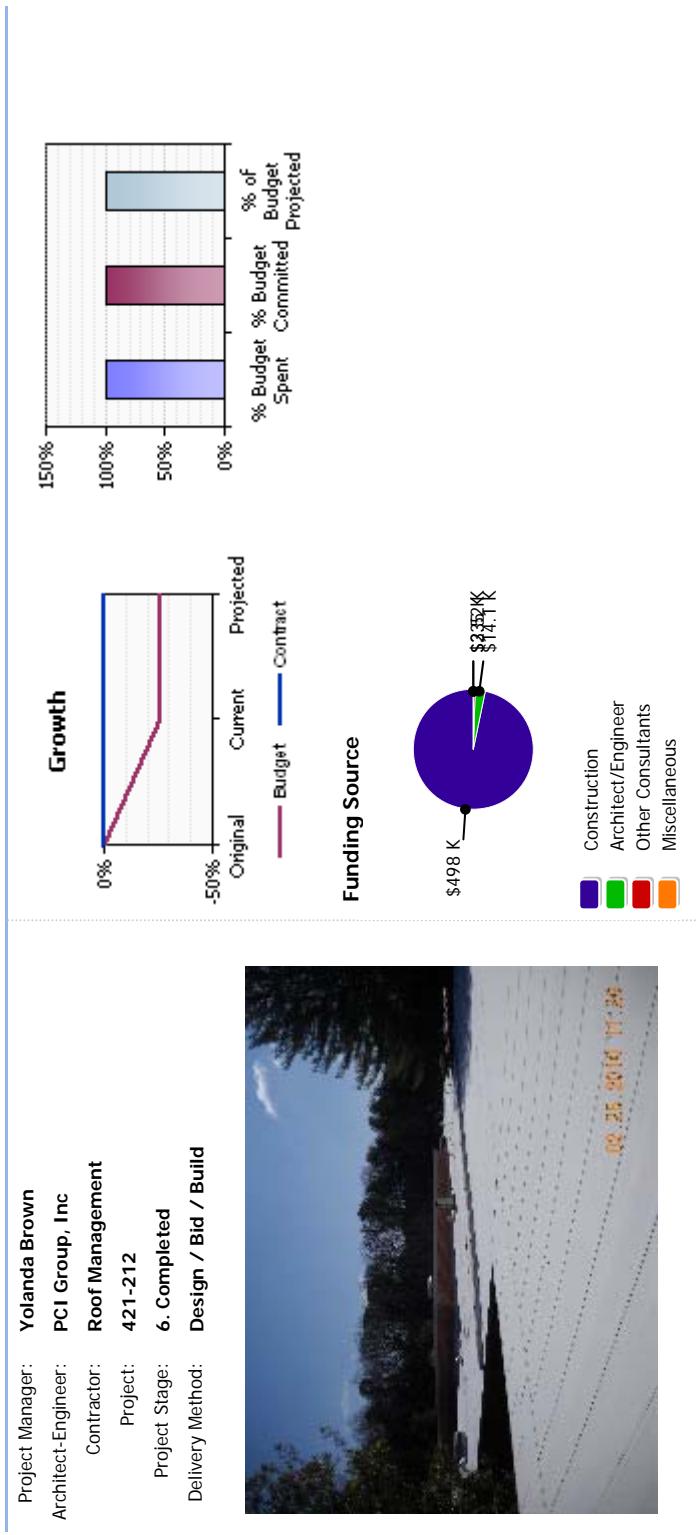

Cost Status by Budget Category:

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	ETC Completion	Estimate At Uncommitted
CIIT Managed												
Architect/Engineer: 7100-7101	\$39,116	(\$24,991)	\$14,125	\$13,800		\$13,800	\$13,525	\$275		\$325	\$14,125	
Other Consultants: 7100-7105	\$2,321	\$2,321	\$2,321	\$2,321		\$2,321	\$2,521	\$2,521			\$2,521	
Management Fees: 7200-7201	\$13,305	(\$13,305)										
Construction: 7300-7301	\$612,813	(\$114,354)	\$498,459	\$498,459	(\$1,875)	\$496,584	\$496,583	\$1		\$1,875	\$498,459	
Miscellaneous: 7300-7302	\$335	\$335					\$335	\$335				\$335
Contingency: 9999-9999	\$35,012	(\$35,012)										
CIIT Managed Subtotal	\$700,246	(\$184,806)	\$515,440	\$515,115	(\$1,875)	\$513,240	\$512,964	\$276		\$2,200	\$515,440	
Project Total	\$700,246	(\$184,806)	\$515,440	\$515,115	(\$1,875)	\$513,240	\$512,964	\$276		\$2,200	\$515,440	

Program\DeKalb County\Redan HS - Roof, HVAC, Career Tech, ADA
High Schools\SPLCOST III

Project Manager: Danny Gilmore
Architect-Engineer: Warren Epstein & Associates
Contractor: Meja Construction, Inc
Project: 421-111
Project Stage: 5. Close-out
Delivery Method: Design / Bid / Build

Growth

Original Budget: \$8.95 M

Current Budget: \$1.14 M

Projected Budget: \$384 K

Spent: \$32 K

Budget Committed: \$540 K

Funding Source

Construction: \$8.95 M

Architect/Engineer: \$1.14 M

FF & E: \$32 K

Contingency: \$540 K

Others: \$384 K

Financials


Category	Value
% of Budget Spent	74%
% Budget Committed	72%
% Budget Projected	78%

Timeline

Original — Current — Projected

Photo

A photograph of a modern, angular building with a grey and white facade. A blue car is parked in front. An American flag is flying from a pole on the left side of the building. The date "10.14.2010 09:43" is overlaid on the right side of the photo.



Cost Status by Budget Category:								
Budget Category		Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date
IT Managed	Architect/Engineer: 7100-7101	\$540,126	\$540,126	\$676,000	\$12,650	\$688,650	\$509,918	\$169,787
	Surveying: 7100-7102	\$20,000	\$10,000	\$30,000	\$20,650	\$20,650	\$20,650	\$9,350
	Construction Testing: 7100-7103	\$78,574		\$78,574	\$49,257	\$44,883	\$4,374	\$29,000
	Abatement: 7100-7104	\$175,000		\$175,000	\$139,938	\$139,938	\$131,638	\$35,000
	Other Consultants: 7100-7105	\$48,706		\$48,706	\$17,052	\$17,052	\$13,263	\$0
	Management Fees: 7200-7201	\$320,603	(\$320,603)					\$31,000
	Construction Technology: 7300-7301	\$8,950,280		\$8,950,280	\$6,729,773	\$239,260	\$6,969,033	\$6,180,835
	Construction Technology: 7300-7301.22	\$14,000		\$14,000	\$1,600	\$1,600	\$1,600	\$1,600
	Miscellaneous: 7300-7302	\$176,057		\$176,057	\$169,892	\$169,892	\$16,239	\$130,530
	Security: 7400-7401	\$55,000		\$55,000				\$55,000

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	ETC At Completion	Uncommitted
Utilities: 7500-7501	\$135,000		\$135,000	\$175,000	\$115,262	\$114,360	\$682		\$135,000	\$135,000		
Moving / Relocation: 7500-7502	\$175,000		\$175,000	\$100,000	\$4,680	\$4,258	\$422		\$59,000	\$174,262	\$738	
Trailers: 7600-7503	\$250,000	(\$150,000)	\$100,000	\$199,000	\$233,616				\$95,300	\$99,980	\$20	
Contingency: 9999-9999	\$482,616	(\$199,000)	\$10,761,359	\$7,924,104	\$251,910	\$8,176,014	\$7,036,043	\$1,073,822	\$133,000	\$133,000	\$150,616	
CIT Managed Subtotal	\$11,231,962	(\$470,603)							\$2,583,650	\$10,685,878	\$75,481	
DCSS Managed												
FF & E: 7700-7504	\$282,120	\$150,000	\$432,120	\$266,375	\$266,375	\$0			\$165,745	\$432,120	\$0	
Technology: 7800-7801	\$150,000		\$150,000	\$152,467	\$152,467	\$105,036	\$47,431			\$152,467	(\$2,467)	
DCSS Managed Subtotal	\$432,120	\$150,000	\$582,120	\$418,842	\$418,842	\$371,411	\$47,432		\$165,745	\$584,587	(\$2,467)	
Project Total	\$11,664,082	(\$320,603)	\$11,343,479	\$8,342,946	\$251,910	\$8,594,857	\$7,407,454	\$1,121,254	(\$73,786)	\$2,749,395	\$11,270,465	\$73,014

Program\DeKalb County\421 SPLOST III\Elementary Schools\Rockbridge ES - HVAC & ADA

Project Manager: Brad Jacobs
Architect-Engineer: Epsten Group
Contractor: 421-133
Project Stage: 2. Design
Delivery Method: Design / Bid / Build

Growth

Funding Source

Building Image

The dashboard displays the following data:

- Timeline Progress:** A bar chart showing % Budget Spent vs % Budget Committed. The bars are dark red, light blue, and light red.
- Growth:** A line graph showing growth from -3% to 0% over time.
- Budget Comparison:** A pie chart comparing Original, Current, and Projected budgets. The segments are colored purple, pink, green, orange, yellow, and blue.
- Funding Sources:** A pie chart showing the distribution of funds by source: Construction Testing (\$1.34 M), Architect/Engineer (\$50.0 K), Miscellaneous (\$68.9 K), Moving / Relocation (\$79.7 K), and Others.
- Building Image:** A photograph of a modern building under construction with a blue roof and white walls.


Scope of Work:

- HVAC, Ceiling and Lighting replacement and other improvements including new generator, parking lot lighting, grease trap, and cooler / freezer boxes.

Remarks:


Cost Status by Budget Category:

Program\DeKalb County\421 SPLOST III\Elementary Schools\Sagamore Hills ES - Roof

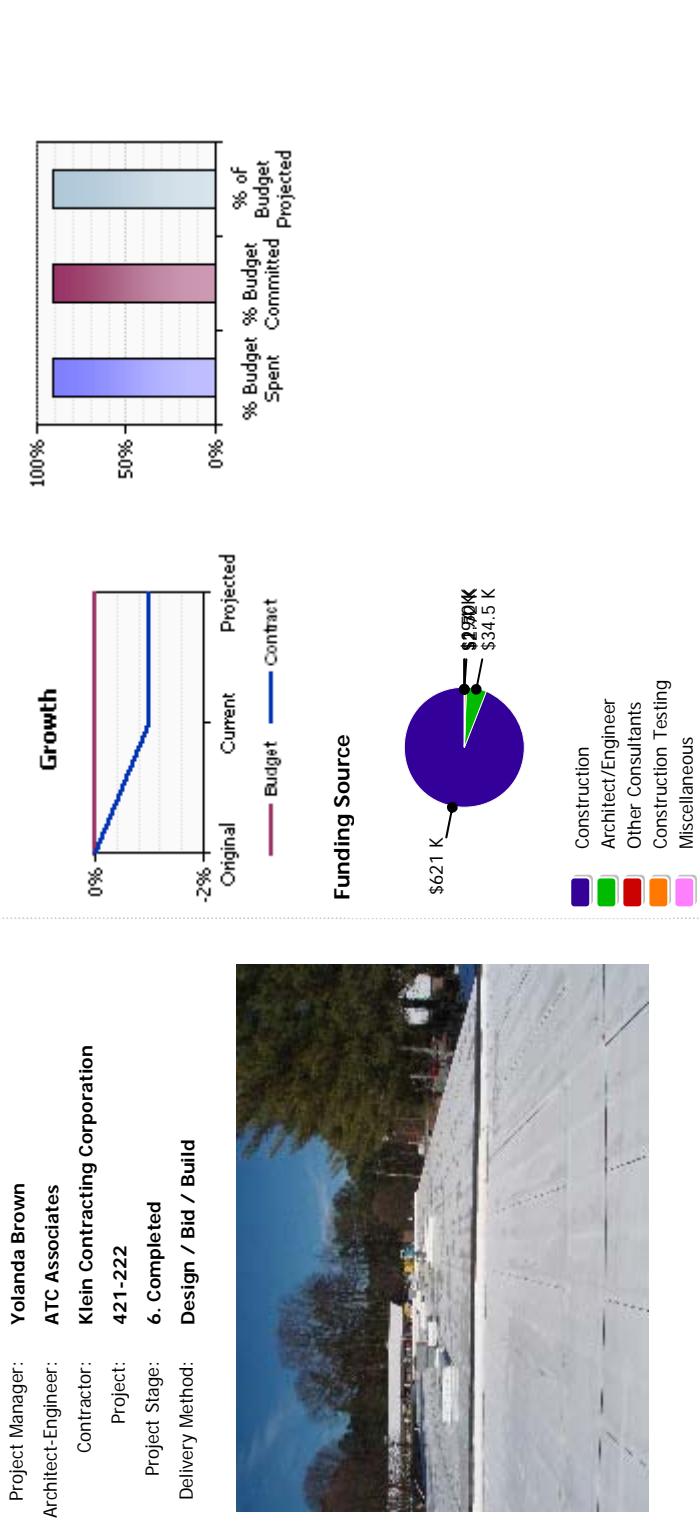

Cost Status by Budget Category:		Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORS	ETC Forecast	Estimate At Completion	Uncommitted
CIT Managed														
Architect/Engineer: 7100-7101	\$34,838	(\$294)	\$34,544	\$19,500				\$19,500	\$19,500				\$19,500	\$15,044
Construction Testing: 7100-7103	\$1,500		\$1,500											\$1,500
Other Consultants: 7100-7105	\$2,723		\$2,723	\$3,375				\$3,375	\$3,375				\$3,375	(\$652)
Construction: 7300-7301	\$620,577		\$620,577	\$586,920	(\$7,731)			\$579,189	\$579,189				\$579,189	\$41,388
Miscellaneous: 7300-7302	\$294		\$294	\$294				\$294	\$294				\$294	
CIT Managed Subtotal	\$659,638		\$659,638	\$610,089	(\$7,731)			\$602,358	\$602,358				\$602,358	\$57,280
Project Total	\$659,638		\$659,638	\$610,089	(\$7,731)								\$602,358	\$57,280


Program\DeKalb County\421 SPLOST III\Other Facilities\Sam Moss Service Center - HVAC and Roof

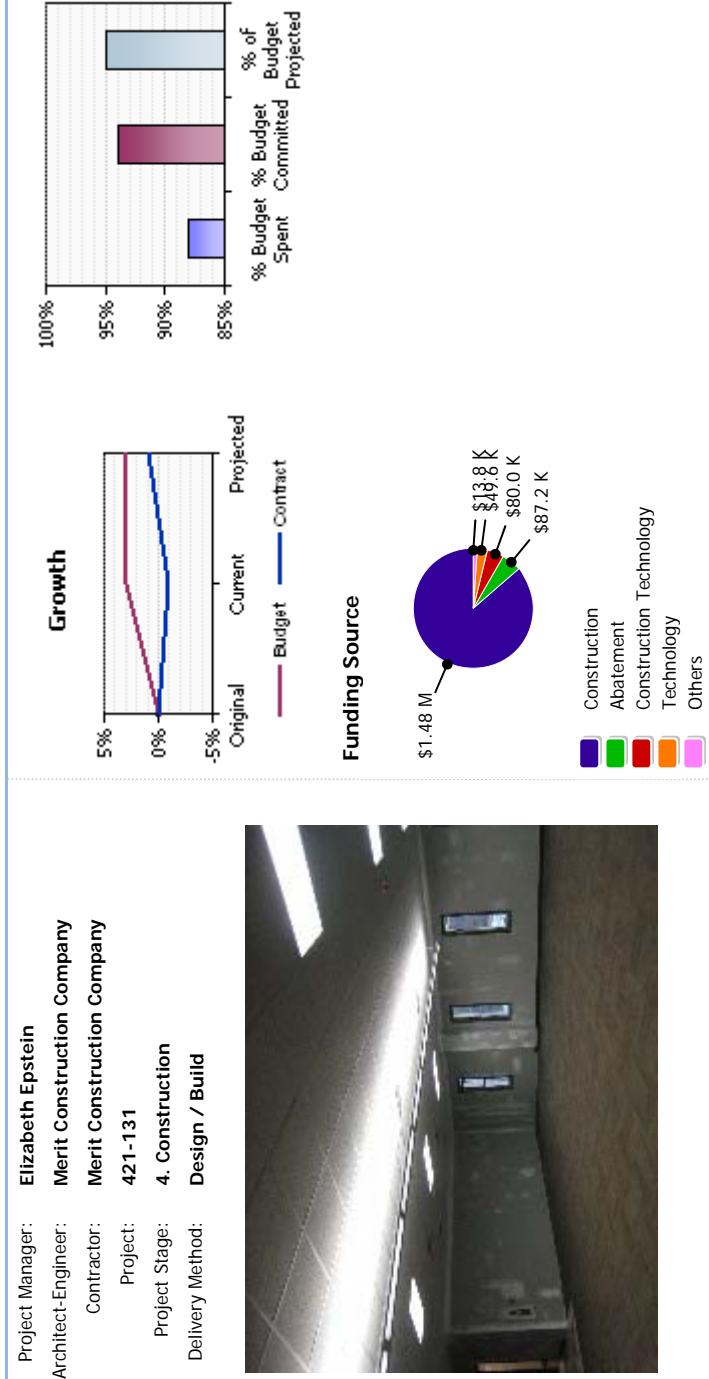

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORS Forecast	ETC Forecast	Estimate At Completion	Uncommitted
CIT Managed												
Architect/Engineer: 7100-7101	\$87,696	(\$80,196)	\$7,500	\$8,000		\$8,000	\$8,000				\$8,000	(\$500)
Construction Testing: 7100-7103	\$15,232	(\$15,232)										
Abatement: 7100-7104	\$8,000	\$79,200	\$87,200	\$72,180		\$72,180	\$0		\$1,787	\$73,967	\$13,233	
Other Consultants: 7100-7105	\$16,324	(\$16,000)	\$324	\$120		\$120			\$204	\$324		
Management Fees: 7200-7201	\$27,930	(\$27,930)										
Construction: 7300-7301	\$1,416,462	\$59,396	\$1,475,858	\$1,459,370	(\$9,186)	\$1,450,183	\$1,321,690	\$117,214	\$21,336	\$1,471,519	\$4,339	
Construction Technology: 7300-7301-22	\$80,000	\$80,000	\$18,192	\$18,749	(\$557)	\$18,192			\$10,000	\$281,192	\$51,808	
Trailers: 7600-7503	\$6,000	\$6,000	\$2,925			\$2,925			\$3,075		\$6,000	


Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORS	ETC Forecast	Estimate At Completion	Uncommitted
Contingency: 9999.9999	\$82,718	(\$82,718)										
CIT Managed Subtotal	\$1,654,362	\$2,550	\$1,656,882	\$1,560,787	(\$9,186)	\$1,551,600	\$1,423,663	\$116,657	\$21,336	\$15,066	\$1,588,002	\$68,880
DCSS Managed												
Technology: 7800-7801	\$49,550	\$49,550	\$48,793			\$48,793	\$48,793				\$48,793	\$757
DCSS Managed Subtotal	\$49,550	\$49,550	\$48,793			\$48,793	\$48,793				\$48,793	\$757
Project Total	\$1,654,362	\$52,070	\$1,706,432	\$1,609,580	(\$9,186)	\$1,600,393	\$1,472,456	\$116,657	\$21,336	\$15,066	\$1,636,795	\$69,637

Program\DeKalb County\421 SPLOST III\Site Improvements\Site Improvements 1 (321)\Security Lighting

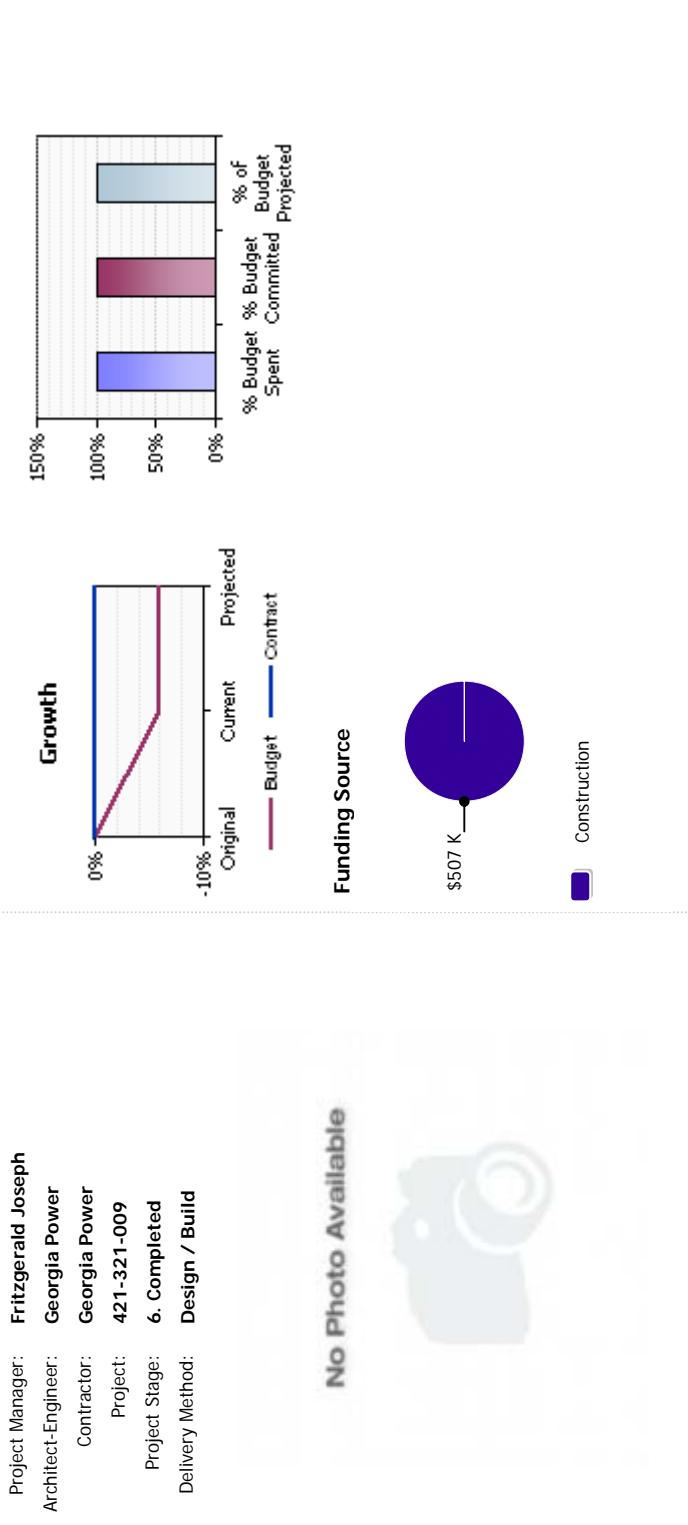

Cost Status by Budget Category:													
Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	ETC Completion	Estimate At Completion	Uncommitted
CIT Managed													
Construction:	\$537,360	(\$30,820)	\$506,540	\$506,540		\$506,540	\$506,540					\$506,540	
CIT Managed Subtotal	\$537,360	(\$30,820)	\$506,540	\$506,540		\$506,540	\$506,540					\$506,540	
Project Total	\$537,360	(\$30,820)	\$506,540	\$506,540		\$506,540	\$506,540					\$506,540	

Program\DeKalb County\421 SPLOST III\Local School Requests\LSPR 2 (341)\Security Upgrade Systems

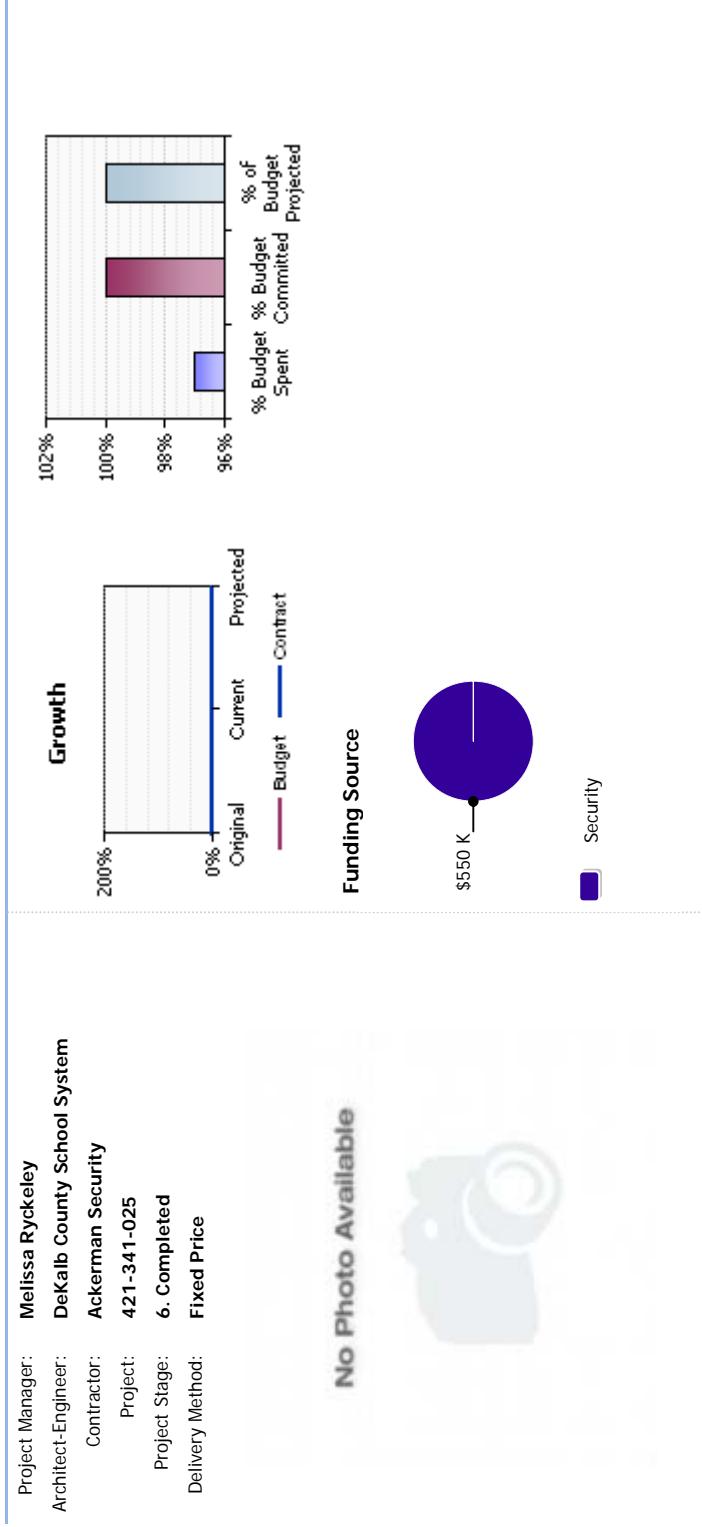

Scope of Work:

- Access control points for various schools and installation of AIPHONE systems at 61 elementary schools and centers.


Remarks:

- WA#1 is 100% complete-
Allgood ES, Flat Rock ES, Oak Grove ES, Princeton ES, Student Relations, East Campus, Livsey ES, Peachtree MS, Lithonia HS, Woodridge ES, Austin ES, Woodward ES, WA#2 is 100% complete-
Bob Mathis ES, Briar Vista ES, Briar Lake ES, Brookett ES, Carey Reynolds ES Montclair ES, Columbia ES, Dresden ES, Coralwood CTR, Dunaire ES, Eagle Woods CTR, E L Bouie ES
WA#3 is 100% complete-
E.L. Miller ES, Evansdale ES, Fernbank Science CTR, Flatshoals ES, Hambrick ES, Henderson MS, Henderson Mill ES, Huntley Hills ES, Idlewood ES, Indian Creek ES, International CTR, Jolly ES,
Kingsley ES, Kittridge Magnet ES, WA#4 is 100% complete-
Gresham ES, Clifton ES, Kelley Lake ES, Stone Mtn ES, Knollwood ES, Laurel Ridge ES, Marbut Theme ES, Meadowview ES, Medlock ES, Stone View ES, Midvale ES, Midway ES, Montgomery ES, Narvie J Harris ES,
WA#5 is 100% complete-
OakView ES, Panola Way ES, Snapfinger ES, Peachcrest ES, Pine Ridge ES, Rainbow ES, Robert Shaw Theme ES, Rockbridge ES, Rowland ES, Sagamore Hills ES, Shadow Rock CTR, Stephenson HS, Shamrock MS, Smokerise ES,
WA#6 is 100% complete-
Terry Mill/DESA ES, Toney ES, Vanderlyn ES, Wadsworth ES, Warren Tech CTR, WBBC Wynbrooke ES, Eagle Woods CTR, DSA HS, Montclair ES, Flat Rock ES, Princeton ES,
Ashford Park ES, Hawthorne ES, International CTR, WA#7 100% complete-
Freeman A & B, Columbia HS, McClendon ES, Salem ES, Chesnut Charter ES, Redan ES Arabia Mtn, Drivers ED N, McNair ES, Sam Moss CTR, Clarkston HS, Redan HS Chapel Hill ES, Chapel Hill MS, Oakcliff ES,
Atherton, Browns Mill, Drivers ED S, McNair HS, Sky Haven ES, Heritage CTR, Rock Chapel ES, Cedar Grove MS, Druid Hills HS, Miller Grove HS, Stone Mill ES, Hightower ES, Tucker HS, Forrest Hills ES, Glen Haven ES, WBBC,

Cost Status by Budget Category:


Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	ETC At Completion	Estimate At Uncommitted
CIT Managed												
Security: 7400-7401	\$550,000		\$550,000	\$550,000		\$550,000	\$535,775	\$14,225			\$550,000	
CIT Managed Subtotal	\$550,000		\$550,000	\$550,000		\$550,000	\$535,775	\$14,225			\$550,000	
Project Total	\$550,000		\$550,000	\$550,000		\$550,000	\$535,775	\$14,225			\$550,000	

Program\DeKalb County\421 SPLOST III\Middle Schools\Sequoyah MS - Roof

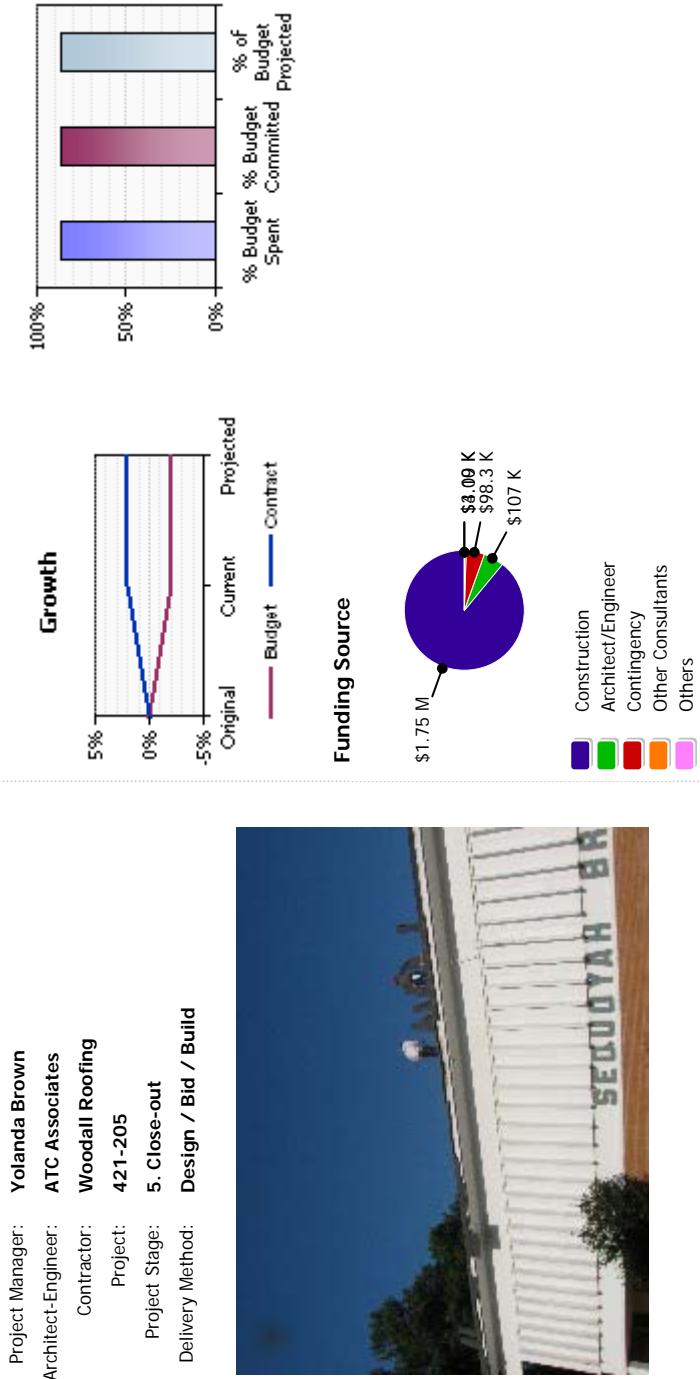

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORS	ETC Forecast	Estimate At Completion	Uncommitted
CIT Managed												
Architect/Engineer: 7100-7101	\$111,539	(\$4,186)	\$107,353	\$21,962		\$21,962	(\$0)		\$85,000	\$106,962		\$391
Construction Testing: 7100-7103		\$1,500	\$1,117		\$1,117	\$1,117	\$0		\$333	\$1,500		
Other Consultants: 7100-7105	\$4,186	\$4,186	\$3,725		\$3,725	\$3,725			\$461			\$4,186
Management Fees: 7200-7201	\$37,938	(\$37,938)	\$1,747,435	\$1,745,935	\$1,638,000	\$34,485	\$1,672,485	\$1,477,311		\$70,000	\$1,742,485	
Construction: 7300-7301	\$1,747,435	(\$1,500)	\$1,500	\$1,500	\$348		\$348			\$1,152	\$1,500	\$3,450
Miscellaneous: 7300-7302		\$1,500		\$98,338	(\$1,500)					\$98,000	\$254,996	\$338
Contingency: 9999-9999	\$99,838									\$1,954,633		
CIT Managed Subtotal	\$1,996,750	(\$37,938)	\$1,958,812	\$1,665,152	\$34,485	\$1,699,637	\$1,504,463	\$0	\$254,996	\$1,954,633		\$4,179
Project Total	\$1,996,750	(\$37,938)	\$1,958,812	\$1,665,152	\$34,485	\$1,699,637	\$1,504,463	\$0	\$254,996	\$1,954,633		\$4,179

Program\DeKalb County\421 SPLOST III\Elementary Schools\Sky Haven ES - Roof

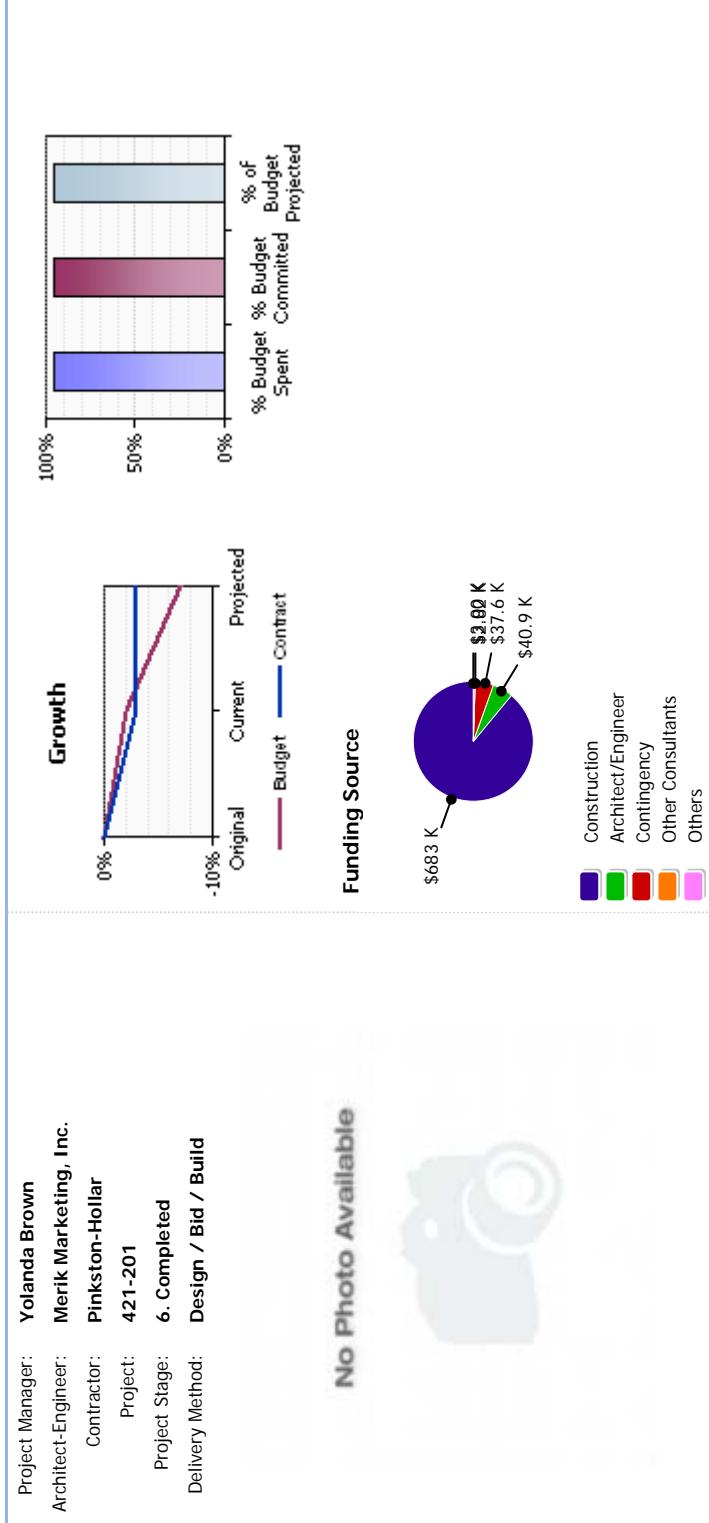


Cost Status by Budget Category:		Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORS	ETC Forecast	Estimate At Completion	Uncommitted
CIT Managed	CIT Unmanaged													
Architect/Engineer: 7100-7101	\$43,720	(\$2,819)	\$40,901	\$28,100		\$28,100		\$28,100		\$28,100		\$28,100	\$12,801	
Construction Testing: 7100-7103	\$1,500	\$1,500	\$923			\$923		\$923		\$923		\$923	\$577	
Other Consultants: 7100-7105	\$2,819	\$2,819	\$2,819			\$2,819		\$2,819		\$2,819		\$2,819		
Management Fees: 7200-7201	\$14,867	(\$14,867)	\$14,867											
Construction: 7300-7301	\$684,757	(\$1,500)	\$683,257	\$719,157	(\$22,701)	\$696,456	\$692,156	\$2				\$696,456	(\$13,199)	
Miscellaneous: 7300-7302	\$1,500	\$1,500	\$100			\$100	\$100					\$100	\$1,400	
Contingency: 9999-9999	\$39,124	(\$1,500)	\$37,624									\$14,000	\$14,000	\$23,624
CIT Managed Subtotal	\$782,468	(\$14,867)	\$767,601	\$751,098	(\$22,701)	\$728,397	\$724,097	\$2				\$742,397	\$25,204	
Project Total	\$782,468	(\$14,867)	\$767,601	\$751,098	(\$22,701)	\$728,397	\$724,097	\$2				\$742,397	\$25,204	

Program\DeKalb County\421 SPLOST III\Elementary Schools\Snapfinger ES - Roof




Cost Status by Budget Category:												
Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
CIT Managed												
Architect/Engineer: 7100-7101	\$24,634	(\$2,500)	\$22,134	\$13,800			\$13,800	\$9,958	\$3,842		\$8,334	\$22,134
Construction Testing: 7100-7103	\$5,500	\$5,500	\$2,500	\$2,222							\$1,500	\$1,500
Other Consultants: 7100-7105	\$2,500	\$2,500									\$278	\$2,500
Management Fees: 7200-7201	\$8,379	(\$8,379)	\$298,500	\$684,437	\$630,000	\$425,046	\$204,954	\$696			\$54,437	\$684,437
Construction: 7300-7301	\$385,937										\$804	\$1,500
Miscellaneous: 7300-7302	\$5,500	\$5,500	\$5,96								\$20,550	\$20,550
Contingency: 9999-9999	\$22,050	(\$1,500)	\$20,550								\$85,903	\$732,621
CIT Managed Subtotal	\$441,000	\$291,621	\$732,621	\$646,718	\$437,922	\$208,796					\$85,903	\$732,621
Project Total	\$441,000	\$291,621	\$732,621	\$646,718	\$437,922	\$208,796						


Program\DeKalb County\421 SPLIT III\Elementary Schools\Stone Mill ES - HVAC

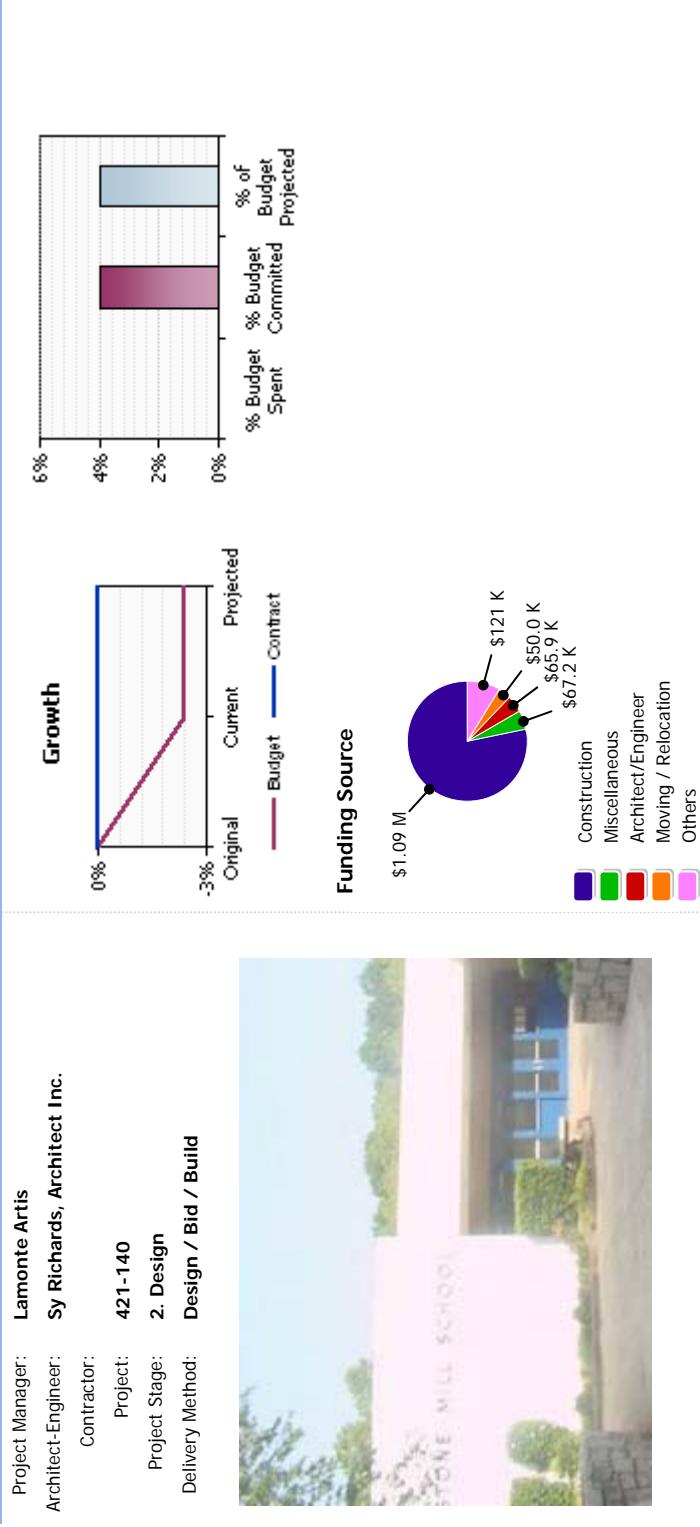

Program\DeKalb County\421 SPLIST III\Elementary Schools\Stone Mountain ES - HVAC & ADA

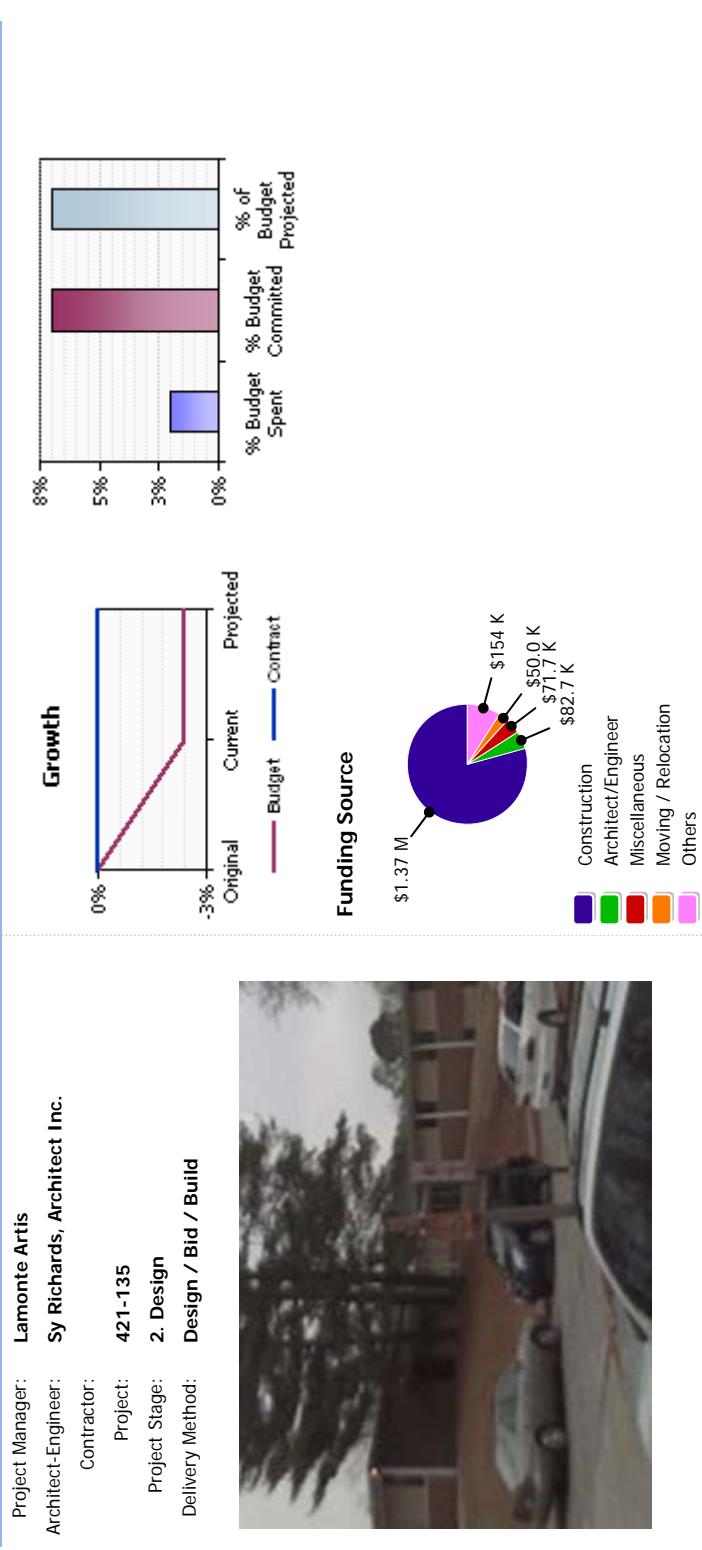


Program\DeKalb County\421 SPLOST III\High Schools\Stone Mountain HS - HVAC, Roof

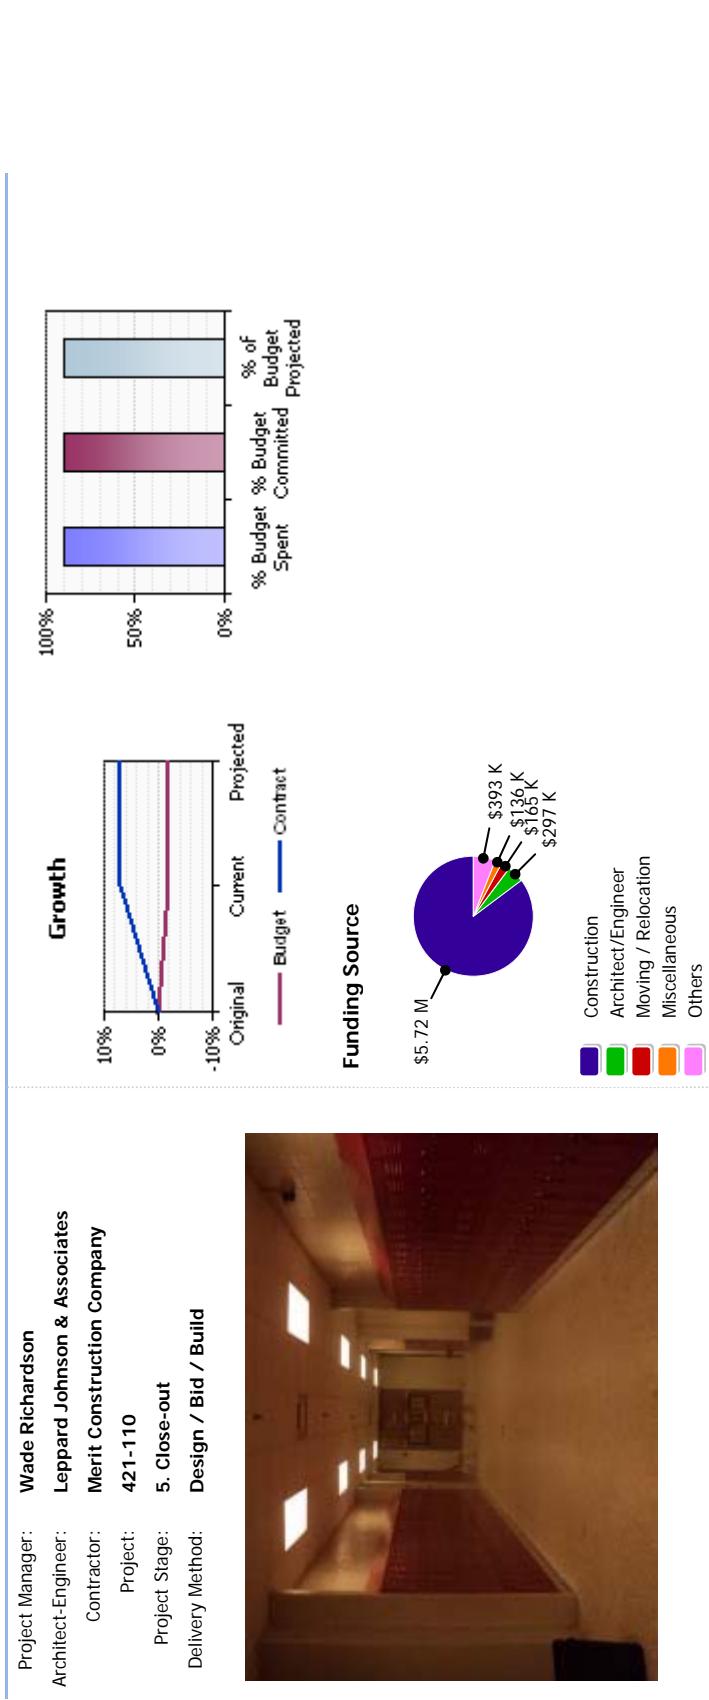

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
Utilities: 7500-7501	\$75,000	(\$45,000)	\$30,000	\$1,620		\$1,620		\$1	\$28,380	\$30,000		
Moving / Relocation: 7500-7502	\$125,000	\$40,000	\$165,000	\$80,576		\$80,576	\$72,203	(\$3,604)	\$84,424	\$165,000	\$0	
Trailers: 7600-7503	\$250,000	(\$238,500)	\$11,500	\$11,500		\$11,500	\$10,514	\$841		\$11,500		
Contingency: 9999-9999	\$335,711	(\$320,711)	\$15,000						\$15,000	\$15,000		
CIT Managed Subtotal	\$6,714,225	(\$227,971)	\$6,486,254	\$5,505,960	\$408,501	\$5,914,461	\$4,847,232	\$11,005	\$571,793	\$6,486,254	\$0	
DCSS Managed												
FF&E: 7700-7504		\$100,000	\$100,000	\$48,942		\$48,942	\$48,942		\$51,058	\$100,000	(\$0)	
Technology: 7800-7801		\$10,000	\$10,000	\$2,842		\$2,842	\$2,796	\$46	\$7,158	\$10,000		
DCSS Managed Subtotal		\$110,000	\$110,000	\$51,784		\$51,784	\$51,738	\$46	\$58,216	\$110,000	(\$0)	
Project Total	\$6,714,225	(\$117,971)	\$6,596,254	\$5,557,744	\$408,501	\$5,966,245	\$4,898,971	\$11,051	\$630,009	\$6,596,254	\$0	

Program\DeKalb County\421 SPLOST III\High Schools\SW DeKalb HS - SPLOST II Deferred, ADA

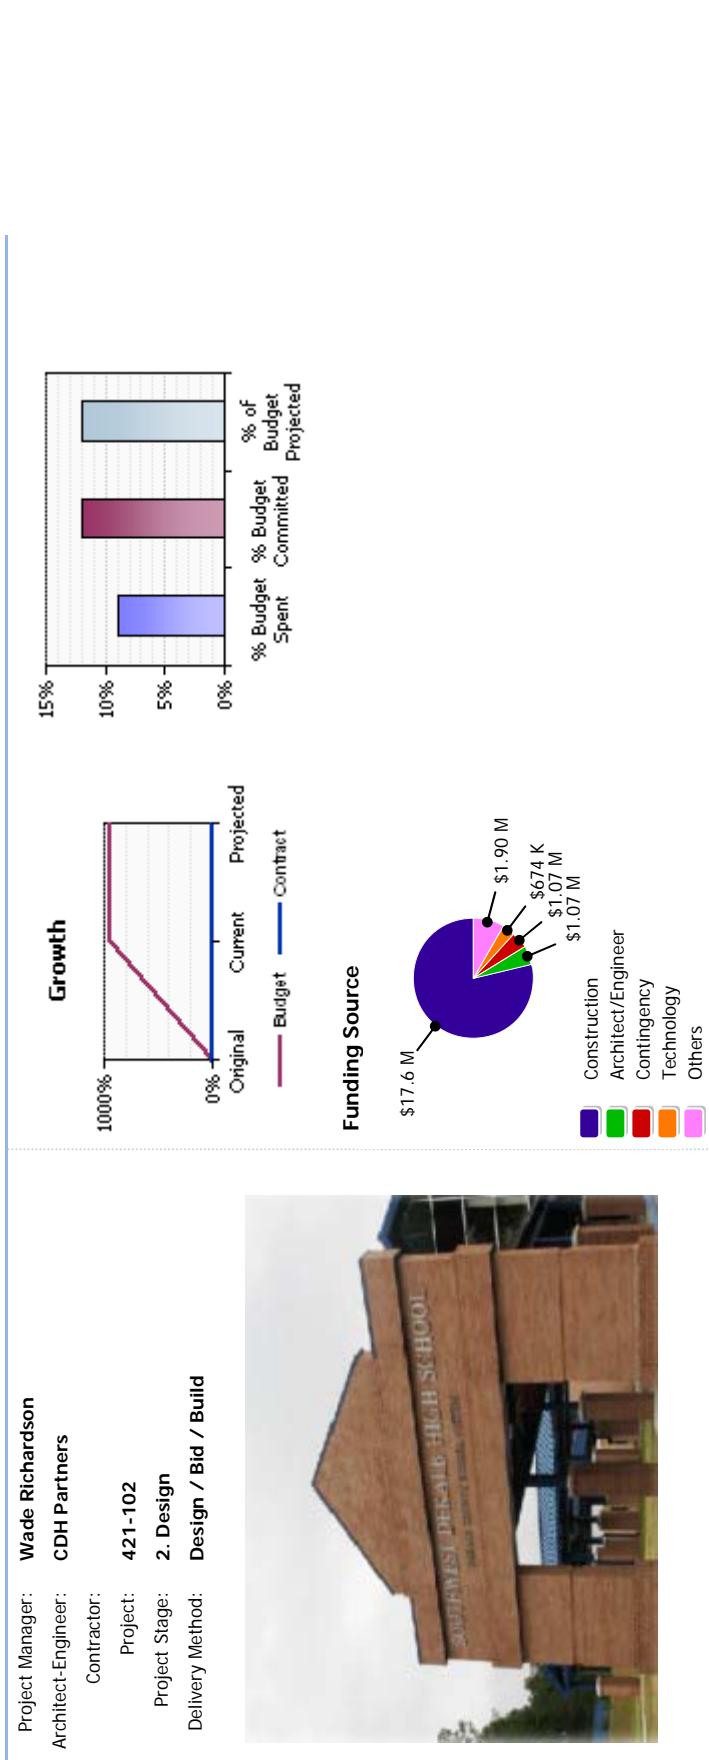

Scope of Work:

- The SPLOST II scope of work included locker room renovations, a new multipurpose building, new roads, parking lot paving, resurfacing the tennis court and baseball/football/soccer field, which has all been completed.

In July, 2009, under SPLOST III, the DeKalb County Board of Education approved an additional \$20.2 million in funding for a new 31-classroom addition, pursuant to the CIP Mid-Program Assessment Report.

Remarks:

- The multi-purpose building construction is complete and the associated contracts have been closed.

Design work for the auditorium and classroom addition began in November, 2010 and is in progress.


Wade Richardson assigned as new PM as of 2/21/11.

Cost Status by Budget Category:

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	Forecast	ETC	Estimate At Completion	Uncommitted
CIT Managed													
Architect/Engineer: 7100-7101	\$100,000	\$98,366	\$1,068,366	\$720,000	\$96,460	\$816,460	\$186,460	\$612,000		\$251,900	\$1,068,360	\$6	
Surveying: 7100-7102	\$6,260	\$127,500	\$133,760	\$27,490		\$27,490	\$24,050	\$3,440		\$106,270	\$133,760		
Construction Testing: 7100-7103	\$17,710	\$84,206	\$101,916	\$25,581	\$4,974	\$30,555	\$30,555	\$0		\$71,360	\$101,915	\$1	
Abatement: 7100-7104		\$40,000	\$40,000							\$40,000	\$40,000		

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	Forecast	ETC	Estimate At Completion	Uncommitted
Other Consultants: 7100-7105	\$16,960	\$40,000	\$56,960	\$5,480		\$5,480				\$51,480		\$56,960	
Management Fees: 7200-7201	\$35,420	(\$35,420)	\$16,227,508	\$17,598,908	\$1,384,133	\$83,351	\$1,467,484	\$1,449,416	\$18,068	\$16,131,424	\$17,598,908		
Construction - Construction Technology: 7300-7301.22	\$1,371,400	\$30,000	\$30,000	\$30,000						\$30,000	\$30,000		
Miscellaneous: 7300-7302	\$173,350	\$375,449	\$548,799	\$345			\$345			\$548,454	\$548,799		
Security: 7400-7401	\$10,000	\$87,200	\$97,200	\$22,200			\$22,200	\$22,180	\$20	\$75,000	\$97,200		
Utilities: 7500-7501		\$125,000	\$125,000							\$25,000	\$125,000		
Moving / Relocation: 7500-7502	\$30,000	\$100,000	\$130,000							\$30,000	\$130,000		
Contingency: 9999-9999	\$91,175	\$976,325	\$1,067,500							\$1,067,500	\$1,067,500		
CIT Managed Subtotal	\$1,892,275	\$19,146,134	\$20,998,409	\$2,185,229	\$184,785	\$2,370,014	\$1,718,486	\$633,528		\$18,628,388	\$20,998,402	\$7	
DCSS Managed													
FF&E: 7700-7504	\$31,760	\$606,049	\$637,809	\$3,030			\$3,030			\$637,809		(\$0)	
Technology: 7800-7801	\$260,000	\$414,032	\$674,032	\$254,913			\$254,913			\$419,000	\$673,913	\$119	
DCSS Managed Subtotal	\$291,760	\$1,020,081	\$1,311,841	\$257,943			\$257,943			\$1,053,779	\$1,311,722	\$119	
Project Total	\$2,144,035	\$20,166,215	\$22,310,250	\$2,431,172	\$184,785	\$2,627,957	\$1,976,429	\$633,528		\$19,682,167	\$22,310,124	\$126	

Program\DeKalb County\421 SPLOST III\Elementary Schools\Terry Mill ES (DESA) - Roof

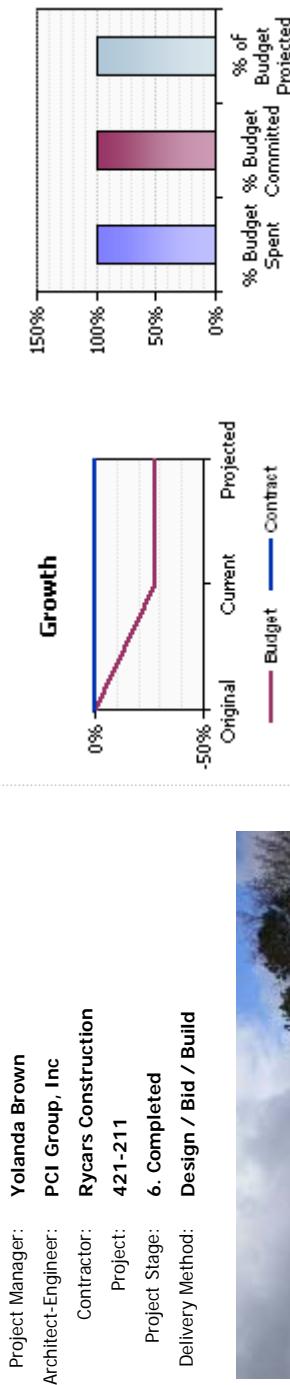

Scope of Work:

- The installation of a new modified bitumen roofing system.

Remarks:

- Project was completed in 4th quarter 2009.

Cost Status by Budget Category:

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
CIIT Managed												
Architect/Engineer: 7100-7101	\$47,329	(\$30,929)	\$16,400	\$16,400			\$16,400	\$16,400			\$16,400	
Other Consultants: 7100-7105	\$3,037	\$3,037	\$3,037	\$3,037			\$3,037	\$3,037			\$3,037	
Management Fees: 7200-7201	\$16,098	(\$16,098)										
Other Consultants: 7300-7301	\$741,480	(\$151,078)	\$590,402	\$592,902	(\$2,500)	\$590,402	\$590,402				\$590,402	
Construction: 7300-7302												
Miscellaneous: 9999-9999	\$42,364	(\$42,364)										
Contingency: 9999-9999	\$827,271	(\$237,084)	\$610,187	\$612,687	(\$2,500)	\$610,187	\$610,187				\$610,187	
CIIT Managed Subtotal	\$847,271	(\$237,084)	\$610,187	\$612,687	(\$2,500)	\$610,187	\$610,187				\$610,187	
Project Total	\$847,271	(\$237,084)	\$610,187	\$612,687	(\$2,500)	\$610,187	\$610,187				\$610,187	

Program\DeKalb County\421 SPLOST III\High Schools\Towers HS - SPLOST II Deferred

Project Manager: Virgil Bryan
Architect-Engineer: YLH Construction Co.
Project: 421-103
Project Stage: 5. Close-out
Delivery Method: Design / Build

Growth

Bar chart showing Growth from 86% to 94%.

Category	Value
Original	86%
Current	94%
Projected	94%

Funding Source

Pie chart showing Funding Source distribution.

Source	Amount
Construction	\$2.59 M
Technology	\$138 K
FF & E	\$60.0 K
Security	\$104 K
Others	\$150 K

Photograph

A photograph of a modern building under construction, surrounded by trees and a dirt road.

Scope of Work:

- The scope includes a 3 Classroom Suite Career Technology addition and bus loop renovation. Existing square footage is 170,679.


Remarks:

 - 02/17/11: The addition has been turned over to the school and in use. Close-out is in progress. The temporary exit from the cafeteria is being reviewed for conversion to a permanent exit for trash removal/commactor access

Cost Status by Budget Category:

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
Moving / Relocation: 7500-7502	\$50,000	(\$40,000)	\$10,000	\$1,600		\$1,600	\$1,599	\$2			\$1,600	\$8,400
Trailers: 7600-7503	\$100,000	(\$94,000)	\$6,000	\$6,000		\$6,000	\$6,000				\$6,000	
Contingency: 9999-9999	\$128,000	(\$118,000)	\$10,000									\$10,000
CIT Managed Subtotal	\$2,844,000	(\$51,200)	\$2,792,800	\$2,567,084	\$102,723	\$2,669,807	\$2,515,411	\$154,396	(\$1,060)	\$31,000	\$2,699,747	\$93,053
DCSS Managed												
FF&E: 7700-7504	\$103,600		\$103,600	\$76,829		\$76,829				\$32,807	\$109,636	(\$6,036)
Technology: 7800-7801	\$150,000		\$150,000	\$100,989		\$100,989	\$100,989			\$25,000	\$125,989	\$24,011
DCSS Managed Subtotal	\$253,600		\$253,600	\$177,818		\$177,818	\$177,818			\$57,807	\$235,625	\$17,975
Project Total	\$3,097,600	(\$51,200)	\$3,046,400	\$2,744,902	\$102,723	\$2,847,625	\$2,693,229	\$154,396	(\$1,060)	\$88,807	\$2,935,372	\$111,028

Program\DeKalb County\421 SPLOST III\High Schools\Tucker HS - New Replacement High School

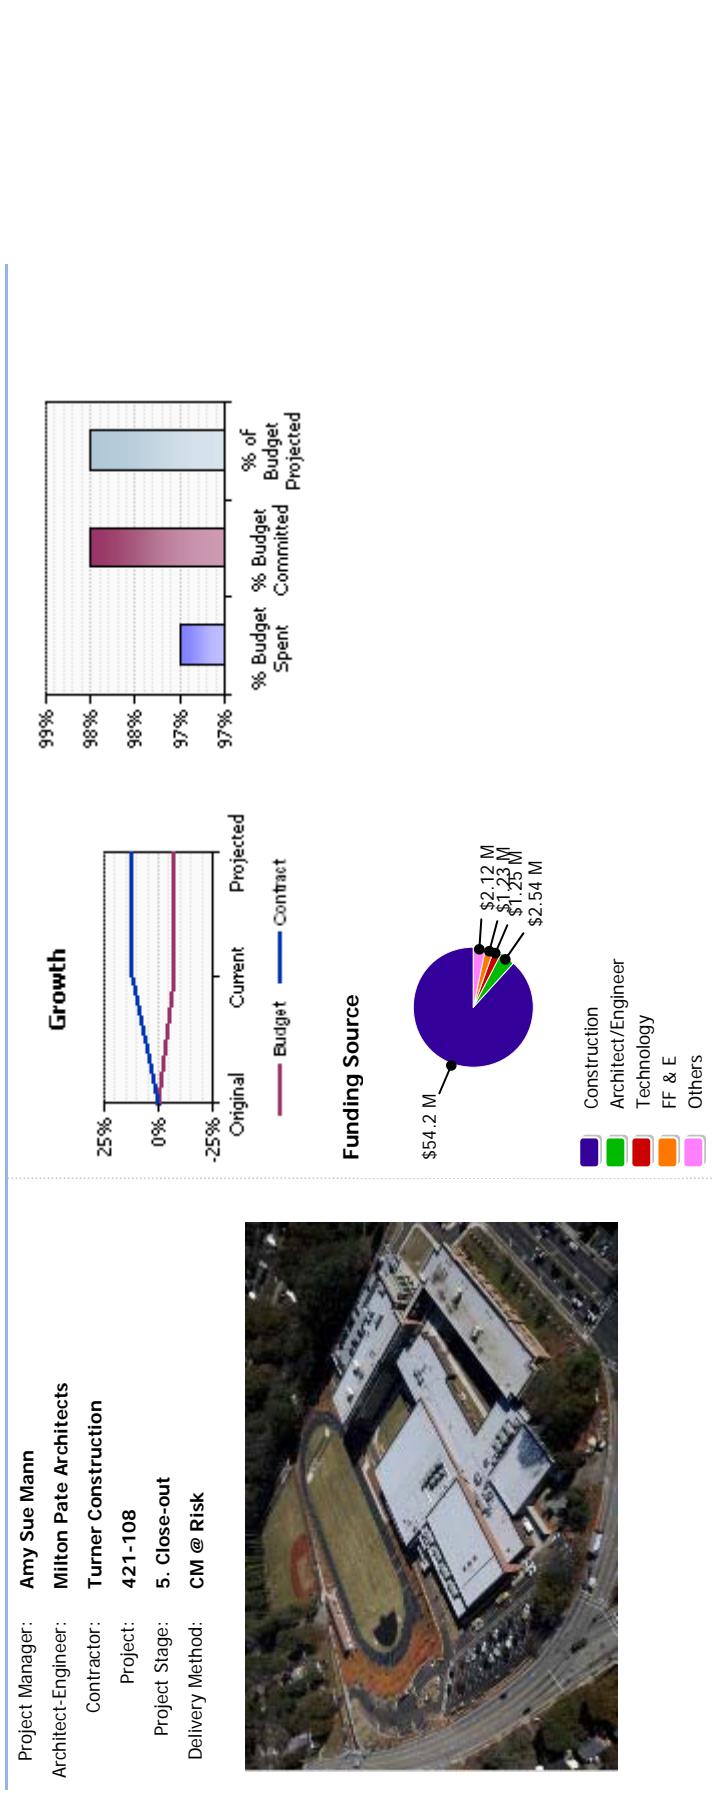

Scope of Work:

- The new facility will be built in two phases around the existing school. Phase 1 includes a two story building fronting LaVista Road which will house academic classrooms and the 9th Grade Academy. Additionally, a four story general classroom wing with administrative offices and a media center and a three story parking deck will be constructed. Phase 2 consists of the Career Technology Labs, Auditorium, Fine Arts and Gymnasium facilities. Site work for the new fields will also be completed in this phase.

Remarks:


- The conversion of the Tucker Middle School Softball field for high school competition softball use and additional work at the baseball field to replace items originally constructed by the Booster Club, but not included in the original project, will be completed over the summer 2011. This project is in close out.

Cost Status by Budget Category:


Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
CIT Managed												
Architect/Engineer: 7100-7101	\$3,035,428	(\$500,000)	\$2,535,428	\$2,066,346	\$363,835	\$2,430,181	\$2,375,371	\$28,145		\$105,000	\$2,535,181	\$247
Surveying: 7100-7102	\$15,000	\$21,000	\$36,000	\$18,709		\$18,709	\$18,709			\$17,000	\$35,709	\$291
Construction Testing: 7100-7103	\$225,000	\$105,900	\$330,900	\$316,509		\$316,509	\$303,823	(\$836)		\$14,000	\$330,509	\$391
Abatement: 7100-7104	\$100,000	\$60,000	\$160,000	\$135,532		\$135,532	\$134,242	\$1,290		\$24,000	\$159,532	\$468
Other Consultants: 7100-7105	\$365,000	(\$300,000)	\$65,000							\$65,000	\$65,000	
Management Fees: 7200-7201	\$1,365,000	(\$1,365,000)										
Construction: 7300-7301	\$51,530,466	\$2,700,000	\$54,230,466	\$48,133,648	\$6,045,664	\$54,179,312	\$48,318,140	\$508,199	(\$40,818)	\$91,900	\$54,230,394	\$72
Miscellaneous: 7300-7302	\$712,050	(\$242,900)	\$469,150	\$25,691		\$25,691	\$13,646	\$3,028		\$443,400	\$469,091	\$59

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
Security: 7400-7401	\$200,000	(\$167,000)	\$33,000	\$29,147		\$29,147	\$29,147			\$3,800	\$32,947	\$53
Utilities: 7500-7501	\$200,000	\$200,000	\$200,000	\$111,527		\$111,527	\$31,707	(\$0)		\$88,000	\$199,527	\$473
Moving / Relocation: 7500-7502	\$250,000	\$250,000	\$250,000	\$63,560		\$63,560	\$62,227	(\$12)	\$5,313	\$181,000	\$249,873	\$127
Trailers: 7600-7503	\$2,000,000	(\$2,000,000)										
Contingency: 9999-9999	\$4,075,000	(\$3,778,085)	\$296,915									
CIT Managed Subtotal	\$64,072,944	(\$5,466,085)	\$58,606,859	\$50,900,669	\$6,409,499	\$57,310,168	\$51,287,012	\$539,813	(\$35,505)	\$1,330,000	\$58,604,663	\$2,196
DCSS Managed												
Land: 7100-7150	\$276,085	\$276,085	\$276,084			\$276,084	\$276,084				\$276,084	\$2
FF&E: 7700-7504	\$1,007,072	\$225,000	\$1,232,072	\$1,171,167		\$1,171,167	\$1,171,165	\$1		\$60,900	\$1,232,067	\$56
Technology: 7800-7801	\$1,250,000	\$1,250,000	\$1,115,214			\$1,115,214	\$1,115,394	(\$180)		\$134,780	\$1,249,994	\$6
DCSS Managed Subtotal	\$2,257,072	\$501,085	\$2,758,157	\$2,562,464		\$2,562,464	\$2,562,642	(\$78)		\$195,680	\$2,758,144	\$13
Project Total	\$66,330,016	(\$4,965,000)	\$61,365,016	\$53,463,133	\$6,409,499	\$59,872,632	\$53,849,654	(\$35,634)	(\$35,505)	\$1,525,680	\$61,362,807	\$2,209


Program\DeKalb County\421 SPLOST III\Elementary Schools\Vanderlyn ES - HVAC, Roof, ADA

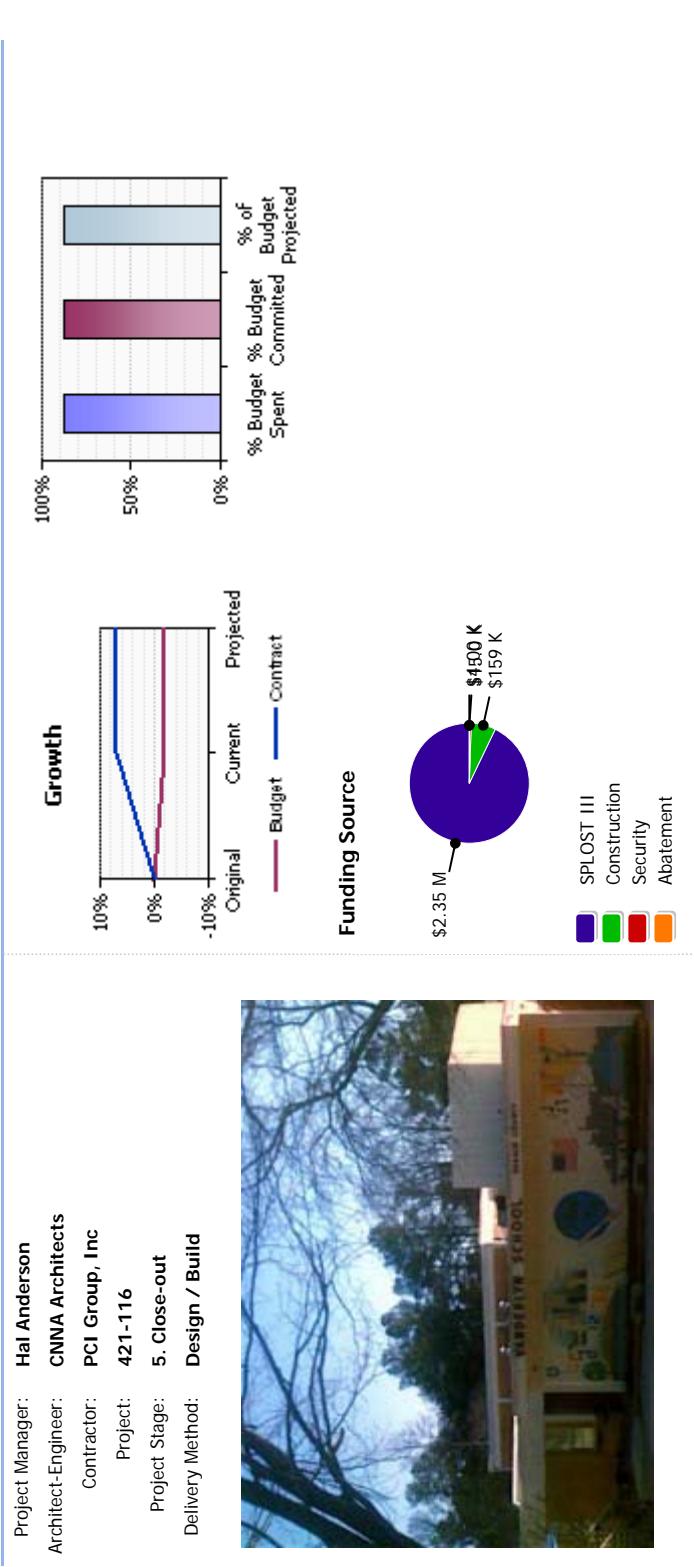

Program\DeKalb County\421 SPLOST III\Elementary Schools\Wadsworth ES - Roof

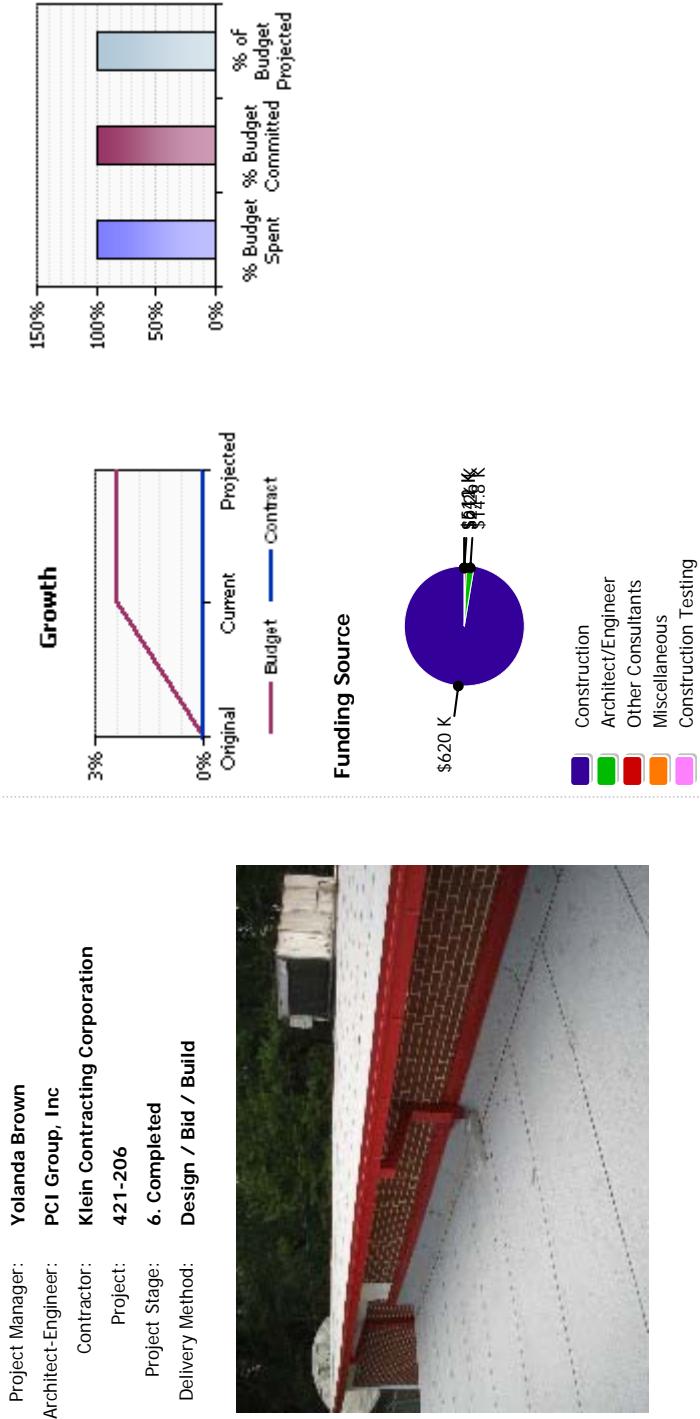

Program\DeKalb County\421 SPLOST III\Other Facilities\Warren Tech - HVAC

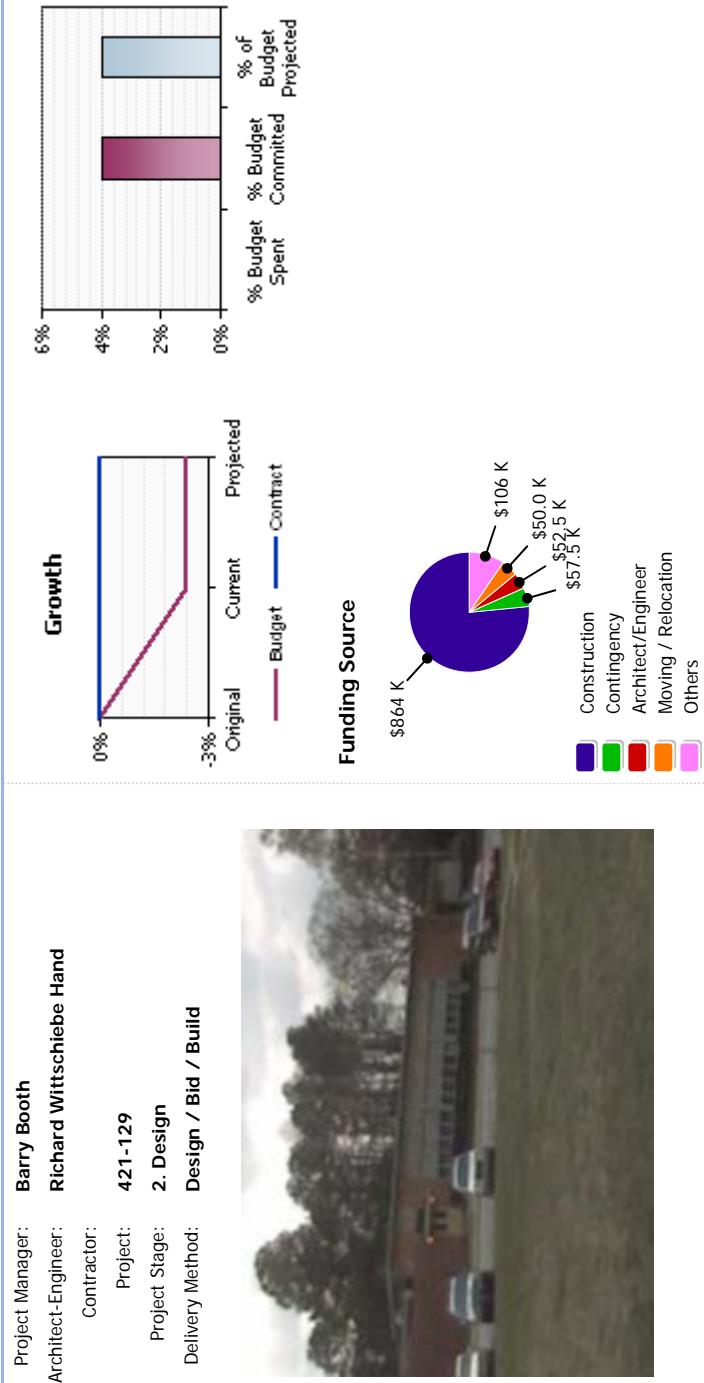

- The design kick off meeting was held on March 23, 2011. A walk through with the architect will take place at the school on March 29, 2011 to gather information for Finding of Fact and the Preliminary Report.

Program\DeKalb County\421 SPLC\Other Facilities\William Bradley Bryant Center

Project Manager: Brad Jacobs
Architect-Engineer:
Contractor: 421-228
Project: 3. Procurement
Project Stage: Design / Bid / Build
Delivery Method:

Growth

Original Current Projected

% Budget Spent — Contract

0% 50% 100% 150%

Funding Source

- Technology: \$1.25 M
- Construction: \$440 K
- Contingency: \$150 K
- Architect/Engineer: \$160 K
- Others: [color swatches]

Construction Site Photo: A photograph of a construction site featuring a large concrete foundation, rebar, and wooden formwork for a bridge pier. The background shows trees and a clear sky.



- Scope of work includes:**

 - renovations to the front offices to accommodate MLS personnel, to be relocated from vacated Admin Building A
 - Increase in the size of electrical service to the building to accommodate relocated data equipment.
 - Conversion of the existing cafeteria into the new MLS Data Center
 - Relocation of data equipment from Building A to WBBC, as well as infrastructure / fiber optic relocations.
 - Parking lot improvements
 - Improvements to interior finishes



Remarks:

- Design complete. RFP for construction has been issued, with a June, 2011 contract award anticipated.


Cost Status by Budget Category:													
Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORS	Forecast	ETC	Estimate At Completion	Uncommitted
CT Managed													
Architect/Engineer: 7100-7101	\$150,000		\$150,000				\$4,950	\$4,950			\$150,000	\$150,000	
Surveying: 7100-7102	\$10,000		\$10,000								\$5,050	\$10,000	
Construction Testing: 7100-7103	\$35,000		\$35,000		\$5,337		\$5,337	\$2,600		\$2,737	\$29,663	\$35,000	
Abatement: 7100-7104	\$20,000										\$20,000	\$20,000	
Construction: 7300-7301	\$1,250,000										\$1,250,000	\$1,250,000	

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
Miscellaneous: 7300-7302	\$75,000	\$75,000	\$75,000	\$232		\$232	\$406	(\$174)		\$74,768	\$75,000	
Security: 7400-7401	\$25,000		\$25,000							\$25,000	\$25,000	
Utilities: 7500-7501	\$75,000		\$75,000							\$75,000	\$75,000	
Moving / Relocation: 75000-7502	\$100,000		\$100,000							\$100,000	\$100,000	
Contingency: 9999-9999	\$160,000		\$160,000							\$160,000	\$160,000	
CLT Managed Subtotal	\$1,900,000		\$1,900,000	\$10,519		\$10,519	\$7,956	\$2,563		\$1,889,481	\$1,900,000	\$0
DCSS Managed												
FF&E: 7700-7504	\$100,000		\$100,000							\$100,000	\$100,000	
Technology: 7800-7801	\$1,500,000		\$1,500,000							\$1,500,000	\$1,500,000	
DCSS Managed Subtotal	\$1,600,000		\$1,600,000	\$3,500,000	\$10,519	\$10,519	\$7,956	\$2,563		\$1,600,000	\$1,600,000	
Project Total	\$3,500,000									\$3,489,481	\$3,500,000	\$0

Program\DeKalb County\421 SPLOST III\Elementary Schools\Woodridge ES - Roof
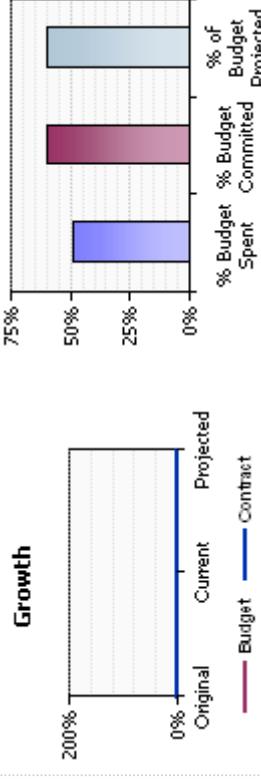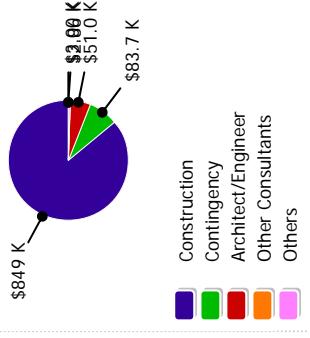
<p>Project Manager: Yolanda Brown Architect-Engineer: PCI Group, Inc Contractor: Roof Management Project: 421-227 Project Stage: 4. Construction Delivery Method: Design / Bid / Build</p> 																																																																																																																																																	
<p>Growth</p>  <p>Funding Source</p>  <table border="1"> <thead> <tr> <th>Funding Source Category</th> <th>Amount (\$K)</th> </tr> </thead> <tbody> <tr> <td>Construction</td> <td>\$849 K</td> </tr> <tr> <td>Contingency</td> <td>\$1.00 K</td> </tr> <tr> <td>Architect/Engineer</td> <td>\$51.0 K</td> </tr> <tr> <td>Other Consultants</td> <td>\$32.0 K</td> </tr> <tr> <td>Others</td> <td>\$83.7 K</td> </tr> </tbody> </table> <p>Scope of Work:</p> <ul style="list-style-type: none"> Full roof replacement. <p>Remarks:</p> <ul style="list-style-type: none"> The demolition is complete and installation of the base sheet is almost complete. 	Funding Source Category	Amount (\$K)	Construction	\$849 K	Contingency	\$1.00 K	Architect/Engineer	\$51.0 K	Other Consultants	\$32.0 K	Others	\$83.7 K	<p>Cost Status by Budget Category:</p> <table border="1"> <thead> <tr> <th>Budget Category</th> <th>Original Budget</th> <th>Budget Revision</th> <th>Current Budget</th> <th>Current Contract</th> <th>Original Contract</th> <th>Executed Changes</th> <th>Current Contract</th> <th>Paid To Date</th> <th>Contract Balance</th> <th>CORS</th> <th>ETC Forecast</th> <th>Estimate At Completion</th> <th>Uncommitted</th> </tr> </thead> <tbody> <tr> <td>CIT Managed</td> <td></td> </tr> <tr> <td>Architect/Engineer: 7100-7101</td> <td>\$50,968</td> <td></td> <td>\$50,968</td> <td>\$22,000</td> <td></td> <td></td> <td></td> <td>\$7,800</td> <td></td> <td></td> <td>\$28,968</td> <td>\$50,968</td> </tr> <tr> <td>Construction Testing: 7100-7103</td> <td>\$1,500</td> <td></td> <td>\$1,500</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>\$1,500</td> <td>\$1,500</td> </tr> <tr> <td>Other Consultants: 7100-7105</td> <td>\$2,856</td> <td></td> <td>\$2,856</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>\$2,856</td> <td>\$2,856</td> </tr> <tr> <td>Construction: 7300-7301</td> <td>\$849,473</td> <td></td> <td>\$849,473</td> <td>\$571,474</td> <td></td> <td></td> <td></td> <td>\$469,179</td> <td>\$102,295</td> <td></td> <td>\$277,999</td> <td>\$849,473</td> </tr> <tr> <td>Miscellaneous: 7300-7302</td> <td>\$1,500</td> <td></td> <td>\$1,500</td> <td>\$348</td> <td></td> <td></td> <td></td> <td>\$348</td> <td></td> <td></td> <td>\$1,152</td> <td>\$1,500</td> </tr> <tr> <td>Contingency: 9999-9999</td> <td>\$83,703</td> <td></td> <td>\$83,703</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>\$83,703</td> <td>\$83,703</td> </tr> <tr> <td>CIT Managed Subtotal</td> <td>\$990,000</td> <td></td> <td>\$990,000</td> <td>\$593,822</td> <td></td> <td></td> <td></td> <td>\$593,822</td> <td>\$483,727</td> <td>\$110,095</td> <td>\$396,178</td> <td>\$990,000</td> </tr> <tr> <td>Project Total</td> <td>\$990,000</td> <td></td> <td>\$990,000</td> <td>\$593,822</td> <td></td> <td></td> <td></td> <td>\$593,822</td> <td>\$483,727</td> <td>\$110,095</td> <td>\$396,178</td> <td>\$990,000</td> </tr> </tbody> </table>	Budget Category	Original Budget	Budget Revision	Current Budget	Current Contract	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORS	ETC Forecast	Estimate At Completion	Uncommitted	CIT Managed														Architect/Engineer: 7100-7101	\$50,968		\$50,968	\$22,000				\$7,800			\$28,968	\$50,968	Construction Testing: 7100-7103	\$1,500		\$1,500								\$1,500	\$1,500	Other Consultants: 7100-7105	\$2,856		\$2,856								\$2,856	\$2,856	Construction: 7300-7301	\$849,473		\$849,473	\$571,474				\$469,179	\$102,295		\$277,999	\$849,473	Miscellaneous: 7300-7302	\$1,500		\$1,500	\$348				\$348			\$1,152	\$1,500	Contingency: 9999-9999	\$83,703		\$83,703								\$83,703	\$83,703	CIT Managed Subtotal	\$990,000		\$990,000	\$593,822				\$593,822	\$483,727	\$110,095	\$396,178	\$990,000	Project Total	\$990,000		\$990,000	\$593,822				\$593,822	\$483,727	\$110,095	\$396,178	\$990,000
Funding Source Category	Amount (\$K)																																																																																																																																																
Construction	\$849 K																																																																																																																																																
Contingency	\$1.00 K																																																																																																																																																
Architect/Engineer	\$51.0 K																																																																																																																																																
Other Consultants	\$32.0 K																																																																																																																																																
Others	\$83.7 K																																																																																																																																																
Budget Category	Original Budget	Budget Revision	Current Budget	Current Contract	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORS	ETC Forecast	Estimate At Completion	Uncommitted																																																																																																																																				
CIT Managed																																																																																																																																																	
Architect/Engineer: 7100-7101	\$50,968		\$50,968	\$22,000				\$7,800			\$28,968	\$50,968																																																																																																																																					
Construction Testing: 7100-7103	\$1,500		\$1,500								\$1,500	\$1,500																																																																																																																																					
Other Consultants: 7100-7105	\$2,856		\$2,856								\$2,856	\$2,856																																																																																																																																					
Construction: 7300-7301	\$849,473		\$849,473	\$571,474				\$469,179	\$102,295		\$277,999	\$849,473																																																																																																																																					
Miscellaneous: 7300-7302	\$1,500		\$1,500	\$348				\$348			\$1,152	\$1,500																																																																																																																																					
Contingency: 9999-9999	\$83,703		\$83,703								\$83,703	\$83,703																																																																																																																																					
CIT Managed Subtotal	\$990,000		\$990,000	\$593,822				\$593,822	\$483,727	\$110,095	\$396,178	\$990,000																																																																																																																																					
Project Total	\$990,000		\$990,000	\$593,822				\$593,822	\$483,727	\$110,095	\$396,178	\$990,000																																																																																																																																					

Program\DeKalb County\421 SPLOST III\Elementary Schools\Woodward ES - HVAC, Roof

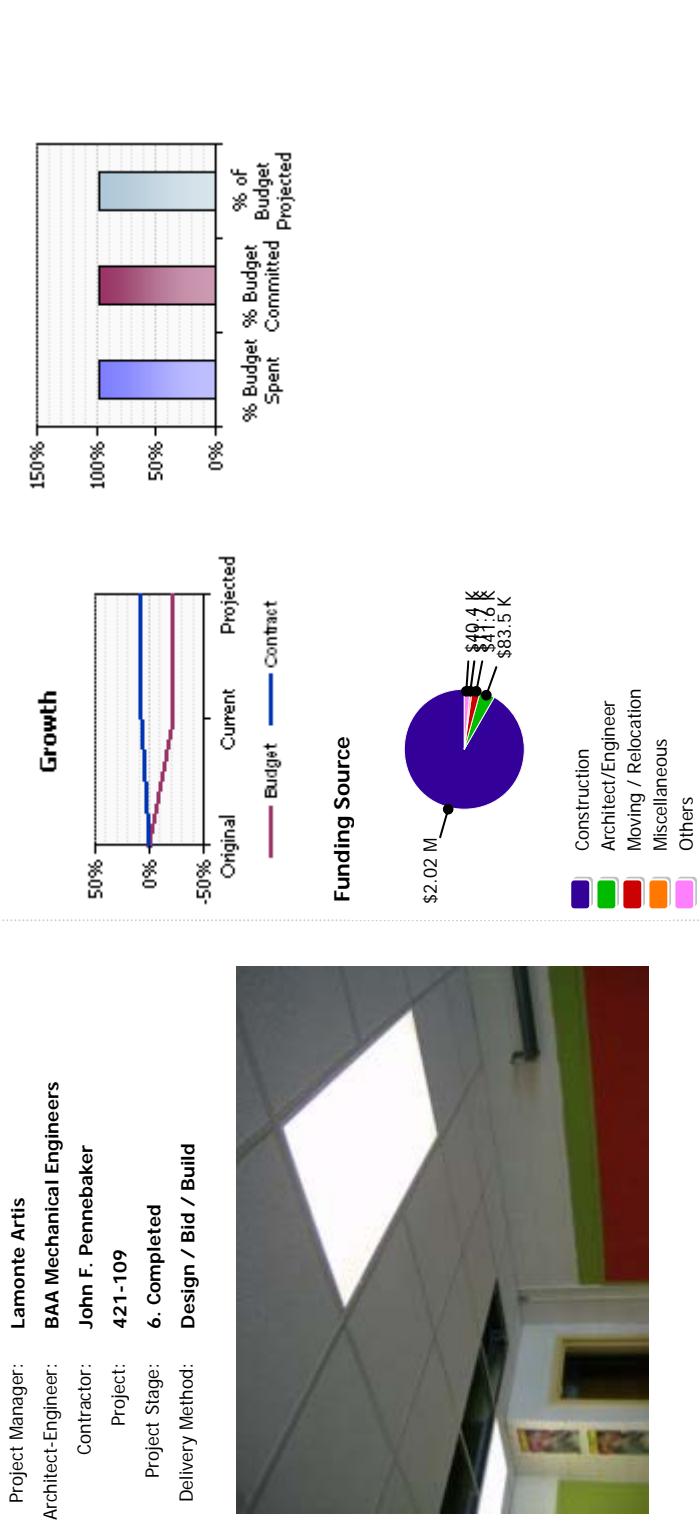

Cost Status by Budget Category:											
Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion
CIT Managed											
Architect/Engineer: 7100-7101	\$143,505	(\$60,000)	\$83,505	\$68,250		\$68,250					
Construction Testing: 7100-7103	\$17,260	(\$17,260)									
Abatement: 7100-7104	\$10,000	\$646	\$10,646	\$7,676		\$7,676					
Other Consultants: 7100-7105	\$17,434	(\$10,000)	\$7,434								
Management Fees: 7200-7201	\$52,921	(\$52,921)									
Construction: 7300-7301	\$2,324,598	(\$300,000)	\$2,024,598	\$1,875,000	\$143,219	\$2,018,219					
Miscellaneous: 7300-7302	\$80,312	(\$68,600)	\$11,712	\$3,680		\$3,680					
Security: 7400-7401	\$10,000		\$10,000	\$9,995		\$9,995					
Utilities: 7500-7501	\$25,000	(\$25,000)									
Moving / Relocation: 7500-7502	\$50,000	(\$8,417)	\$41,583	\$41,583		\$41,583					

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
Contingency: 9999-9999	\$143,738	(\$135,000)	\$8,738								\$8,738	
CLT Managed Subtotal	\$2,874,768	(\$676,552)	\$2,198,216	\$2,006,183	\$143,219	\$2,149,402	\$2,149,402				\$2,149,402	
DCSS Managed											\$48,814	
Technology: 7800-7801	\$3,600	\$3,600	\$2,047			\$2,047	\$2,047				\$1,553	
DCSS Managed Subtotal	\$3,600	\$3,600	\$2,047			\$2,047	\$2,047				\$1,553	
Project Total	\$2,874,768	(\$672,952)	\$2,201,816	\$2,008,231	\$143,219	\$2,151,450	\$2,151,450				\$50,366	

SPLOST III Capital Improvement Program

Project Bid List

Monthly Status Report

ACTIVE BID ITEMS

No.	Project	Scope	Bid Type	Dates	Questions Due	Issue Addendum	Due Date	Due Time	Agenda Mo.	Comments	Project Manager
				Issue	Pre Bid Proposal	Time	#1	Final			
410-358	Henderson MS	Soil Boring & Geotechnical Services	RFP Prequalified	3/29/2011	N/A	4/4/2011	TBD	4/12/2011	12:00 PM	N/A	RFP Submission
410-364	WBBC	Front Office Renovation	GC RFP	3/24/2011	4/19/2011	10:00 AM	4/25/2011	TBD	4/28/2011	5/3/2011	2:00 PM
410-364-001	WBBC	Data Center Racks, Power Distribution and Cooling Systems	GC RFP	3/24/2011	4/20/2011	10:00 AM	4/26/2011	TBD	4/29/2011	5/4/2011	2:00 PM
421-123	Avondale HS	Roof Replacement	Hard Bid Prequalified	3/24/2011	4/21/2011	10:00 AM	4/27/2011	TBD	5/2/2011	5/5/2011	2:00 PM
421-321-015	Emergency Generators	(Redan ES and Rainbow ES)	ITB	4/5/2011	4/19/2011	2:00 PM	4/27/2011	TBD	5/2/2011	5/5/2011	3:00 PM
421-108	Tucker HS	Land Survey	RFP Prequalified	4/6/2011	N/A	N/A	4/13/2011	TBD	4/18/2011	4/20/2011	12:00 PM

Leon Glasser/
Tony Hunter

Brad Jacobs

Melissa Ryckley

Wade Richardson

Larry Williams

Amy Sue Mann

SPLOST III Capital Improvement Program

Project Bid List

Monthly Status Report

PENDING BID ITEMS

No.	Project	Scope	Bid Type	Release Draft	Status	Comments	Project Manager	Solicitor	A/E Firm
421-132	Knollwood ES	HVAC & ADA Modifications	A/E RFP	4/5/2011	Scope Development		Robert Mitchell	Joshua Williams	N/A
N/A	Arabia Mountain HS	Storage Facility	TB Prequalified	4/5/2011	Scope Development		Wade Richardson	Joshua Williams	Perkins + Will
421-110	Stone Mountain HS	Career Technology Lab Renovation	TB Prequalified	4/5/2011	Scope Development		Wade Richardson	Joshua Williams	Sheifer & Grant
421-108	Tucker HS	Press Box & Concessions	GC RFP	TBD			Amy Sue Mann	Joshua Williams	Milton Pate
421-108	Tucker HS	Softball Field Conversion	GC RFP	TBD			Amy Sue Mann	Joshua Williams	Milton Pate
421-303-011	Hawthorne ES	ADA Modifications	TB Prequalified	4/1/2011		Solicitation planned for Summer 2011	Bernard Levert	Joshua Williams	The Epsten Group
N/A	Prequalification	Various	RFQ	TBD	Preparing Docs		Amy Sue Mann	Joshua Williams	N/A
421-117	Chamblee HS	Traffic Study	RFP	TBD			Amy Sue Mann	Joshua Williams	N/A
421-118	Cedar Grove HS	Restroom Upgrades	A/E RFP	TBD	Scope Development	Pending Board approval of additional allocation of funds	Carlton Parker	Joshua Williams	N/A
421-128	Averdale HS	Renovations	GG-RFP	TBD	Scope Development	CANCELLED	Virgil Bayan	Joshua Williams	N/A
421-302-003	Group B-3	ADA Modifications	A/E RFP	TBD	Under Evaluation	Pending results from Student Services	Bernard Levert	Liz Epstein	N/A
421-303	Group C	ADA Modifications	A/E RFP	TBD	Under Evaluation	Pending results from Student Services	Bernard Levert	Liz Epstein	N/A
421-304	Group D	ADA Modifications	A/E RFP	TBD	Under Evaluation	Pending results from Student Services	Bernard Levert	Liz Epstein	N/A
421-305	Group E	ADA Modifications	A/E RFP	TBD	Under Evaluation	Pending results from Student Services	Bernard Levert	Liz Epstein	N/A
421-102	Southwest DeKalb	Addition	GC RFP	TBD	Scope Development	25% Construction Documents	Wade Richardson	Joshua Williams	CDH Partners
421-111	Redan HS	Renovations	GC RFP	TBD	Scope Development	25% Construction Documents	Wade Richardson	Joshua Williams	Richard Wittschiebe
421-127	MLK Jr. HS	Addition	GC RFP	TBD	Scope Development	On Hold	Amy Sue Mann	Joshua Williams	R.L. Brown
421-128	Miller Grove HS	Addition	GC RFP	TBD	Scope Development	25% Construction Documents	Robert Mitchell	Joshua Williams	Manley Spangler Smith
421-341-027	Wadsworth Magnet ES	Minor HVAC, Ceiling & Lighting Replacement	A/E RFP	TBD	Scope Development		Melissa Ryckley	Joshua Williams	N/A
421-341-043	Allgood ES	Kitchen Renovation	A/E RFP	TBD	Scope Development		Robert Mitchell	Joshua Williams	N/A
421-226	Old Chamblee MS	Roof Replacement	A/E RFP	TBD	Draft Complete	On Hold	Yolanda Brown	Joshua Williams	N/A
421-341-039	Clifton ES	Ceiling Tile Replacement	TB	TBD	Scope Development		Melissa Ryckley	Joshua Williams	N/A

CLOSED BIDS

No.	Project	Scope	Bid Type	Dates	Time	Questions Due	Issue Addendum	Due Date	Due Time	Agenda Mo.	Comments	Project Manager
421-218	Evansdale ES	Roof Replacement	Hard Bid Prequalified	12/30/2010	1/27/2011	10:00 AM	2/2/2011	TBD	2/7/2011	2:00 PM	March	Pending Contract Execution
421-219	Flat Shoals ES	Roof Replacement	Hard Bid Prequalified	12/30/2010	1/27/2011	10:00 AM	2/2/2011	TBD	2/7/2011	2:00 PM	March	Pending Contract Execution
421-223	Hambrick ES	Roof Replacement	Hard Bid Prequalified	2/10/2011	3/1/2011	10:00 AM	3/7/2011	TBD	3/10/2011	2:00 PM	April	BOA Item Prepared
421-224	Hawthorne ES	Roof Replacement	Hard Bid Prequalified	2/10/2011	3/1/2011	10:00 AM	3/7/2011	TBD	3/10/2011	2:00 PM	April	BOA Item Prepared
410-359	Shamrock MS	MS Conversion	GC RFP	2/10/2011	3/3/2011	10:00 AM	3/9/2011	TBD	3/14/2011	10:00 AM	April	BOA Item Prepared
410-359	Sequoyah MS	MS Conversion	GC RFP	2/10/2011	3/3/2011	10:00 AM	3/9/2011	TBD	3/14/2011	10:00 AM	April	BOA Item Prepared
410-359	Henderson MS	MS Conversion	GC RFP	2/10/2011	3/3/2011	10:00 AM	3/9/2011	TBD	3/14/2011	10:00 AM	April	BOA Item Prepared
421-321-015	Emergency Generators	Labor Only (Dresden ES and Idlewood ES)	ITB	2/15/2011	3/2/2011	10:00 AM	3/9/2011	TBD	3/14/2011	2:00 PM	April	BOA Item Prepared
421-117	Chamblee HS	Replacement High School	CM/GC @ Risk RFP	2/17/2011	3/9/2011	10:00 AM	3/14/2011	TBD	3/17/2011	10:00 AM	April	BOA Item Prepared
421-341-0420	Chamblee MS	Painting Various Areas	ITB	2/17/2011	3/10/2011	10:00 AM	3/16/2011	TBD	3/21/2011	1:00 PM	April	BOA Item Prepared
421-341-035	Oak Grove ES	Classroom Lighting	ITB Prequalified	2/17/2011	3/10/2011	2:00 PM	3/16/2011	TBD	3/21/2011	2:00 PM	April	BOA Item Prepared

SPL OST III Capital Improvement Program

Budget Reallocations for This Period

DeKalb County School System

Monthly Status Report

Cost Code	Code Description	Code Type	Current Budget	Change	Revised Budget
-----------	------------------	-----------	----------------	--------	----------------

421.73.01.00.110421.752.0000	Stone Mountain High School	Construction	\$5,387,833.00	\$170,000.00	\$5,557,833.00
421.74.01.00.110421.752.0000	Stone Mountain High School	Security	\$40,000.00	\$40,000.00	\$80,000.00
421.71.01.00.110421.752.0000	Stone Mountain High School	Architect/Engineer	\$272,300.00	(\$25,000.00)	\$247,300.00
421.71.03.00.110421.752.0000	Stone Mountain High School	Construction Testing	\$27,582.00	(\$15,000.00)	\$12,582.00
421.71.04.00.110421.752.0000	Stone Mountain High School	Abatement	\$175,000.00	(\$65,000.00)	\$110,000.00
421.75.01.00.110421.752.0000	Stone Mountain High School	Utilities	\$75,000.00	(\$45,000.00)	\$30,000.00
421.75.03.00.110421.752.0000	Stone Mountain High School	Trailers	\$50,000.00	(\$20,000.00)	\$30,000.00
421.99.99.00.110421.752.0000	Stone Mountain High School	Project Contingency	\$79,711.00	(\$40,000.00)	\$39,711.00
421.74.01.00.119421.752.0000	Druid Hills High School	Security	\$45,000.00	\$25,000.00	\$70,000.00
421.99.99.00.119421.752.0000	Druid Hills High School	Project Contingency	\$80,138.00	(\$25,000.00)	\$55,138.00
421.71.03.00.120421.752.0000	Dunwoody High School	Construction Testing	\$100,000.00	\$25,000.00	\$125,000.00
421.73.02.00.120421.752.0000	Dunwoody High School	Miscellaneous	\$89,241.00	(\$25,000.00)	\$64,241.00
421.99.99.00.900421.752.0000	Program Contingency	Program Contingency	\$5,272,799.00	\$440,000.00	\$5,712,799.00
421.73.01.00.101421.752.0000	Emergency HVAC Work	Construction	\$5,076,397.00	(\$440,000.00)	\$4,636,397.00
421.99.99.00.900421.752.0000	Program Contingency	Program Contingency	\$5,712,799.00	\$400,114.00	\$6,112,913.00
421.99.99.00.104421.752.0000	Columbia High School	Project Contingency	\$400,114.00	(\$400,114.00)	\$0.00
421.99.99.00.900421.752.0000	Program Contingency	Program Contingency	\$6,112,913.00	\$1,365,000.00	\$7,477,913.00
421.73.02.00.106421.752.0000	Cross Keys High School	Miscellaneous	\$356,346.00	(\$250,000.00)	\$106,346.00
421.74.01.00.106421.752.0000	Cross Keys High School	Security	\$150,000.00	(\$110,000.00)	\$40,000.00
421.75.01.00.106421.752.0000	Cross Keys High School	Utilities	\$100,000.00	(\$55,000.00)	\$45,000.00
421.75.03.00.106421.752.0000	Cross Keys High School	Trailers	\$1,000,000.00	(\$850,000.00)	\$150,000.00
421.99.99.00.106421.752.0000	Cross Keys High School	Project Contingency	\$313,222.00	(\$100,000.00)	\$213,222.00
421.99.99.00.900421.752.0000	Program Contingency	Program Contingency	\$7,477,913.00	\$2,988,650.00	\$10,466,563.00
421.71.02.00.107421.752.0000	Land	Surveying	\$90,000.00	(\$87,650.00)	\$2,350.00
421.71.50.00.107421.752.0000	Land	Land	\$2,910,000.00	(\$2,901,000.00)	\$9,000.00
421.99.99.00.900421.752.0000	Program Contingency	Program Contingency	\$10,466,563.00	\$3,600,000.00	\$14,066,563.00
421.71.01.00.108421.752.0000	Tucker High School	Architect/Engineer	\$3,035,428.00	(\$500,000.00)	\$2,535,428.00
421.71.05.00.108421.752.0000	Tucker High School	Other Consultants	\$165,000.00	(\$100,000.00)	\$65,000.00
421.99.99.00.108421.752.0000	Tucker High School	Project Contingency	\$3,296,915.00	(\$3,000,000.00)	\$296,915.00



SPL OST III Capital Improvement Program


Budget Reallocations for This Period

Monthly Status Report

Cost Code	Code Description	Code Type	Current Budget	Change	Revised Budget
421.99.99.00.900421.752.0000	Program Contingency	Program Contingency	\$14,066,563.00	\$620,031.00	\$14,686,594.00
421.71.01.00.109421.752.0000	Woodward Elementary School	Architect/Engineer	\$143,505.00	(\$60,000.00)	\$83,505.00
421.71.03.00.109421.752.0000	Woodward Elementary School	Construction Testing	\$17,260.00	(\$17,260.00)	\$0.00
421.71.04.00.109421.752.0000	Woodward Elementary School	Abatement	\$30,000.00	(\$19,354.00)	\$10,646.00
421.71.05.00.109421.752.0000	Woodward Elementary School	Other Consultants	\$17,434.00	(\$10,000.00)	\$7,434.00
421.73.01.00.109421.752.0000	Woodward Elementary School	Construction	\$2,324,598.00	(\$300,000.00)	\$2,024,598.00
421.73.02.00.109421.752.0000	Woodward Elementary School	Miscellaneous	\$76,712.00	(\$65,000.00)	\$11,712.00
421.75.01.00.109421.752.0000	Woodward Elementary School	Utilities	\$25,000.00	(\$25,000.00)	\$0.00
421.75.02.00.109421.752.0000	Woodward Elementary School	Moving / Relocation	\$65,000.00	(\$23,417.00)	\$41,583.00
421.99.99.00.109421.752.0000	Woodward Elementary School	Project Contingency	\$108,738.00	(\$100,000.00)	\$8,738.00
421.99.99.00.900421.752.0000	Program Contingency	Program Contingency	\$14,686,594.00	\$154,050.00	\$14,840,644.00
421.71.03.00.1112421.752.0000	Midvale Elementary School	Construction Testing	\$15,769.00	(\$12,000.00)	\$3,769.00
421.71.04.00.1112421.752.0000	Midvale Elementary School	Abatement	\$56,329.00	(\$28,750.00)	\$27,579.00
421.71.05.00.1112421.752.0000	Midvale Elementary School	Other Consultants	\$10,627.00	(\$5,500.00)	\$5,127.00
421.73.01.00.1112421.752.0000	Midvale Elementary School	Construction	\$3,016,870.00	(\$58,500.00)	\$2,958,370.00
421.73.02.00.1112421.752.0000	Midvale Elementary School	Miscellaneous	\$25,460.00	(\$22,600.00)	\$2,860.00
421.75.01.00.1112421.752.0000	Midvale Elementary School	Utilities	\$10,000.00	(\$10,000.00)	\$0.00
421.75.02.00.1112421.752.0000	Midvale Elementary School	Moving / Relocation	\$30,000.00	(\$16,700.00)	\$13,300.00
421.99.99.00.900421.752.0000	Program Contingency	Program Contingency	\$14,840,644.00	\$525,000.00	\$15,365,644.00
421.73.01.00.1115421.752.0000	Cedar Grove High School	Construction	\$5,328,233.00	(\$350,000.00)	\$4,978,233.00
421.75.03.00.1115421.752.0000	Cedar Grove High School	Trailers	\$225,001.00	(\$175,000.00)	\$50,001.00
421.99.99.00.900421.752.0000	Program Contingency	Program Contingency	\$15,365,644.00	\$3,000,000.00	\$18,365,644.00
421.71.01.00.1118421.752.0000	Clarkston High School	Architect/Engineer	\$721,378.00	(\$100,000.00)	\$621,378.00
421.71.04.00.1118421.752.0000	Clarkston High School	Abatement	\$183,143.00	(\$150,000.00)	\$33,143.00
421.73.01.00.1118421.752.0000	Clarkston High School	Construction	\$12,002,960.00	(\$2,255,000.00)	\$9,747,960.00
421.73.02.00.1118421.752.0000	Clarkston High School	Miscellaneous	\$106,983.00	(\$50,000.00)	\$56,983.00
421.74.01.00.1118421.752.0000	Clarkston High School	Security	\$75,000.00	(\$50,000.00)	\$25,000.00
421.75.01.00.1118421.752.0000	Clarkston High School	Utilities	\$165,000.00	(\$125,000.00)	\$40,000.00

SPL OST III Capital Improvement Program

Budget Reallocations for This Period



Monthly Status Report

Cost Code	Code Description	Code Type	Current Budget	Change	Revised Budget
421.75.02.00.118421.752.0000	Clarkston High School	Moving / Relocation	\$100,000.00	(\$45,000.00)	\$55,000.00
421.99.99.00.118421.752.0000	Clarkston High School	Project Contingency	\$305,325.00	(\$225,000.00)	\$80,325.00
421.99.99.00.900421.752.0000	Program Contingency	Program Contingency	\$18,365,644.00	\$720,808.00	\$19,086,452.00
421.71.02.00.119421.752.0000	Druid Hills High School	Surveying	\$18,250.00	(\$10,000.00)	\$8,250.00
421.73.02.00.119421.752.0000	Druid Hills High School	Miscellaneous	\$270,000.00	(\$195,000.00)	\$75,000.00
421.75.01.00.119421.752.0000	Druid Hills High School	Utilities	\$15,000.00	(\$8,990.00)	\$6,010.00
421.75.03.00.119421.752.0000	Druid Hills High School	Trailers	\$36,632.00	(\$6,818.00)	\$29,814.00
421.75.04.00.119421.752.0000	Druid Hills High School	FF&E	\$1,421,613.00	(\$500,000.00)	\$921,613.00
421.99.99.00.900421.752.0000	Program Contingency	Program Contingency	\$19,086,452.00	\$1,000,240.00	\$20,086,692.00
421.71.03.00.130421.752.0000	McLendon Elementary School	Construction Testing	\$14,087.00	(\$14,087.00)	\$0.00
421.71.05.00.130421.752.0000	McLendon Elementary School	Other Consultants	\$13,522.00	(\$13,522.00)	\$0.00
421.73.01.00.130421.752.0000	McLendon Elementary School	Construction	\$2,837,189.00	(\$847,000.00)	\$1,990,189.00
421.74.01.00.130421.752.0000	McLendon Elementary School	Security	\$10,000.00	(\$10,000.00)	\$0.00
421.75.01.00.130421.752.0000	McLendon Elementary School	Utilities	\$25,000.00	(\$25,000.00)	\$0.00
421.75.02.00.130421.752.0000	McLendon Elementary School	Moving / Relocation	\$50,000.00	(\$10,631.00)	\$39,369.00
421.99.99.00.130421.752.0000	McLendon Elementary School	Project Contingency	\$83,044.00	(\$80,000.00)	\$3,044.00
421.99.99.00.900421.752.0000	Program Contingency	Program Contingency	\$20,086,692.00	\$171,501.00	\$20,258,193.00
421.71.01.00.212421.752.0000	Nancy Creek Elementary School	Architect/Engineer	\$36,279.00	(\$22,154.00)	\$14,125.00
421.71.03.00.212421.752.0000	Nancy Creek Elementary School	Construction Testing	\$1,500.00	(\$1,500.00)	\$0.00
421.71.04.00.212421.752.0000	Nancy Creek Elementary School	Abatement	\$12,000.00	(\$12,000.00)	\$0.00
421.71.05.00.212421.752.0000	Nancy Creek Elementary School	Other Consultants	\$2,837.00	(\$316.00)	\$2,521.00
421.73.01.00.212421.752.0000	Nancy Creek Elementary School	Construction	\$611,313.00	(\$112,854.00)	\$498,459.00
421.73.02.00.212421.752.0000	Nancy Creek Elementary School	Miscellaneous	\$1,500.00	(\$1,165.00)	\$335.00
421.99.99.00.212421.752.0000	Nancy Creek Elementary School	Project Contingency	\$21,512.00	(\$21,512.00)	\$0.00
421.99.99.00.900421.752.0000	Program Contingency	Program Contingency	\$20,258,193.00	\$218,134.00	\$20,476,327.00
421.71.01.00.215421.752.0000	DeKalb High School of Technology	Architect/Engineer	\$31,043.00	(\$18,783.00)	\$12,260.00
421.71.02.00.215421.752.0000	DeKalb High School of Technology	Surveying	\$6,000.00	(\$6,000.00)	\$0.00
421.71.03.00.215421.752.0000	DeKalb High School of Technology	Construction Testing	\$1,500.00	(\$1,500.00)	\$0.00
421.71.05.00.215421.752.0000	DeKalb High School of Technology	Other Consultants	\$1,438.00	(\$160.00)	\$1,278.00



Budget Reallocations for This Period

Cost Code	Code Description	Code Type	Current Budget	Change	Revised Budget
421.73.01.00.215421.752.0000	DeKalb High School of Technology	Construction	\$499,713.00	(\$168,965.00)	\$330,748.00
421.73.02.00.215421.752.0000	DeKalb High School of Technology	Miscellaneous	\$1,500.00	(\$1,152.00)	\$348.00
421.99.99.00.215421.752.0000	DeKalb High School of Technology	Project Contingency	\$21,574.00	(\$21,574.00)	\$0.00
421.99.99.00.900421.752.0000	Program Contingency	Program Contingency	\$20,476,327.00	\$424,306.00	\$20,900,633.00
421.71.01.00.216421.752.0000	Eldridge L. Miller Elementary School	Architect/Engineer	\$46,362.00	(\$30,962.00)	\$15,400.00
421.71.03.00.216421.752.0000	Eldridge L. Miller Elementary School	Construction Testing	\$1,500.00	(\$722.00)	\$778.00
421.71.05.00.216421.752.0000	Eldridge L. Miller Elementary School	Other Consultants	\$3,591.00	(\$400.00)	\$3,191.00
421.73.01.00.216421.752.0000	Eldridge L. Miller Elementary School	Construction	\$781,093.00	(\$347,857.00)	\$433,236.00
421.73.02.00.216421.752.0000	Eldridge L. Miller Elementary School	Miscellaneous	\$1,500.00	(\$1,152.00)	\$348.00
421.99.99.00.216421.752.0000	Eldridge L. Miller Elementary School	Project Contingency	\$43,213.00	(\$43,213.00)	\$0.00
421.99.99.00.900421.752.0000	Program Contingency	Program Contingency	\$20,900,633.00	\$1,816,317.00	\$22,716,950.00
421.71.01.00.226421.752.0000	Chamblee Middle School	Architect/Engineer	\$98,040.00	(\$98,040.00)	\$0.00
421.71.03.00.226421.752.0000	Chamblee Middle School	Construction Testing	\$1,500.00	(\$1,500.00)	\$0.00
421.71.05.00.226421.752.0000	Chamblee Middle School	Other Consultants	\$1,277.00	(\$1,277.00)	\$0.00
421.73.01.00.226421.752.0000	Chamblee Middle School	Construction	\$1,634,000.00	(\$1,634,000.00)	\$0.00
421.73.02.00.226421.752.0000	Chamblee Middle School	Miscellaneous	\$1,500.00	(\$1,500.00)	\$0.00
421.99.99.00.226421.752.0000	Chamblee Middle School	Project Contingency	\$163,683.00	(\$80,000.00)	\$83,683.00
Total:			\$270,499,230.00	\$0.00	\$270,499,230.00

* There were no Budget Reallocations for This Period.
