

Dekalb County School System



Capital Improvements Team Progress & Status Report

Allgood ES



Lakeside HS



Cross Keys HS



Glen Haven ES

May 2011



Table of Contents

1. Executive Summary
2. SPLOST III Funding
3. Program Financial Summary
4. Project Financial Summary
5. Project Status by Phase
6. Program Change Order Details
7. Local School Priority Request Projects
8. Site Improvement Projects
9. Program Master Schedule
10. Project Detail Status
11. Project Bid List
12. Budget Reallocations Approved This Period

SPLOST III Capital Improvement Program

Monthly Status Report

Glossary of Construction and CIP Terms

This glossary lists some of the terms used throughout construction and the capital improvement program.

ADA	The Americans with Disabilities Act gives civil rights protection to individuals with disabilities similar to those provided to individuals on the basis of race, color, sex, national origin, age, and religion. It guarantees equal opportunity for individuals with disabilities in public accommodations, employment, transportation, state and local government services, and telecommunications.
Addendum	(Addenda) Written information adding to, clarifying or modifying the bidding documents. An addendum is generally issued by the owner to the contractor during the bidding process and as such, addenda are intended to become part of the contract documents when the construction contract is executed.
Alternate Bid	Amount stated in the bid to be added or deducted from the base bid amount proposed for alternate materials and/or methods of construction.
Application for Payment	Contractor's written request for payment for completed portions of the work and, for materials delivered or stored and properly labeled for the respective project.
BAFO	Best And Final Offer. During contract negotiations, this is a term used to describe quote submissions from vendors to the project owner.
Bid	An offer or proposal of a price, including the amount offered or proposed.
Bid Form	A standard written form furnished to all bidders for the purpose of obtaining the requested information and required signatures from the authorized bidding representatives.
Bid Opening	The actual process of opening and tabulating bids submitted within the prescribed bid date/time and conforming with the bid procedures. A Bid Opening can be open (where the bidders are permitted to attend) or closed (where the bidders are not permitted to attend).
Bid Price	The stipulated sum stated in the bidder's bid.
Bidding Documents	The published advertisement or written invitation to bid, instructions to bidders, the bid form and the proposed contract documents including any acknowledged addenda issued prior to receipt of bids.
Building Process	A term used to express every step of a construction project from the conception to final acceptance and occupancy.
Change Order	A written document authorizing a change in the work or an adjustment in the contract sum or the contract time. A change order may be signed by the architect or engineer, provided they have written authority from the owner for such procedure and that a copy of such written authority is furnished to the contractor upon request. The contract sum and the contract time may be changed only by change order. A change order may be in the form of additional compensation or time; or less compensation or time known as a Deduction (from the contract) the amount deducted from the contract sum by change order.
Facility or Site Analysis	A visual inspection of a building and on-site improvements for functional or physical deterioration; prepare optional Replacement Cost Estimate for making recommendations to improve functional and physical deficiencies to increase market value; AND/OR prepare a Reserve Study over five (5) years to increase Net Operating Income (NOI) for the facility.
General Conditions	A written portion of the contract documents set forth by the owner stipulating the contractor's minimum acceptable performance requirements including the rights, responsibilities and relationships of the parties involved in the performance of the contract. General conditions are usually included in the book of specifications but are sometimes found in the architectural drawings.
Indirect Cost (or expense)	A contractor's or consultant's overhead expense; expenses indirectly incurred and not chargeable to a specific project or task. The terms indirect costs and soft costs are synonymous.
Lump Sum Contract	A written contract between the owner and contractor wherein the owner agrees to pay the contractor a specified sum of money for completing a scope of work consisting of a variety of unspecified items or work.
Plans	A term used to represent all drawings including sections and details; and any supplemental drawings for complete execution of a specific project.
Preliminary Drawings	The drawings that precede the final approved drawings. Usually these drawings are stamped or titled "PRELIMINARY"; and the "PRELIMINARY" is removed from the drawings upon being reviewed and approved by the owner.
Pre-qualification of prospective bidders	A screening process wherein the owner or his/her appointed representative gathers background information from a contractor or construction professional for selection purposes. Qualifying considerations include competence, integrity, dependability, responsiveness, bonding rate, bonding capacity, work on hand, similar project experience, and other specific owner requirements.

SPLOST III Capital Improvement Program

Monthly Status Report

Glossary of Construction and CIP Terms

R.F.I.	An abbreviation for Request for Information. A written request from a contractor to the owner or architect for clarification or information about the contract documents following contract award.	Subb An abbreviation for Subcontractor.
RFP	1. An abbreviation for Request for Proposal. 2. A written request from the requestor (usually the owner or a contractor) to a contractor, design professional or subcontractor for an estimate or cost proposal. The RFP usually contains a specific scope of work.	Subcontract A written form of agreement between the prime or main contractor and another contractor or supplier for the satisfactory performance of services or delivery or material as set forth in the plans and specifications for a specific project.
Safety Report	The Occupational Safety and Health Act of 1970 clearly states the common goal of safe and healthful working conditions. A Safety Report is prepared following a regularly scheduled project safety inspection of the specific project.	Subcontractor A qualified subordinate contractor to the prime or main contractor.
Schedule of Values	A statement furnished by the contractor to the architect or engineer reflecting the portions of the contract sum allotted for the various parts of the work and used as the basis for reviewing the contractor's applications for progress payments.	TM An abbreviation for a contracting method called Time and Materials. A written agreement between the owner and the contractor wherein payment is based on the contractor's actual cost for labor, equipment, materials, and services plus a fixed add-on amount to cover the contractor's overhead and profit.
Schematic	A preliminary sketch or diagram representing the proposed intent of the designer.	Unit Price Contract A written contract wherein the owner agrees to pay the contractor a specified amount of money for each unit of work successfully completed as set forth in the contract.
Schematic Design Phase	The first phase of the architect's basic services in which the architect consults with the owner to ascertain the requirements of the project and prepares schematic design studies consisting of drawings and other documents showing the scale and project components for the owner's approval.	Variance This report uses the term variance to indicate the calculation of the current budget less the forecasted cost at completion. A positive variance amount does not indicate that funds are available for use on additional projects. The original scope of work must be completed before funds can be reallocated.
Scheme	A chart, a diagram, or an outline of a system being proposed.. An orderly combination of related construction systems and components for a specific project or purpose.	Zoning Restrictions of areas or regions of land within specific geographical areas based on permitted building size, character, and uses as established by governing urban authorities.
Scope of Work	A written range of view or action; outlook; hence, room for the exercise of faculties or function; capacity for achievement; all in connection with a designated project.	Zoning Permit A document issued by a governing urban authority permitting land to be used for a specific purpose.
Special Conditions		
	A section of the conditions of the contract, other than the General Conditions and Supplementary Conditions, which may be prepared for a particular project. Specific clauses setting forth conditions or requirements peculiar to the project under consideration, and covering work or materials involved in the proposal and estimate, but not satisfactorily covered by the General Conditions. (See General Conditions)	
Structural Design		
	A term used to represent the proportioning of structural members to carry loads in a building structure.	

SPL OST III Capital Improvement Program

Monthly Status Report

Glossary of Construction and CIP Terms

Construction Delivery Methods

Design/Bid/Build

Under this traditional method, an architectural firm is hired and serves as the owner's agent. Although the firm may have numerous responsibilities, including the selection of consultants, its primary responsibility is to provide and oversee the design and construction documents for the project. As the design progresses, cost estimates are periodically prepared by the architectural firm and external cost estimators. Once the construction documents and specifications are completely finished, and other requirements of the owner have been met, the project is bid and subsequently awarded to the Bidder whose bid is the lowest responsive responsible bid.

Design/Propose/Build

Under this traditional method, an architectural firm is hired and serves as the owner's agent. Although the firm may have numerous responsibilities, including the selection of consultants, its primary responsibility is to provide and oversee the design and construction documents for the project. As the design progresses, cost estimates are periodically prepared by the architectural firm and external cost estimators. Once the construction documents and specifications are completely finished, and other requirements of the owner have been met, the project is solicited as a Request for Proposals and subsequently awarded to the Offeror whose proposal is most advantageous to the Board of Education.

Construction Manager at Risk

This system of delivery is similar to that of Design/Bid/Build with three key differences. First, a construction manager is hired during the preconstruction phase to manage the construction process, including the selection of subcontractors. Second, through coordination between the architect and construction manager, the design and construction phases can be overlapped thereby expediting the delivery process. Third, the construction manager, who is responsible for quality control, scheduling and the estimate of construction costs, provides a guaranteed maximum price for the project.

Design/Build

Rather than hiring an architect, under Design/Build the owner enters into a contract with a single firm with design and building capabilities or a construction entity that employs the architect as a consultant. As with the aforementioned delivery system, a guaranteed maximum price for the entire project may be provided, construction management techniques to overlap design and construction phases are utilized, and the overall project delivery is expedited.

CIP Project Phase Descriptions

Planning/ Programming

The research and decision-making process that identifies the scope of work to be designed.

Design

This phase consists of the development. Detail scope, program requirements, budgets, and schedules are developed.

Procurement

This is the phase where architectural and/or general contractor services are procured for a project. It may involve the RFP, bidding, award, contract review, and contract execution activities.

Construction

Construction begins once the project has been awarded to the contractor.

Close-out

The final inspection, submission of necessary documentation, acceptance, and concluding payment on a construction project, as required by the contract documents.

Completed

All design, construction, and close-out requirements for the project have been completed and accepted by the owner.

On-Going SPL OST Activity

This phase relates to activities within the CIP that are on-going throughout the length of the program. These projects are generally supporting activities.

On Hold

A project is placed on hold when the detailed scope, budget, or necessity may need to be further defined.

Deemed Unnecessary

A project within the CIP may be deemed unnecessary in situations where the project may have already been completed using other funds, the project may have been incorporated into larger construction projects, or the project may no longer be required due to current applicability

SPL OST III Capital Improvement Program

Monthly Status Report

Executive Summary May 2011

This report summarizes the DeKalb County School System's SPL OST III Capital Improvement Program through May 2011. Sales tax revenue collections are ahead of the estimated schedule. Over 76% of the total projects within the program are under construction, in close-out, or completed. Several projects are on hold and deemed unnecessary pending the project's current applicability and necessity.

School Design Highlights


ADA projects within the program are under design. Final scope definition and review will occur over the summer months.

Knollwood Elementary School - HVAC & ADA design is complete and pending construction contract execution. Stone Mountain High School - Career Technology Lab Renovation design is complete and pending construction contract execution.

School Construction Highlights

Hambrick Elementary School - roofing project is under construction and is scheduled for completion in the fall.

Woodridge Elementary School - Roof project is approaching final completion. Several local school priority request projects are underway and will be completed over the summer months. These projects include bulk purchase plumbing fixtures and metal lockers and carpet replacement at various facilities.

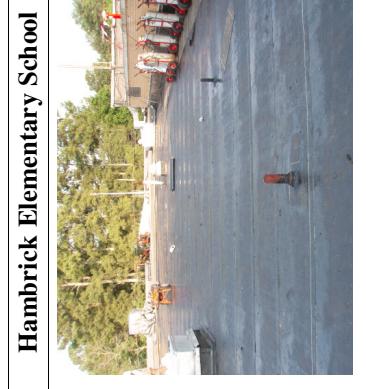

Program Status		No. of Projects	Current Budget	% Budget
Planning & Programming	4	\$2,172,372	0%	
Design	14	\$54,439,542	11%	
Procurement	4	\$7,507,000	1%	
Construction	27	\$79,340,874	15%	
Close-out	24	\$184,247,804	36%	
Completed	100	\$26,893,991	5%	
On-Going SPLOST Activity	10	\$146,038,139	28%	
On Hold	10	\$12,300,862	2%	
Deemed Unnecessary	6	\$529,379	0%	
Total Projects:	199	\$513,469,963	100%	

Revenue Status	
Sales tax receipts are 13% ahead of schedule. This has allowed projects to start on time, and some projects have been moved ahead of schedule.	

Expenditures Status	
The Monthly CIP expenditures are anticipated at \$9.5 million per month for the 2011 calendar year. This will have the CIP anticipated total expenditures at 75% complete by the end of 2011 calendar year.	

CIP Current Budget:	\$513,469,963
Committed Costs:	\$398,586,467
Expenditures:	\$300,605,453

SPLOST III Capital Improvement Program

SPLOST III Funding

The sales tax collections through May 2011 are:
 Expenditures through this time period are:

\$369,021,025
 \$300,605,453

Monthly Status Report



SPLOST III Capital Improvement Program

The sales tax collections through May 2011 are:
 Expenditures through this time period are:

\$369,021,025
 \$300,605,453

SPLOST III Funding

Planned SPLOST III

Budgeted SPLOST III

Actual SPLOST III

% Collected

Month

Total

SPLOST III Actual Expenditures

Month

Total

SPLOST III Actual Expenditures

Month

Total

SPLOST III Actual Expenditures

Month

Total

SPLOST III Actual Expenditures

Month

Total

SPLOST III Actual Expenditures

Month

Total

SPLOST III Actual Expenditures

Month

Total

Month

SPLOST III Capital Improvement Program

SPLOST III Funding

The sales tax collections through May 2011 are: \$369,021,025
 Expenditures through this time period are: \$300,605,453

Monthly Status Report

Month	Planned SPLOST III		Budgeted SPLOST III		Actual SPLOST III		% Collected		SPLOST III Actual Expenditures
	Month	Total	Month	Total	Month	Total	Month	Total	
May-2010	\$8,269,952	\$257,081,908	\$7,677,261	\$238,657,299	\$7,650,002	\$272,400,473	100%	114%	\$5,166,802
Jun-2010	\$8,661,111	\$265,743,019	\$8,040,386	\$246,697,685	\$8,389,540	\$280,790,013	104%	114%	\$27,778,632
Jul-2010	\$8,255,996	\$273,999,014	\$7,664,305	\$254,361,990	\$7,643,256	\$288,433,269	100%	113%	\$1,125,087
Aug-2010	\$8,240,993	\$282,240,007	\$7,650,377	\$262,012,368	\$7,976,221	\$296,409,490	104%	113%	\$211,525,699
Sep-2010	\$8,342,170	\$290,582,178	\$7,744,304	\$269,756,671	\$8,546,697	\$304,956,187	110%	113%	\$11,693,428
Oct-2010	\$9,322,599	\$299,904,777	\$8,654,467	\$278,411,138	\$7,871,571	\$312,827,758	91%	112%	\$223,219,127
Nov-2010	\$8,644,081	\$308,548,858	\$8,024,577	\$286,435,715	\$7,884,395	\$320,712,153	98%	112%	\$234,608,985
Dec-2010	\$7,834,072	\$316,382,930	\$7,272,620	\$293,708,335	\$7,397,636	\$328,109,789	102%	112%	\$251,648,112
Jan-2011	\$8,345,683	\$324,728,613	\$7,747,565	\$301,455,900	\$9,428,375	\$337,538,164	122%	112%	\$17,039,127
Feb-2011	\$10,134,573	\$334,863,186	\$9,408,249	\$310,864,149	\$7,474,784	\$345,012,947	79%	111%	\$263,203,116
Mar-2011	\$9,366,493	\$344,229,679	\$8,695,215	\$319,559,364	\$8,020,271	\$353,033,218	92%	110%	\$12,543,023
Apr-2011	\$9,377,000	\$353,606,679	\$8,704,969	\$328,264,332	\$8,131,029	\$361,164,248	93%	110%	\$275,746,138
May-2011	\$9,031,024	\$362,637,703	\$8,383,788	\$336,648,121	\$7,856,777	\$369,021,025	94%	110%	\$283,026,119
Jun-2011	\$8,351,729	\$370,989,431	\$7,753,177	\$344,401,298					\$4,520,080
Jul-2011	\$8,874,946	\$379,864,377	\$8,238,896	\$352,640,194					\$287,546,199
Aug-2011	\$9,591,730	\$389,456,107	\$8,904,310	\$361,544,504					\$6,504,652
Sep-2011	\$10,029,208	\$399,485,315	\$9,310,435	\$370,854,939					\$294,050,851
Oct-2011	\$9,879,504	\$409,364,820	\$9,171,460	\$380,026,399					\$6,554,602
Nov-2011	\$11,373,160	\$420,737,980	\$10,558,069	\$390,584,468					\$300,605,453
Dec-2011	\$6,909,225	\$427,647,205	\$6,414,054	\$396,998,522					
Jan-2012	\$8,372,755	\$436,019,960	\$7,772,696	\$404,771,218					
Feb-2012	\$10,052,757	\$446,072,717	\$9,332,296	\$414,103,514					
Mar-2012	\$9,109,914	\$455,182,631	\$8,457,025	\$422,560,539					
Apr-2012	\$8,948,472	\$464,131,103	\$8,307,153	\$430,867,692					
May-2012	\$8,672,337	\$472,803,440	\$8,050,808	\$438,918,500					
Jun-2012	\$10,361,622	\$483,165,062	\$9,619,025	\$448,537,525					
Jul-2012	\$10,037,552	\$493,202,614	\$9,318,181	\$457,855,706					
Aug-2012	\$8,773,040	\$501,975,654	\$8,144,294	\$466,000,000					

SPL OST III Capital Improvement Program

Program Financial Summary

Monthly Status Report

Budget Category

Current Budget

Original Contract

Executed Change Orders

Current Contract

Paid To Date

Contract Balance

Approved CORs

Current Contract Plus CORs

Uncommitted

Budget Category	Current Budget	Original Contract	Executed Change Orders	Current Contract	Paid To Date	Contract Balance	Approved CORs	Current Contract Plus CORs	Uncommitted
-----------------	----------------	-------------------	------------------------	------------------	--------------	------------------	---------------	----------------------------	-------------

CIT Managed									
-------------	--	--	--	--	--	--	--	--	--

Architect/Engineer	\$16,700,325	\$13,302,543		\$1,726,170	\$15,028,713	\$9,659,756	\$5,368,957	\$6,500	\$15,035,213
Surveying	\$764,771	\$443,043			\$443,043	\$418,303	\$24,740	\$0	\$443,043
Construction Testing	\$1,727,912	\$926,584		\$24,554	\$951,139	\$868,242	\$82,897	\$0	\$951,139
Abatement	\$1,535,081	\$1,008,506			\$1,008,506	\$934,560	\$73,946	\$0	\$1,008,506
Other Consultants	\$2,887,454	\$2,216,043		\$2,477	\$2,218,520	\$1,951,940	\$266,580	\$1,500	\$2,220,020
Management Fees	\$15,374,724	\$15,374,724			\$15,374,724	\$14,042,036	\$1,332,688	\$0	\$15,374,724
Construction	\$293,980,841	\$202,791,058		\$31,179,367	\$233,970,425	\$202,058,639	\$31,911,786	\$342,705	\$234,313,130
Construction Infrastructure	\$1,431,200	\$137,475			\$137,475	\$120,014	\$17,461	\$0	\$137,475
Miscellaneous	\$58,962,025	\$56,154,593			\$56,154,593	\$607,175	\$55,547,418	\$0	\$56,154,593
Security	\$1,696,839	\$1,033,850			\$1,033,850	\$925,496	\$108,354	\$0	\$1,033,850
Utilities	\$1,563,510	\$145,813			\$145,813	\$133,441	\$12,372	\$0	\$145,813
Moving / Relocation	\$3,089,105	\$1,516,218			\$1,516,218	\$1,500,173	\$16,045	\$5,313	\$1,521,531
Trailers	\$1,004,256	\$477,043			\$477,043	\$259,722	\$217,321	\$0	\$477,043
Contingency	\$37,694,671	\$10,640,000			\$10,640,000	\$0	\$10,640,000	\$0	\$10,640,000
CIT Managed	\$438,412,734	\$306,167,493		\$32,932,568	\$339,100,062	\$233,479,497	\$105,620,565	\$356,018	\$339,456,080
DOSS Managed									

Land	\$3,285,085	\$285,084		\$285,084	\$285,084	\$0	\$0	\$285,084	\$500,002
FF&E	\$13,640,138	\$8,572,885		\$8,572,885	\$8,449,268	\$123,617	\$0	\$8,572,885	\$179,990
Technology	\$46,132,006	\$38,284,187		\$38,284,187	\$38,162,063	\$122,124	\$0	\$38,284,187	\$1,432,343
Transportation	\$12,000,000	\$11,988,231		\$11,988,231	\$11,988,231	\$0	\$0	\$11,988,231	\$11,769
DOSS Managed	\$75,057,229	\$59,130,387		\$59,130,387	\$58,884,646	\$245,741	\$0	\$59,130,387	\$2,124,104
Grand Total	\$513,469,263	\$365,297,880		\$32,932,568	\$398,230,449	\$292,364,143	\$105,866,306	\$356,018	\$398,586,467
									\$28,348,110

SPL OST III Capital Improvement Program

Project Financial Summary

Monthly Status Report

Budget Category

Budget Category	Project Number	Current Budget	Original Contract	Executed Change Orders	Current Contract	Paid To Date	Contract Balance	Approved CORs	Current Contract Plus CORs	Uncommitted
ADA Group A- Main Project	421-301	\$81,808	\$91,389	\$0	\$91,389	\$90,692	\$697	\$0	\$91,389	(\$9,581)
ADA Group A-2A	421-301-021	\$56,574	\$533,490	\$23,284	\$556,774	\$256,774	\$0	\$0	\$556,774	\$4,800
ADA Group A-2B	421-301-022	\$678,336	\$650,000	\$28,336	\$678,336	\$448,525	\$229,811	\$0	\$678,336	\$0
ADA Group B- Main Project	421-302	\$510,448	\$1,935	\$0	\$1,935	\$1,935	\$0	\$0	\$1,935	\$0
ADA Group B-1	421-302-001	\$496,000	\$495,645	\$0	\$495,645	\$405,589	\$90,056	\$2,604	\$498,249	(\$2,249)
ADA Group B-2	421-302-002	\$407,299	\$388,199	(\$23,231)	\$364,968	\$355,004	\$9,964	\$38,396	\$403,364	\$3,935
ADA Group B-3	421-302-003	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
ADA Group C- Main Project	421-303	\$1,023,071	\$57,521	\$0	\$57,521	\$56,701	\$820	\$0	\$57,521	\$2,343
ADA Group D	421-304	\$337,051	\$2,343	\$0	\$2,343	\$2,343	\$0	\$0	\$2,343	\$0
ADA Group E	421-305	\$427,202	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Administrative & Instructional Complex (AIC)	421-124	\$31,824,966	\$26,955,036	\$4,175,524	\$31,130,560	\$30,920,713	\$209,847	\$69,307	\$31,199,867	\$111,846
Allgood ES - ADA	421-301-010	\$32,556	\$32,556	\$0	\$32,556	\$32,556	\$0	\$0	\$32,556	\$0
Allgood ES - Roof	421-217	\$585,240	\$448,759	\$25,303	\$474,062	\$405,739	\$68,323	\$0	\$474,062	\$0
Allgood ES- Kitchen	421-341-043	\$400,000	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$400,000
Ashford Park ES- ADA	421-301-007	\$54,200	\$44,924	\$0	\$44,924	\$0	\$44,924	\$0	\$44,924	\$9,276
Atherton ES- Chiller Replacement	421-341-022	\$123,176	\$118,336	\$4,840	\$123,176	\$123,176	\$0	\$0	\$123,176	\$0
Avondale ES - ADA	421-301-005	\$22,406	\$22,406	\$0	\$22,406	\$22,406	\$0	\$0	\$22,406	\$0
Avondale ES - Roof	421-209	\$578,746	\$596,221	(\$17,475)	\$578,746	\$578,379	\$367	\$0	\$578,746	\$0
Basin Heaters	421-321-014	\$345,500	\$345,500	\$0	\$345,500	\$345,500	\$0	\$0	\$345,500	\$0
Bob Mathis ES - ADA	421-301-001	\$22,299	\$22,299	\$0	\$22,299	\$22,299	\$0	\$0	\$22,299	\$0
Brockett ES - Make-up Air Units	421-320-001	\$94,030	\$94,030	\$0	\$94,030	\$94,030	\$0	\$0	\$94,030	\$0
Bulk Purchase - Plumbing Fixtures	421-322-001	\$2,043,950	\$825,512	\$40,625	\$866,137	\$55,090	\$411,047	\$0	\$866,137	\$10,777
Bulk Purchase- Ceiling Tile and Grid	421-600-002	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Bulk Purchase- Fixed Audience Seating	421-600-006	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Bulk Purchase- Metal Lockers	421-600-003	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Bulk Purchase- Theatrical Lighting & Sound Syst	421-600-004	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Bulk Purchasing- Lighting	421-600-005	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Buses 1	421-401	\$3,479,453	\$3,479,453	\$0	\$3,479,453	\$3,479,453	\$0	\$0	\$3,479,453	\$0
Buses 2	421-402	\$4,536,167	\$4,524,398	\$0	\$4,524,398	\$4,524,398	\$0	\$0	\$4,524,398	\$11,769
Buses 3	421-403	\$3,984,380	\$3,984,380	\$0	\$3,984,380	\$3,984,380	\$0	\$0	\$3,984,380	\$0
Capital Improvement Team Compensation	421-650	\$15,374,724	\$15,374,724	\$0	\$15,374,724	\$14,042,036	\$1,332,688	\$0	\$15,374,724	\$0
Carpet Replacement - Multiple Schools (LSPR 1	421-341-031	\$10,237	\$0	\$10,237	\$0	\$10,237	\$0	\$0	\$10,237	\$0

SPL OST III Capital Improvement Program

Project Financial Summary

Monthly Status Report

Budget Category

Project Number

Current Budget

Original Contract

Executed Change Orders

Current Contract

Paid To Date

Contract Balance

Approved CORs

Current Contract Plus CORs

Uncommitted

Carpet Replacement - Multiple Schools (LSPR 2	421-341-040	\$30,667	\$29,836	\$0	\$29,836	\$29,836	\$0	\$0	\$29,836	\$831
Cedar Grove HS - HVAC, Lighting, Ceiling & Ro	421-115	\$6,211,315	\$4,834,297	\$336,162	\$5,170,459	\$4,556,751	\$613,703	\$0	\$5,170,459	\$695,856
Chamblee Charter HS - Lockers	421-341-014	\$50,000	\$43,457	\$0	\$43,457	\$0	\$43,457	\$0	\$43,457	\$6,543
Chamblee HS- New Replacement High School	421-117	\$11,152,507	\$3,177,362	\$0	\$3,177,362	\$75,606	\$3,101,756	\$1,500	\$3,178,862	\$510,761
Chamblee MS - Roof	421-226	\$83,683	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$83,683
Chamblee MS - Sound Panels	421-341-050	\$27,500	\$38,900	\$0	\$38,900	\$38,900	\$0	\$0	\$38,900	(\$11,400)
Chamblee MS- Mirror	421-341-049	\$960	\$960	\$0	\$960	\$960	\$0	\$0	\$960	\$0
Chamblee MS- Painting	421-341-042	\$145,000	\$9,135	\$0	\$9,135	\$0	\$9,135	\$0	\$9,135	\$135,865
Champion MS - ADA	421-301-020	\$15,362	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$15,362
Champion Theme MS - Roof	421-208	\$382,342	\$382,342	\$0	\$382,342	\$362,922	\$19,420	\$0	\$382,342	\$0
Champion Theme MS- Chiller Replacement	421-341-010	\$47,539	\$38,464	\$9,075	\$47,539	\$47,539	\$0	\$0	\$47,539	\$0
Chapel Hill ES- Chiller Replacement	421-341-009	\$69,964	\$69,964	\$0	\$69,964	\$69,964	\$0	\$0	\$69,964	\$0
Chapel Hill MS- Ceiling Tiles & Site Work	421-341-028	\$240,275	\$275	\$0	\$275	\$262	\$13	\$0	\$275	\$0
Chapel Hill MS- Track & Tennis Court	421-341-051	\$243,956	\$237,142	\$18,380	\$255,522	\$255,522	\$0	\$0	\$255,522	(\$11,566)
Chestnut Charter ES- Basketball Court Replacement	421-322-004	\$52,957	\$52,957	\$0	\$52,957	\$4,980	\$47,977	\$0	\$52,957	\$0
Chestnut ES - ADA	421-303-002	\$448,179	\$417,642	\$26,137	\$443,779	\$442,329	\$1,450	\$0	\$443,779	\$4,400
Clarkston Center- Roof	421-207	\$0	\$0	\$0	\$0	\$6,333	(\$6,333)	\$0	\$0	\$0
Clarkston HS - Renovation & Addition	421-118	\$12,275,194	\$9,632,672	\$812,970	\$10,445,642	\$6,233,058	\$4,212,584	\$113,278	\$10,558,920	\$194,303
CLEA 2008- Comprehensive Lighting Energy Au	421-600-001	\$98,032	\$98,032	\$0	\$98,032	\$98,032	\$0	\$0	\$98,032	\$0
Clifton ES - HVAC	421-114	\$172,792	\$172,792	\$0	\$172,792	\$172,792	\$0	\$0	\$172,792	\$0
Clifton ES- Ceiling Tiles	421-341-039	\$110,000	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$110,000
Columbia HS - SPLOST II Deferred	421-104	\$11,452,000	\$10,441,256	\$854,545	\$11,295,801	\$12,414,811	(\$1,119,010)	\$0	\$11,295,801	(\$6,661)
COPPS Debt Reduction	421-001	\$66,000,000	\$66,000,000	\$0	\$66,000,000	\$0	\$66,000,000	\$0	\$66,000,000	\$0
Corralwood Diagnostic Cir. - Renovation & Additi	421-213	\$423,427	\$365,263	\$0	\$365,263	\$149,263	\$216,000	\$0	\$365,263	\$58,164
Cross Keys HS - Renovation & Addition	421-106	\$18,612,631	\$2,573,190	\$14,760,494	\$17,333,684	\$16,201,809	\$1,131,875	\$44,082	\$17,377,766	\$227,552
DeKalb HS of Tech North - Roof	421-221	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
DeKalb HS of Tech South - Roof	421-215	\$352,288	\$351,428	\$0	\$351,428	\$340,818	\$10,610	\$0	\$351,428	\$860
DeKalb International Student Center- Canopy	421-341-047	\$2,000	\$9,340	\$0	\$9,340	\$1,000	\$8,340	\$0	\$9,340	(\$7,340)
Druif Hills HS - Renovation & Addition	421-119	\$18,633,137	\$18,243,673	(\$36,854)	\$18,206,819	\$16,877,386	\$1,329,433	\$0	\$18,206,819	\$221,068
DSA Relocation to Avondale HS - Modifications	421-123	\$5,563,715	\$4,635,500	\$118,869	\$4,754,369	\$4,700,729	\$53,640	\$47,317	\$4,801,686	\$530,529
DSA Relocation to Avondale HS - Renovations	421-123-002	\$4,265,700	\$255,042	\$49,266	\$304,608	\$141,718	\$162,890	\$0	\$304,608	\$0
Dunwoody HS - Renovation & Addition	421-120	\$20,530,480	\$15,855,086	\$2,344,532	\$18,199,618	\$16,462,398	\$1,737,220	\$32,058	\$18,231,676	\$76,316

SPL OST III Capital Improvement Program

Project Financial Summary

Monthly Status Report

Budget Category

Budget Category	Project Number	Current Budget	Original Contract	Executed Change Orders	Current Contract	Paid To Date	Contract Balance	Approved CORs	Current Contract Plus CORs	Uncommitted
Eagle Wood Academy- Replace Windows & Repa	421-321-011	\$55,435	\$55,435	\$0	\$55,435	\$55,435	\$0	\$0	\$55,435	\$0
East Campus - APHONE	421-341-026	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Eldridge L. Miller ES - Roof	421-216	\$452,953	\$477,453	(\$24,500)	\$452,953	\$452,953	\$0	\$0	\$452,953	\$0
Emergency Generators	421-321-015	\$3,800,000	\$443,992	\$0	\$443,992	\$78,584	\$365,408	\$0	\$443,992	\$8
Emergency HVAC Work	421-101	\$4,636,397	\$4,542,916	\$26,478	\$4,569,394	\$4,474,415	\$94,979	\$0	\$4,569,394	(\$33,997)
Energy Management System Update	421-322-002	\$948,000	\$948,000	\$0	\$948,000	\$948,000	\$0	\$0	\$948,000	\$0
Evansdale ES - Roof	421-218	\$647,608	\$520,953	\$0	\$520,953	\$6,142	\$514,811	\$0	\$520,953	\$0
Facilities Assessment	421-700	\$1,770,367	\$1,770,367	\$0	\$1,770,367	\$1,533,192	\$237,175	\$0	\$1,770,367	\$0
Fairlington ES- HVAC, Ceilings & Lighting	421-121	\$1,977,131	\$1,901,978	\$48,380	\$1,950,358	\$1,923,678	\$26,680	\$0	\$1,950,358	\$3,605
FF&E- LS PR 1 Q09	421-341-033	\$44,379	\$44,379	\$0	\$44,379	\$44,379	\$0	\$0	\$44,379	\$0
FF&E- LS PR 2Q09	421-341-048	\$21,100	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$21,100
Flat Shoals ES - Roof	421-219	\$764,826	\$539,871	\$0	\$539,871	\$7,000	\$532,871	\$0	\$539,871	\$0
Forrest Hills ES - HVAC	421-137	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
General Services Main Project	421-600	\$302,149	\$193,991	\$0	\$193,991	\$187,349	\$6,642	\$0	\$193,991	\$108,158
Glen Haven ES - ADA	421-301-016	\$93,771	\$93,771	\$0	\$93,771	\$93,771	\$0	\$0	\$93,771	\$0
Glen Haven ES - Roof	421-225	\$990,000	\$629,027	\$0	\$629,027	\$572,749	\$56,278	\$6,075	\$635,102	(\$6,075)
Glen Haven ES - Widen Drive	421-341-032	\$131,200	\$129,802	\$0	\$129,802	\$15,670	\$114,132	\$0	\$129,802	\$1,398
Glen Haven ES- Replace Toilet Fixtures & Carpet	421-321-004	\$94,950	\$94,950	\$0	\$94,950	\$94,950	\$0	\$0	\$94,950	\$0
Gresham Park ES - ADA	421-301-017	\$80,516	\$75,886	\$4,631	\$80,517	\$80,517	\$0	\$0	\$80,517	(\$1)
Gresham Park ES- Replace carpet in Media Cente	421-320-008	\$16,947	\$16,947	\$0	\$16,947	\$8,287	\$8,660	\$0	\$16,947	\$0
Hambrick ES - HVAC	421-136	\$1,871,891	\$72,500	\$0	\$72,500	\$5,438	\$67,062	\$0	\$72,500	\$0
Hambrick ES - Roof	421-223	\$1,090,000	\$663,766	\$0	\$663,766	\$8,122	\$655,644	\$0	\$663,766	(\$16,926)
Hawthorne ES - ADA	421-303-011	\$13,750	\$13,750	\$0	\$13,750	\$6,876	\$6,874	\$0	\$13,750	\$0
Hawthorne ES - Roof	421-224	\$1,100,000	\$8,470	\$0	\$8,470	\$8,122	\$348	\$0	\$8,470	\$0
Henderson Mill ES - Chiller Replacement	421-341-008	\$69,228	\$69,228	\$0	\$69,228	\$69,228	\$0	\$0	\$69,228	\$0
Henderson Mill ES - New Door	421-341-034	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Henderson Mill ES- Ceiling Tiles	421-341-046	\$3,911	\$3,911	\$0	\$3,911	\$3,911	\$0	\$0	\$3,911	\$0
Henderson MS- Classroom & Restroom Upgrades	421-320-002	\$128,052	\$164,715	\$0	\$164,715	\$164,715	\$0	\$0	\$164,715	(\$36,663)
Henderson MS- Gym Light Switches	421-341-013	\$6,670	\$6,670	\$0	\$6,670	\$6,670	\$0	\$0	\$6,670	\$0
Henderson MS- Hold-Opens & Toilets	421-341-052	\$75,278	\$74,800	\$0	\$74,800	\$75,720	(\$920)	\$0	\$74,800	\$478
Henderson MS- Repair/Replace uneven tile near r	421-320-007	\$2,985	\$2,985	\$0	\$2,985	\$2,985	\$0	\$0	\$2,985	\$0
Heritage Center - Roof	421-204	\$351,097	\$349,597	\$0	\$349,597	\$350,979	(\$1,382)	\$0	\$349,597	\$1,500

SPL OST III Capital Improvement Program

Project Financial Summary

Monthly Status Report

Budget Category

Budget Category	Project Number	Current Budget	Original Contract	Executed Change Orders	Current Contract	Paid To Date	Contract Balance	Approved CORs	Current Contract Plus CORs	Uncommitted
Hooper Alexander ES - HVAC & ADA	421-134	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Huntley Hills ES - Roof	421-220	\$0	\$0	\$0	\$0	\$2,380	(\$2,380)	\$0	\$0	\$0
Huntley Hills ES - Restroom Renovations	421-321-006	\$66,767	\$66,767	\$0	\$66,767	\$66,767	\$0	\$0	\$66,767	\$0
Idlwood ES - ADA	421-301-003	\$9,611	\$9,611	\$0	\$9,611	\$9,611	\$0	\$0	\$9,611	\$0
Idlwood ES- Carpet Replacement	421-341-001	\$1,325	\$1,325	\$0	\$1,325	\$1,325	\$0	\$0	\$1,325	\$0
Idlwood ES- Parking Lots	421-321-010	\$237,201	\$237,202	\$0	\$237,202	\$237,202	\$0	\$0	\$237,202	(\$1)
Indian Creek ES - ADA	421-301-013	\$23,948	\$23,948	\$0	\$23,948	\$23,948	\$0	\$0	\$23,948	\$0
Indian Creek ES - HVAC	421-139	\$1,164,368	\$50,150	\$0	\$50,150	\$7,522	\$42,628	\$0	\$50,150	\$0
Kelley Lake ES - Courtyard	421-341-041	\$10,000	\$12,800	\$0	\$12,800	\$12,800	\$0	\$0	\$12,800	(\$2,800)
Kingsley Charter ES- Media Center Furniture	421-341-003	\$18,194	\$18,194	\$0	\$18,194	\$18,194	\$0	\$0	\$18,194	\$0
Kingsley ES - ADA	421-301-004	\$8,600	\$13,927	(\$5,327)	\$8,600	\$8,600	\$0	\$0	\$8,600	\$0
Kittredge Magnet ES- Chiller Replacement	421-341-020	\$99,202	\$99,202	\$0	\$99,202	\$99,202	\$0	\$0	\$99,202	\$0
Knollwood ES - HVAC & ADA	421-132	\$1,662,372	\$1,650	\$0	\$1,650	\$0	\$1,650	\$0	\$1,650	\$69,920
Lakeside HS - Career Tech, ADA	421-125	\$24,289,410	\$20,861,161	\$760,090	\$21,621,251	\$3,718,933	\$17,902,318	\$19,507	\$21,640,758	\$567,946
Lakeside HS - Natatorium	421-341-012	\$293,903	\$274,511	\$13,995	\$288,506	\$271,394	\$17,112	\$0	\$288,506	\$5,397
Land	421-107	\$11,350	\$20,350	\$0	\$20,350	\$20,350	\$0	\$0	\$20,350	(\$9,000)
Laurel Ridge ES - ADA	421-301-006	\$67,396	\$67,396	\$0	\$67,396	\$67,396	\$0	\$0	\$67,396	\$0
Laurel Ridge- Replace Parking Lot & Tennis Cou	421-321-012	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Lithonia HS - Addition	421-126	\$0	\$25,488	\$0	\$25,488	\$25,488	\$0	\$0	\$25,488	(\$25,488)
Lithonia MS - Renovations	421-341-044	\$207,000	\$197,245	\$0	\$197,245	\$0	\$197,245	\$0	\$197,245	(\$194,455)
Lithonia MS - Security Cameras	421-341-045	\$85,982	\$85,982	\$0	\$85,982	\$100,398	(\$14,416)	\$0	\$85,982	\$0
Lithonia MS- Band Room Carpet	421-341-004	\$6,028	\$6,028	\$0	\$6,028	\$6,028	\$0	\$0	\$6,028	\$0
LSPR 1- Main Project	421-320	\$163,176	\$165,862	\$0	\$165,862	\$165,862	\$0	\$0	\$165,862	(\$2,686)
LSPR 2- Main Project	421-341	\$617,138	\$108,848	\$0	\$108,848	\$88,875	\$19,973	\$0	\$108,848	(\$53,949)
Marbut/Bouie ES- New Multi-purpose Bldg. Restr	421-321-003	\$239,039	\$232,941	\$6,098	\$239,039	\$239,039	\$0	\$0	\$239,039	\$0
Margaret Harris Center- Paving	421-321-007	\$31,232	\$31,232	\$0	\$31,232	\$31,232	\$0	\$0	\$31,232	\$0
Margaret Harris Center- Washing Machines	421-321-007D	\$9,050	\$9,050	\$0	\$9,050	\$9,050	\$0	\$0	\$9,050	\$0
Margaret Harris- Dryers	421-321-007E	\$704	\$704	\$0	\$704	\$704	\$0	\$0	\$704	\$0
Margaret Harris ES- Door Release System	421-341-005	\$6,748	\$6,748	\$0	\$6,748	\$6,748	\$0	\$0	\$6,748	\$0
Margaret Harris- Exterior Facade & RR Renovati	421-321-007B	\$326,943	\$320,440	\$6,503	\$326,943	\$326,943	\$0	\$0	\$326,943	\$0
Martin Luther King, Jr. HS - Addition	421-127	\$9,889,279	\$465,639	\$0	\$465,639	\$143,937	\$321,702	\$0	\$465,639	\$0
McLendon ES - HVAC & ADA	421-130	\$2,098,390	\$1,887,320	\$164,673	\$2,051,993	\$2,046,643	\$5,350	\$15,916	\$2,067,909	\$7,381

SPL OST III Capital Improvement Program

Project Financial Summary

Monthly Status Report

Budget Category

Budget Category	Project Number	Current Budget	Original Contract	Executed Change Orders	Current Contract	Paid To Date	Contract Balance	Approved CORs	Current Contract Plus CORs	Uncommitted
McLendon ES- Basketball Court, Paint & Blinds	421-341-030	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
McNair HS - SPLOST II Deferred	421-105	\$869,475	\$844,547	\$0	\$844,547	\$844,323	\$224	\$0	\$844,547	\$24,928
McNair MS- Ceiling Tile Replacement	421-341-015	\$49,058	\$49,058	\$0	\$49,058	\$49,058	\$0	\$0	\$49,058	\$0
McNair MS- Chiller Replacement	421-341-023	\$192,000	\$192,000	\$0	\$192,000	\$192,000	\$0	\$0	\$192,000	\$0
Middle School- Additional Parking Lot Lighting	421-341-038	\$200,382	\$200,382	\$0	\$200,382	\$200,382	\$0	\$0	\$200,382	\$0
Midvale ES - HVAC, Roof, ADA	421-112	\$3,070,205	\$2,935,201	\$71,919	\$3,007,120	\$2,981,327	\$25,793	\$0	\$3,007,120	\$4,102
Midway ES- Roof	421-214	\$547,056	\$556,661	(\$9,605)	\$547,056	\$547,056	\$0	\$0	\$547,056	\$0
Miller Grove HS - Addition	421-128	\$5,792,887	\$242,163	\$0	\$242,163	\$63,597	\$178,566	\$0	\$242,163	\$0
Modular Ramps ADA	421-303-001	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Montclair ES - Chiller Replacement	421-341-021	\$170,000	\$119,602	\$1,823	\$121,425	\$121,425	\$0	\$0	\$121,425	\$48,575
Montgomery ES - HVAC	421-138	\$1,599,826	\$69,000	\$0	\$69,000	\$6,900	\$62,100	\$0	\$69,000	\$0
Monggomery ES - Parking Lot, underground detent	421-320-005	\$234,448	\$217,000	\$12,530	\$229,530	\$234,447	(\$4,917)	\$4,917	\$234,447	\$1
Murphy Candler ES - Roof	421-202	\$654,341	\$645,446	\$8,895	\$654,341	\$654,341	\$0	\$0	\$654,341	\$0
Murphy Candler ES - Carpet Replacement	421-341-002	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Nancy Creek (Kittridge) ES - Roof	421-212	\$515,440	\$515,115	(\$1,875)	\$513,240	\$512,964	\$276	\$0	\$513,240	\$0
Nancy Creek ES - Parking Lot & bus loop	421-320-004	\$365,425	\$365,425	\$0	\$365,425	\$365,425	\$0	\$0	\$365,425	\$0
Narvie J Harris ES- Carpet Replacement	421-341-016	\$17,705	\$17,705	\$0	\$17,705	\$17,705	\$0	\$0	\$17,705	\$0
Oak Grove ES- Classroom Lighting	421-341-035	\$111,733	\$101,798	\$0	\$101,798	\$8,211	\$93,587	\$0	\$101,798	\$9,935
Oak Grove ES- Downspouts	421-321-013	\$43,331	\$43,331	\$0	\$43,331	\$43,331	\$0	\$0	\$43,331	\$0
Oak Grove ES- Exterior Lighting	421-341-029	\$75,000	\$8,925	\$0	\$8,925	\$0	\$8,925	\$0	\$8,925	\$66,075
Oak Grove ES- Paving	421-341-036	\$100,225	\$92,562	\$2,900	\$95,462	\$84,716	\$10,746	\$0	\$95,462	\$4,763
Panola Way ES - ADA	421-301-009	\$11,464	\$11,464	\$0	\$11,464	\$11,464	\$0	\$0	\$11,464	\$0
Program Contingency	421-900	\$22,716,950	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$22,716,950
Rainbow ES - Roof	421-203	\$370,791	\$325,178	\$46,022	\$371,200	\$371,200	\$0	\$0	\$371,200	(\$409)
Rainbow ES- Chiller Replacement	421-341-011	\$69,964	\$69,964	\$0	\$69,964	\$69,964	\$0	\$0	\$69,964	\$0
Redian HS - Roof, HVAC, Career Tech, ADA	421-111	\$11,343,479	\$8,342,946	\$251,910	\$8,594,857	\$7,868,265	\$726,592	(\$73,786)	\$8,521,071	\$73,013
Rockbridge ES - HVAC & ADA	421-133	\$1,671,149	\$75,229	\$0	\$75,229	\$11,284	\$63,945	\$0	\$75,229	\$0
Sagamore Hills ES - Roof	421-222	\$659,638	\$610,089	(\$7,731)	\$602,358	\$602,358	\$0	\$0	\$602,358	\$57,280
Sagamore Hills ES- Media Center Carpet Replace	421-341-017	\$7,142	\$7,142	\$0	\$7,142	\$7,142	\$0	\$0	\$7,142	\$0
Salem MS - Replace chalk boards w/white boards	421-320-010	\$24,406	\$24,406	\$0	\$24,406	\$24,406	\$0	\$0	\$24,406	\$0
Sam Moss Center - Paint and Carpet	421-341-019	\$67,700	\$41,904	\$0	\$41,904	\$35,486	\$6,418	\$0	\$41,904	\$25,796
Sam Moss Center- Paving Repair and Replaceme	421-341-037	\$474,855	\$402,265	\$72,590	\$474,855	\$474,855	\$0	\$0	\$474,855	\$0

SPL OST III Capital Improvement Program

Project Financial Summary

Monthly Status Report

Budget Category

Budget Category	Project Number	Current Budget	Original Contract	Executed Change Orders	Current Contract	Paid To Date	Contract Balance	Approved CORs	Current Contract Plus CORs	Uncommitted
Sam Moss Service Center - HVAC and Roof	421-131	\$1,706,432	\$1,590,532	(\$9,186)	\$1,581,345	\$1,477,699	\$103,646	\$21,336	\$1,602,681	\$90,472
School Choice/Relocation	421-320-003	\$271,205	\$226,861	\$0	\$226,861	\$213,812	\$13,049	\$0	\$226,861	\$44,344
Security Equipment	421-341-018	\$103,978	\$207,956	\$0	\$207,956	\$103,978	\$0	\$0	\$207,956	(\$103,978)
Security Lighting	421-321-009	\$506,540	\$506,540	\$0	\$506,540	\$506,540	\$0	\$0	\$506,540	\$0
Security Upgrade Systems	421-341-025	\$550,000	\$550,000	\$0	\$550,000	\$535,775	\$14,225	\$0	\$550,000	\$0
Sequoayah MS - Roof	421-205	\$1,958,812	\$1,665,152	\$34,485	\$1,699,637	\$1,550,094	\$149,543	\$0	\$1,699,637	\$4,179
Site Improvements 1- Main Project	421-321	\$42,891	\$15,071	\$0	\$15,071	\$15,071	\$0	\$0	\$15,071	\$27,820
Site Improvements 2- Main Project	421-322	\$62,534	\$536	\$0	\$536	\$536	\$0	\$0	\$536	\$62,018
Sky Haven ES - Roof	421-201	\$767,601	\$751,098	(\$22,701)	\$728,397	\$724,097	\$4,300	\$0	\$728,397	\$25,204
Sky Haven ES- Window Replacement	421-341-006	\$384,379	\$373,499	\$0	\$373,499	\$6,510	\$366,989	\$0	\$373,499	\$10,880
Smoke Rise ES - 20 classroom dry eraser boards	421-320-009	\$13,848	\$13,848	\$0	\$13,848	\$13,848	\$0	\$0	\$13,848	\$0
Snappinger ES - Roof	421-210	\$732,621	\$646,718	\$0	\$646,718	\$436,922	\$209,796	\$0	\$646,718	\$0
SPL OST Audit	421-000	\$30,000	\$47,880	\$0	\$47,880	\$63,760	(\$15,880)	\$0	\$47,880	(\$17,880)
Stephenson HS-Triack Field Improvements	421-321-001	\$259,658	\$259,658	\$0	\$259,658	\$259,658	\$0	\$0	\$259,658	\$0
Stephenson MS - HVAC	421-113	\$35,120	\$35,120	\$0	\$35,120	\$35,120	\$0	\$0	\$35,120	\$0
Stone Mill ES - HVAC	421-140	\$1,396,903	\$52,500	\$0	\$52,500	\$3,938	\$48,562	\$0	\$52,500	\$0
Stone Mountain ES - HVAC & ADA	421-135	\$1,731,048	\$116,240	\$0	\$116,240	\$33,206	\$83,034	\$0	\$116,240	\$0
Stone Mountain HS - HVAC, Roof	421-110	\$6,596,254	\$5,557,744	\$408,501	\$5,966,245	\$5,421,808	\$544,437	\$0	\$5,966,245	\$31,352
Stonemill ES- Parking Lot Repair	421-321-001A	\$53,373	\$53,373	\$0	\$53,373	\$53,373	\$0	\$0	\$53,373	\$0
Stoneview ES- Chiller Replacement	421-341-024	\$94,180	\$91,420	\$0	\$91,420	\$94,180	(\$2,760)	\$2,760	\$94,180	\$0
Stoneview ES- Kitchen Equipment	421-341-007	\$162,907	\$164,952	\$5,018	\$169,970	\$145,706	\$24,264	\$0	\$169,970	(\$7,063)
SW DeKalb HS - SPLOST II Deferred, ADA	421-102	\$22,310,250	\$2,443,842	\$184,785	\$2,628,627	\$1,994,429	\$634,198	\$0	\$2,628,627	\$330
Technology	421-503	\$6,000,000	\$5,625,249	\$0	\$5,625,249	\$5,625,249	\$0	\$0	\$5,625,249	\$0
Technology - Media Center Upgrades	421-502	\$10,000,000	\$9,608,861	\$0	\$9,608,861	\$9,608,861	\$0	\$0	\$9,608,861	\$0
Technology - Refresh Cycle for all Schools and Ct	421-501	\$19,598,581	\$18,340,164	\$0	\$18,340,164	\$18,430,902	(\$90,738)	\$0	\$18,340,164	\$1,258,417
Terry Mill ES - Parking Lot Paving	421-320-011	\$339,297	\$328,509	\$11,279	\$339,788	\$339,788	\$0	\$0	\$339,788	(\$491)
Terry Mill ES - Reloc Hooper Alex DESA, renova	421-320-006	\$536,460	\$512,217	\$27,184	\$539,401	\$566,563	(\$27,162)	\$0	\$539,401	(\$2,941)
Terry Mill ES (DESA) - Roof	421-211	\$610,187	\$612,687	(\$2,500)	\$610,187	\$610,187	\$0	\$0	\$610,187	\$0
Towers HS - SPLOST II Deferred	421-103	\$3,046,400	\$2,744,902	\$102,723	\$2,847,625	\$2,845,913	\$1,712	(\$1,060)	\$2,846,565	\$117,565
Tucker HS - New Replacement High School	421-108	\$61,365,016	\$53,463,433	\$6,918,977	\$60,382,410	\$59,199,946	\$1,182,464	\$11,813	\$60,394,223	(\$454,987)
Vanderlyn ES - HVAC, Roof, ADA	421-116	\$2,308,591	\$1,894,208	\$129,933	\$2,024,141	\$1,987,290	\$36,851	\$0	\$2,024,141	\$99
Vanderlyn ES- Replace Toilet Fixtures	421-321-005	\$71,116	\$71,116	\$0	\$71,116	\$71,116	\$0	\$0	\$71,116	\$0

SPL OST III Capital Improvement Program

Project Financial Summary

Monthly Status Report

Budget Category	Project Number	Current Budget	Original Contract	Executed Change Orders	Current Contract	Paid To Date	Contract Balance	Approved CORs	Current Contract Plus CORs	Uncommitted
Wadsworth ES - Roof	421-206	\$638,290	\$638,919	(\$629)	\$638,290	\$638,290	\$0	\$0	\$638,290	\$0
Wadsworth ES- Band Lockers	421-320-003D	\$24,000	\$24,000	\$0	\$24,000	\$24,000	\$0	\$0	\$24,000	\$0
Wadsworth Magnet- HVAC & Lighting	421-341-027	\$400,000	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$400,000
Warren Tech - HVAC	421-129	\$1,130,212	\$46,863	\$0	\$46,863	\$9,373	\$37,490	\$0	\$46,863	\$0
William Bradley Bryant Center	421-228	\$3,500,000	\$10,519	\$0	\$10,519	\$7,956	\$2,563	\$0	\$10,519	\$0
Woodridge ES - Roof	421-227	\$990,000	\$593,822	\$0	\$593,822	\$483,727	\$110,095	\$0	\$593,822	\$0
Woodward ES - HVAC, Roof	421-109	\$2,201,816	\$2,008,231	\$143,219	\$2,151,450	\$2,151,450	\$0	\$0	\$2,151,450	\$50,366
Grand Total		\$513,469,963	\$365,297,879	\$32,932,569	\$398,230,448	\$292,364,147	\$105,866,301	\$356,020	\$398,586,468	\$28,348,113

SPLOST III Capital Improvement Program

Projects Status by Phase

Monthly Status Report

Project Name	Project Number	Delivery Method	Current Budget	Current Contract
1. Planning & Programming				
1 Bulk Purchasing- Lighting	421-600-005	Fixed Price	\$0	\$0
2 Clifton ES- Ceiling Tiles	421-341-039	Fixed Price	\$110,000	\$0
3 Knollwood ES - HVAC & ADA	421-132	Design / Bid / Build	\$1,662,372	\$1,650
4 Wadsworth Magnet- HVAC & Lighting	421-341-027	Design / Build	\$400,000	\$0
1. Planning & Programming Subtotal:			\$2,172,372	\$1,650
2. Design				
1 ADA Group D	421-304	Design / Bid / Build	\$337,051	\$2,343
2 Chamblee HS- New Replacement High School	421-117	CM @ Risk	\$11,152,507	\$3,177,362
3 DeKalb International Student Center- Canopy	421-341-047	Fixed Price	\$2,000	\$9,340
4 DSA Relocation to Avondale HS - Renovations	421-123-002	Design / Bid / Build	\$4,265,700	\$304,608
5 Hambrick ES - HVAC	421-136	Design / Bid / Build	\$1,871,891	\$72,500
6 Hawthorne ES - ADA	421-303-011	Design / Bid / Build	\$13,750	\$13,750
7 Indian Creek ES - HVAC	421-139	Design / Bid / Build	\$1,164,368	\$50,150
8 Miller Grove HS - Addition	421-128	Design / Bid / Build	\$5,792,887	\$242,163
9 Montgomery ES - HVAC	421-138	Design / Bid / Build	\$1,599,826	\$69,000
10 Rockbridge ES - HVAC & ADA	421-133	Design / Bid / Build	\$1,671,149	\$75,229
11 Stone Mill ES - HVAC	421-140	Design / Bid / Build	\$1,396,903	\$52,500
12 Stone Mountain ES - HVAC & ADA	421-135	Design / Bid / Build	\$1,731,048	\$116,240
13 SW DeKalb HS - SPLOST II Deferred, ADA	421-102	Design / Bid / Build	\$22,310,250	\$2,628,627
14 Warren Tech - HVAC	421-129	Design / Bid / Build	\$1,130,212	\$46,863
2. Design Subtotal:			\$54,439,542	\$6,860,675
3. Procurement				
1 Bulk Purchase- Ceiling Tile and Grid	421-600-002	Fixed Price	\$0	\$0
2 Emergency Generators	421-321-015	Design / Bid / Build	\$3,800,000	\$443,992
3 Lithonia MS - Renovations	421-341-044	Fixed Price	\$207,000	\$197,245
4 William Bradley Bryant Center	421-228	Design / Bid / Build	\$3,500,000	\$10,519
3. Procurement Subtotal:			\$7,507,000	\$651,756
4. Construction				
1 ADA Group A- Main Project	421-301	Fixed Price	\$81,808	\$91,389
2 ADA Group B- Main Project	421-302	Design / Build	\$510,448	\$1,935
3 ADA Group B-1	421-302-001	Design / Build	\$496,000	\$495,645

SPL OST III Capital Improvement Program

Projects Status by Phase

Monthly Status Report

Project Name	Project Number	Delivery Method	Current Budget	Current Contract
4. Construction				
4 ADA Group B-2	421-302-002	Design / Build	\$407,299	\$364,968
5 Bulk Purchase - Plumbing Fixtures	421-322-001	Fixed Price	\$2,043,950	\$866,137
6 Bulk Purchase- Fixed Audience Seating	421-600-006	Fixed Price	\$0	\$0
7 Bulk Purchase- Metal Lockers	421-600-003	Fixed Price	\$0	\$0
8 Carpet Replacement - Multiple Schools (LSPR 2Q09)	421-341-040	Fixed Price	\$30,667	\$29,836
9 Cedar Grove HS - HVAC, Lighting, Ceiling & Roof	421-115	Fixed Price	\$6,211,315	\$5,170,459
10 Chapel Hill MS- Ceiling Tiles & Site Work	421-341-028	Fixed Price	\$240,275	\$275
11 Clarkston HS - Renovation & Addition	421-118	Design / Bid / Build	\$12,275,194	\$10,445,642
12 Dunwoody HS - Renovation & Addition	421-120	Design / Bid / Build	\$20,530,480	\$18,199,618
13 Emergency HVAC Work	421-101		\$4,636,397	\$4,569,394
14 Evansdale ES - Roof	421-218	Design / Bid / Build	\$647,608	\$520,953
15 FF&E- LSPR 2Q09	421-341-048	Fixed Price	\$21,100	\$0
16 Flat Shoals ES - Roof	421-219	Design / Bid / Build	\$764,826	\$539,871
17 General Services Main Project	421-600	Fixed Price	\$302,149	\$193,991
18 Glen Haven ES - Widen Drive	421-341-032	Design / Build	\$131,200	\$129,802
19 Hambrick ES - Roof	421-223	Design / Bid / Build	\$1,090,000	\$663,766
20 Hawthorne ES - Roof	421-224	Design / Bid / Build	\$1,100,000	\$8,470
21 Lakeside HS - Career Tech, ADA	421-125	Guaranteed Maximum Price	\$24,289,410	\$21,621,251
22 LSPR 2- Main Project	421-341	Design / Bid / Build	\$617,138	\$108,848
23 Oak Grove ES- Classroom Lighting	421-341-035	Fixed Price	\$111,733	\$101,798
24 Sam Moss Service Center - HVAC and Roof	421-131	Design / Build	\$1,706,432	\$1,581,345
25 Site Improvements 1- Main Project	421-321		\$42,891	\$15,071
26 Site Improvements 2- Main Project	421-322		\$62,554	\$536
27 Woodridge ES - Roof	421-227	Design / Bid / Build	\$990,000	\$593,822
4. Construction Subtotal:				\$66,314,822
5. Close-out				
1 ADA Group A-2A	421-301-021	Design / Build	\$561,574	\$556,774
2 ADA Group A-2B	421-301-022	Design / Build	\$678,336	\$678,336
3 Administrative & Instructional Complex (AIC)	421-124	Design / Build	\$31,824,966	\$31,130,560
4 Allgood ES - Roof	421-217	Design / Bid / Build	\$585,240	\$474,062
5 Chесnut Charter ES- Basketball Court Replacement	421-322-004	Design / Bid / Build	\$52,957	\$52,957
6 Columbia HS - SPLOST II Deferred	421-104	CM @ Risk	\$11,452,000	\$11,295,801

SPLCOT III Capital Improvement Program

Projects Status by Phase

Monthly Status Report

Project Name

Project Name	Project Number	Delivery Method	Current Budget	Current Contract
--------------	----------------	-----------------	----------------	------------------

5. Close-out

7 Cross Keys HS -Renovation & Addition	421-106	CM @ Risk	\$18,612,631	\$17,333,684
8 Druid Hills HS - Renovation & Addition	421-119	CM @ Risk	\$18,633,137	\$18,206,819
9 DSA Relocation to Avondale HS - Modifications	421-123	Design / Bid / Build	\$5,563,715	\$4,754,369
10 Fairington ES- HVAC, Ceilings & Lighting	421-121	Design / Build	\$1,977,131	\$1,950,358
11 Glen Haven ES - Roof	421-225	Design / Bid / Build	\$990,000	\$629,027
12 Henderson MS- Hold-Opens & Toilets	421-341-052	Design / Bid / Build	\$75,278	\$74,800
13 Lakeside HS - Natatorium	421-341-012	Fixed Price	\$293,903	\$288,506
14 Margaret Harris- Exterior Facade & RR Renovation	421-321-007B	Fixed Price	\$326,943	\$326,943
15 McLendon ES - HVAC & ADA	421-130	Design / Build	\$2,098,390	\$2,051,993
16 Midvale ES -HVAC, Roof, ADA	421-112	Design / Build	\$3,070,205	\$3,007,120
17 Oak Grove ES- Paving	421-341-036	Design / Bid / Build	\$100,225	\$95,462
18 Redan HS -Roof, HVAC, Career Tech, ADA	421-111	Design / Bid / Build	\$111,343,479	\$8,594,857
19 Sequoyah MS - Roof	421-205	Design / Bid / Build	\$1,958,812	\$1,699,637
20 Snapfinger ES - Roof	421-210	Design / Bid / Build	\$732,621	\$646,718
21 Stone Mountain HS - HVAC, Roof	421-110	Design / Bid / Build	\$6,596,254	\$5,966,245
22 Towers HS - SPLOST II Deferred	421-103	Design / Build	\$3,046,400	\$2,847,625
23 Tucker HS - New Replacement High School	421-108	CM @ Risk	\$61,365,016	\$60,382,410
24 Vanderlyn ES - HVAC, Roof, ADA	421-116	Design / Build	\$2,308,591	\$2,024,141

5. Close-out Subtotal:

\$184,247,804

\$175,069,204

6. Completed

1 Allgood ES - ADA	421-301-010	Fixed Price	\$32,556	\$32,556
2 Atherton ES- Chiller Replacement	421-341-022	Fixed Price	\$123,176	\$123,176
3 Avondale ES - ADA	421-301-005	Fixed Price	\$22,406	\$22,406
4 Avondale ES - Roof	421-209	Design / Bid / Build	\$578,746	\$578,746
5 Baisin Heaters	421-321-014	Fixed Price	\$345,500	\$345,500
6 Bob Mathis ES - ADA	421-301-001	Fixed Price	\$22,299	\$22,299
7 Brockett ES - Make-up Air Units	421-320-001	Fixed Price	\$94,030	\$94,030
8 Buses 1	421-401		\$3,479,453	\$3,479,453
9 Buses 3	421-403		\$3,984,380	\$3,984,380
10 Carpet Replacement - Multiple Schools (LSPR 1Q09)	421-341-031	Fixed Price	\$10,237	\$10,237
11 Chamblee Charter HS - Lockers	421-341-014	Fixed Price	\$50,000	\$43,457
12 Chamblee MS - Sound Panels	421-341-050	Fixed Price	\$27,500	\$38,900

SPL OST III Capital Improvement Program

Projects Status by Phase

Monthly Status Report

Project Name	Project Number	Delivery Method	Current Budget	Current Contract
6. Completed				
13 Chamblee MS- Mirror	421-341-049	Fixed Price	\$960	\$960
14 Champion MS - ADA	421-301-020	Fixed Price	\$15,362	\$0
15 Champion Theme MS - Roof	421-208	Design / Bid / Build	\$382,342	\$382,342
16 Champion Theme MS- Chiller Replacement	421-341-010	Fixed Price	\$47,539	\$47,539
17 Chapel Hill ES- Chiller Replacement	421-341-009	Fixed Price	\$69,964	\$69,964
18 Chapel Hill MS- Track & Tennis Court	421-341-051	Fixed Price	\$243,956	\$255,522
19 Chestnut ES - ADA	421-303-002	Design / Build	\$448,179	\$443,779
20 CLEA 2008- Comprehensive Lighting Energy Audit	421-600-001	Fixed Price	\$98,032	\$98,032
21 Clifton ES - HVAC	421-114		\$172,792	\$172,792
22 DeKalb HS of Tech North - Roof	421-221		\$0	\$0
23 DeKalb HS of Tech South - Roof	421-215	Design / Bid / Build	\$352,288	\$351,428
24 Eagle Wood Academy- Replace Windows & Repair Doors	421-321-011	Fixed Price	\$55,435	\$55,435
25 East Campus - APHONE	421-341-026		\$0	\$0
26 Eldridge L. Miller ES - Roof	421-216	Design / Bid / Build	\$452,953	\$452,953
27 Energy Management System Update	421-322-002	Fixed Price	\$948,000	\$948,000
28 FF&E- LSPPR 1Q09	421-341-033	Fixed Price	\$44,379	\$44,379
29 Glen Haven ES - ADA	421-301-016	Design / Build	\$93,771	\$93,771
30 Glen Haven ES- Replace Toilet Fixtures & Carpet	421-321-004	Fixed Price	\$94,950	\$94,950
31 Gresham Park ES - ADA	421-301-017	Fixed Price	\$80,516	\$80,517
32 Gresham Park ES- Replace carpet in Media Center	421-320-008	Fixed Price	\$16,947	\$16,947
33 Henderson Mill ES - Chiller Replacement	421-341-008	Fixed Price	\$69,228	\$69,228
34 Henderson Mill ES- Ceiling Tiles	421-341-046	Fixed Price	\$3,911	\$3,911
35 Henderson MS- Classroom & Restroom Upgrades	421-320-002	Fixed Price	\$128,052	\$164,715
36 Henderson MS- Gym Light Switches	421-341-013	Fixed Price	\$6,670	\$6,670
37 Henderson MS- Repair/Replace uneven tile near ref	421-320-007	Fixed Price	\$2,985	\$2,985
38 Heritage Center - Roof	421-204	Design / Bid / Build	\$351,097	\$349,597
39 Hooper Alexander ES - HVAC & ADA	421-134		\$0	\$0
40 Huntley Hills ES- Restroom Renovations	421-321-006	Fixed Price	\$66,767	\$66,767
41 Idlewood ES - ADA	421-301-003	Fixed Price	\$9,611	\$9,611
42 Idlewood ES- Carpet Replacement	421-341-001	Fixed Price	\$1,325	\$1,325
43 Idlewood ES- Parking Lots	421-321-010	Design / Build	\$237,201	\$237,202
44 Indian Creek ES - ADA	421-301-013	Fixed Price	\$23,948	\$23,948
45 Kelley Lake ES - Courtyard	421-341-041		\$10,000	\$12,800

SPL OST III Capital Improvement Program

Projects Status by Phase

Monthly Status Report

Project Name	Project Number	Delivery Method	Current Budget	Current Contract
6. Completed				
46 Kingsley Charter ES- Media Center Furniture	421-341-003	Fixed Price	\$18,194	\$18,194
47 Kingsley ES - ADA	421-301-004	Fixed Price	\$8,600	\$8,600
48 Kittridge Magnet ES- Chiller Replacement	421-341-020	Fixed Price	\$99,202	\$99,202
49 Laurel Ridge ES - ADA	421-301-006	Design / Build	\$67,396	\$67,396
50 Laurel Ridge- Replace Parking Lot & Tennis Court	421-321-012		\$0	\$0
51 Lithonia MS - Security Cameras	421-341-045	Fixed Price	\$85,982	\$85,982
52 Lithonia MS- Band Room Carpet	421-341-004	Fixed Price	\$6,028	\$6,028
53 LSPR 1- Main Project	421-320		\$163,176	\$165,862
54 Marbut/Bouie ES- New Multi-purpose Bldg. Restrooms	421-321-003	Design / Build	\$239,039	\$239,039
55 Margaret Harris Center- Paving	421-321-007	Fixed Price	\$31,232	\$31,232
56 Margaret Harris Center- Washing Machines	421-321-007D	Fixed Price	\$9,050	\$9,050
57 Margaret Harris-Dryers	421-321-007E	Fixed Price	\$704	\$704
58 Margaret Harris ES- Door Release System	421-341-005	Fixed Price	\$6,748	\$6,748
59 McLendon ES- Basketball Court, Paint & Blinds	421-341-030		\$0	\$0
60 McNair HS - SPLOST II Deferred	421-105	Design / Bid / Build	\$869,475	\$844,547
61 McNair MS- Ceiling Tile Replacement	421-341-015	Fixed Price	\$49,058	\$49,058
62 McNair MS- Chiller Replacement	421-341-023	Fixed Price	\$192,000	\$192,000
63 Middle School- Additional Parking Lot Lighting	421-341-038	Design / Build	\$200,382	\$200,382
64 Midway ES - Roof	421-214	Design / Bid / Build	\$547,056	\$547,056
65 Modular Ramps ADA	421-303-001		\$0	\$0
66 Monclair ES - Chiller Replacement	421-341-021	Fixed Price	\$170,000	\$121,425
67 Montgomery ES - Parking Lot, undergroud detention	421-320-005	Design / Build	\$234,448	\$229,530
68 Murphy Candler ES - Roof	421-202	Design / Bid / Build	\$654,341	\$654,341
69 Murphy Candler ES- Carpet Replacement	421-341-002	Fixed Price	\$0	\$0
70 Nancy Creek (Kittridge) ES - Roof	421-212	Design / Bid / Build	\$515,440	\$513,240
71 Nancy Creek ES- Parking Lot & bus loop	421-320-004	Design / Build	\$365,425	\$365,425
72 Narvie J Harris ES- Carpet Replacement	421-341-016	Fixed Price	\$17,705	\$17,705
73 Oak Grove ES- Downspouts	421-321-013	Design / Build	\$43,331	\$43,331
74 Oak Grove ES- Exterior Lighting	421-341-029	Fixed Price	\$75,000	\$8,925
75 Panola Way ES - ADA	421-301-009	Fixed Price	\$11,464	\$11,464
76 Rainbow ES - Roof	421-203		\$370,791	\$371,200
77 Rainbow ES- Chiller Replacement	421-341-011	Fixed Price	\$69,964	\$69,964
78 Saganore Hills ES - Roof	421-222	Design / Bid / Build	\$659,638	\$602,358

SPL OST III Capital Improvement Program

Projects Status by Phase

Monthly Status Report

Project Name	Project Number	Delivery Method	Current Budget	Current Contract
6. Completed				
79 Sagamore Hills ES- Media Center Carpet Replacement	421-341-017	Fixed Price	\$7,142	\$7,142
80 Salem MS - Replace chalk boards w/white boards	421-320-010	Fixed Price	\$24,406	\$24,406
81 Sam Moss Center - Paint and Carpet	421-341-019	Fixed Price	\$67,700	\$41,904
82 Sam Moss Center- Paving Repair and Replacement	421-341-037	Design / Build	\$474,855	\$474,855
83 School Choice/Relocation	421-320-003		\$271,205	\$226,861
84 Security Equipment	421-341-018		\$103,978	\$207,956
85 Security Lighting	421-321-009	Design / Build	\$506,540	\$506,540
86 Security Upgrade Systems	421-341-025	Fixed Price	\$550,000	\$550,000
87 Sky Haven ES - Roof	421-201	Design / Bid / Build	\$767,601	\$728,397
88 Smoke Rise ES - 20 classroom dry eraser boards	421-320-009	Fixed Price	\$13,848	\$13,848
89 Stephenson HS- Track Field Improvements	421-321-001	Design / Build	\$259,658	\$259,658
90 Stephenson MS -HVAC	421-113		\$35,120	\$35,120
91 Stonemill ES- Parking Lot Repair	421-321-001A	Fixed Price	\$53,373	\$53,373
92 Stoneview ES- Chiller Replacement	421-341-024	Fixed Price	\$94,180	\$91,420
93 Stoneview ES- Kitchen Equipment	421-341-007	Fixed Price	\$162,907	\$169,970
94 Terry Mill ES - Parking Lot Paving	421-320-011	Fixed Price	\$339,297	\$339,788
95 Terry Mill ES - Reloc Hooper Alex DESA, renovation	421-320-006	Design / Bid / Build	\$536,460	\$539,401
96 Terry Mill ES (DESA) - Roof	421-211	Design / Bid / Build	\$610,187	\$610,187
97 Vanderlyn ES- Replace Toilet Fixtures	421-321-005	Fixed Price	\$71,116	\$71,116
98 Wadsworth ES- Roof	421-206	Design / Bid / Build	\$638,290	\$638,290
99 Wadsworth ES- Band Lockers	421-320-003D	Fixed Price	\$24,000	\$24,000
100 Woodward ES - HVAC, Roof	421-109	Design / Bid / Build	\$2,201,816	\$2,151,450
6. Completed Subtotal:			\$26,893,991	\$26,678,879
7. On-Going SPL OST Activity				
1 Buses 2			\$4,536,167	\$4,524,398
2 Capital Improvement Team Compensation	421-650		\$15,374,724	\$15,374,724
3 COPS Debt Reduction	421-001		\$66,000,000	\$66,000,000
4 Facilities Assessment	421-700	Fixed Price	\$1,770,367	\$1,770,367
5 Land	421-107		\$11,350	\$20,350
6 Program Contingency	421-900		\$22,716,950	\$0
7 SPLOST Audit	421-000		\$30,000	\$47,880
8 Technology	421-503		\$6,000,000	\$5,625,249

SPLCOST III Capital Improvement Program

Monthly Status Report

Projects Status by Phase

Project Name	Project Number	Delivery Method	Current Budget	Current Contract
--------------	----------------	-----------------	----------------	------------------

7. On-Going SPLCOST Activity

9 Technology - Media Center Upgrades	421-502		\$10,000,000	\$9,608,861
10 Technology - Refresh Cycle for all Schools and Ctr	421-501		\$19,598,581	\$18,340,164
7. On-Going SPLCOST Activity Subtotal			\$146,038,139	\$121,311,993

8. On Hold

1 ADA Group B-3	421-302-003	Design / Bid / Build	\$0	\$0
2 ADA Group C- Main Project	421-303	Design / Bid / Build	\$1,023,071	\$57,521
3 ADA Group E	421-305	Design / Bid / Build	\$427,202	\$0
4 Allgood ES- Kitchen	421-341-043	Fixed Price	\$40,000	\$0
5 Ashford Park ES - ADA	421-301-007	Fixed Price	\$54,200	\$44,924
6 Chamblee MS - Roof	421-226		\$83,683	\$0
7 Coralwood Diagnostic Ctr. - Renovation & Addition	421-213	Design / Bid / Build	\$423,427	\$365,263
8 Huntley Hills ES - Roof	421-220		\$0	\$0
9 Lithonia HS - Addition	421-126		\$0	\$25,488
10 Martin Luther King, Jr. HS - Addition	421-127	Design / Bid / Build	\$9,889,279	\$465,639
8. On Hold Subtotal:			\$12,300,862	\$958,835

9. Deemed Unnecessary

1 Bulk Purchase- Theatrical Lighting & Sound System	421-600-004	Fixed Price	\$0	\$0
2 Chamblee MS- Painting	421-341-042	Fixed Price	\$145,000	\$9,135
3 Clarkston Center - Roof	421-207		\$0	\$0
4 Forrest Hills ES - HVAC	421-137		\$0	\$0
5 Henderson Mill ES - New Door	421-341-034		\$0	\$0
6 Sky Haven ES- Window Replacement	421-341-006	Fixed Price	\$384,379	\$373,499
9. Deemed Unnecessary Subtotal:			\$529,379	\$382,634

SPL OST III Capital Improvement Program

Projects Status by Phase

Monthly Status Report

Project Name

Project Name	Project Number	Delivery Method	Current Budget	Current Contract
Program Totals:	\$513,469,963		\$398,230,448	

Project Budgets by Phase

Close-out, \$184,247,804

Planning & Programming, \$2,172,372

Procurement, \$7,507,000

On-Going SPLOST Activity, \$146,038,139

Design, \$54,439,542

Deemed Unnecessary

On Hold

Completed, \$26,893,991

Construction, \$79,340,874

Planning & Programming

Procurement

SPLOST III Capital Improvement Program

Monthly Status Report

Change Order Details for the Month of May 2011

Project Name: Allgood ES - Roof						
Project No. / Vendor Name	CO No.	CO Date	CO Amount	COR No.	COR Date	COR Amount
421-217 Klein Contracting	1	5/12/2011	\$24,706		3/21/2011	\$24,706
Project Name / Vendor Name	CO No.	CO Date	CO Amount	COR No.	COR Date	COR Amount
421-217 PCI Group	1	5/3/2011	\$597	1	8/19/2010	\$597 Additional Services
Project Name: Cedar Grove HS - HVAC, Lighting, Ceiling & Roof						
Project No. / Vendor Name	CO No.	CO Date	CO Amount	COR No.	COR Date	COR Amount
421-115 Talbot Construction	CO 6	5/12/2011	\$30,485	18	4/1/2011	\$806 New one hour wall was constructed to separate a classroom from a corridor so a new one hour door was furnished and installed per Fire Marshal request.
				23	9/2/2010	\$11,006 Additional painting of Cafe Stage ceiling, Health Rm & door, upper gym walls
				24	2/10/2010	\$21,893 Install additional electrical and life safety items per Fire Marshal
				25	12/30/2010	\$2,834 Install shaft wall around one (1) duct in Weight Room and two (2) ducts in Gym Stage Storage Rooms.
				28	12/15/2010	\$1,594 Relocate existing drain per Fire Marshal's request in lower mechanical room under the locker room where the fire line comes into the building.
				30	4/18/2011	(\$7,648) Credit back to Owner for Talbot not protecting gym floor surface while performing summer work as well as reinstallation of sound system due to Talbot cutting wires, etc. during summer work.



SPLOST III Capital Improvement Program

Monthly Status Report

Change Order Details for the Month of May 2011

Project Name: Cross Keys HS - Renovation & Addition

Project Name: Cross Keys HS - Renovation & Addition						
Project No. / Vendor Name	CO No.	CO Date	CO Amount	COR No.	COR Date	COR Amount
421-106 Evergreen Construction	26	5/23/2011	\$43,069	5contingenc	2/22/2011	\$0
						Conduit for AT&T Fiber Optic
	5contingenc	3/3/2011				RFI-102 Piping Connections from Sand Filter to Cooling Tower
	26savings	3/31/2011				Raise Light Fixtures in Construction Technology
	26savings	1/25/2011				Door Frame and Door modifications to existing frames (Area 7, band, music, and gym)
	26savings	1/25/2011				Door, Frame and hardware
	26savings	1/25/2011				RFI#34 - Door, hardware and frame questions.
	26savings	1/25/2011				Wing 2 Door and Frame Revisions
	26savings	2/10/2011				Relocate Hood fan from Home economics classroom to the Health science lab
	26savings	2/16/2011				RFI 206-HVAC and electrical revisions rooms 100.7 and 100.8
	26savings	3/31/2011				RFI 170-Equipment Yard Fencing
	26savings	2/28/2011				Flooring and Other miscellaneous Changes--No Cost
	26savings	3/24/2011				RFI 147-Issued Women's Locker Room Sketch
	26scope	3/3/2011				RFI 156-HVAC Work at Admin Area
	26scope	2/10/2011				Relocate Security Monitors from main office to 301.2
	26scope	2/28/2011				Rewire existing compressors for science labs in wings 2 and 3
	26scope	3/15/2011				RFI #201-Electrical for Equipment in Wing 1 and Wing 2
	26scope	2/28/2011				Noise at gym return air grilles
	26scope	2/10/2011				Tie in trailer intercom speakers to new head end unit
	26scope	3/3/2011				Add power to existing exterior lighting
421-106 Evergreen Construction	28	5/18/2011	\$49,383	5/4/2011	\$24,453	RFP 11-RFI 146 Replace existing exterior light fixtures
				5/4/2011	\$6,218	Additional outlets within the automotive tech room per DCSS
				5/4/2011	\$5,564	Replace Grass Under Trailers when demobilized. Option B-Quads: backfill and re-grass.
				4/29/2011	\$5,205	Removing fencing, interior partitions and ramps for quads.
				5/4/2011	\$4,319	Additional white boards and tack boards
				4/29/2011	\$2,014	Add teacher cabinet in Rm. 301
				4/29/2011	\$1,610	Provide Additional Data and Power Drops as Requested By DCSS/MIS
421-106 Evergreen Construction	30	5/27/2011	\$402,636		\$402,636	Raise roof structure at Auto Technology lab
Project Name: Dunwoody HS - Renovation & Addition						
Project No. / Vendor Name	CO No.	CO Date	CO Amount	COR No.	COR Date	COR Amount
421-120 Doster Construction C	18	5/5/2011	\$33,282	6/20/2011	\$360	This adjustment corrects the shortage that was made in CO#13 that was caused by a transpositional error.
	121	4/21/2011				Sound mixing console
	123	4/29/2011				South Stair Demo Credit
	57	4/25/2011				Smoke rate basement.

SPLOST III Capital Improvement Program

Monthly Status Report

Change Order Details for the Month of May 2011

Project Name: Lakeside HS - Career Tech, ADA						
Project No. / Vendor Name	CO No.	CO Date	CO Amount	COR No.	COR Date	COR Amount
421-125 Hogan Construction G	2	5/11/2011	\$53,205	012R	4/13/2011	(\$2,813)
				013R	3/21/2011	\$1,559
				016R	3/31/2011	(\$2,258)
				022R	4/27/2011	(\$1,044)
				03 Revised	2/2/2011	(\$21,042)
				15	3/3/2011	\$1,205
				17	3/29/2011	(\$4,200)
				18	4/19/2011	(\$1,992)
				2	12/9/2010	\$83,790
				COR 010R	3/21/2011	\$0

Pricing Corrections made 4/13
Revised COR 13 to remove time extension, which will be submitted under a separate change request pending approval of COR 10R.

COR 16 has been revised to address Kenneth's comments. We need to release the Door Hardware package ASAP. Please let me know if you need anything else with this or COR #010 in order to approve.

I have updated the COR to correct an error in the Guard Rail proposal.

COR #03 has been revised to include a count of 59 wire moulds in lieu of 27.

Lead paint testing

Credit to use Fireglass 20 in lieu of specified glass for door window kits.

Casework changes related to shop drawings.

RE: PR02 - Provide initial Sediment Storage.

Adjusted Request for time extension

Project Name: Sam Moss Service Center - HVAC and Roof

Project Name: Sam Moss Service Center - HVAC and Roof						
Project No. / Vendor Name	CO No.	CO Date	CO Amount	COR No.	COR Date	COR Amount
421-131 Merit Construction Co	5	5/17/2011	\$1,492	6	10/18/2010	\$656
				8	4/6/2011	\$836

Add 6 elec./data connections in Stokes conf. rm.

Furnishing eight (8) semi-recessed fire extinguisher cabinets with full glass lites in doors.



Project Name	Project Number	Current Budget	Encumbered	Balance
Planning & Programming				
Clifton ES- Ceiling Tiles	421-341-039	\$110,000	\$0	\$110,000
Wadsworth Magnet- HVAC & Lighting	421-341-027	\$400,000	\$0	\$400,000
Planning & Programming Subtotal:				
Design		\$510,000	\$0	\$510,000
DeKalb International Student Center- Canopy	421-341-047	\$2,000	\$9,340	(\$7,340)
Design Subtotal:				
Procurement		\$2,000	\$9,340	(\$7,340)
Lithonia MS - Renovations	421-341-044	\$207,000	\$197,245	\$9,755
Procurement Subtotal:				
Construction		\$207,000	\$197,245	\$9,755
Carpet Replacement - Multiple Schools (LSPR 2Q09)	421-341-040	\$30,667	\$29,836	\$831
Chapel Hill MS- Ceiling Tiles & Site Work	421-341-028	\$240,275	\$275	\$240,000
FF&E- LSPR 2Q09	421-341-048	\$21,100	\$0	\$21,100
Glen Haven ES - Widen Drive	421-341-032	\$131,200	\$129,802	\$1,398
LSPR 2- Main Project	421-341	\$617,138	\$108,848	\$508,290
Oak Grove ES- Classroom Lighting	421-341-035	\$111,733	\$101,798	\$9,935
Construction Subtotal:				
Close-out		\$1,152,113	\$370,559	\$781,554
Henderson MS- Hold-Opens & Toilets	421-341-052	\$75,278	\$74,800	\$478
Lakeside HS - Natatorium	421-341-012	\$293,903	\$288,506	\$5,397
Oak Grove ES- Paving	421-341-036	\$100,225	\$95,463	\$4,763
Close-out Subtotal:				
Completed		\$469,406	\$458,769	\$10,638
Atherton ES- Chiller Replacement	421-341-022	\$123,176	\$123,176	\$0
Brockett ES - Make-up Air Units	421-320-001	\$94,030	\$94,030	\$0
Carpet Replacement - Multiple Schools (LSPR 1Q09)	421-341-031	\$10,237	\$10,237	\$0
Chamblee Charter HS - Lockers	421-341-014	\$50,000	\$43,457	\$6,543
Chamblee MS - Sound Panels	421-341-050	\$27,500	\$38,900	(\$11,400)
Chamblee MS- Mirror	421-341-049	\$960	\$960	\$0
Champion Theme MS- Chiller Replacement	421-341-010	\$47,539	\$47,539	\$0

SPOLOST III Capital Improvement Program

Local School Priority Requests

Monthly Status Report



Project Name	Project Number	Current Budget	Encumbered	Balance
Completed				
Chapel Hill ES- Chiller Replacement	421-341-009	\$69,964	\$69,964	\$0
Chapel Hill MS- Track & Tennis Court	421-341-051	\$243,956	\$255,522	(\$11,566)
East Campus - AIPHONE	421-341-026	\$0	\$0	\$0
FF&E- LSPR 1Q09	421-341-033	\$44,379	\$44,379	\$0
Gresham Park ES- Replace carpet in Media Center	421-320-008	\$16,947	\$16,947	\$0
Henderson Mill ES - Chiller Replacement	421-341-008	\$69,228	\$69,228	\$0
Henderson Mill ES- Ceiling Tiles	421-341-046	\$3,911	\$3,911	\$0
Henderson MS- Classroom & Restroom Upgrades	421-320-002	\$128,052	\$164,716	(\$36,663)
Henderson MS- Gym Light Switches	421-341-013	\$6,670	\$6,670	\$0
Henderson MS- Repair/Replace uneven tile near ref	421-320-007	\$2,985	\$2,985	\$0
Idlewood ES- Carpet Replacement	421-341-001	\$1,325	\$1,325	\$0
Kelley Lake ES - Courtyard	421-341-041	\$10,000	\$12,800	(\$2,800)
Kingsley Charter ES- Media Center Furniture	421-341-003	\$18,194	\$18,194	\$0
Kittredge Magnet ES- Chiller Replacement	421-341-020	\$99,202	\$99,202	\$0
Lithonia MS - Security Cameras	421-341-045	\$85,982	\$85,982	\$0
Lithonia MS- Band Room Carpet	421-341-004	\$6,028	\$6,028	\$0
LSPR 1- Main Project	421-320	\$163,176	\$165,862	(\$2,686)
Margaret Harris ES- Door Release System	421-341-005	\$6,748	\$6,748	\$0
McLendon ES- Basketball Court, Paint & Blinds	421-341-030	\$0	\$0	\$0
McNair MS- Ceiling Tile Replacement	421-341-015	\$49,058	\$49,058	\$0
McNair MS- Chiller Replacement	421-341-023	\$192,000	\$192,000	\$0
Middle School- Additional Parking Lot Lighting	421-341-038	\$200,382	\$200,382	\$0
Montclair ES - Chiller Replacement	421-341-021	\$170,000	\$121,425	\$48,575
Montgomery ES - Parking Lot, undergroud detention	421-320-005	\$234,448	\$229,530	\$4,918
Murphy Candler ES- Carpet Replacement	421-341-002	\$0	\$0	\$0
Nancy Creek ES - Parking Lot & bus loop	421-320-004	\$365,425	\$365,425	\$0
Narvie J Harris ES- Carpet Replacement	421-341-016	\$17,705	\$17,705	\$0
Oak Grove ES- Exterior Lighting	421-341-029	\$75,000	\$8,925	\$66,075
Rainbow ES- Chiller Replacement	421-341-011	\$69,964	\$69,964	\$0
Sagamore Hills ES- Media Center Carpet Replacement	421-341-017	\$7,142	\$7,142	\$0
Salem MS - Replace chalk boards w/white boards	421-320-010	\$24,406	\$24,406	\$0
Sam Moss Center - Paint and Carpet	421-341-019	\$67,700	\$41,904	\$25,796



Project Name

Project Name	Project Number	Current Budget	Encumbered	Balance
--------------	----------------	----------------	------------	---------

Completed

Sam Moss Center- Paving Repair and Replacement	421-341-037	\$474,855	\$474,855	\$0
School Choice/Relocation	421-320-003	\$271,205	\$226,861	\$44,344
Security Equipment	421-341-018	\$103,978	\$207,956	(\$103,978)
Security Upgrade Systems	421-341-025	\$550,000	\$550,000	\$0
Smoke Rise ES - 20 classroom dry eraser boards	421-320-009	\$13,848	\$13,848	\$0
Stoneview ES- Chiller Replacement	421-341-024	\$94,180	\$91,420	\$2,760
Stoneview ES- Kitchen Equipment	421-341-007	\$162,207	\$169,970	(\$7,063)
Terry Mill ES - Parking Lot Paving	421-320-011	\$359,297	\$339,788	(\$491)
Terry Mill ES - Reloc Hooper Alex DESA, renovation	421-320-006	\$536,460	\$539,402	(\$2,942)
Wadsworth ES- Band Lockers	421-320-003D	\$24,000	\$24,000	\$0

Completed Subtotal:

\$5,374,149

On Hold

Allgood ES- Kitchen	421-341-043	\$400,000	\$0	\$400,000

Deemed Unnecessary

Chamblee MS- Painting	421-341-042	\$145,000	\$9,135	\$135,865
Henderson Mill ES - New Door	421-341-034	\$0	\$0	\$0
Sky Haven ES- Window Replacement	421-341-006	\$384,379	\$373,499	\$10,880

Deemed Unnecessary Subtotal:

\$529,379

\$382,634

\$146,745

LSPR Program Totals:	\$8,644,047	\$6,773,274	\$1,870,774
----------------------	--------------------	--------------------	--------------------



Overview:

Project Name	Project Number	Current Budget	Encumbered	Balance
--------------	----------------	----------------	------------	---------

Project Name

Project Number

Current Budget

Encumbered

Balance

Current Budget


Encumbered

Balance

Current Budget

Encumbered

Balance

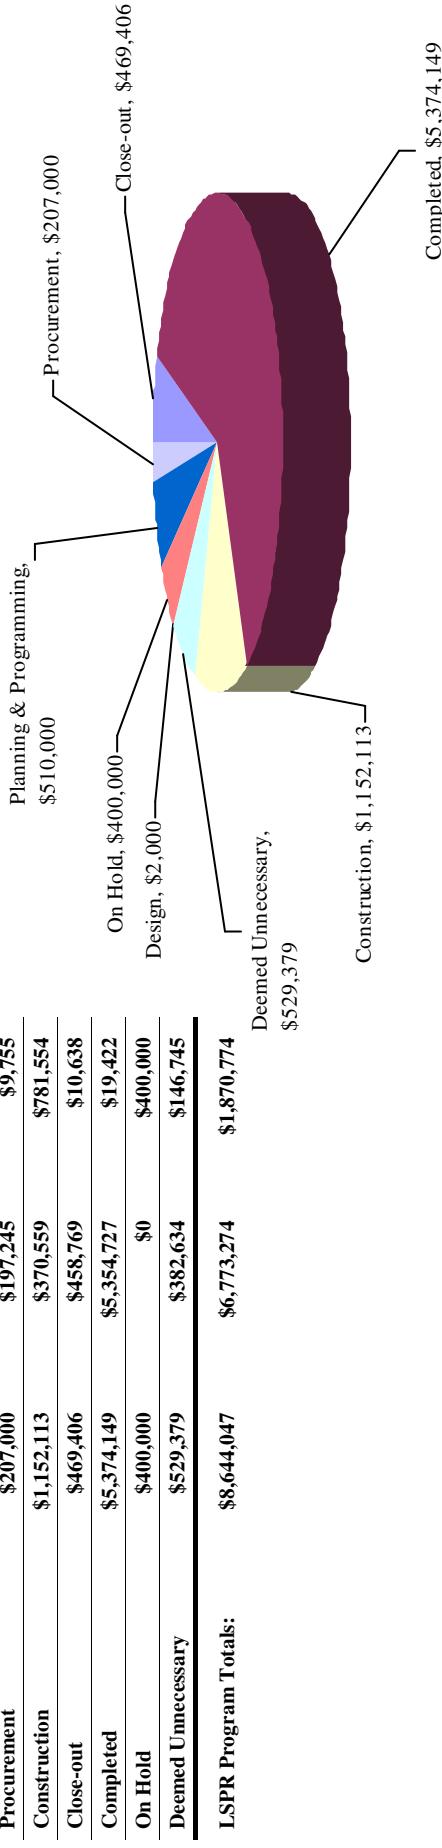



Project Name	Project Number	Current Budget	Encumbered	Balance
Procurement				
Emergency Generators	421-321-015	\$3,800,000	\$443,992	\$3,356,008
Construction				
Bulk Purchase - Plumbing Fixtures	421-322-001	\$2,043,950	\$866,137	\$1,177,813
Site Improvements 1- Main Project	421-321	\$42,891	\$15,071	\$27,820
Site Improvements 2- Main Project	421-322	\$62,554	\$536	\$62,018
Close-out				
Chesnut Charter ES- Basketball Court Replacement	421-322-004	\$52,957	\$52,957	\$0
Margaret Harris- Exterior Facade & RR Renovation	421-321-007B	\$326,943	\$326,943	\$1
Completed				
Basin Heaters	421-321-014	\$345,500	\$345,500	\$0
Eagle Wood Academy- Replace Windows & Repair Doors	421-321-011	\$55,435	\$55,435	\$0
Energy Management System Update	421-322-002	\$948,000	\$948,000	\$0
Glen Haven ES- Replace Toilet Fixtures & Carpet	421-321-004	\$94,950	\$94,950	\$0
Huntley Hills ES- Restroom Renovations	421-321-006	\$66,767	\$66,767	\$0
Idlewood ES- Parking Lots	421-321-010	\$237,201	\$237,201	(\$1)
Laurel Ridge- Replace Parking Lot & Tennis Court	421-321-012	\$0	\$0	\$0
Marbut/Bouie ES- New Multi-purpose Bldg. Restrooms	421-321-003	\$239,039	\$239,039	\$0
Margaret Harris Center- Paving	421-321-007	\$31,232	\$31,232	\$0
Margaret Harris Center- Washing Machines	421-321-007D	\$9,050	\$9,050	\$0
Margaret Harris- Dryers	421-321-007E	\$704	\$704	\$0
Oak Grove ES- Downspouts	421-321-013	\$43,331	\$43,331	\$0
Security Lighting	421-321-009	\$506,540	\$506,540	\$0
Stephenson HS- Track Field Improvements	421-321-001	\$259,658	\$259,658	\$0
Stonemill ES- Parking Lot Repair	421-321-001A	\$53,373	\$53,373	\$0

SPLOST III Capital Improvement Program

Site Improvement Projects

Monthly Status Report

Project Name

Project Name	Project Number	Current Budget	Encumbered	Balance
--------------	----------------	----------------	------------	---------

Completed

Vanderlyn ES- Replace Toilet Fixtures

Completed Subtotal:	\$2,961,896	\$2,961,897	(\$1)
Site Improvements Program Totals:	\$9,291,191	\$4,667,533	\$4,623,659

Overview:

Stage

Stage	Current Budget	Encumbered	Balance
-------	----------------	------------	---------

Procurement \$3,800,000 \$443,992 \$3,356,008

Construction \$2,149,395 \$881,744 \$1,267,651


Close-out \$379,900 \$379,900 \$1

Completed \$2,961,896 \$2,961,897 (\$1)

SI Program Totals: \$9,291,191 \$4,667,533 \$4,623,659

Current Budget by Phase

Close-out, \$379,900




Construction,
\$2,149,395

SPLOST III CIP Master Program Schedule


D	Project ID/WBS Code	Project Name	Start	Finish	Duration	2007				2008				2009				2010				2011				2012				
						Qr 1	Qr 2	Qr 3	Qr 4	Qr 1	Qr 2	Qr 3	Qr 4	Qr 1	Qr 2	Qr 3	Qr 4	Qr 1	Qr 2	Qr 3	Qr 4	Qr 1	Qr 2	Qr 3	Qr 4	Qr 1	Qr 2	Qr 3	Qr 4	
1	421-101	Emergency HVAC Work	Mon 10/1/07	Tue 5/31/11	957 days																									
2	421-102	Southwest DeKalb HS-Deferred Work	Thu 11/23/06	Fri 8/2/13	1747 days																									
12	421-103	Towers High School	Tue 5/12/09	Tue 1/4/11	431 days																									
16	421-104	Columbia High School	Mon 1/1/07	Fri 9/11/09	705 days																									
21	421-105	McNair High School	Mon 12/17/07	Wed 10/28/09	488 days																									
26	421-106	Cross Keys High School	Tue 6/12/07	Wed 8/31/11	1102 days																									
31	421-107	Land	Wed 1/13/10	Thu 5/3/12	602 days																									
32	421-108	Tucker High School	Mon 5/14/07	Tue 11/16/10	917 days																									
37	421-109	Woodward Elementary School	Wed 8/29/07	Fri 1/29/10	633 days																									
42	421-110	Stone Mountain High School	Mon 6/2/08	Thu 11/18/10	644 days																									
47	421-111	Redan High School	Mon 4/14/08	Fri 9/24/10	640 days																									
52	421-112	Midvale Elementary School	Fri 5/1/09	Fri 9/3/10	351 days																									
56	421-113	Stephenson Middle School	Fri 11/17/06	Mon 9/8/08	472 days																									
60	421-114	Clifton Elementary School	Fri 11/17/06	Mon 9/8/08	472 days																									
64	421-115	Cedar Grove High School	Mon 6/23/08	Fri 12/17/10	650 days																									
68	421-116	Vanderlyn Elementary School	Mon 5/25/09	Fri 3/4/11	465 days																									
73	421-117	Chamblee High School	Wed 4/8/09	Tue 12/11/12	960 days																									
78	421-118	Clarkston High School	Mon 2/25/08	Fri 12/30/11	1005 days																									
83	421-119	Druid Hills High School	Mon 5/14/07	Thu 7/29/10	839 days																									
88	421-120	Dunwoody High School	Tue 4/29/08	Mon 3/26/12	1020 days																									
93	421-121	Fairington Elementary School	Mon 6/1/09	Thu 9/23/10	344 days																									
97	421-123	DeKalb School of Arts Relocation	Mon 4/14/08	Thu 5/31/12	1079 days																									
103	421-124	Mountain Industrial Center	Tue 5/22/07	Fri 4/30/10	769 days?																									
112	421-125	Lakeside High School	Mon 3/2/09	Thu 5/10/12	834 days																									
117	421-127	MLK Jr. High School	Mon 4/4/10	Mon 4/1/13	846 days																									
122	421-128	Miller Grove High School	Mon 1/4/10	Mon 4/1/13	846 days																									
127	421-129	Warren Tech	Thu 7/1/10	Mon 7/18/11	273 days																									
132	421-130	McLendon Elementary School	Fri 7/31/09	Tue 3/1/11	413 days																									
136	421-131	Sam Moss Center	Mon 6/30/08	Thu 10/14/10	599 days?																									
138	421-132	Knollwood Elementary School	Thu 7/1/10	Mon 8/15/11	293 days																									
143	421-133	Rockbridge Elementary School	Thu 7/1/10	Mon 8/15/11	293 days																									
148	421-135	Stone Mountain Elementary School - HVAC	Thu 7/1/10	Mon 8/15/11	293 days																									
153	421-136	Hambrick Elementary School - HVAC	Thu 7/1/10	Mon 8/15/11	293 days																									
158	421-138	Montgomery Elementary School	Thu 7/1/10	Mon 8/15/11	293 days																									
163	421-139	Indian Creek Elementary School	Thu 7/1/10	Mon 8/15/11	293 days																									
168	421-140	Stone Mill Elementary School	Thu 7/1/10	Mon 8/15/11	293 days																									
172	421-201	Sky Haven Elementary School	Thu 7/1/10	Mon 8/15/11	293 days																									
177	421-202	Murphy Candler Elementary School	Thu 7/1/10	Mon 8/15/11	293 days																									
182	421-203	Rainbow Elementary School	Thu 7/1/10	Mon 8/15/11	293 days																									
187	421-205	Sequoyah Middle School - Roof Replacement	Mon 5/4/09	Mon 9/13/10	356 days																									
192	421-206	Wedsworth Elementary School	Wed 10/1/08	Tue 8/25/09	235 days																									
197	421-208	Champion Middle School	Mon 4/16/07	Mon 5/24/10	811 days																									
202	421-209	Avondale Elementary School	Wed 10/1/08	Tue 9/1/09	240 days																									
207	421-210	Snappingfinger Elementary School - Roof	Mon 6/1/09	Wed 9/15/10	338 days																									

SPLLOST III CIP Master Program Schedule

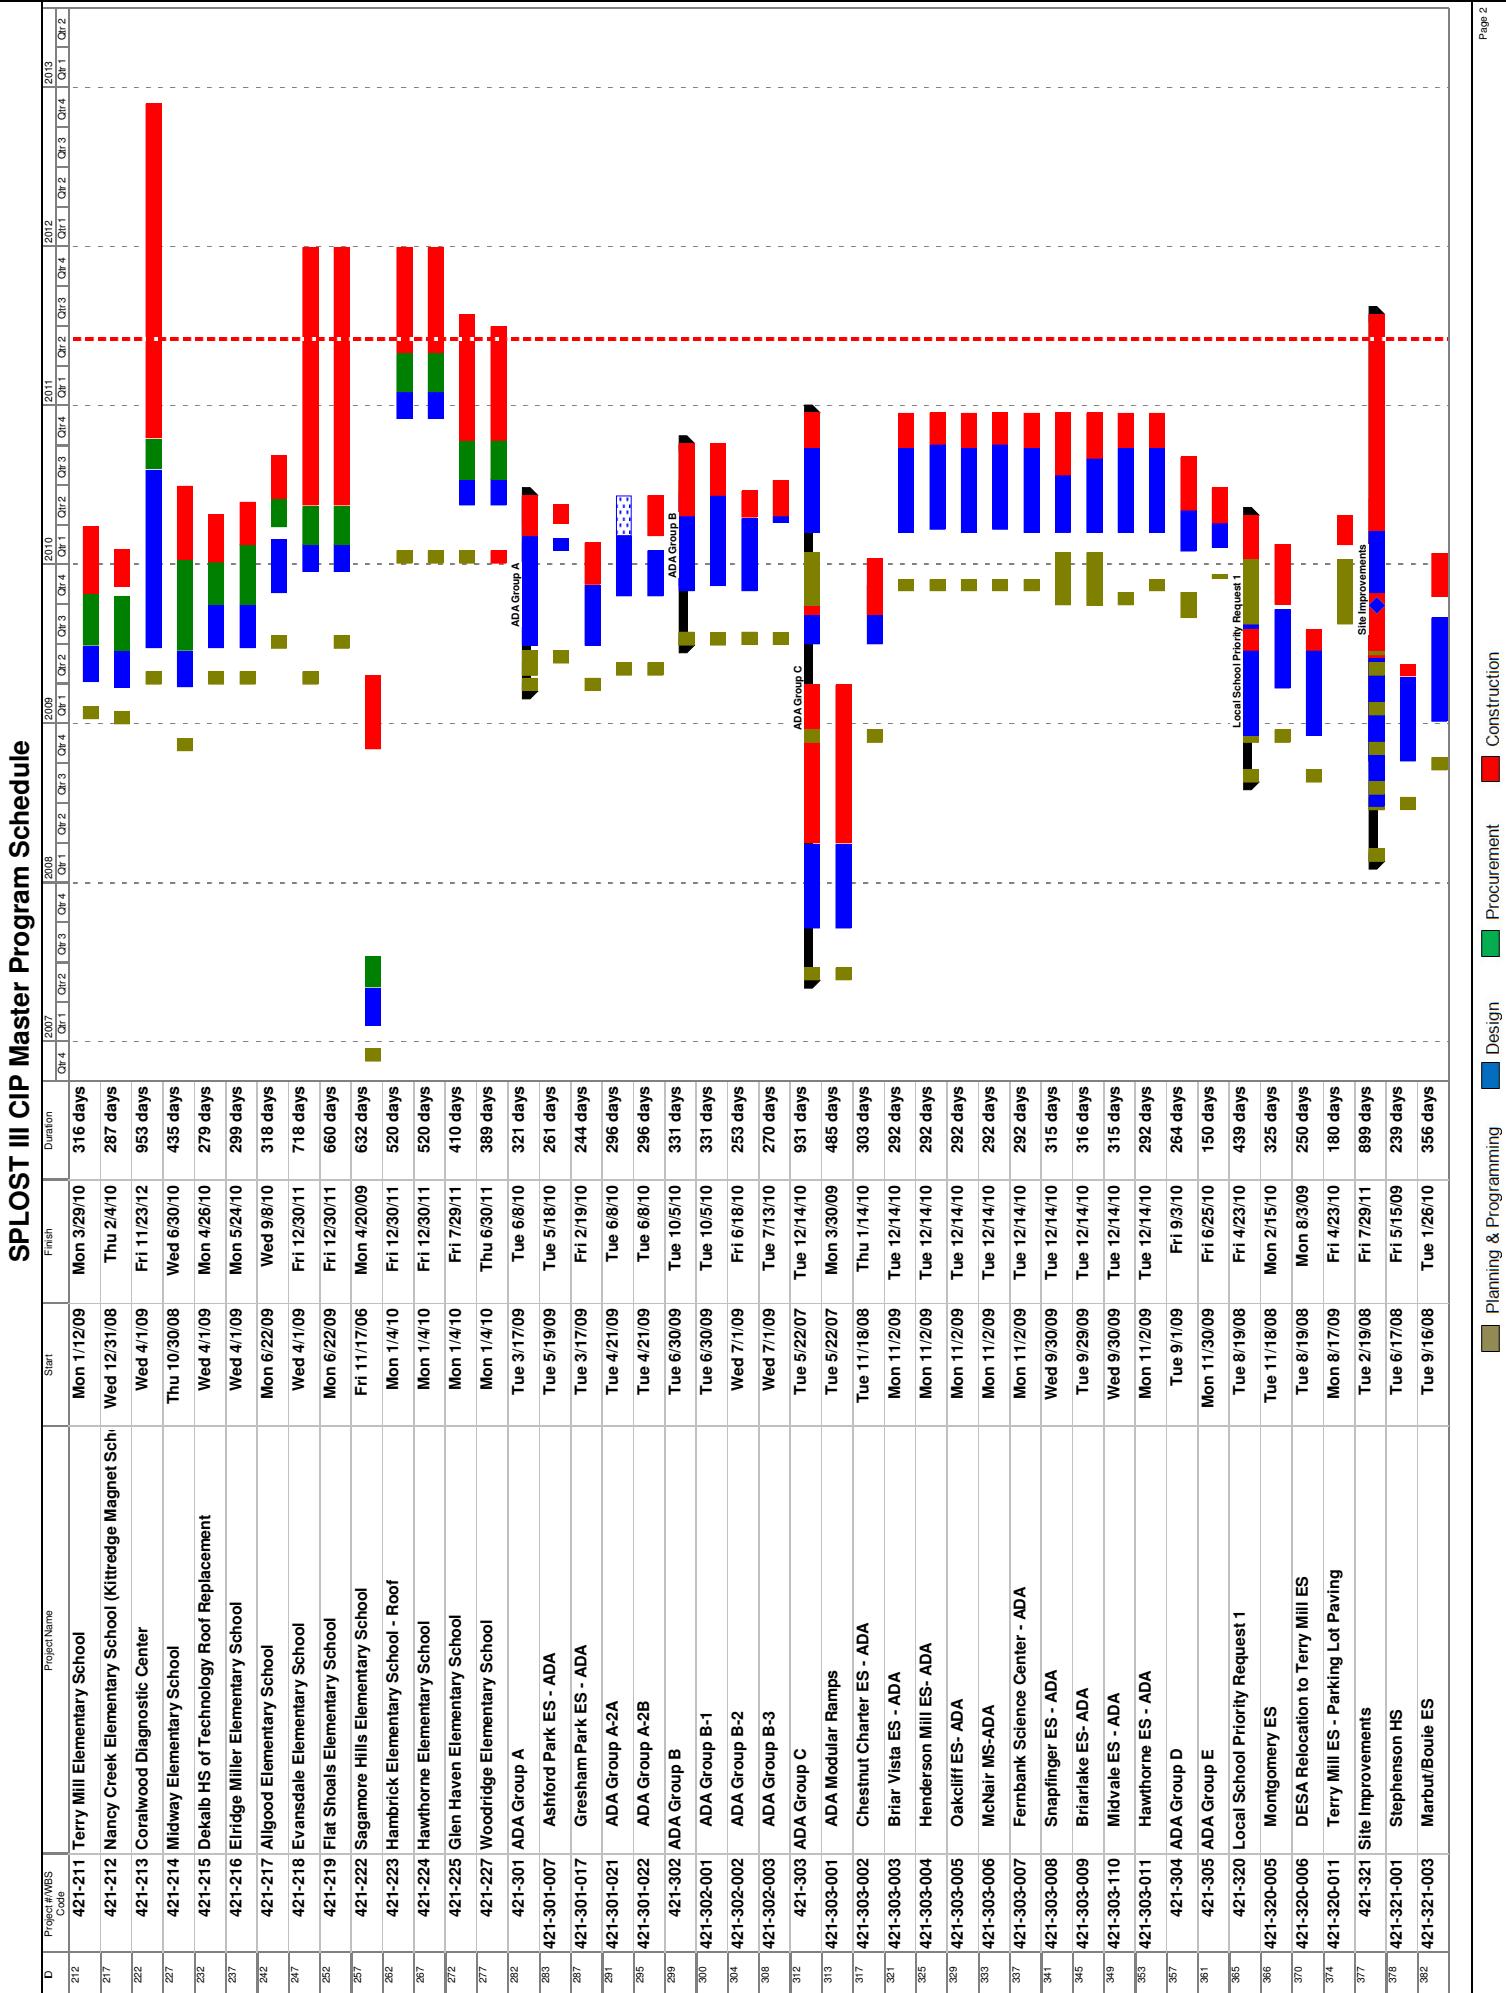

Planning & Programming ■ Design ■ Procurement ■ Construction

SPLOST III CIP Master Program Schedule

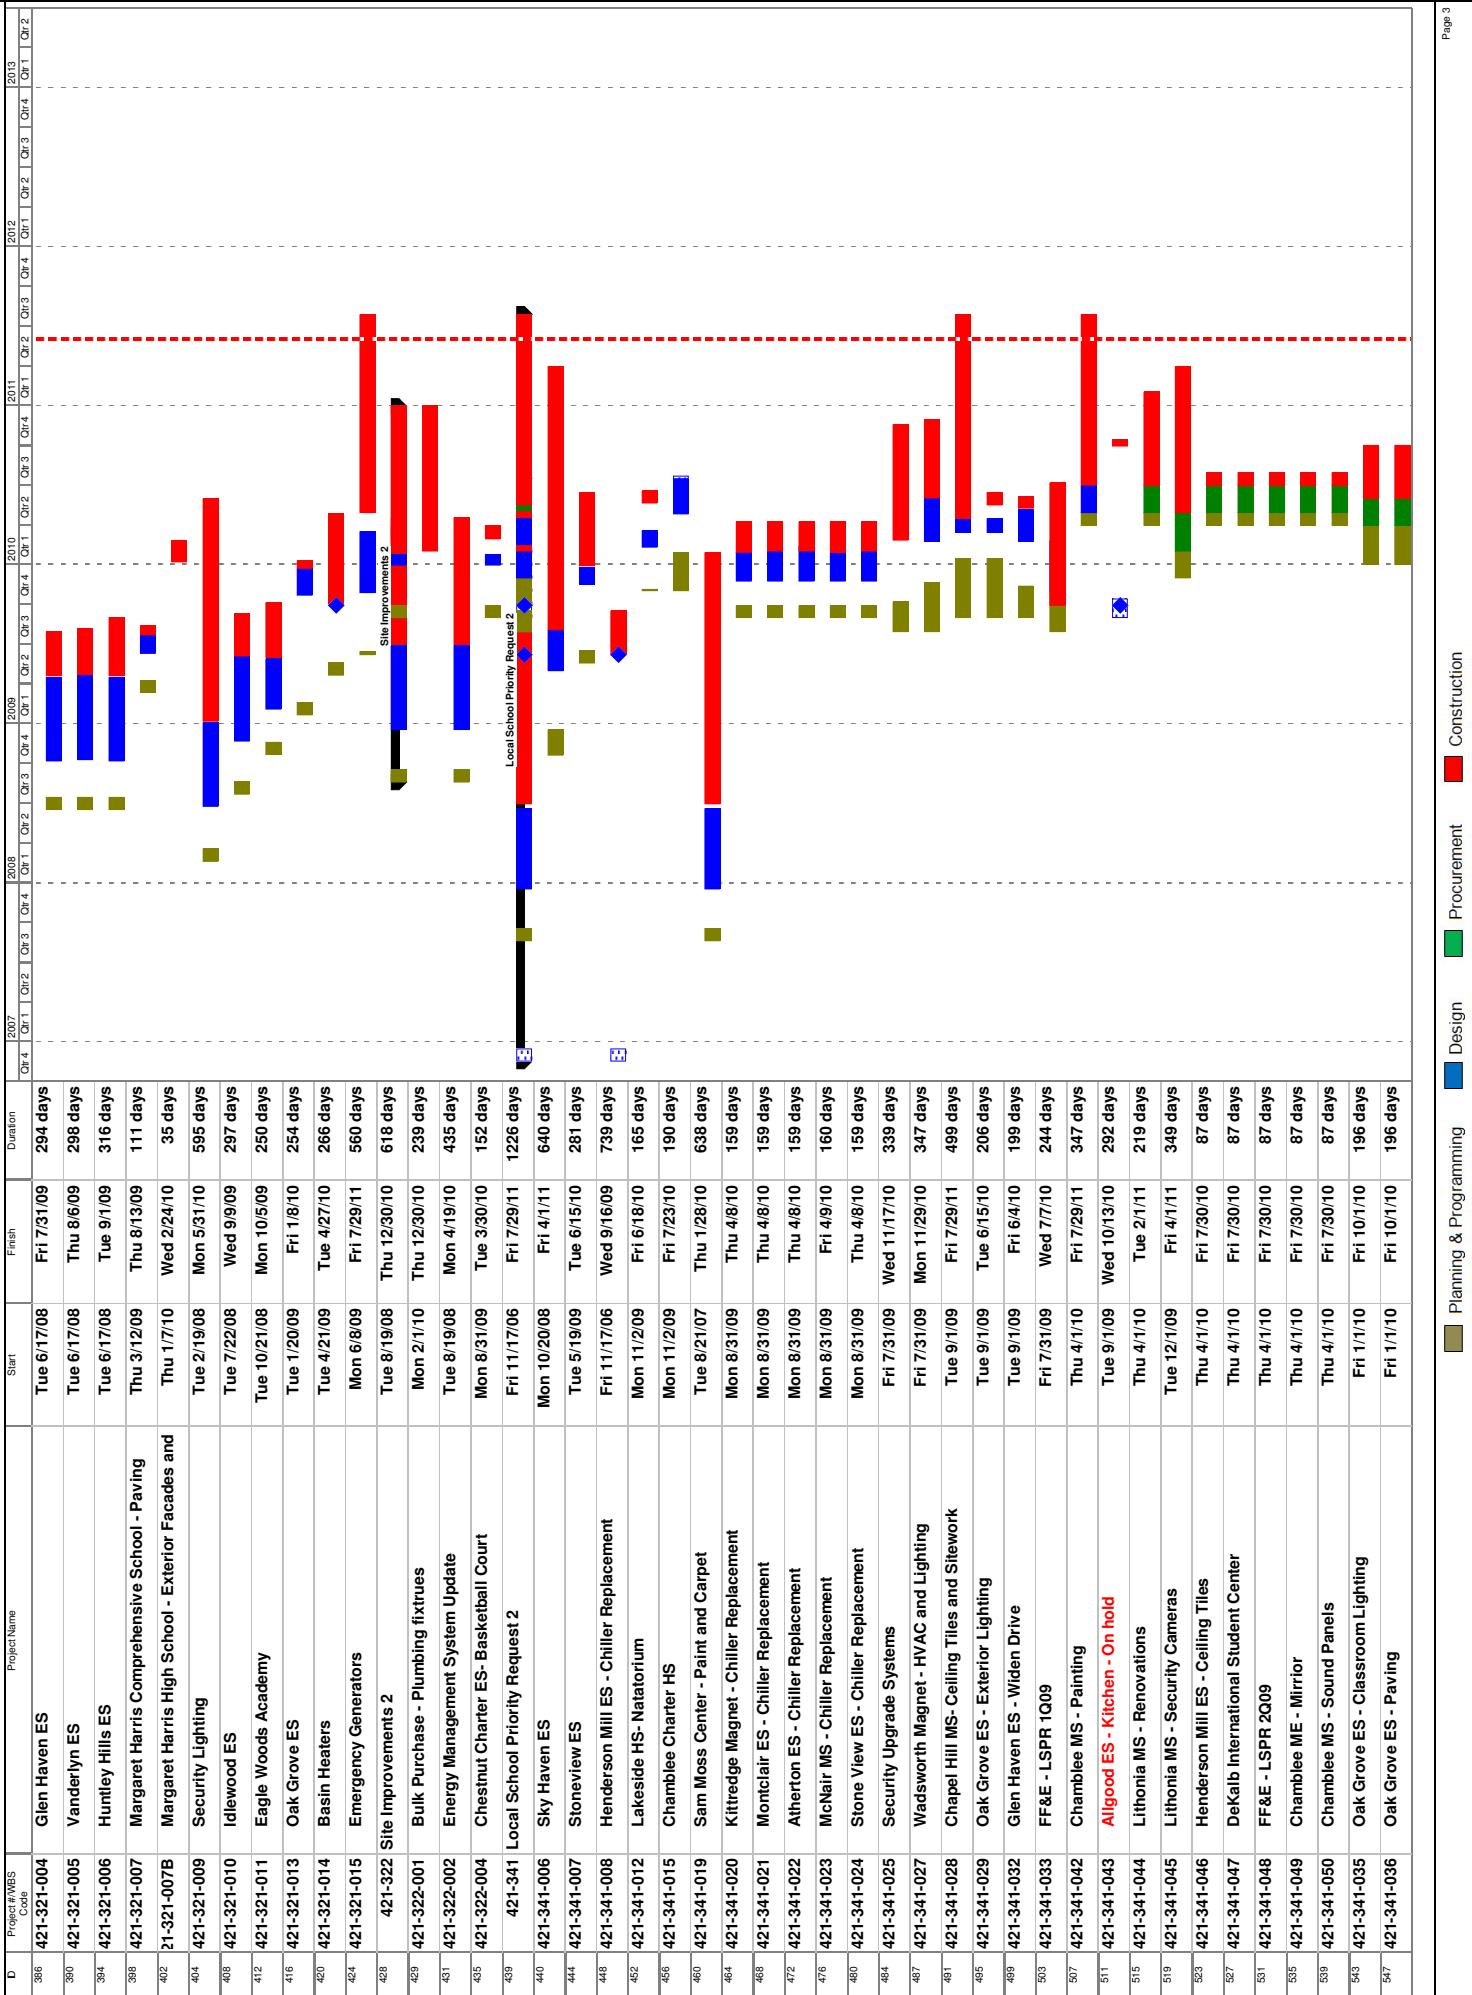


SPLOST III CIP Master Program Schedule

D Project #/WBS Code	Project Name	Start	Finish	Duration	2007				2008				2009				2010				2011				2012				
					Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	
55_1 421-341-038	MS Additional Parking Lot Lighting	Fri 1/1/10	Fri 4/30/10	86 days																									
55_5 421-341-039	Clifton ES - Ceiling Tiles - On hold	Tue 9/1/09	Wed 10/13/10	292 days																									
55_9 421-341-040	Carpet Replacement	Thu 10/1/09	Mon 2/1/10	88 days																									
56_3 421-341-041	Kelley Lakes ES - Courtyard - On hold	Tue 9/1/09	Wed 10/13/10	292 days																									
56_7 421-341-037	Sam Moss Center Paving Repair and Replacement	Thu 10/1/09	Fri 4/30/10	152 days																									
57_1 421-341-051	Chapel Hill MS - Track and Tennis Court	Mon 8/3/09	Mon 8/16/10	271 days																									
57_5 421-401	Buses 1	Thu 1/1/09	Wed 12/30/09	52 wks																									
57_6 421-402	Buses 2	Fri 1/1/10	Thu 12/30/10	52 wks?																									
57_7 421-403	Buses 3	Thu 1/1/09	Wed 12/30/09	52 wks																									
57_8 421-501	Technology Refresh	Thu 1/1/09	Wed 12/30/09	52 wks																									
57_9 421-502	Technology - Media Centers	Fri 1/1/10	Thu 12/30/10	52 wks																									
58_0 421-503	Technology	Fri 1/1/10	Thu 12/30/10	52 wks																									
58_1 421-600	General Services	Mon 2/15/10	Thu 11/3/11	449 days																									
58_2 421-600-002	Bulk Purchase - Ceiling Tile and Grid	Tue 6/1/10	Mon 5/30/11	52 wks																									
58_3 421-600-003	Bulk Purchase - Metal Lockers	Mon 2/15/10	Fri 2/11/11	52 wks																									
58_4 421-600-004	Bulk Purchases - Theatrical Lighting and Sound Sys	Fri 11/5/10	Thu 11/3/11	52 wks																									
58_5 421-600-005	Bulk Purchase - Lighting	Fri 11/5/10	Thu 11/3/11	52 wks																									
58_6 421-600-006	Bulk Purchase - Fixed Audience Seating	Tue 3/9/10	Mon 3/7/11	52 wks																									

 Planning & Programming
  Design
  Procurement
  Construction

Program\DeKalb County\421 SPLOST III\Other Facilities\Administrative & Instructional Complex (AIC)

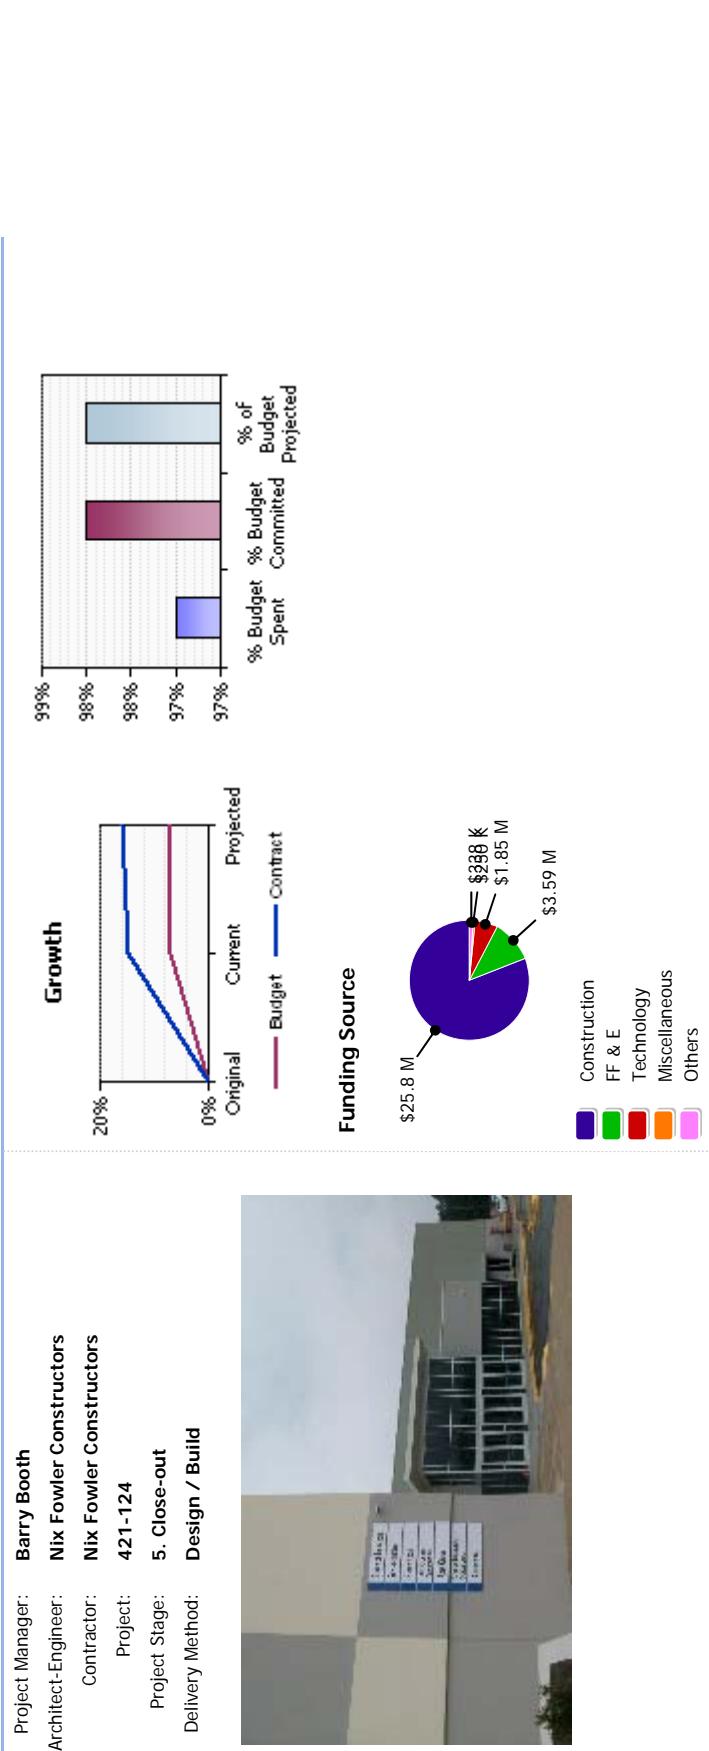

- Phase I (DECA, with Hogan Construction as Design/Builder) was completed in 2008.
- Phase II (all other areas, with Nix-Fowler Constructors as Design/Builder) received the final Certificate of Occupancy on 7/22/10. Project is in the closeout phase. Budget Reallocation is in place for June 2011.

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
Contingency: 9999-9999	\$1,491,815	(\$1,491,815)										
CIT Managed Subtotal	\$27,041,070	(\$650,235)	\$26,390,835	\$21,814,501	\$4,098,276	\$25,912,777	\$25,828,831	\$80,179	\$109,417	\$230,967	\$26,253,161	\$137,674
DCSS Managed												
FF&E: 7700-7504	\$2,045,226	\$1,539,905	\$3,585,131	\$3,573,821		\$3,537,296	\$36,524			\$3,573,821		\$11,310
Technology: 7800-7801	\$750,000	\$1,099,000	\$1,849,000	\$1,566,714		\$1,549,087	\$17,402			\$282,286	\$1,849,000	(\$0)
DCSS Managed Subtotal	\$2,795,226	\$2,638,905	\$5,434,131	\$5,140,535		\$5,086,383	\$53,927			\$282,286	\$5,422,821	\$11,310
Project Total	\$29,836,296	\$1,988,670	\$31,824,966	\$26,955,036	\$4,098,276	\$31,053,312	\$30,915,213	\$134,105	\$109,417	\$513,253	\$31,675,981	\$148,985

Program\DeKalb County\421 SPLOST III\Elementary Schools\Allgood ES - Roof

Project Manager: Yolanda Brown
Architect-Engineer: PCI Group, Inc
Contractor: Klein Contracting Corporation
Project: 421-217
Project Stage: 4. Construction
Delivery Method: Design / Bid / Build

Growth

Period	Value (%)
Original	65%
Current	80%
Projected	85%

Funding Source

Source	Amount (\$K)
Construction	\$521 K
Architect/Engineer	\$3.09 K
Contingency	\$28.3 K
Other Consultants	\$30.2 K
Others	

Budget vs. Actual Spending

Category	Budget	Actual
Original	0%	0%
Contract	10%	10%

Photograph: A large, modern school building with a red roof and glass windows. A sign in the foreground reads "Allgood Elementary School Stone Mountain Georgia".

Scope of Work:	Remarks:
► Full roof replacement	


Scope of Work:

- Full roof replacement with a modified bitumen roofing system.

In Construction Phase - Klein Contracting Corporation is the GC on the project. The cap sheet has been installed in all areas except in the immediate area of the Cafeteria. The work will resume around this area when the replacement of unknown deteriorated or abated material is complete by a change in scope.

Cost Status by Budget Category:												
Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
CT Managed												
Architect/Engineer: 7100-7101	\$30,151		\$15,960		\$597	\$16,557	\$13,318	\$3,239		\$13,594	\$30,151	
Construction Testing: 7100-7103	\$1,500		\$1,500							\$1,500	\$1,500	
Other Consultants: 7100-7105	\$3,174		\$3,121			\$3,121	\$3,121			\$53	\$3,174	
Construction: 7300-7301	\$520,586		\$428,977		\$24,706	\$453,684	\$388,604	\$65,080		\$66,902	\$520,586	
Miscellaneous: 7300-7302	\$1,500		\$700			\$700	\$696	\$4		\$800	\$1,500	
Contingency: 9999-9999	\$28,329									\$28,329	\$28,329	
CT Managed Subtotal	\$585,240		\$448,759		\$25,303	\$474,062	\$405,739	\$68,323		\$111,178	\$585,240	
Project Total	\$585,240		\$448,759		\$25,303	\$474,062	\$405,739	\$68,323		\$111,178	\$585,240	

Program\DeKalb County\421 SPLOST III\Elementary Schools\Avondale ES - Roof

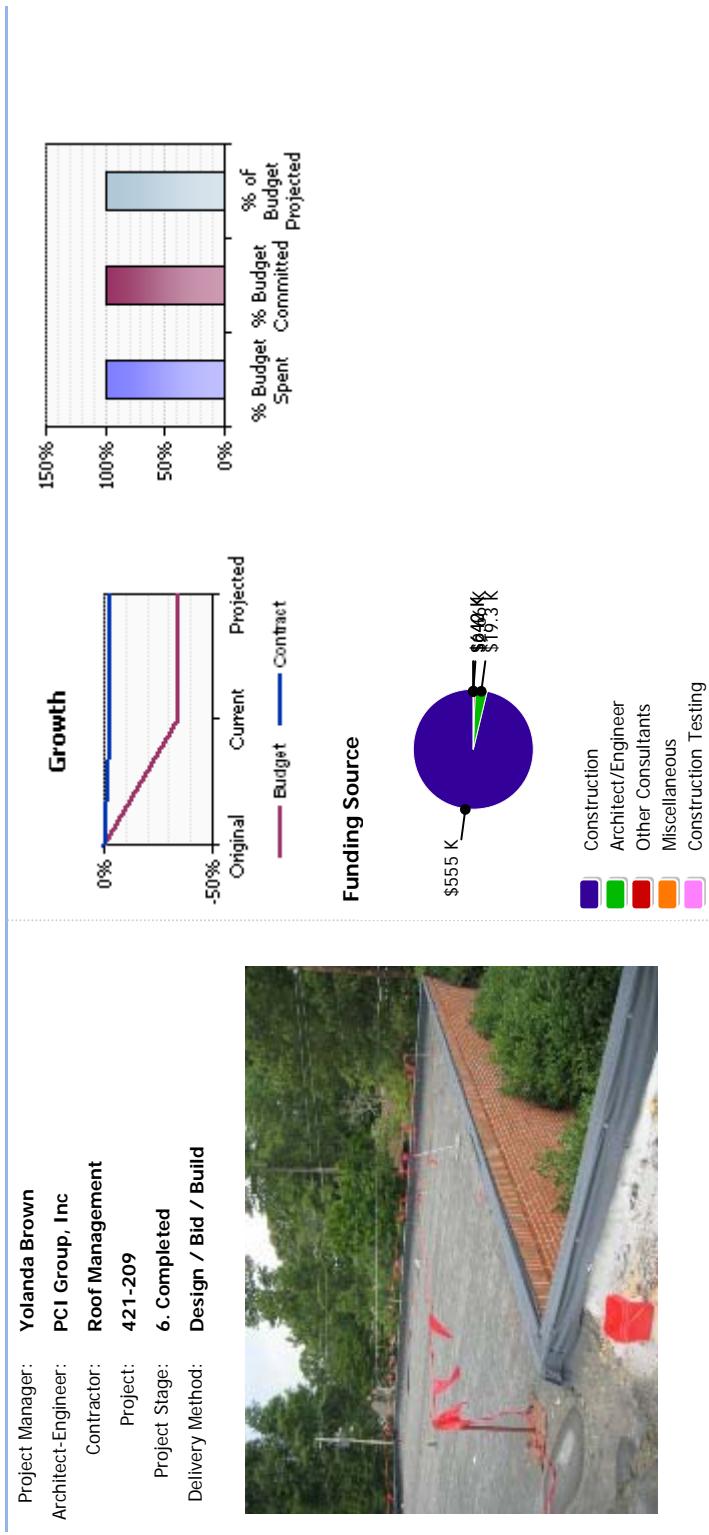


Program\DeKalb County\421 SPLOST III\High Schools\DSA/Avondale HS Relocation to Avondale HS - Modifications

<p>Project Manager: Virgil Bryan</p> <p>Architect-Engineer: Warren Epstein & Associates</p> <p>Contractor: Samples Construction</p> <p>Project: 421-123</p> <p>Project Stage: 5. Close-out</p> <p>Delivery Method: Design / Bid / Build</p>	<p>Growth</p> <table border="1"> <thead> <tr> <th>Original</th> <th>Current</th> <th>Projected</th> <th>% Budget Spent</th> <th>% Budget Committed</th> <th>% Budget Projected</th> </tr> </thead> <tbody> <tr> <td>83%</td> <td>84%</td> <td>86%</td> <td>84%</td> <td>85%</td> <td>87%</td> </tr> </tbody> </table>	Original	Current	Projected	% Budget Spent	% Budget Committed	% Budget Projected	83%	84%	86%	84%	85%	87%	<p>Funding Source</p> <table border="1"> <thead> <tr> <th>Category</th> <th>Amount</th> </tr> </thead> <tbody> <tr> <td>Budget</td> <td>\$3.45 M</td> </tr> <tr> <td>Contract</td> <td>\$666 K</td> </tr> <tr> <td>Construction</td> <td>\$561 K</td> </tr> <tr> <td>FF & E</td> <td>\$380 K</td> </tr> <tr> <td>Architect/Engineer</td> <td>\$512 K</td> </tr> <tr> <td>Technology</td> <td>\$300 K</td> </tr> <tr> <td>Others</td> <td>\$100 K</td> </tr> </tbody> </table>	Category	Amount	Budget	\$3.45 M	Contract	\$666 K	Construction	\$561 K	FF & E	\$380 K	Architect/Engineer	\$512 K	Technology	\$300 K	Others	\$100 K	<p>Scope of Work:</p> <ul style="list-style-type: none"> The project includes renovation of the third wing at Avondale HS to accommodate the relocation of DeKalb School of the Arts (DSA) and an addition to the existing auditorium. Also included is a renovation to the technology wing to accommodate ROTC and the gym stage to accommodate the band. Four (4) new classrooms were also built for the 9th grade academy. <p>Remarks:</p> <ul style="list-style-type: none"> 02/17/11: Warranty walk through has taken place, and a list of repairs has been provided to the GC. Work to be scheduled during late Feb to early March 2011. Met with GC to review close out and payment holds - there remains 2 items to resolve in order for close out to be completed. 	<p>Cost Status by Budget Category:</p> <table border="1"> <thead> <tr> <th>Budget Category</th> <th>Original Budget</th> <th>Budget Revision</th> <th>Current Budget</th> <th>Original Contract</th> <th>Executed Changes</th> <th>Current Contract</th> <th>Paid To Date</th> <th>Contract Balance</th> <th>CORs</th> <th>ETC Forecast</th> <th>Estimate At Completion</th> <th>Uncommitted</th> </tr> </thead> <tbody> <tr> <td>CIT Managed</td> <td></td> </tr> <tr> <td>Architect/Engineer: 7100-7101</td> <td>\$491,540</td> <td>\$20,000</td> <td>\$511,540</td> <td>\$406,500</td> <td>\$11,500</td> <td>\$418,000</td> <td>\$408,168</td> <td>\$9,832</td> <td></td> <td>\$8,000</td> <td>\$426,000</td> <td>\$85,540</td> </tr> <tr> <td>Surveying: 7100-7102</td> <td>\$25,000</td> <td>(\$10,700)</td> <td>\$14,300</td> <td>\$14,300</td> <td></td> <td>\$14,300</td> <td>\$14,300</td> <td></td> <td></td> <td></td> <td>\$14,300</td> <td></td> </tr> <tr> <td>Construction Testing: 7100-7103</td> <td>\$52,751</td> <td>\$45,000</td> <td>\$97,751</td> <td>\$59,498</td> <td></td> <td>\$59,498</td> <td>\$59,498</td> <td></td> <td></td> <td></td> <td>\$28,200</td> <td>\$87,698</td> </tr> <tr> <td>Abatement: 7100-7104</td> <td>\$30,000</td> <td>\$40,000</td> <td>\$70,000</td> <td>\$23,579</td> <td></td> <td>\$23,579</td> <td>\$23,579</td> <td></td> <td></td> <td></td> <td>\$16,400</td> <td>\$10,053</td> </tr> <tr> <td>Other Consultants: 7100-7105</td> <td>\$83,587</td> <td>\$83,587</td> <td>\$83,587</td> <td>\$5,300</td> <td>\$2,477</td> <td>\$7,777</td> <td>\$800</td> <td>\$6,977</td> <td></td> <td></td> <td>\$39,979</td> <td>\$30,021</td> </tr> <tr> <td>Management Fees: 7200-7201</td> <td>\$170,585</td> <td>(\$170,585)</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>\$75,000</td> <td>\$82,777</td> </tr> </tbody> </table>	Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted	CIT Managed													Architect/Engineer: 7100-7101	\$491,540	\$20,000	\$511,540	\$406,500	\$11,500	\$418,000	\$408,168	\$9,832		\$8,000	\$426,000	\$85,540	Surveying: 7100-7102	\$25,000	(\$10,700)	\$14,300	\$14,300		\$14,300	\$14,300				\$14,300		Construction Testing: 7100-7103	\$52,751	\$45,000	\$97,751	\$59,498		\$59,498	\$59,498				\$28,200	\$87,698	Abatement: 7100-7104	\$30,000	\$40,000	\$70,000	\$23,579		\$23,579	\$23,579				\$16,400	\$10,053	Other Consultants: 7100-7105	\$83,587	\$83,587	\$83,587	\$5,300	\$2,477	\$7,777	\$800	\$6,977			\$39,979	\$30,021	Management Fees: 7200-7201	\$170,585	(\$170,585)									\$75,000	\$82,777
Original	Current	Projected	% Budget Spent	% Budget Committed	% Budget Projected																																																																																																																																			
83%	84%	86%	84%	85%	87%																																																																																																																																			
Category	Amount																																																																																																																																							
Budget	\$3.45 M																																																																																																																																							
Contract	\$666 K																																																																																																																																							
Construction	\$561 K																																																																																																																																							
FF & E	\$380 K																																																																																																																																							
Architect/Engineer	\$512 K																																																																																																																																							
Technology	\$300 K																																																																																																																																							
Others	\$100 K																																																																																																																																							
Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted																																																																																																																												
CIT Managed																																																																																																																																								
Architect/Engineer: 7100-7101	\$491,540	\$20,000	\$511,540	\$406,500	\$11,500	\$418,000	\$408,168	\$9,832		\$8,000	\$426,000	\$85,540																																																																																																																												
Surveying: 7100-7102	\$25,000	(\$10,700)	\$14,300	\$14,300		\$14,300	\$14,300				\$14,300																																																																																																																													
Construction Testing: 7100-7103	\$52,751	\$45,000	\$97,751	\$59,498		\$59,498	\$59,498				\$28,200	\$87,698																																																																																																																												
Abatement: 7100-7104	\$30,000	\$40,000	\$70,000	\$23,579		\$23,579	\$23,579				\$16,400	\$10,053																																																																																																																												
Other Consultants: 7100-7105	\$83,587	\$83,587	\$83,587	\$5,300	\$2,477	\$7,777	\$800	\$6,977			\$39,979	\$30,021																																																																																																																												
Management Fees: 7200-7201	\$170,585	(\$170,585)									\$75,000	\$82,777																																																																																																																												

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
Construction: 7300-7301	\$7,290,748	(\$3,845,000)	\$3,445,748	\$3,274,304	\$104,892	\$3,379,196	\$3,292,583	\$18,603	\$47,317		\$3,426,513	\$19,235
Miscellaneous: 7300-7302	\$370,039	(\$354,999)	\$15,040	\$7,707		\$7,707	\$5,907	\$1,633			\$7,707	\$7,333
Security: 7400-7401	\$25,000	\$50,000	\$15,000	\$22,752		\$22,752	\$22,752				\$44,752	\$30,248
Utilities: 7500-7501	\$75,000	(\$50,000)	\$25,000								\$25,000	\$25,000
Moving / Relocation: 7500-7502	\$125,000	\$5,000	\$93,094		\$93,094	\$93,094	\$695	\$11,900			\$104,994	\$25,006
Trailers: 7600-7503	\$54,999	\$54,999	\$13,045		\$13,045	\$13,045	\$10,718	\$1,956			\$13,045	\$41,954
Contingency: 99999-99999	\$500,000	(\$400,000)	\$100,000									\$100,000
CIT Managed Subtotal	\$9,239,250	(\$4,616,285)	\$4,622,965	\$3,920,080	\$118,869	\$4,038,949	\$3,931,439	\$38,307	\$47,317	\$186,500	\$4,272,766	\$350,199
DCSS Managed												
FF&E: 7700-7504	\$460,750	\$100,000	\$560,750	\$429,581		\$429,581	\$406,591	\$22,990			\$460,581	\$100,169
Technology: 7800-7801	\$300,000	\$80,000	\$280,000	\$285,839		\$285,839	\$285,746	\$93			\$299,839	\$80,161
DCSS Managed Subtotal	\$760,750	\$180,000	\$940,750	\$715,420		\$715,420	\$692,338	\$23,083			\$760,420	\$180,330
Project Total	\$10,000,000	(\$4,436,285)	\$5,563,715	\$4,635,500	\$118,869	\$4,754,369	\$4,623,777	\$61,390	\$47,317	\$231,500	\$5,033,186	\$530,529

Program\DeKalb County\421 SPLOST III\High Schools\DSA/Avondale HS Relocation to Avondale HS - Renovations

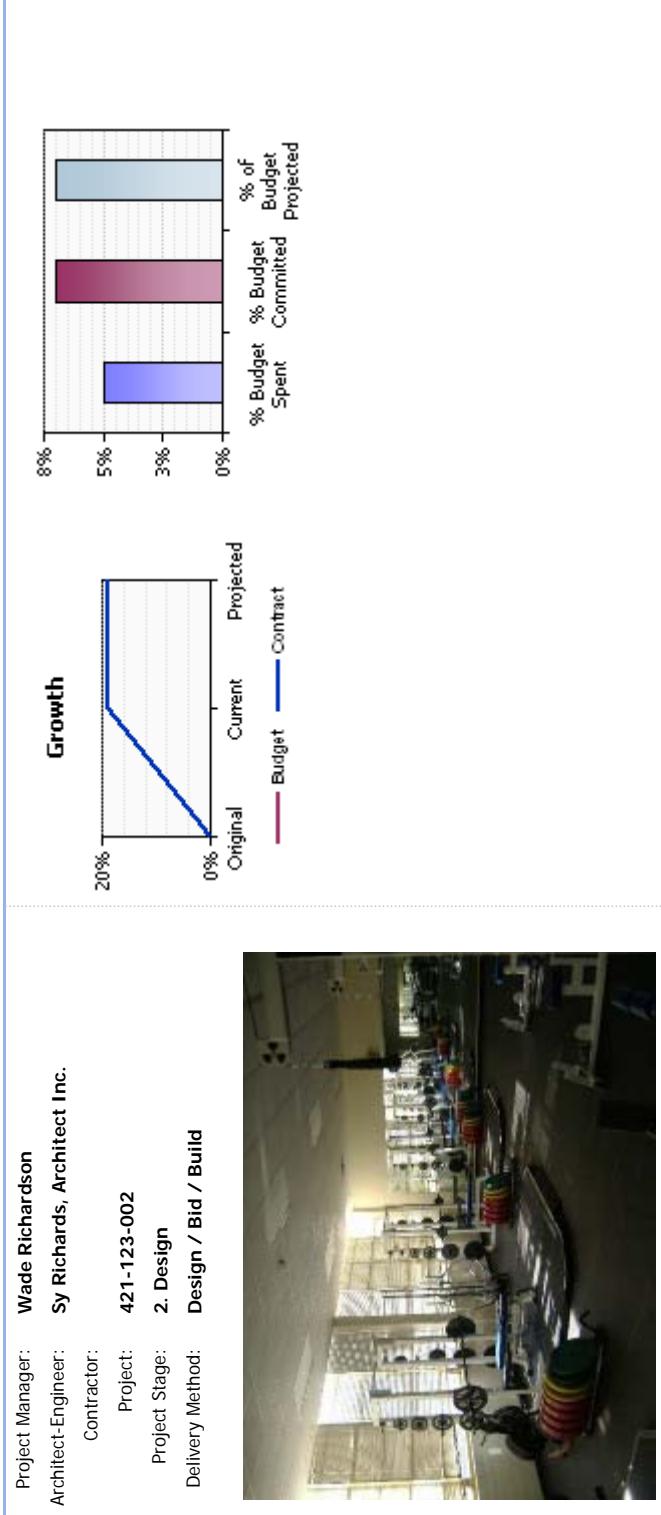

Scope of Work:


- Redesign of the existing locker rooms and adjacent spaces, window replacement, weight room, dumpster pad, roof replacement, renovation of four existing science labs, site modifications - damaged sidewalks, ROTC drill pad, and parking lot repair (if allowed within the budget)
- Remarks:
- 100% Design documents for AHS/DSA Roof replacement has been submitted and under review. The roof replacement is projected to be ready for bid in April. DSA is reviewing proposed A/V system program prepared by Larry Steele.

Cost Status by Budget Category:

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORS	ETC Forecast	Estimate At Completion	Uncommitted
CIT Managed												
Architect/Engineer: 7100-7101	\$200,000	\$200,000	\$137,500	\$49,566	\$187,066	\$40,247	\$113,127			\$12,934	\$200,000	
Surveying: 7100-7102	\$10,700	\$10,700								\$10,700	\$10,700	
Construction Testing: 7100-7103	\$40,000	\$40,000								\$40,000	\$40,000	
Abatement: 7100-7104	\$60,000	\$60,000	\$6,687			\$6,687				\$53,313	\$60,000	
Construction: 7300-7301	\$3,595,000	\$3,595,000	\$59,498			\$59,498	\$13,841			\$3,535,502	\$3,595,000	
Miscellaneous: 7300-7302	\$70,000	\$70,000	\$25,838			\$25,838	\$25,337	\$501		\$44,162	\$70,000	
Utilities: 7500-7501	\$50,000	\$50,000	\$2,327			\$2,327				\$47,673	\$50,000	

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORS	ETC Forecast	Estimate At Completion	Uncommitted
Moving / Relocation: 7500-7502	\$20,000	\$20,000	\$15,925			\$15,925	\$10,934	\$3,816		\$4,075	\$20,000	
Trailers: 7600-7503	\$50,000	\$50,000	\$3,267			\$3,267	\$2,350	(\$590)		\$46,733	\$50,000	
Contingency: 99999-99999	\$165,000	\$165,000								\$165,000	\$165,000	
CIT Managed Subtotal	<u>\$4,260,700</u>	<u>\$4,260,700</u>	<u>\$251,042</u>	<u>\$49,566</u>	<u>\$300,608</u>	<u>\$99,417</u>	<u>\$116,854</u>			<u>\$3,960,092</u>	<u>\$4,260,700</u>	
DCSS Managed												
FF&E: 7700-7504	\$5,000	\$5,000	\$4,000			\$4,000	\$4,000			\$1,000	\$5,000	
DCSS Managed Subtotal	<u>\$5,000</u>	<u>\$5,000</u>	<u>\$4,000</u>	<u>\$4,000</u>	<u>\$4,000</u>	<u>\$4,000</u>	<u>\$4,000</u>	<u>\$1,000</u>	<u>\$1,000</u>	<u>\$5,000</u>	<u>\$5,000</u>	
Project Total	<u>\$4,265,700</u>	<u>\$4,265,700</u>	<u>\$255,042</u>	<u>\$49,566</u>	<u>\$304,608</u>	<u>\$103,417</u>	<u>\$116,854</u>			<u>\$3,961,092</u>	<u>\$4,265,700</u>	

Program\DeKalb County\421 SPlOSt III\Site Improvements\Site Improvements 2 (322)\Bulk Purchase - Plumbing Fixtures

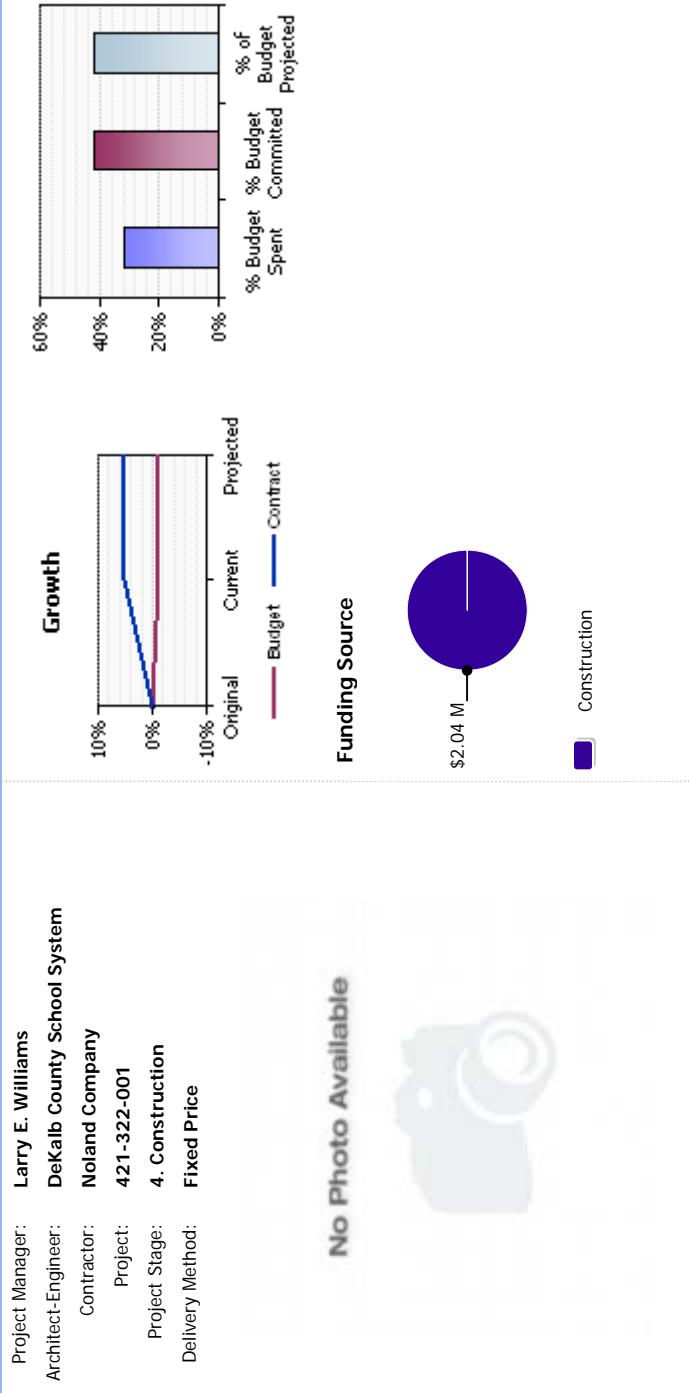

Scope of Work:

- Bulk purchase consisting of toilets, sinks, drinking fountains, and urinals. The budget includes installation at selected schools.


Remarks:

- The following schools plumbing fixtures have been replaced; Oak Grove ES, McLendon ES, Woodridge ES, Brockett ES, Cedar Grove ES, Livsey ES, Austin ES, Kingsley ES, Ashford Park ES, Dresden ES, Rainbow ES and Rock Chapel ES, Hambrick ES, Sagamore ES, Henderson Mill ES, Idlewood ES, Indian Creek ES and Woodward ES. Schools with pending WAs are Huntley ES/Montgomery ES and Cary Reynolds ES/Smoke Rise ES

Cost Status by Budget Category:


Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
CIT Managed												
Construction: 7300-7301	\$2,069,950	(\$26,000)	\$2,043,950	\$825,512	\$40,625	\$866,137	\$442,320	\$368,681		\$1,167,036	\$2,033,173	\$10,777
CIT Managed Subtotal	\$2,069,950	(\$26,000)	\$2,043,950	\$825,512	\$40,625	\$866,137	\$442,320	\$368,681		\$1,167,036	\$2,033,173	\$10,777
Project Total	\$2,069,950	(\$26,000)	\$2,043,950	\$825,512	\$40,625	\$866,137	\$442,320	\$368,681		\$1,167,036	\$2,033,173	\$10,777

Program\DeKalb County\421 SPLOST III\High Schools\Cedar Grove HS - HVAC, Ceiling, Lighting & Roof

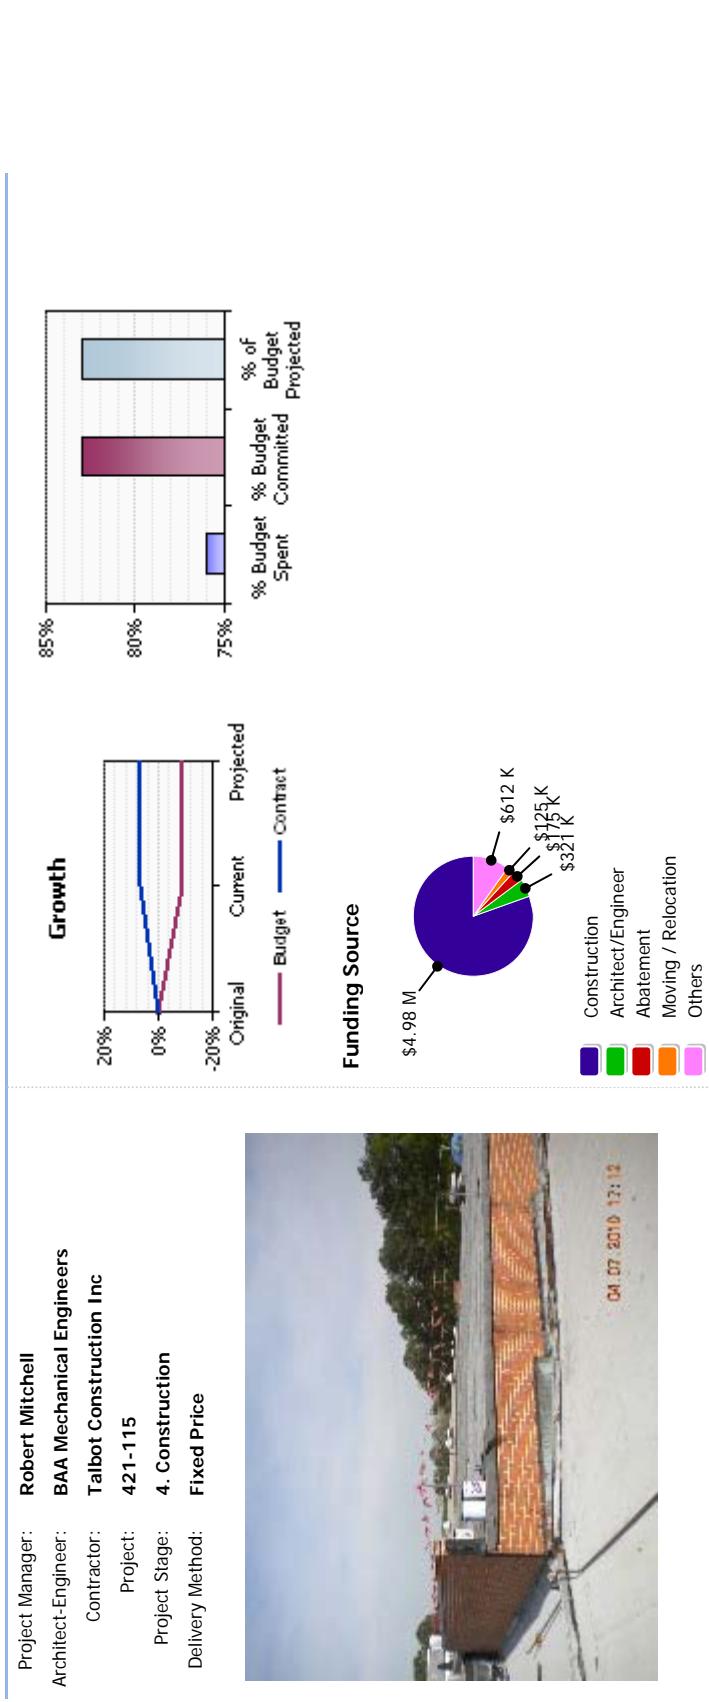

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
Security: 7400-7401	\$30,000	\$40,000	\$70,000	\$27,425		\$27,425	\$51,905	(\$24,480)	\$40,000	\$67,425	\$2,575	
Utilities: 7500-7501	\$75,000	\$75,000									\$75,000	
Moving / Relocation: 7500-7502	\$125,000	\$125,000	\$100,843			\$100,843	\$78,760	\$17,674	\$20,000	\$120,843	\$4,157	
Trailers: 7600-7503	\$250,000	(\$199,999)	\$50,001								\$50,001	
Contingency: 9999-9999	\$342,850	(\$278,000)	\$6,850	\$4,755,874	\$327,310	\$5,083,183	\$4,174,865	\$860,454	\$10,000	\$10,000	\$54,850	
CIT Managed Subtotal	\$6,856,998	(\$760,682)	\$6,096,316						\$305,000	\$5,388,183	\$708,133	
DCSS Managed												
Technology: 7800-7801	\$114,999	\$114,999	\$71,983			\$71,983	\$24,947	\$46,209	\$40,000	\$111,983	\$3,016	
DCSS Managed Subtotal	\$114,999	\$114,999	\$71,983			\$71,983	\$24,947	\$46,209	\$40,000	\$111,983	\$3,016	
Project Total	\$6,856,998	(\$645,683)	\$6,211,315	\$4,827,857	\$327,310	\$5,155,166	\$4,199,812	\$906,664	\$345,000	\$5,500,166	\$711,149	

Program\DeKalb County\421 SPLOST III\High Schools\Chamblee HS- New Replacement High School

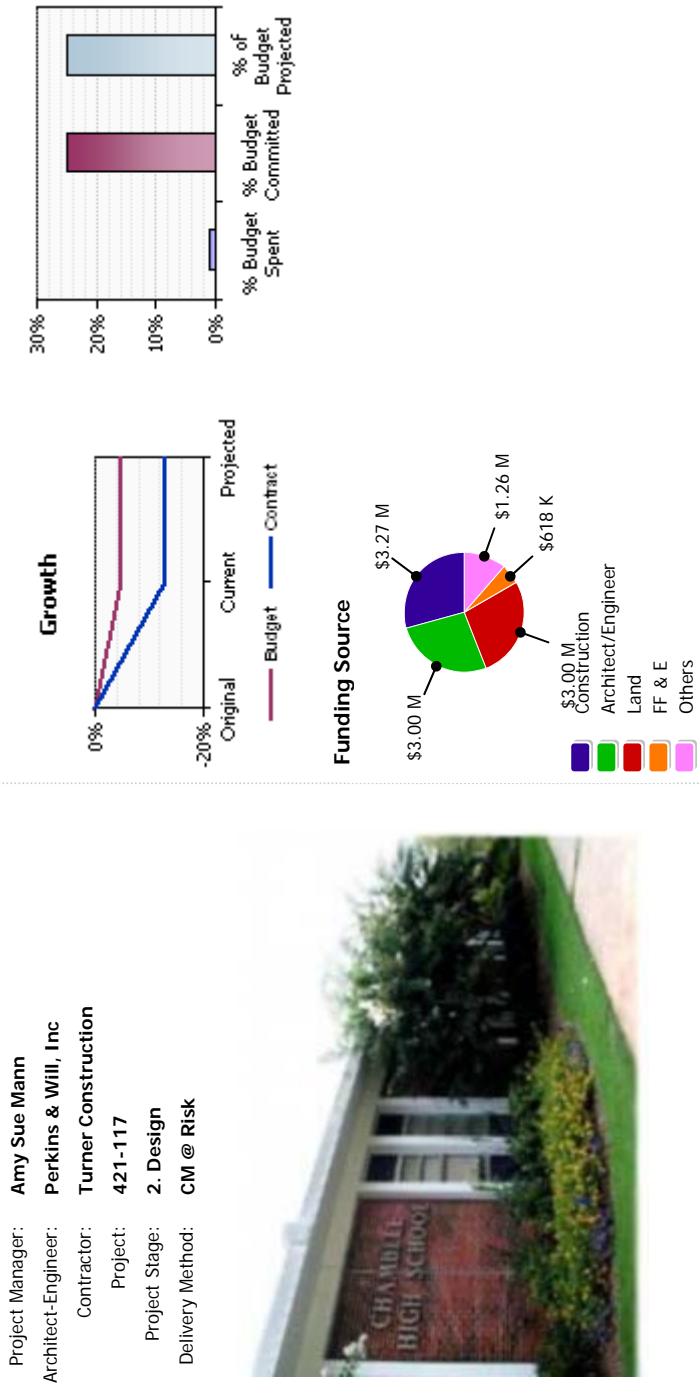


Cost Status by Budget Category:

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	Forecast	ETC	Estimate At Completion	Uncommitted
CIT Managed													
Architect/Engineer: 7100-7101	\$540,126	\$2,459,874	\$3,000,000	\$2,905,051		\$2,905,051	\$31,301	\$2,873,750		\$94,949	\$3,000,000		
Surveying: 7100-7102	\$20,000		\$20,000	\$13,495		\$13,495				\$6,505	\$20,000		
Construction Testing: 7100-7103	\$78,500			\$27,910		\$12,420				\$50,590	\$78,500		
Other Consultants: 7100-7105	\$67,300	\$2,500	\$69,800	\$36,242		\$15,232				\$32,058	\$69,800		
Management Fees: 7200-7201	\$572,800	(\$572,800)											
Construction: 7300-7301	\$8,932,106	(\$5,659,874)	\$3,272,232										
Construction Technology: 7300-7301.22		\$94,000	\$94,000								\$94,000		
Miscellaneous: 7300-7302	\$183,436	(\$2,500)	\$180,936	\$1,425		\$1,425	\$960				\$179,511	\$180,936	
Security: 7400-7401	\$50,000		\$50,000								\$50,000		

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
Utilities: 7500-7501	\$100,000		\$100,000	\$75,000	\$4,000		\$4,000	\$1,733	(\$221)	\$100,000	\$100,000	
Moving / Relocation: 7500-7502	\$75,000		\$200,000	\$200,000	\$182,002		\$182,002	\$182,002		\$71,000	\$75,000	
Trailers: 7600-7503											\$182,002	\$17,998
Contingency: 9999-9999	\$338,450	(\$94,000)	\$244,450							\$244,450		
CIT Managed Subtotal	\$10,957,718	(\$3,572,800)	\$7,384,918	\$3,170,125		\$3,170,125	\$75,141	\$3,062,590	\$1,500	\$4,195,295	\$7,366,920	\$17,998
DCSS Managed												
Land: 7100-7150	\$3,000,000	\$3,000,000								\$2,500,000	\$2,500,000	\$500,000
FF&E: 7700-7504	\$617,589		\$617,589							\$617,589		
Technology: 7800-7801	\$150,000		\$150,000							\$150,000		
DCSS Managed Subtotal	\$767,589	\$3,000,000	\$3,767,589							\$3,267,589		
Project Total	\$11,725,307	(\$572,800)	\$11,152,507	\$3,170,125		\$3,170,125	\$75,141	\$3,062,590	\$1,500	\$7,462,884	\$10,634,509	\$517,998

Program\DeKalb County\421 SPLOST III\High Schools\Clarkston HS - Renovation & Addition

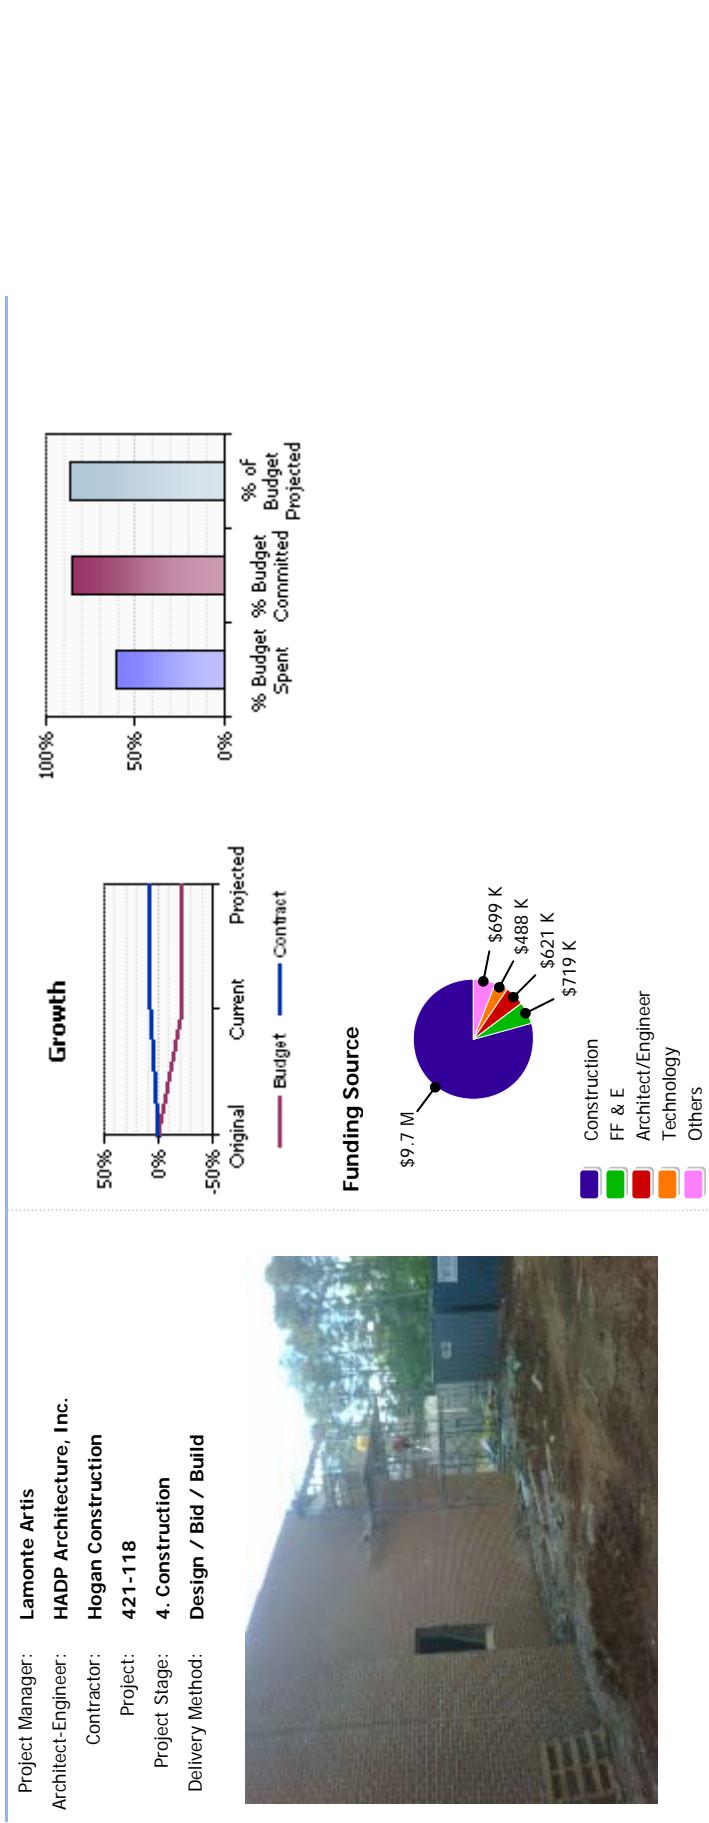

Scope of Work:

- A building addition of 32,000 SF that includes Career Technology space and a new auditorium. Also included is replacement of HVAC, ceiling and lighting systems in the existing building as well as other facility improvements.
- Construction and renovation activities are currently taking place in Phases 7 and 13. The new exhaust hood for the professional food service program has been installed in phase 7. The roof structure for the new addition is 80% complete. New emergency generator has been tested and passed for proper sequencing. Construction started on June 2, 2010, anticipated completion date 3rd quarter 2011. Budget Reallocation in process for June 2011.


Remarks:

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
CIT Managed												
Architect/Engineer: 7100-7101	\$721,378	(\$100,000)	\$621,378	\$588,101	\$17,340	\$605,441	\$554,714	\$27,760		\$15,937	\$621,378	
Surveying: 7100-7102	\$20,000	\$19,000	\$39,000	\$32,030		\$32,030	\$30,250			\$6,970	\$39,000	
Construction Testing: 7100-7103	\$100,000		\$100,000	\$34,979		\$35,933	(\$6,606)			\$65,021	\$100,000	
Abatement: 7100-7104	\$20,000			\$17,640		\$17,640	\$7,492			\$15,503	\$33,143	
Other Consultants: 7100-7105	\$57,672		\$57,672	\$4,843		\$4,843	\$4,843			\$52,829	\$57,672	
Management Fees: 7200-7201	\$419,488	(\$419,488)										
Construction: 7300-7301	\$12,002,960	(\$2,255,000)	\$9,747,960	\$8,824,039	\$749,279	\$9,573,318	\$3,821,243	\$2,840,758	\$146,249	(\$188,094)	\$9,531,473	\$216,487
Construction Technology: 7300-7301-22	\$212,000		\$212,000	\$11,451		\$11,451				\$200,549	\$212,000	
Miscellaneous: 7300-7302	\$270,126	(\$213,143)	\$56,983	\$557		\$557				\$56,426	\$56,983	

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
Security: 7400-7401	\$75,000	<u>(\$50,000)</u>	\$25,000							\$25,000	\$25,000	
Utilities: 7500-7501	\$165,000	<u>(\$125,000)</u>	\$40,000	\$8,424		\$8,424				\$31,500	\$39,924	\$76
Moving / Relocation: 7500-7502	\$100,000	<u>(\$45,000)</u>	\$55,000	\$60,415		\$53,945					\$60,415	<u>(\$5,415)</u>
Contingency: 9999-9999	\$536,325	<u>(\$456,000)</u>	\$80,325							\$73,600	\$73,600	\$6,725
CIT Managed Subtotal	\$14,487,949	<u>(\$3,419,488)</u>	\$11,068,461	\$9,582,478	<u>\$766,619</u>	\$10,349,097	<u>\$4,508,977</u>	\$2,879,826	<u>\$146,249</u>	\$355,241	\$10,850,587	\$217,874
DCSS Managed												
FF & E: 7700-7504	\$718,733		\$718,733	\$30,453		\$30,453				\$688,189	\$718,642	\$91
Technology: 7800-7801	\$488,000		\$488,000	\$9,459		\$9,459				\$478,541	\$488,000	<u>(\$90)</u>
DCSS Managed Subtotal	\$1,206,733		<u>\$1,206,733</u>	\$39,912		\$39,912				\$19,323	\$1,166,730	\$1,206,642
Project Total	\$15,694,682	<u>(\$3,419,488)</u>	\$12,275,194	\$9,622,390	<u>\$766,619</u>	\$10,389,009	<u>\$4,524,997</u>	\$2,899,149	<u>\$146,249</u>	\$1,521,971	<u>\$12,057,229</u>	\$217,965

Program\DeKalb County\421 SPLOST III\High Schools\Columbia HS - SPLOST II Deferred

Project Manager: Vincent Pope and Associates
 Architect-Engineer: Merit Construction Company
 Contractor: Merit Construction Company
 Project: 421-104
 Project Stage: 5. Close-out
 Delivery Method: CM @ Risk

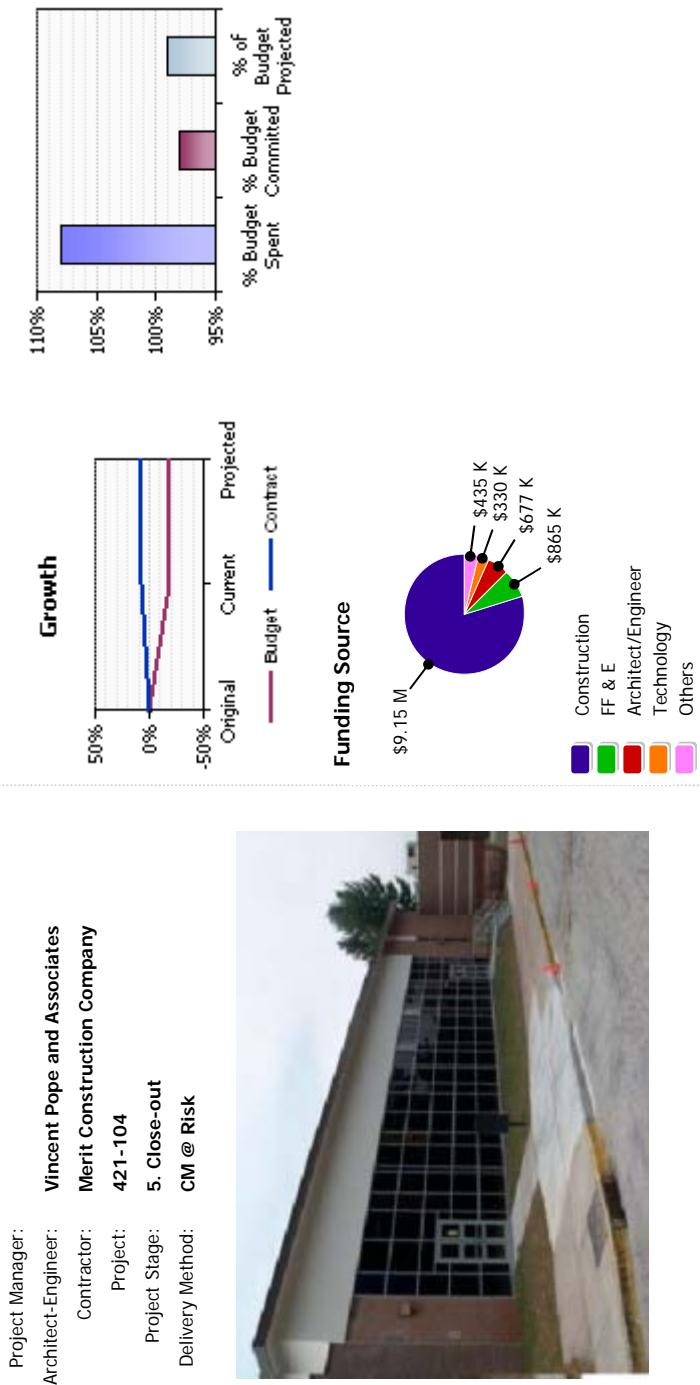

Scope of Work:

- Scope includes a Fine Arts building addition, resurfacing of the track, restoring the baseball dugouts, regarding the football field and miscellaneous renovations inside the existing buildings, which includes HVAC, ceiling and lighting improvements.

Remarks:




- Contract closeout documentation is being submitted and reviewed. Internal budget transfer in place to cover outstanding cost in Construction Technology Cost Category, for June 2011.

Cost Status by Budget Category:

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
CIT Managed												
Architect/Engineer: 7100-7101	\$660,137	\$16,863	\$677,000	\$625,000	\$52,000	\$677,000	\$655,419	\$21,581			\$677,000	
Surveying: 7100-7102	\$30,000	(\$15,300)	\$14,700	\$14,700		\$14,700	\$14,700				\$14,700	
Construction Testing: 7100-7103	\$45,022	(\$21,664)	\$23,358	\$23,358		\$23,358	\$23,358				\$23,358	\$0
Abatement: 7100-7104	\$70,000	(\$56,400)	\$13,600	\$13,600		\$13,600	\$13,600				\$13,600	
Other Consultants: 7100-7105	\$115,022	(\$87,773)	\$27,249	\$27,249		\$27,249	\$27,249				\$27,249	\$0
Management Fees: 7200-7201	\$230,045	(\$230,045)										
Construction: 7300-7301	\$10,255,916	(\$1,110,731)	\$9,145,185	\$8,194,812	\$778,413	\$8,973,225	\$10,137,948	(\$1,164,723)	\$24,132	\$147,828	\$9,145,185	\$0
Miscellaneous: 7300-7302	\$556,364	(\$239,108)	\$317,256	\$317,256		\$317,256	\$317,256				\$317,256	(\$0)
Security: 7400-7401	\$25,000	(\$24,459)	\$541	\$541		\$541	\$541				\$541	\$0
Utilities: 7500-7501	\$75,000	(\$75,000)	\$17,030	\$1,998		\$1,998	\$1,998				\$15,032	\$0
Moving / Relocation: 7500-7502	\$75,000	(\$57,970)									\$17,030	(\$0)

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
Trailers: 7600-7503	\$200,000	(\$179,058)	\$20,942	\$20,942		\$20,942	\$20,942				\$20,942	
Contingency: 9999-9999	\$575,114	(\$575,114)										
CLT Managed Subtotal	\$12,912,620	(\$2,655,759)	\$10,256,861	\$9,239,455	\$830,413	\$10,069,868	\$11,213,010	(\$1,143,142)	\$24,132	\$162,860	\$10,256,860	\$1
DCSS Managed												
FF&E: 7700-7504	\$750,000	\$115,000	\$865,000	\$934,276		\$934,276	\$934,276	(\$0)			\$934,276	(\$69,276)
Technology: 7800-7801	\$255,139	\$75,000	\$330,139	\$267,525		\$267,525	\$267,525				\$267,525	\$62,614
DCSS Managed Subtotal	\$1,005,139	\$190,000	\$1,195,139	\$1,201,800	\$830,413	\$1,201,801	\$1,201,801	(\$0)			\$1,201,800	(\$6,661)
Project Total	\$13,917,759	(\$2,465,759)	\$11,452,000	\$10,441,256	\$830,413	\$11,271,669	\$12,414,811	(\$1,143,142)	\$24,132	\$162,860	\$11,458,661	

Program\DeKalb County\421 SPLUST III\Other Facilities\Corralwood Diagnostic Ctr. - Renovation & Addition

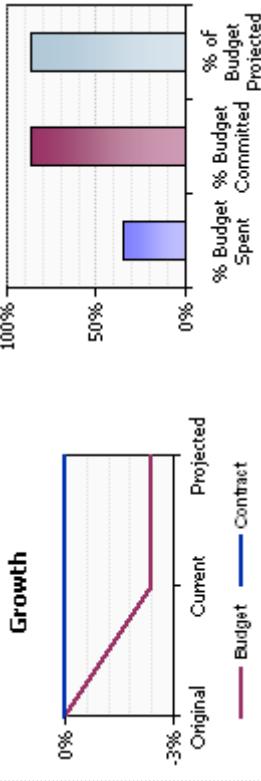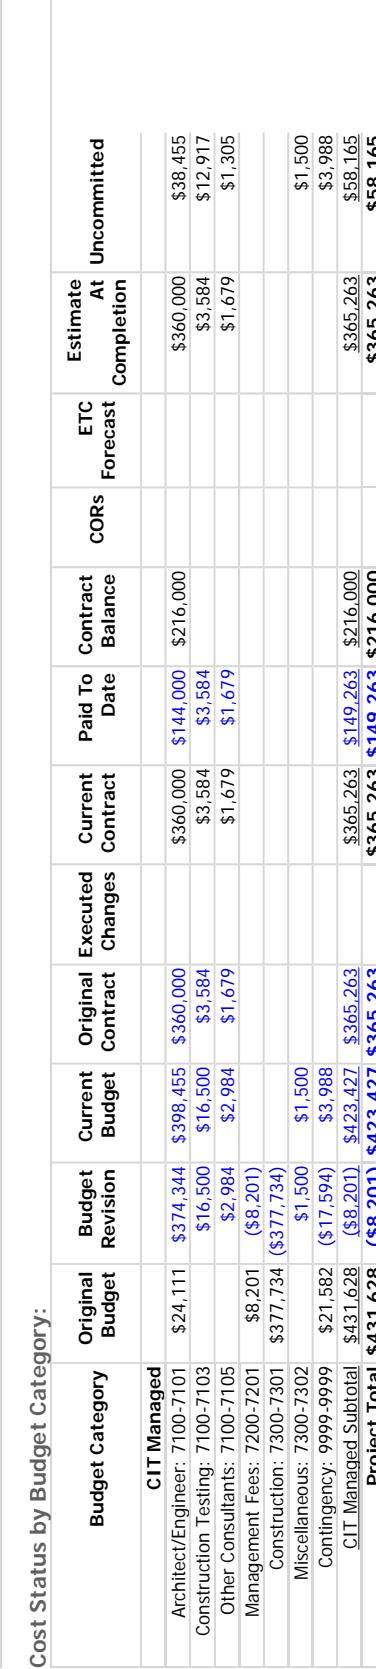Project Manager:	R.L. Brown and Associates	Growth											
Architect-Engineer:													
Contractor:													
Project:	421-213												
Project Stage:	8. On Hold												
Delivery Method:	Design / Bid / Build												
		Funding Source											
			<p>Architect/Engineer Construction Testing Contingency Other Consultants Miscellaneous</p>										
		No Photo Available											
		Scope of Work:											
		Remarks:											
		Cost Status by Budget Category:											
Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	ETC	Estimate At Completion	Uncommitted
CIT Managed													
Architect/Engineer: 7100-7101	\$24,111	\$374,344	\$398,455	\$360,000		\$144,000	\$216,000					\$360,000	\$38,455
Construction Testing: 7100-7103		\$16,500	\$16,500	\$3,584		\$3,584	\$3,584					\$3,584	\$12,917
Other Consultants: 7100-7105		\$2,984	\$2,984	\$1,679		\$1,679	\$1,679					\$1,679	\$1,305
Management Fees: 7200-7201	\$8,201	(\$8,201)											
Construction: 7300-7301	\$377,734	(\$377,734)											
Miscellaneous: 7300-7302				\$1,500									
Contingency: 9999-9999	\$21,582	(\$17,594)	\$3,988										
CIT Managed Subtotal	\$431,628	(\$8,201)	\$423,427	\$365,263		\$149,263	\$216,000					\$365,263	\$58,165
Project Total	\$431,628	(\$8,201)	\$423,427	\$365,263								\$365,263	\$58,165

Program\DeKalb County\421 SPLOST III\High Schools\Cross Keys HS - Renovation & Addition

Project Manager: Janene Glasman
Architect-Engineer: Richard Wittsiebe Hand
Contractor: Evergreen Construction
Project: 421-106
Project Stage: 5. Close-out
Delivery Method: CM @ Risk

Growth

Original Budget: \$15.0 M

Current Budget: \$14.27 M

Projected Budget: \$14.27 M

Spent: \$13.27 M

Committed: \$13.27 M

Budgeted: \$13.27 M

Projected: \$13.27 M

Funding Source

Construction: \$1.18 M

FF & E: \$723 K

Architect/Engineer: \$792 K

Technology: \$926 K

Others: \$0 K

Project Status Summary

Category	Value
Original Budget	\$15.0 M
Current Budget	\$14.27 M
Projected Budget	\$14.27 M
Spent	\$13.27 M
Committed	\$13.27 M
Budgeted	\$13.27 M
Projected	\$13.27 M

Scope of Work:


- This project includes renovation and upgrades to HVAC, ceilings, lighting, and electrical systems. Also included is a 15,000 SF expansion to a classroom wing to accommodate the relocation of DeKalb High School of Technology North and re-roofing of the existing building.

Cost Status by Budget Category:

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORS	ETC Forecast	Estimate At Completion	Uncommitted
Moving / Relocation: 7500-7502	\$125,000	\$25,000	\$150,000	\$142,705		\$142,705	\$129,260	\$13,445		\$5,000	\$147,705	\$2,205
Trailers: 7600-7503	\$1,000,000	(\$860,000)	\$140,000	\$64,955		\$64,955	\$62,453	\$1,962		\$35,000	\$99,955	\$40,045
Contingency: 9999-9999	\$549,222	(\$526,000)	\$23,222									\$23,222
CIT Managed Subtotal	\$15,260,936	\$1,380,783	\$16,641,719	\$1,496,724	\$14,760,494	\$16,257,218	\$15,114,234	\$700,530	\$50,252	\$69,879	\$16,377,349	\$264,310
DCSS Managed												
FF&E: 7700-7504	\$916,412	\$262,500	\$1,178,912	\$901,283		\$901,283	\$885,700			\$277,629	\$1,178,912	(\$0)
Technology: 7800-7801	\$750,000	\$42,000	\$792,000	\$132,195		\$132,195		\$132,195		\$659,805	\$792,000	\$0
DCSS Managed Subtotal	\$1,666,412	\$304,500	\$1,970,912	\$1,033,478		\$1,033,478	\$1,017,895			\$937,134	\$1,970,912	\$0
Project Total	\$16,927,348	\$1,685,283	\$18,612,631	\$2,530,202	\$14,760,494	\$17,290,696	\$16,132,129	\$700,530	\$50,252	\$1,007,313	\$18,348,261	\$264,310

Program\DeKalb County\421 SPLOST III\High Schools\DeKalb HS of Tech South - Roof


Project Manager:	Yolanda Brown
Architect-Engineer:	PCI Group, Inc
Contractor:	Roof Management
Project:	421-215
Project Stage:	6. Completed
Delivery Method:	Design / Bid / Build

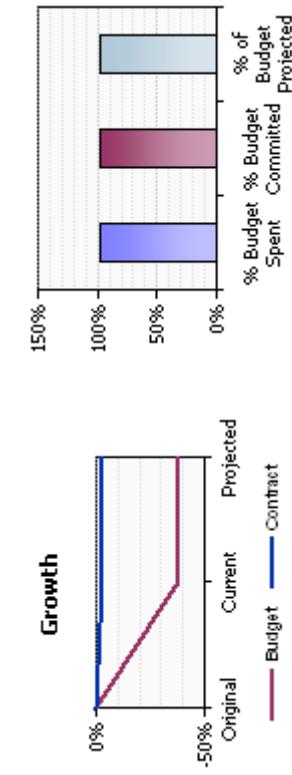

No Photo Available



Funding Source



Construction
Architect/Engineer
Abatement
Other Consultants
Miscellaneous

Scope of Work:

- Full roof replacement



Remarks:

- Construction was completed May 1010.

Cost Status by Budget Category:


Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	ETC Estimate At Completion	Uncommitted
CIT Managed												
Architect/Engineer: 7100-7101	\$31,043	(\$18,783)	\$12,260	\$11,400			\$11,400	\$11,400			\$11,400	\$860
Surveying: 7100-7102	\$6,000	(\$6,000)										
Construction Testing: 7100-7103	\$1,500	(\$1,500)										
Abatement: 7100-7104	\$7,654	\$7,654	\$7,654									
Other Consultants: 7100-7105	\$1,438	(\$160)	\$1,278	\$1,278			\$1,278	\$1,278			\$7,654	\$0
Construction: 7300-7301	\$507,367	(\$176,619)	\$330,748	\$330,748			\$330,748	\$320,138	\$10,610		\$1,278	\$330,748
Miscellaneous: 7300-7302	\$1,500	(\$1,152)	\$348	\$348			\$348					\$348
Contingency: 9999-9999	\$21,574	(\$21,574)										
CIT Managed Subtotal	\$570,422	(\$218,134)	\$352,288	\$351,428			\$351,428	\$340,818	\$10,610		\$351,428	\$860
Project Total	\$570,422	(\$218,134)	\$352,288	\$351,428			\$351,428	\$340,818	\$10,610			

Program\DeKalb County\421 SPLOST III\High Schools\Druid Hills HS - Renovation & Addition
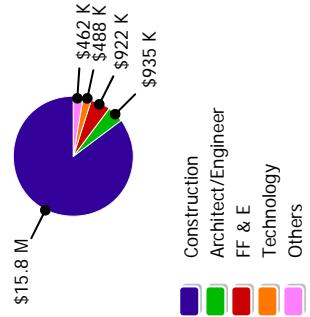
<p>Project Manager: Janene Glasman Architect-Engineer: Perkins & Will, Inc Contractor: Merit Construction Company Project: 421-119 Project Stage: 5. Close-out Delivery Method: CM @ Risk</p> 	<p>Growth</p>  <p>Funding Source</p>  <table border="1"> <thead> <tr> <th>Category</th> <th>Budget</th> <th>Contract</th> <th>Spent</th> <th>Committed</th> <th>Projected</th> </tr> </thead> <tbody> <tr> <td>Construction</td> <td>\$15.8 M</td> <td>\$935 K</td> <td>\$462 K</td> <td>\$488 K</td> <td>\$922 K</td> </tr> <tr> <td>Architect/Engineer</td> <td></td> <td></td> <td></td> <td></td> <td></td> </tr> <tr> <td>FF & E</td> <td></td> <td></td> <td></td> <td></td> <td></td> </tr> <tr> <td>Technology</td> <td></td> <td></td> <td></td> <td></td> <td></td> </tr> <tr> <td>Others</td> <td></td> <td></td> <td></td> <td></td> <td></td> </tr> </tbody> </table>	Category	Budget	Contract	Spent	Committed	Projected	Construction	\$15.8 M	\$935 K	\$462 K	\$488 K	\$922 K	Architect/Engineer						FF & E						Technology						Others						<p>Scope of Work:</p> <ul style="list-style-type: none"> This project includes renovation and upgrades to HVAC, ceilings, lighting, and electrical systems. A 31,000 SF, two-story science classroom addition is also included. <p>Remarks:</p> <ul style="list-style-type: none"> This project is substantially complete. Punchlist work is ongoing. 	<p>Cost Status by Budget Category:</p> <table border="1"> <thead> <tr> <th>Budget Category</th> <th>Original Budget</th> <th>Budget Revision</th> <th>Current Budget</th> <th>Original Contract</th> <th>Executed Changes</th> <th>Current Contract</th> <th>Paid To Date</th> <th>Contract Balance</th> <th>CORs</th> <th>ETC Forecast</th> <th>ETC Completion</th> <th>Uncommitted</th> </tr> </thead> <tbody> <tr> <td>CIT Managed</td> <td></td> </tr> <tr> <td>Architect/Engineer: 7100-7101</td> <td>\$951,411</td> <td>(\$16,861)</td> <td>\$924,550</td> <td>\$924,550</td> <td></td> <td>\$922,322</td> <td>\$2,228</td> <td>\$2,000</td> <td>\$926,550</td> <td></td> <td>\$8,000</td> </tr> <tr> <td>Surveying: 7100-7102</td> <td>\$30,000</td> <td>(\$21,750)</td> <td>\$8,250</td> <td>\$8,250</td> <td></td> <td>\$8,250</td> <td></td> <td></td> <td></td> <td>\$8,250</td> <td></td> </tr> <tr> <td>Construction Testing: 7100-7103</td> <td>\$125,000</td> <td>(\$77,070)</td> <td>\$47,930</td> <td>\$44,664</td> <td></td> <td>\$41,340</td> <td>\$829</td> <td></td> <td>\$1,500</td> <td>\$46,164</td> <td>\$1,766</td> </tr> <tr> <td>Abatement: 7100-7104</td> <td>\$22,300</td> <td>\$54,457</td> <td>\$76,757</td> <td>\$65,311</td> <td></td> <td>\$64,953</td> <td>\$1</td> <td></td> <td>\$1,000</td> <td>\$66,311</td> <td>\$10,446</td> </tr> <tr> <td>Other Consultants: 7100-7105</td> <td>\$78,712</td> <td>(\$65,479)</td> <td>\$13,233</td> <td>\$3,233</td> <td></td> <td>\$3,233</td> <td></td> <td></td> <td>\$1,000</td> <td>\$4,233</td> <td>\$9,000</td> </tr> <tr> <td>Management Fees: 7200-7201</td> <td>\$1,235,912</td> <td>(\$1,235,912)</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> </tr> <tr> <td>Construction: 7300-7301</td> <td>\$15,826,842</td> <td>\$15,826,842</td> <td>\$15,728,822</td> <td>(\$36,854)</td> <td>\$15,691,968</td> <td>\$14,393,462</td> <td>\$409,104</td> <td></td> <td>\$122,006</td> <td>\$15,813,974</td> <td>\$12,868</td> </tr> <tr> <td>Miscellaneous: 7300-7302</td> <td>\$446,520</td> <td>(\$392,388)</td> <td>\$54,132</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>\$40,000</td> <td>\$40,000</td> <td>\$14,132</td> </tr> <tr> <td>Security: 7400-7401</td> <td>\$75,000</td> <td>\$15,868</td> <td>\$90,868</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>\$65,868</td> <td>\$25,000</td> </tr> <tr> <td>Utilities: 7500-7501</td> <td>\$175,000</td> <td>(\$168,990)</td> <td>\$6,010</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>\$6,010</td> <td></td> </tr> <tr> <td>Moving / Relocation: 7500-7502</td> <td>\$200,000</td> <td>(\$120,000)</td> <td>\$80,000</td> <td>\$65,763</td> <td></td> <td>\$65,763</td> <td>\$3,891</td> <td></td> <td>\$500</td> <td>\$66,263</td> <td>\$13,738</td> </tr> </tbody> </table>	Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	ETC Completion	Uncommitted	CIT Managed													Architect/Engineer: 7100-7101	\$951,411	(\$16,861)	\$924,550	\$924,550		\$922,322	\$2,228	\$2,000	\$926,550		\$8,000	Surveying: 7100-7102	\$30,000	(\$21,750)	\$8,250	\$8,250		\$8,250				\$8,250		Construction Testing: 7100-7103	\$125,000	(\$77,070)	\$47,930	\$44,664		\$41,340	\$829		\$1,500	\$46,164	\$1,766	Abatement: 7100-7104	\$22,300	\$54,457	\$76,757	\$65,311		\$64,953	\$1		\$1,000	\$66,311	\$10,446	Other Consultants: 7100-7105	\$78,712	(\$65,479)	\$13,233	\$3,233		\$3,233			\$1,000	\$4,233	\$9,000	Management Fees: 7200-7201	\$1,235,912	(\$1,235,912)										Construction: 7300-7301	\$15,826,842	\$15,826,842	\$15,728,822	(\$36,854)	\$15,691,968	\$14,393,462	\$409,104		\$122,006	\$15,813,974	\$12,868	Miscellaneous: 7300-7302	\$446,520	(\$392,388)	\$54,132						\$40,000	\$40,000	\$14,132	Security: 7400-7401	\$75,000	\$15,868	\$90,868							\$65,868	\$25,000	Utilities: 7500-7501	\$175,000	(\$168,990)	\$6,010							\$6,010		Moving / Relocation: 7500-7502	\$200,000	(\$120,000)	\$80,000	\$65,763		\$65,763	\$3,891		\$500	\$66,263	\$13,738
Category	Budget	Contract	Spent	Committed	Projected																																																																																																																																																																																																
Construction	\$15.8 M	\$935 K	\$462 K	\$488 K	\$922 K																																																																																																																																																																																																
Architect/Engineer																																																																																																																																																																																																					
FF & E																																																																																																																																																																																																					
Technology																																																																																																																																																																																																					
Others																																																																																																																																																																																																					
Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	ETC Completion	Uncommitted																																																																																																																																																																																									
CIT Managed																																																																																																																																																																																																					
Architect/Engineer: 7100-7101	\$951,411	(\$16,861)	\$924,550	\$924,550		\$922,322	\$2,228	\$2,000	\$926,550		\$8,000																																																																																																																																																																																										
Surveying: 7100-7102	\$30,000	(\$21,750)	\$8,250	\$8,250		\$8,250				\$8,250																																																																																																																																																																																											
Construction Testing: 7100-7103	\$125,000	(\$77,070)	\$47,930	\$44,664		\$41,340	\$829		\$1,500	\$46,164	\$1,766																																																																																																																																																																																										
Abatement: 7100-7104	\$22,300	\$54,457	\$76,757	\$65,311		\$64,953	\$1		\$1,000	\$66,311	\$10,446																																																																																																																																																																																										
Other Consultants: 7100-7105	\$78,712	(\$65,479)	\$13,233	\$3,233		\$3,233			\$1,000	\$4,233	\$9,000																																																																																																																																																																																										
Management Fees: 7200-7201	\$1,235,912	(\$1,235,912)																																																																																																																																																																																																			
Construction: 7300-7301	\$15,826,842	\$15,826,842	\$15,728,822	(\$36,854)	\$15,691,968	\$14,393,462	\$409,104		\$122,006	\$15,813,974	\$12,868																																																																																																																																																																																										
Miscellaneous: 7300-7302	\$446,520	(\$392,388)	\$54,132						\$40,000	\$40,000	\$14,132																																																																																																																																																																																										
Security: 7400-7401	\$75,000	\$15,868	\$90,868							\$65,868	\$25,000																																																																																																																																																																																										
Utilities: 7500-7501	\$175,000	(\$168,990)	\$6,010							\$6,010																																																																																																																																																																																											
Moving / Relocation: 7500-7502	\$200,000	(\$120,000)	\$80,000	\$65,763		\$65,763	\$3,891		\$500	\$66,263	\$13,738																																																																																																																																																																																										

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
Trailers: 7600-7503	\$156,532	(\$126,818)	\$29,814	\$29,959		\$29,959	\$26,208	\$3,613		(\$2,756)	\$27,203	\$2,611
Contingency: 9999-9999	\$856,915	(\$801,777)	\$55,138							\$40,000	\$40,000	\$15,138
CLT Managed Subtotal	\$20,180,244	(\$2,956,720)	\$17,223,524	\$16,942,430	(\$36,854)	\$16,905,576	\$15,587,251	\$419,666		\$205,250	\$17,110,826	\$112,698
DCSS Managed												
FF&E: 7700-7504	\$1,421,613	(\$500,000)	\$921,613	\$804,149		\$804,149	\$791,987	\$12,162			\$804,149	\$117,464
Technology: 7800-7801	\$488,000		\$488,000	\$497,094		\$497,094	\$497,093	\$1			\$497,094	(\$9,094)
DCSS Managed Subtotal	\$1,909,613	(\$500,000)	\$1,409,613	\$1,301,243		\$1,301,243	\$1,289,080	\$12,163		\$1,301,243	\$108,370	
Project Total:	\$22,089,857	(\$3,456,720)	\$18,633,137	\$18,243,673	(\$36,854)	\$18,206,819	\$16,876,331	\$431,830	\$205,250	\$18,412,069	\$221,068	

Program\DeKalb County\421 SPLOST III\High Schools\Dunwoody HS - Renovation & Addition

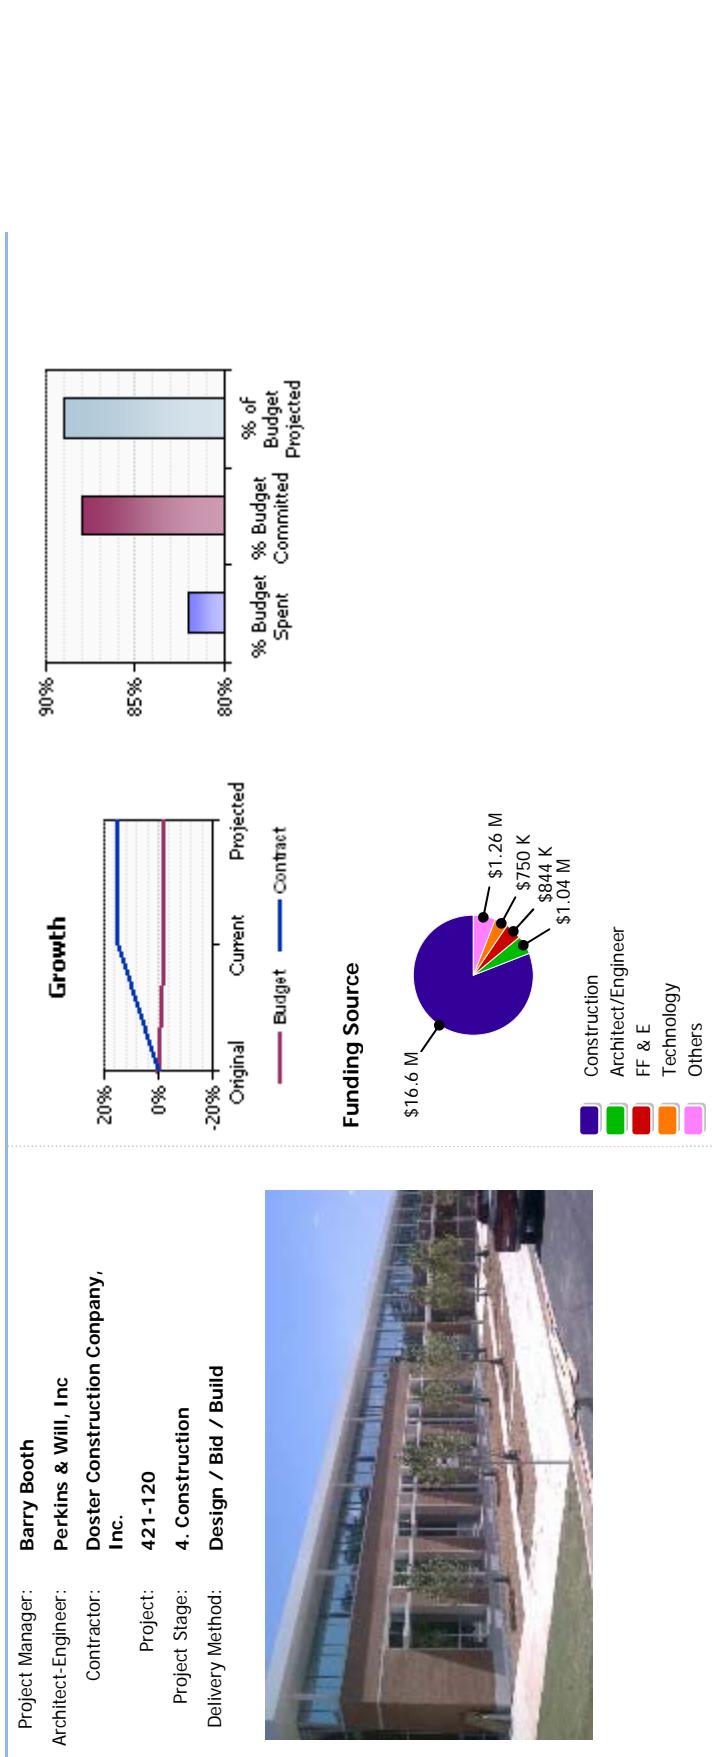

Cost Status by Budget Category:

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	ETC Estimate At Completion	Uncommitted
CIT Managed												
Architect/Engineer: 7100-7101	\$952,137	\$83,100	\$1,035,237	\$913,693	\$107,886	\$1,021,579	\$928,253	\$19,404	\$13,650	\$1,035,229	\$9	
Surveying: 7100-7102	\$30,000	\$16,900	\$46,900	\$46,200		\$46,200	\$38,000	\$8,200	\$700	\$46,900		
Construction Testing: 7100-7103	\$100,000	\$25,000	\$125,000	\$124,862		\$124,862	\$92,118	\$24,566		\$124,862	\$138	
Abatement: 7100-7104	\$20,000	\$50,000	\$70,000	\$75,655		\$75,655	\$37,655	(\$30)		\$75,655	(\$5,655)	
Other Consultants: 7100-7105	\$70,398		\$70,398	\$3,761		\$3,761				\$66,637	\$70,398	
Management Fees: 7200-7201	\$498,866		(\$498,866)									
Construction: 7300-7301	\$15,644,019	\$1,000,000	\$16,644,019	\$14,160,356	\$2,194,734	\$16,355,090	\$13,893,507	\$1,309,760	\$85,739	\$134,000	\$16,574,829	
Miscellaneous: 7300-7302	\$328,375	(\$224,134)	\$104,241	\$31,108		\$31,108	\$9,662	\$21,446		\$73,133	\$104,241	
Security: 7400-7401	\$105,000		\$105,000							\$105,000		
Utilities: 7500-7501	\$235,000	(\$50,000)	\$185,000	\$11,065		\$11,065				\$173,935	\$185,000	
Moving / Relocation: 7500-7502	\$250,000		\$250,000	\$189,472		\$189,472	\$135,723	\$1,612		\$60,528	\$250,000	

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
Trailers: 7600-7503	\$250,000	\$250,000	\$95,661		\$95,661		\$73,376	\$13,953		\$157,339	\$250,000	
Contingency: 9999-9999	\$700,866	(\$650,000)	\$50,866							\$50,000	\$50,000	\$866
CLT Managed Subtotal	\$19,184,661	(\$248,000)	\$18,936,661	\$15,651,832	\$2,302,620	\$17,954,452	\$15,261,120	\$1,398,941	\$85,739	\$831,922	\$18,872,113	\$64,548
DCSS Managed												
FF&E: 7700-7504	\$1,094,685	(\$250,866)	\$843,819	\$84,170		\$84,170	\$75,065	(\$0)		\$759,649	\$843,819	(\$0)
Technology: 7800-7801	\$750,000	\$750,000	\$119,083			\$119,083	\$119,083			\$630,917	\$750,000	(\$0)
DCSS Managed Subtotal	\$1,844,685	(\$250,866)	\$1,593,819	\$203,254		\$203,254	\$194,148	(\$0)		\$1,390,566	\$1,593,820	(\$1)
Project Total	\$21,029,346	(\$498,866)	\$20,530,480	\$15,855,086	\$2,302,620	\$18,157,706	\$15,455,268	\$1,398,941	\$85,739	\$20,465,933	\$20,465,937	

Program\DeKalb County\Eldridge L. Miller ES - Roof


Scope of Work:

- An installation of an energy star rated modified roofing system. There is a (5) year roofing contractor's warranty and a (20) year roofing manufacturer's warranty.

Remarks.

Cost Status by Budget Category:												
Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs Forecast	ETC Forecast	Estimate At Completion	Uncommitted
CTT Managed												
Architect/Engineer: 7100-7101	\$46,362	(\$30,962)	\$15,400	\$15,400		\$15,400	\$15,400				\$15,400	\$0
Construction Testing: 7100-7103	\$1,500	(\$722)	\$778	\$778		\$778	\$778				\$778	
Other Consultants: 7100-7105	\$3,591	(\$400)	\$3,191	\$3,191		\$3,191	\$3,191				\$3,191	
Construction: 7300-7301	\$781,093	(\$347,857)	\$433,236	\$457,736	(\$24,500)	\$433,236	\$433,236				\$433,236	
Miscellaneous: 7300-7302	\$1,500	(\$1,152)	\$348	\$348		\$348	\$348				\$348	
Contingency: 9999-9999	\$43,213	(\$43,213)	\$0	\$0		\$0	\$0					
CTT Managed Subtotal	\$877,259	(\$524,306)	\$452,953	\$477,453	(\$24,500)	\$452,953	\$452,953				\$452,953	\$0
Project Total	\$877,259	(\$524,306)	\$452,953	\$477,453	(\$24,500)	\$452,953	\$452,953				\$452,953	\$0

Program\DeKalb County\421 SPLOST III\Site Improvements\Site Improvements 1 (321)\Emergency Generators

Project Manager:	Larry E. Williams	Growth
Architect-Engineer:	HESMA Consulting Engineers	
Contractor:	Construction Works, Inc	
Project:	421-321-015	
Project Stage:	3. Procurement	
Delivery Method:	Design / Bid / Build	
		 <p>Original Current Projected</p> <p>Budget Contract</p>
		 <p>% Budget Spent % Budget Committed % Budget Projected</p>
		 <p>\$3.80 M</p> <p>Construction</p>
		<p>No Photo Available</p> 

Scope of Work:

- Provide and install emergency generators at 67 of the DeKalb County School System's schools and centers. The generator systems will provide emergency power to support critical systems, including life safety and fire alarm, at each of the sites.


Remarks:

- We have a Board approved vendor to provide emergency generators for this project. Our focus will be to provide emergency generators and associated scope of work for the Head End Sites initially. Dresden ES and Idlewood ES will be the first (2) generators installed, scheduled to start this summer. Rainbow ES and Redan ES will follow.

Cost Status by Budget Category:

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	ETC At Completion	Estimate At Completion	Uncommitted
CIT Managed													
Construction: 7300-7301	\$3,800,000		\$3,800,000	\$443,992		\$443,992	\$36,626	\$365,408		\$3,356,000	\$3,799,992	\$8	
CIT Managed Subtotal	\$3,800,000		\$3,800,000	\$443,992		\$443,992	\$36,626	\$365,408		\$3,356,000	\$3,799,992	\$8	
Project Total	\$3,800,000		\$443,992			\$443,992		\$36,626		\$3,356,000	\$3,799,992	\$8	

Program\DeKalb County\421 SPLOST III\Emergency HVAC Work - SPLOST III\Emergency HVAC Work

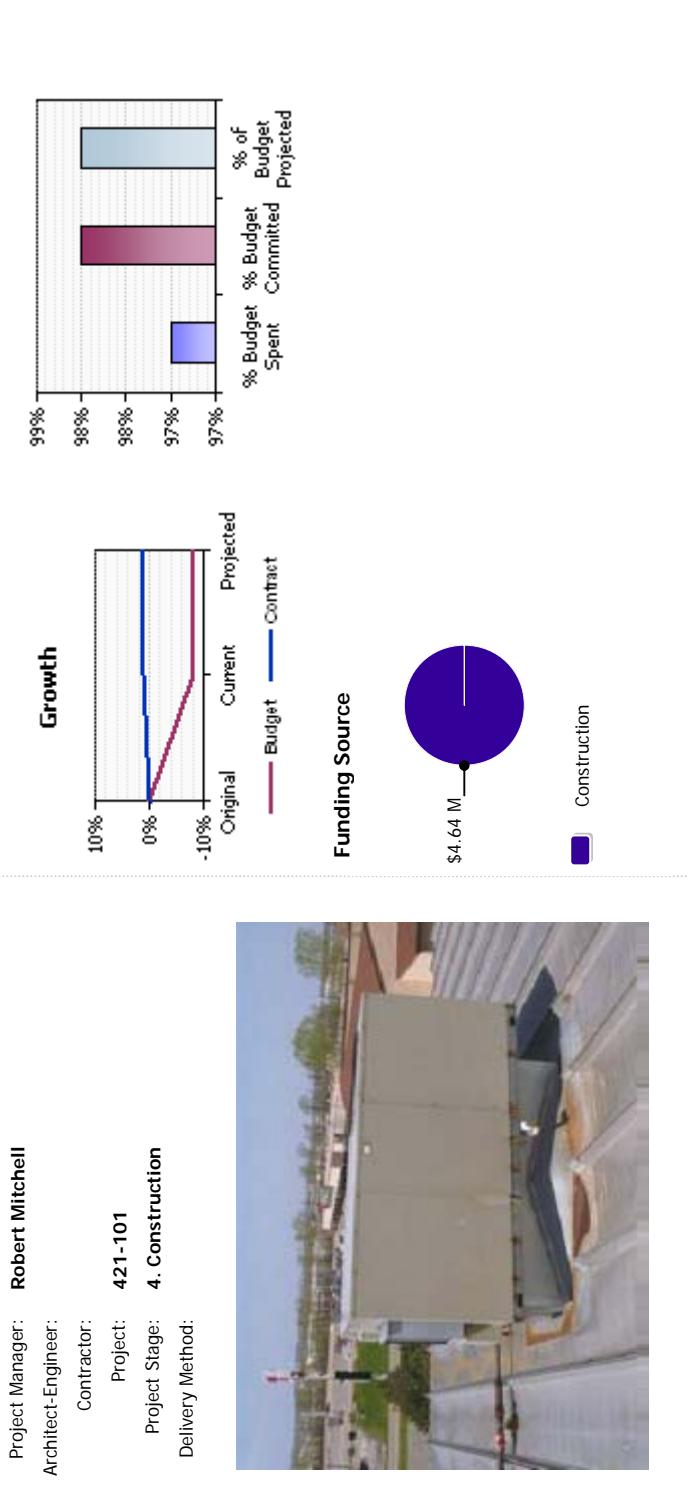

Scope of Work:


- The following are projects and their corresponding values which are funded from this project:
 - Sequoyah MS, 419-633 \$125,000
 - Margaret Harris HS, 419-652 \$349,282
 - Snapfinger ES, 419-660 \$3706,026
 - Avondale HS, 419-755 \$1,152,516
 - Redan ES, 419-763 \$402,800
 - Shamrock MS, 419-772 \$366,318

Remarks:


- Sequoyah MS - In Closeout and working on punchlist
- Margaret Harris HS - Completed
- Snapfinger ES - Completed - Closeout Documents Rec'd and punchlist done
- Avondale HS - Complete
- Redan ES - Complete
- Shamrock MS - Complete

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
CIT Managed												
Construction: 7300-7-301	\$5,026,397	(\$390,000)	\$4,636,397	\$4,508,266	\$26,478	\$4,534,744	\$4,474,415	\$25,028	\$101,000	\$4,635,744	\$653	
CIT Managed Subtotal	\$5,026,397	(\$390,000)	\$4,636,397	\$4,508,266	\$26,478	\$4,534,744	\$4,474,415	\$25,028	\$101,000	\$4,635,744	\$653	
Project Total	\$5,026,397	(\$390,000)	\$4,636,397	\$4,508,266	\$26,478	\$4,534,744	\$4,474,415	\$25,028	\$101,000	\$4,635,744	\$653	

Program\DeKalb County\421 SPLOST III\Site Improvements\Site Improvements 2 (322)\Energy Management System Update

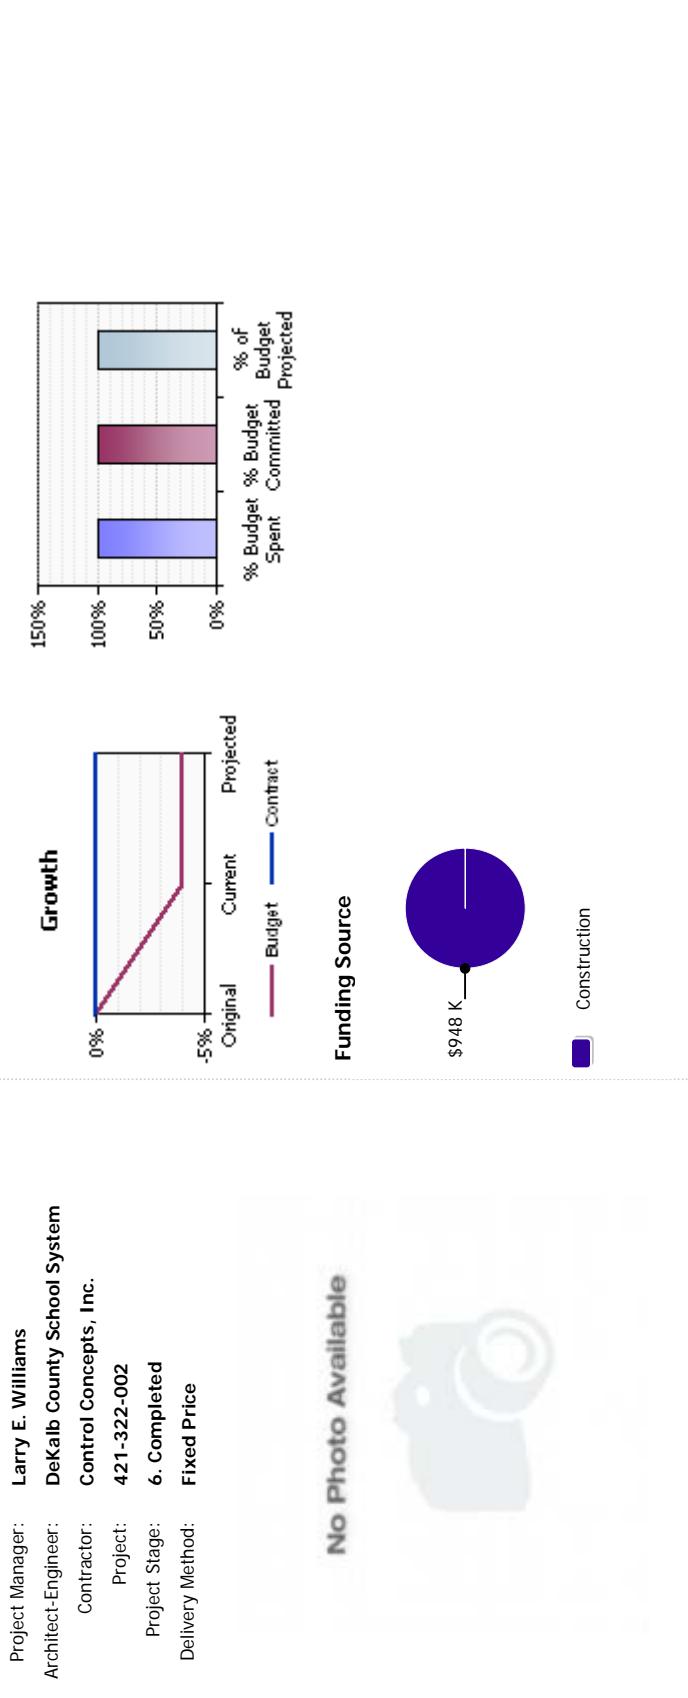

No Photo Available



■ Construction

\$948 K

Scope of Work:

- Update the Energy Management System from Ergon to Staeta/Talon at 49 locations district-wide. This project allows Plant Services to monitor, schedule and control HVAC by zone at the following schools;
- Elementary Schools - Kittredge Magnet, Ivsey, Kingsley, Fernbank, Huntley Hills, McLendon, Henderson Mill, Idlewood, Knollwood, Wadsworth, Atherton, Murphrey Candler, Rock Chapel, Stoneview, Robert Shaw, Rockbridge, Eldridge Miller, Clifton, Montclair, Pleasantdale, Rainbow, Smokerise, Indian Creek, Midway, Glen Haven, Toney, Kelley Lake, Laurel Ridge, Browns Mill, Shadow Rock, Shadow Rock Center, Hambrick, Stone Mill, Allgood, Pinecrest, Montgomery, Dresden, Sagamore Hills, Middle Schools - Ronald McElair, Sr., Chapel Hill, Miller Grove, Champion-Old St. Mt.
- Middle Schools - Ronald McElair, Sr., Chapel Hill, Miller Grove, Champion-Old St. Mt.
- Centers - Warren Tech, Rehoboth, International Student Centers - Warren Tech, Rehoboth, International Student

Remarks:

- Phases 1 through 6 are complete. All documents have been completed to close this project out.


Cost Status by Budget Category:

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	ETC Completion	Estimate At Completion	Uncommitted
CIT Managed	\$988,000	(\$40,000)	\$948,000	\$948,000		\$948,000	\$948,000					\$948,000	
Construction: 7300-7301	\$988,000	(\$40,000)	\$948,000	\$948,000		\$948,000	\$948,000					\$948,000	
CIT Managed Subtotal	\$988,000	(\$40,000)	\$948,000	\$948,000		\$948,000	\$948,000					\$948,000	
Project Total	\$988,000	(\$40,000)	\$948,000	\$948,000		\$948,000	\$948,000					\$948,000	

Program\DeKalb County\421 SPLOST III\Elementary Schools\Evansdale ES - Roof


Cost Status by Budget Category:												
Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
CIT Managed												
Architect/Engineer: 7100-7101	\$34,194	\$12,540										
Construction Testing: 7100-7103	\$1,500	\$1,500										
Other Consultants: 7100-7105	\$2,678	\$2,380										
Construction: 7300-7301	\$576,161	\$505,685										
Miscellaneous: 7300-7302	\$1,500	\$1,500										
Contingency: 9999-9999	\$31,575	\$31,575										
CIT Managed Subtotal	\$647,608		\$520,953			\$6,142	\$514,463		\$126,655		\$647,608	\$647,608
Project Total	\$647,608			\$520,953		\$6,142	\$514,463		\$126,655		\$647,608	\$647,608

Program\DeKalb County\421 SPLOST III\Elementary Schools\Fairington ES- HVAC, Ceilings & Lighting

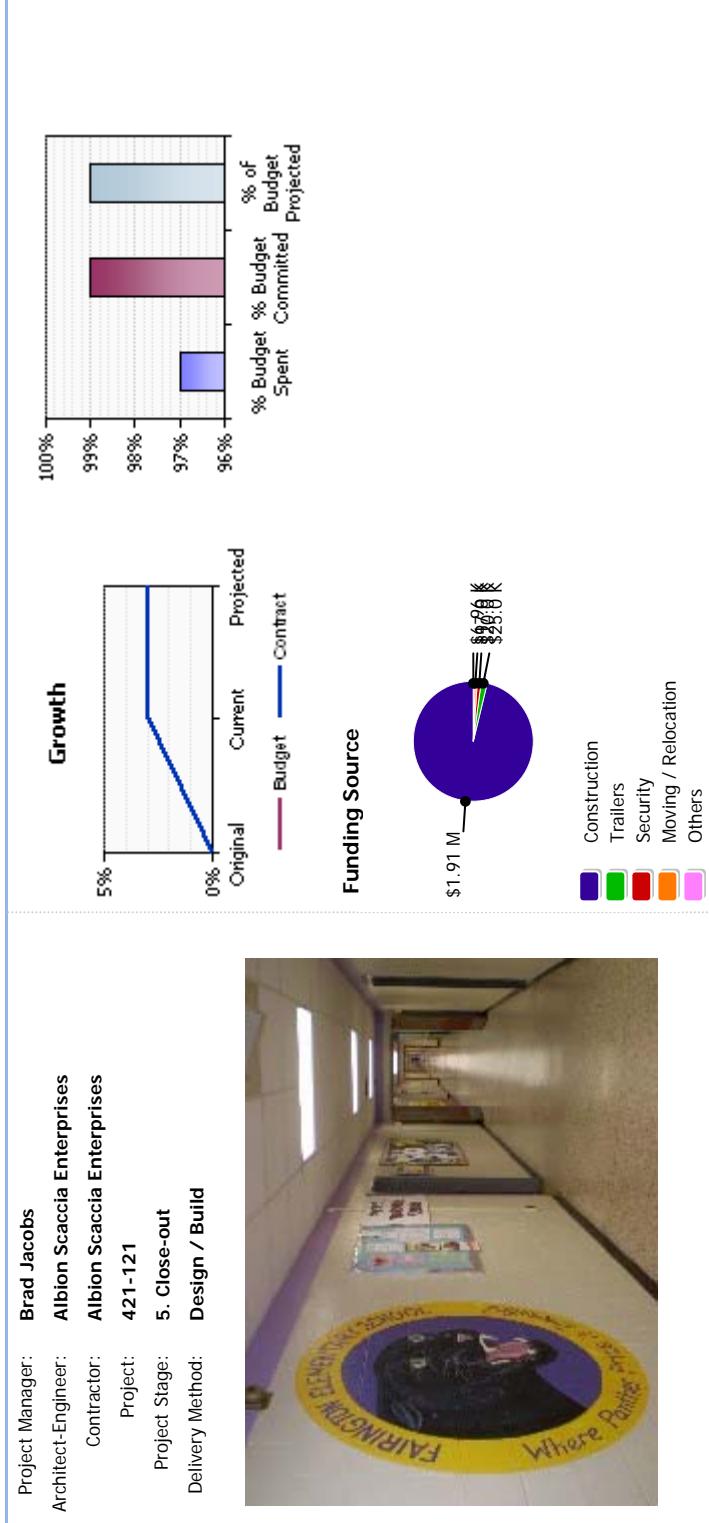


Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	ETC Forecast	CORs Forecast	Estimate At Completion	Uncommitted
Trailers: 7600-7503	\$25,000	\$25,000	\$22,000	\$22,000		\$18,739	\$2,517		\$22,000		\$3,000	
Contingency: 99999-99999	\$98,825	(\$98,825)										
CIT Managed Subtotal	\$1,917,131	\$58,500	\$1,975,631	\$1,900,478	\$48,380	\$1,948,858	\$1,922,178	\$25,936	\$23,168	\$1,972,026	\$3,605	
DCSS Managed												
Technology: 7800-7801	\$1,500	\$1,500	\$1,500	\$1,500		\$1,500	\$1,500				\$1,500	
DCSS Managed Subtotal	\$1,500	\$1,500	\$1,500	\$1,500		\$1,500	\$1,500				\$1,500	
Project Total:	\$1,917,131	\$60,000	\$1,977,131	\$1,901,978	\$48,380	\$1,950,358	\$1,923,678	\$25,936	\$23,168	\$1,973,526	\$3,605	

Program\DeKalb County\421 SPLOST III\Elementary Schools\Flat Shoals ES - Roof

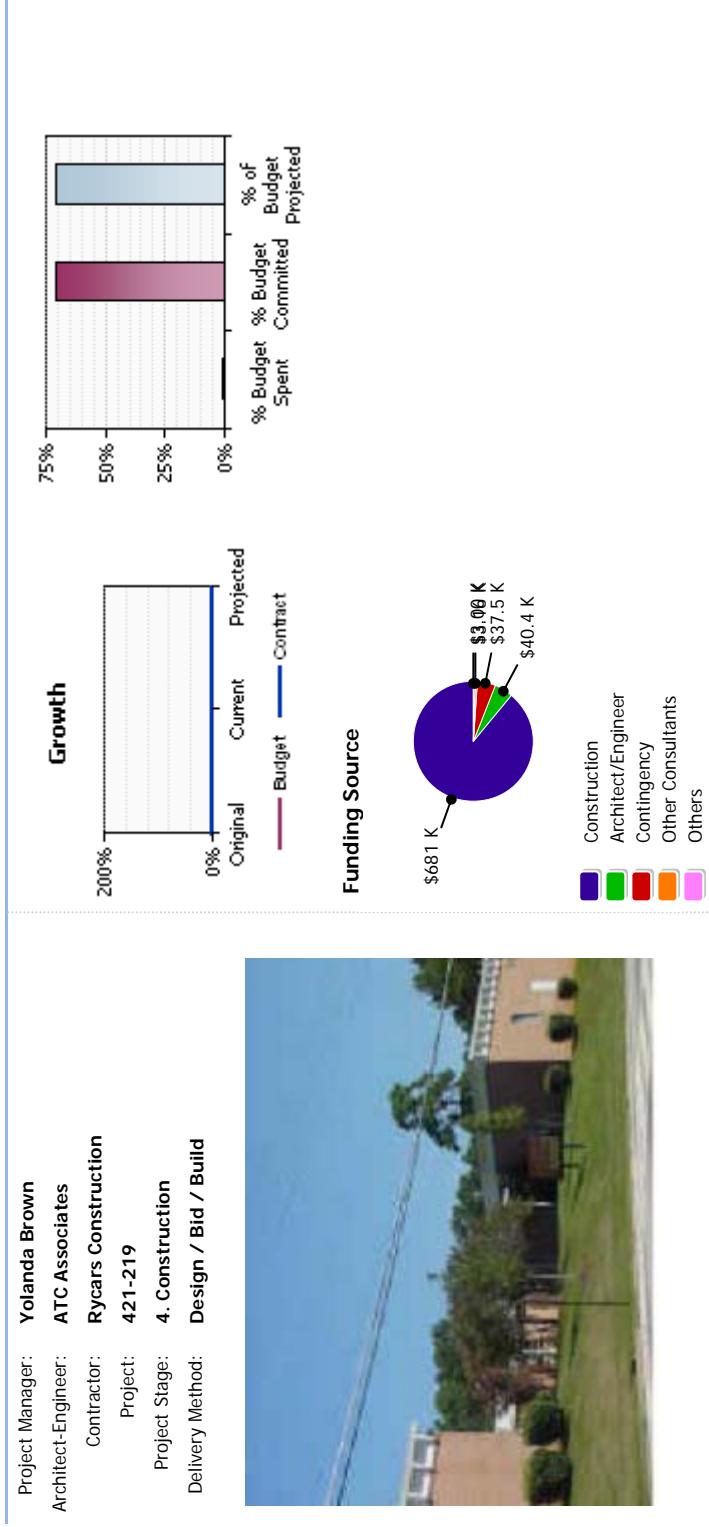

Budget Category	Original Budget	Budget Revision	Current Budget	Current Contract	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORS	ETC Forecast	Estimate At Completion	Uncommitted
CIT Managed													
Architect/Engineer: 7100-7101	\$40,396		\$40,396	\$11,830			\$11,830	\$3,549	\$8,281		\$28,566	\$40,396	
Construction Testing: 7100-7103	\$1,500		\$1,500								\$1,500	\$1,500	
Other Consultants: 7100-7105	\$3,155		\$3,103				\$3,103				\$52	\$3,155	(\$0)
Construction: 7300-7301	\$680,793		\$680,793	\$524,590			\$524,590				\$156,203	\$680,793	
Miscellaneous: 7300-7302	\$1,500		\$1,500	\$348			\$348				\$1,152	\$1,500	
Contingency: 9999-9999	\$37,482		\$37,482								\$37,482	\$37,482	
CIT Managed Subtotal	\$764,826		\$764,826	\$539,871			\$539,871	\$7,000	\$532,871		\$224,955	\$764,826	(-\$0)
Project Total	\$764,826		\$764,826	\$539,871			\$539,871	\$7,000	\$532,871		\$224,955	\$764,826	(-\$0)



Program\DeKalb County\421 SPLOST III\Elementary Schools\Glen Haven ES - Roof

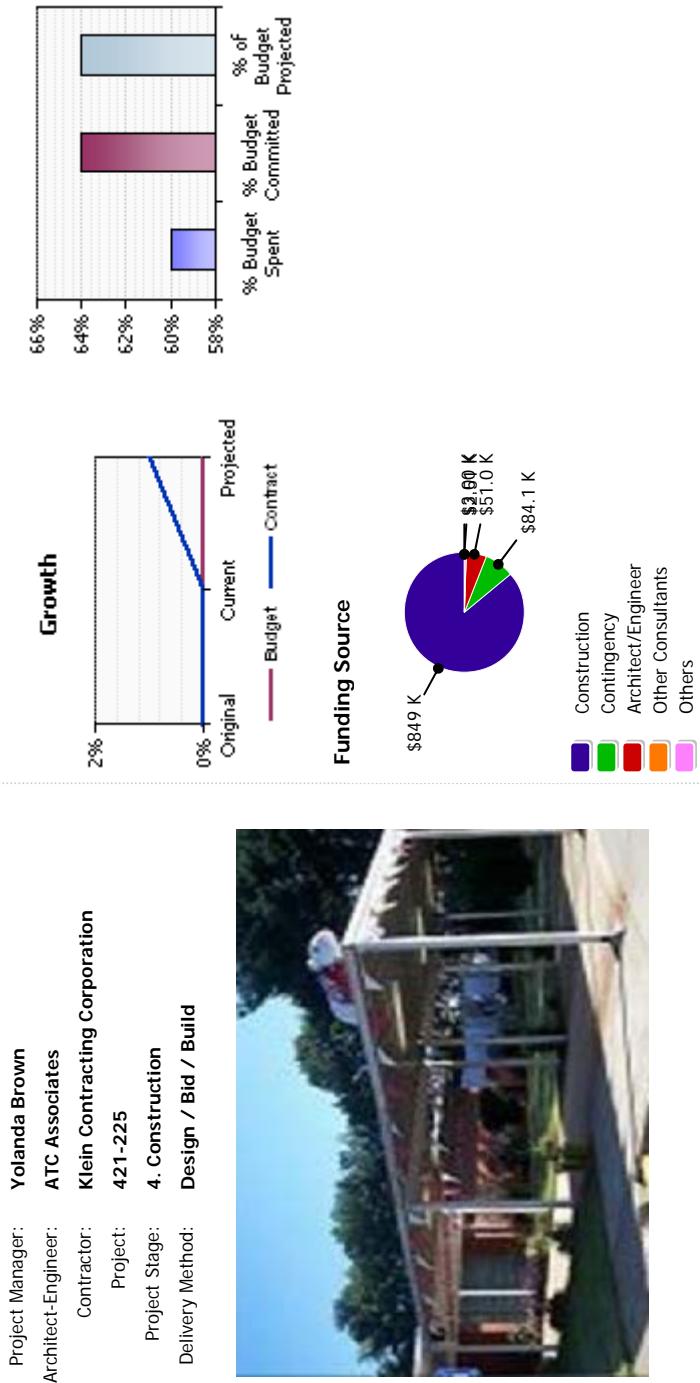


Cost Status by Budget Category:

Budget Category	Original Budget	Budget Revision	Current Budget	Current Contract	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORS	ETC Forecast	ETC	Estimate At Completion	Uncommitted
CIT Managed														
Architect/Engineer: 7100-7101	\$50,968		\$50,968	\$12,589			\$12,589	\$7,553	\$5,036		\$38,379	\$50,968		
Construction Testing: 7100-7103	\$1,500		\$1,500								\$1,500	\$1,500		
Other Consultants: 7100-7105	\$2,508		\$2,508								\$2,508	\$2,508		
Construction: 7300-7301	\$849,473		\$849,473	\$616,090	\$354,046		\$616,090	\$30,805	\$6,075	\$233,383	\$85,548		(\$6,075)	
Miscellaneous: 7300-7302	\$1,500		\$1,500	\$348			\$348				\$1,152	\$1,500		
Contingency: 9999-9999	\$84,051		\$84,051								\$84,051	\$84,051		
CIT Managed Subtotal	\$990,000		\$629,027				\$629,027	\$361,599	\$36,188	\$6,075	\$360,973	\$996,075		
Project Total	\$990,000		\$629,027				\$629,027	\$361,599	\$36,188	\$6,075	\$360,973	\$996,075		(\$6,075)

Program\DeKalb County\421 SPLOST III\Elementary Schools\Hambrick ES - Roof

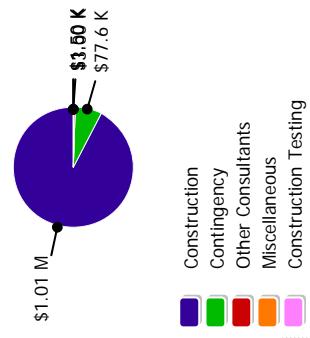
Project Manager:	Yolanda Brown	Growth										
Architect-Engineer:	ATC Associates											
Contractor:	Klein Contracting Corporation											
Project:	421-223											
Project Stage:	3. Procurement											
Delivery Method:	Design / Bid / Build											
												
												
												
Scope of Work:												
		<ul style="list-style-type: none"> Full roof replacement. 										
Remarks:		<ul style="list-style-type: none"> Construction Contract to be released April 2011. Anticipated start in late Spring of 2011 with scheduled completion of construction 3rd quarter 2011. 										
Cost Status by Budget Category:												
Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORS	ETC Forecast	Estimate At Completion	Uncommitted
CIT Managed												
Architect/Engineer: 7100-7101	\$56,968	\$56,968	\$8,122			\$8,122	\$8,122	(\$0)		\$48,846	\$56,968	
Construction Testing: 7100-7103	\$1,500	\$1,500								\$1,500	\$1,500	
Other Consultants: 7100-7105	\$3,004	\$3,004								\$3,004	\$3,004	
Construction: 7300-7301	\$949,473	\$949,473	\$638,370			\$638,370		\$433,116		\$311,103	\$949,473	
Miscellaneous: 7300-7302	\$1,500	\$1,500	\$348			\$348				\$1,152	\$1,500	
Contingency: 9999-9999	\$77,555	\$77,555								\$77,555	\$77,555	
CIT Managed Subtotal	\$1,090,000	\$1,090,000	\$646,840	\$646,840		\$646,840	\$8,122	\$433,116		\$443,160	\$1,090,000	
Project Total	\$1,090,000		\$646,840			\$646,840	\$8,122	\$433,116		\$443,160	\$1,090,000	

Program\DeKalb County\421 SPLIT III\Elementary Schools\Hambrick ES - HVAC

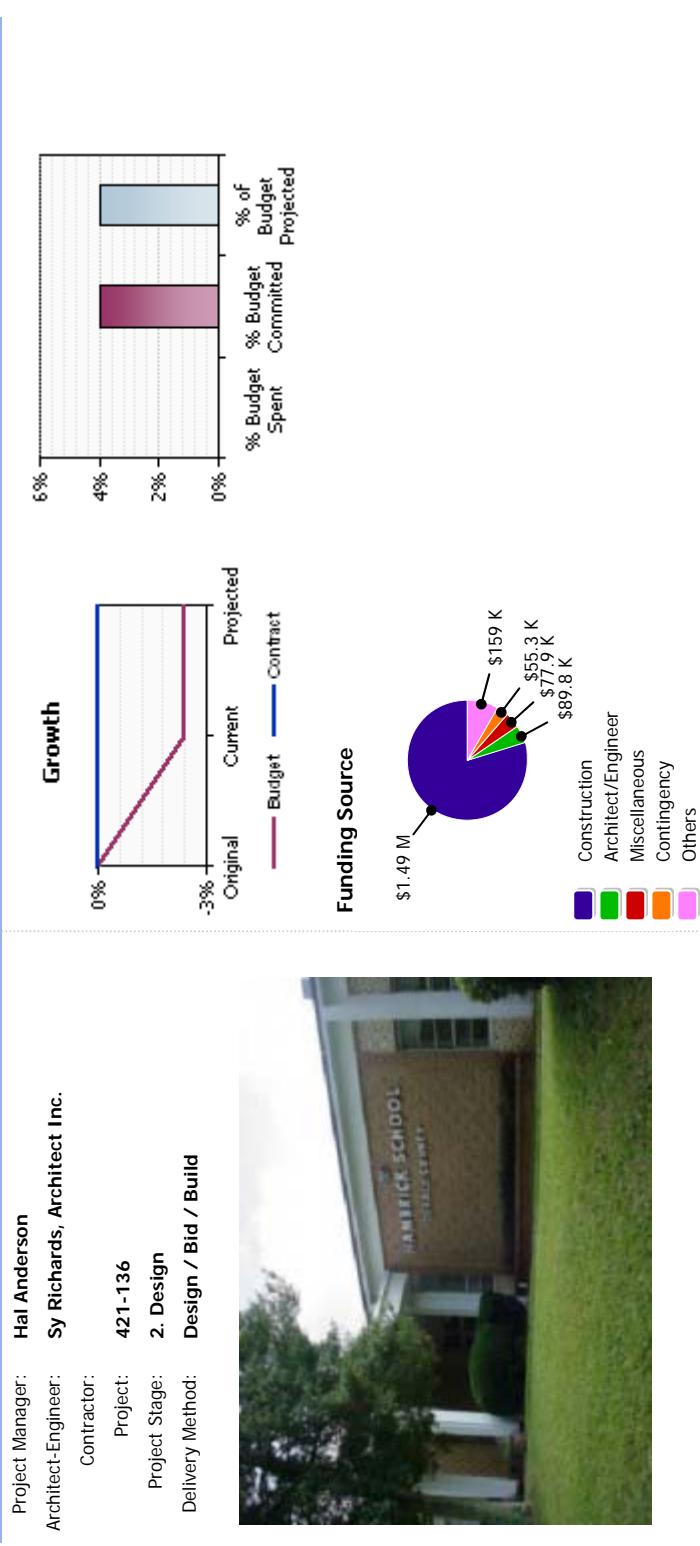


Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORS	ETC Forecast	Estimate At Completion	Uncommitted
CIT Managed												
Architect/Engineer: 7100-7101	\$89,836		\$89,836	\$72,500		\$72,500	\$5,438	\$65,250		\$17,336	\$89,836	
Construction Testing: 7100-7103	\$16,747		\$16,747							\$16,747	\$16,747	
Other Consultants: 7100-7105	\$16,916		\$16,916							\$16,916	\$16,916	
Management Fees: 7200-7201	\$34,522	(\$34,522)										
Construction: 7300-7301	\$1,490,149		\$1,490,149									
Construction Technology: 7300-7301.22	\$40,000		\$40,000							\$40,000	\$40,000	
Miscellaneous: 7300-7302	\$77,922		\$77,922							\$77,922	\$77,922	
Security: 7400-7401	\$10,000		\$10,000							\$10,000	\$10,000	
Utilities: 7500-7501	\$25,000		\$25,000							\$25,000	\$25,000	
Moving / Relocation: 7500-7502	\$50,000		\$50,000							\$50,000	\$50,000	
Contingency: 9999-9999	\$95,321	(\$40,000)	\$55,321							\$55,321	\$55,321	
CIT Managed Subtotal	\$1,906,413	(\$34,522)	\$1,871,891	\$72,500		\$72,500	\$5,438	\$65,250		\$1,799,391	\$1,871,891	
Project Total	\$1,906,413	(\$34,522)	\$1,871,891	\$72,500		\$72,500	\$5,438	\$65,250			\$1,871,891	

Program\DeKalb County\421 SPLOST III\Elementary Schools\Hawthorne ES - Roof

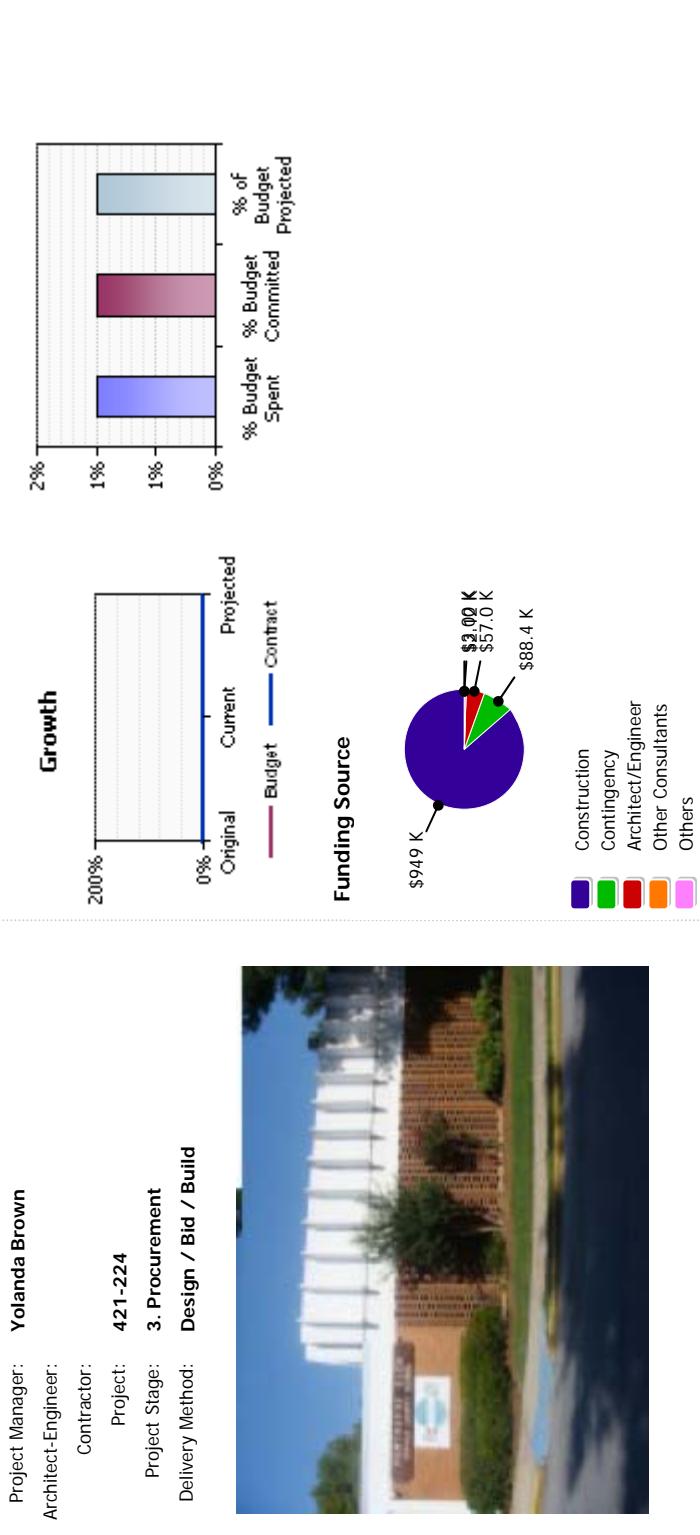

Program\DeKalb County\421 SPlOSt III\Elementary Schools\Indian Creek ES - HVAC

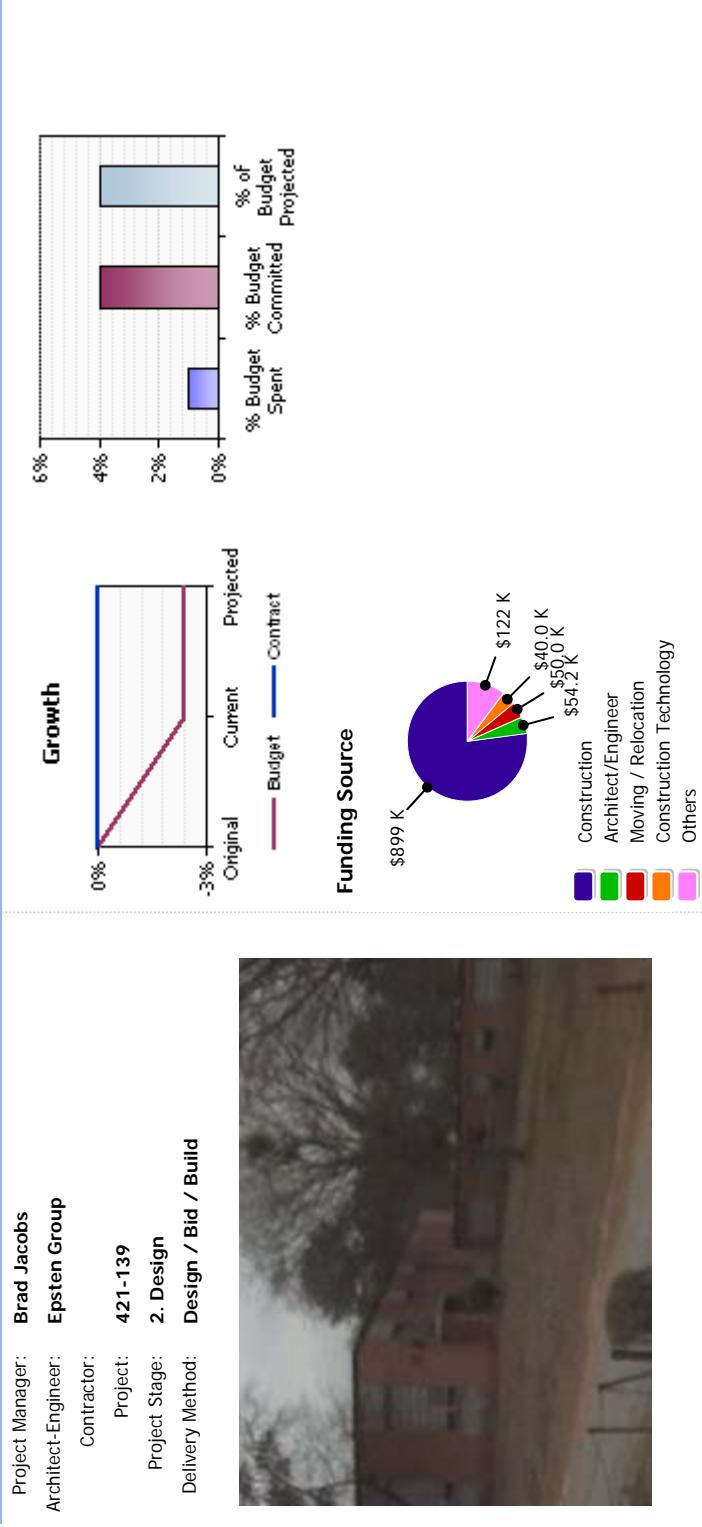

Cost Status by Budget Category:


Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Current Executed Changes	Paid To Date	Contract Balance	CORS	ETC Forecast	Estimate At Completion	Uncommitted
CIT Managed											
Architect/Engineer: 7100-7101	\$54,176	\$50,150				\$50,150	\$7,522	\$40,622		\$4,026	\$54,176
Construction Testing: 7100-7103	\$10,099	\$10,099								\$10,099	\$10,099
Other Consultants: 7100-7105	\$10,201	\$10,201								\$10,201	\$10,201
Management Fees: 7200-7201	(\$20,819)										
Construction: 7300-7301	\$898,642	\$898,642									
Construction Technology: 7300-7301.22	\$40,000	\$40,000									
Miscellaneous: 7300-7302	\$46,991	(\$20,000)	\$26,991								
Security: 7400-7401	\$10,000		\$10,000								
Utilities: 7500-7501	\$25,000		\$25,000								
Moving / Relocation: 7500-7502	\$50,000		\$50,000								
Contingency: 9999-9999	\$59,259	(\$20,000)	\$39,259								
CIT Managed Subtotal	\$1,185,187	(\$20,819)	\$1,164,368	\$50,150	\$7,522	\$40,622				\$1,114,218	\$1,164,368
Project Total	\$1,185,187	(\$20,819)	\$1,164,368	\$50,150	\$7,522	\$40,622				\$1,114,218	\$1,164,368

Program\DeKalb County\421 SPLOST III\Elementary Schools\Knollwood ES - HVAC & ADA

<p>Project Manager: Robert Mitchell</p> <p>Architect-Engineer:</p> <p>Contractor:</p> <p>Project: 421-132</p> <p>Project Stage: 1. Planning & Programming</p> <p>Delivery Method: Design / Bid / Build</p>	<p>Growth</p> <p>0% 50% 100% 150%</p> <p>-3% Current Projected</p> <p>% of Budget Spent % Budget Committed % of Budget Projected</p>	<p>Funding Source</p> <p>\$1.32 M</p> <ul style="list-style-type: none"> Construction Architect/Engineer Construction Technology Moving / Relocation Others 																																																																																																																															
Scope of Work:																																																																																																																																	
<ul style="list-style-type: none"> ADA improvements for this school include interior and exterior accessibility upgrades. In addition, heat pumps will be replaced. 																																																																																																																																	
Remarks:																																																																																																																																	
<ul style="list-style-type: none"> March 2011: Design Review is underway. 																																																																																																																																	
<table border="1"> <thead> <tr> <th colspan="9">Cost Status by Budget Category:</th> </tr> <tr> <th>Budget Category</th> <th>Original Budget</th> <th>Budget Revision</th> <th>Current Budget</th> <th>Original Contract</th> <th>Executed Changes</th> <th>Current Contract</th> <th>Paid To Date</th> <th>Contract Balance</th> </tr> </thead> <tbody> <tr> <td>CIT Managed</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> </tr> <tr> <td>Architect/Engineer: 7100-7101</td> <td>\$79,261</td> <td></td> <td>\$79,261</td> <td>\$1,500</td> <td></td> <td>\$1,500</td> <td></td> <td>\$77,700</td> </tr> <tr> <td>Construction / Testing: 7100-7103</td> <td>\$14,552</td> <td>(\$10,000)</td> <td>\$4,552</td> <td></td> <td></td> <td></td> <td></td> <td>\$79,200</td> </tr> <tr> <td>Abatement: 7100-7104</td> <td>\$10,000</td> <td></td> <td>\$10,000</td> <td>\$150</td> <td></td> <td>\$150</td> <td></td> <td>\$4,552</td> </tr> <tr> <td>Other Consultants: 7100-7105</td> <td>\$14,699</td> <td></td> <td>\$14,699</td> <td></td> <td></td> <td></td> <td></td> <td>\$4,552</td> </tr> <tr> <td>Management Fees: 7200-7201</td> <td>\$30,397</td> <td>(\$30,397)</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>\$150</td> </tr> <tr> <td>Construction: 7300-7301</td> <td>\$1,315,038</td> <td></td> <td>\$1,315,038</td> <td></td> <td></td> <td></td> <td></td> <td>\$9,850</td> </tr> <tr> <td>Construction Technology: 7300-7301.22</td> <td>\$50,000</td> <td></td> <td>\$50,000</td> <td></td> <td></td> <td></td> <td></td> <td></td> </tr> <tr> <td>Miscellaneous: 7300-7302</td> <td>\$68,709</td> <td>(\$20,000)</td> <td>\$48,709</td> <td></td> <td></td> <td></td> <td></td> <td></td> </tr> <tr> <td>Security: 7400-7401</td> <td>\$10,000</td> <td></td> <td>\$10,000</td> <td></td> <td></td> <td></td> <td></td> <td></td> </tr> <tr> <td>Utilities: 7500-7501</td> <td>\$25,000</td> <td></td> <td>\$25,000</td> <td></td> <td></td> <td></td> <td></td> <td></td> </tr> <tr> <td>Moving / Relocation: 7500-7502</td> <td>\$50,000</td> <td></td> <td>\$50,000</td> <td></td> <td></td> <td></td> <td></td> <td></td> </tr> </tbody> </table>				Cost Status by Budget Category:									Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CIT Managed									Architect/Engineer: 7100-7101	\$79,261		\$79,261	\$1,500		\$1,500		\$77,700	Construction / Testing: 7100-7103	\$14,552	(\$10,000)	\$4,552					\$79,200	Abatement: 7100-7104	\$10,000		\$10,000	\$150		\$150		\$4,552	Other Consultants: 7100-7105	\$14,699		\$14,699					\$4,552	Management Fees: 7200-7201	\$30,397	(\$30,397)						\$150	Construction: 7300-7301	\$1,315,038		\$1,315,038					\$9,850	Construction Technology: 7300-7301.22	\$50,000		\$50,000						Miscellaneous: 7300-7302	\$68,709	(\$20,000)	\$48,709						Security: 7400-7401	\$10,000		\$10,000						Utilities: 7500-7501	\$25,000		\$25,000						Moving / Relocation: 7500-7502	\$50,000		\$50,000					
Cost Status by Budget Category:																																																																																																																																	
Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance																																																																																																																									
CIT Managed																																																																																																																																	
Architect/Engineer: 7100-7101	\$79,261		\$79,261	\$1,500		\$1,500		\$77,700																																																																																																																									
Construction / Testing: 7100-7103	\$14,552	(\$10,000)	\$4,552					\$79,200																																																																																																																									
Abatement: 7100-7104	\$10,000		\$10,000	\$150		\$150		\$4,552																																																																																																																									
Other Consultants: 7100-7105	\$14,699		\$14,699					\$4,552																																																																																																																									
Management Fees: 7200-7201	\$30,397	(\$30,397)						\$150																																																																																																																									
Construction: 7300-7301	\$1,315,038		\$1,315,038					\$9,850																																																																																																																									
Construction Technology: 7300-7301.22	\$50,000		\$50,000																																																																																																																														
Miscellaneous: 7300-7302	\$68,709	(\$20,000)	\$48,709																																																																																																																														
Security: 7400-7401	\$10,000		\$10,000																																																																																																																														
Utilities: 7500-7501	\$25,000		\$25,000																																																																																																																														
Moving / Relocation: 7500-7502	\$50,000		\$50,000																																																																																																																														

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
Contingency: 9999-9999	\$85,113	(\$40,000)	\$45,113							\$45,113	\$45,113	
CLT Managed Subtotal	\$1,692,769	(\$40,397)	\$1,652,372	\$1,650						\$1,590,802	\$1,592,452	\$59,920
DCSS Managed												
Technology: 7800-7801												\$10,000
DCSS Managed Subtotal												\$10,000
Project Total	\$1,692,769	(\$30,397)	\$1,662,372	\$1,650						\$1,590,802	\$1,592,452	\$69,920

Program\DeKalb County\421 SPLOST III\High Schools\Lakeside HS - Career Tech, ADA

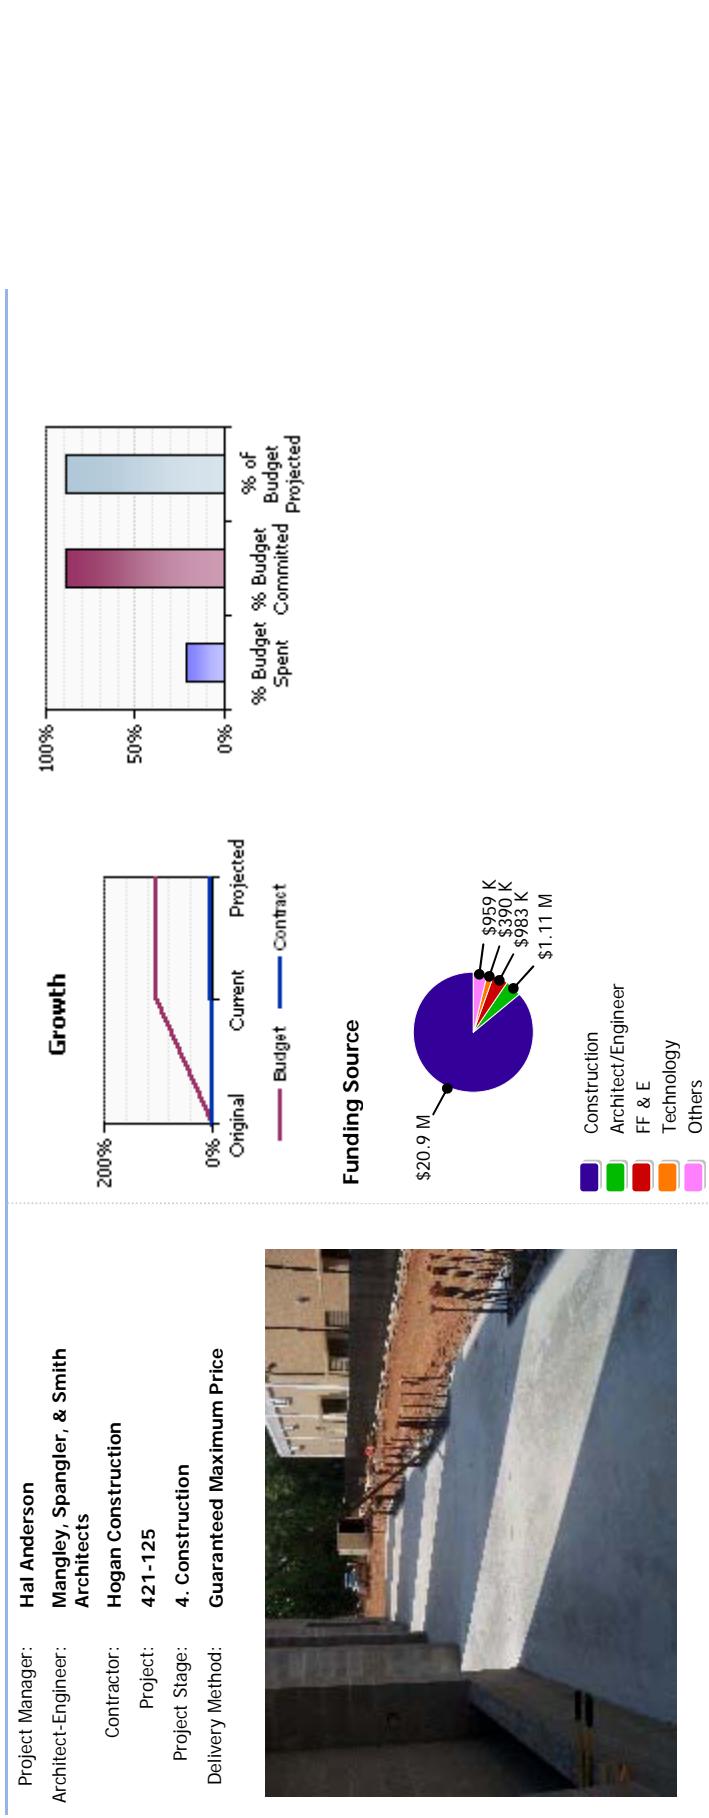

Scope of Work:

- The scope of work includes the design of a two-story Career-Tech building with various new classrooms, new auditorium with new fine arts classrooms, kitchen addition, ADA upgrades and various site improvements. In the existing building, new Boys and Girls athletic locker rooms, coaches offices, ROTC classrooms, and various new classrooms. The existing facility is approximately 164,600 sf and the planned addition is approximately 80,000 sf.

Remarks:


- Hogan Construction Group has poured the slabs for the Fine Arts and Auditorium lobby. The underground detention pond is complete. The footings have started on the Career-Tech Addition. The furniture and technology have been removed from the existing areas for the renovation to start. The demolition is ongoing. 5/31/11

Cost Status by Budget Category:

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	ETC Completion	Estimate At Completion	Uncommitted
CIT Managed													
Architect/Engineer: 7100-7101	\$544,026	\$561,520	\$1,105,546	\$487,800	\$661,866	\$1,149,666	\$868,452	\$261,198			\$1,149,666	(\$44,120)	
Surveying: 7100-7102	\$25,000	\$21,338	\$27,338	\$27,338		\$27,338	\$27,338				\$27,338		
Construction Testing: 7100-7103	\$78,500	(\$3,675)	\$74,825	\$42,000		\$41,998	(\$26,752)				\$8,000	\$50,000	
Abatement: 7100-7104	\$40,000		\$45,668			\$45,668	\$5,973	\$663			\$21,642	\$67,310	
Other Consultants: 7100-7105	\$50,000	(\$20,000)	\$30,000	\$7,792		\$7,792	\$7,792				\$22,208	\$30,000	
Management Fees: 7200-7201	\$475,100	(\$475,100)											
Construction: 7300-7301	\$9,042,106	\$11,809,065	\$20,851,171	\$19,953,751	\$98,224	\$20,051,975	\$2,499,082	\$16,215,207	\$19,507	\$166,000	\$20,237,482	\$613,668	
Construction Technology: 7300-7301-22		\$265,000								\$265,000	\$265,000		
Miscellaneous: 7300-7302	\$289,186	(\$243,575)	\$45,611	\$6,313		\$6,313	\$5,117	\$41		\$39,000	\$45,313	\$29	

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORS	ETC Forecast	Estimate At Completion	Uncommitted
Security: 7400-7401	\$50,000	(\$50,000)	\$62,500	\$4,840		\$4,840	\$4,839	\$1		\$57,660	\$62,500	\$
Utilities: 7500-7501	\$100,000	(\$37,500)	\$325,000	\$213,611		\$273,611	\$246,293	\$27,318		\$51,000	\$324,611	\$38
Moving / Relocation: 7500-7502	\$75,000	\$250,000	\$60,000	\$12,048		\$12,048	\$12,048			\$47,952	\$60,000	\$
Trailers: 7600-7503	\$60,000	\$319,225	\$29,000							\$28,825	\$28,825	\$17
Contingency: 9999.9999	\$348,225	(\$319,225)	\$22,915,991	\$20,861,161	\$760,090	\$21,621,251	\$3,718,933	\$16,477,678	\$19,507	\$707,287	\$22,348,045	\$567.94
CIT Managed Subtotal	\$11,077,143	\$11,838,848										
DCSS Managed												
FF&E: 7700-7504	\$639,039	\$244,000	\$983,039							\$983,039	\$983,039	
Technology: 7800-7801	\$150,000	\$240,380	\$390,380							\$390,380	\$390,380	
DCSS Managed Subtotal	\$789,039	\$584,380	\$1,373,419							\$1,373,419	\$1,373,419	
Project Total	\$11,866,182	\$12,423,228	\$24,289,410	\$20,861,161	\$760,090	\$21,621,251	\$3,718,933	\$16,477,678	\$19,507	\$2,080,706	\$23,721,464	\$567.94


Program\DeKalb County\421 SPLOST III\High Schools\Martin Luther King, Jr. HS - Addition

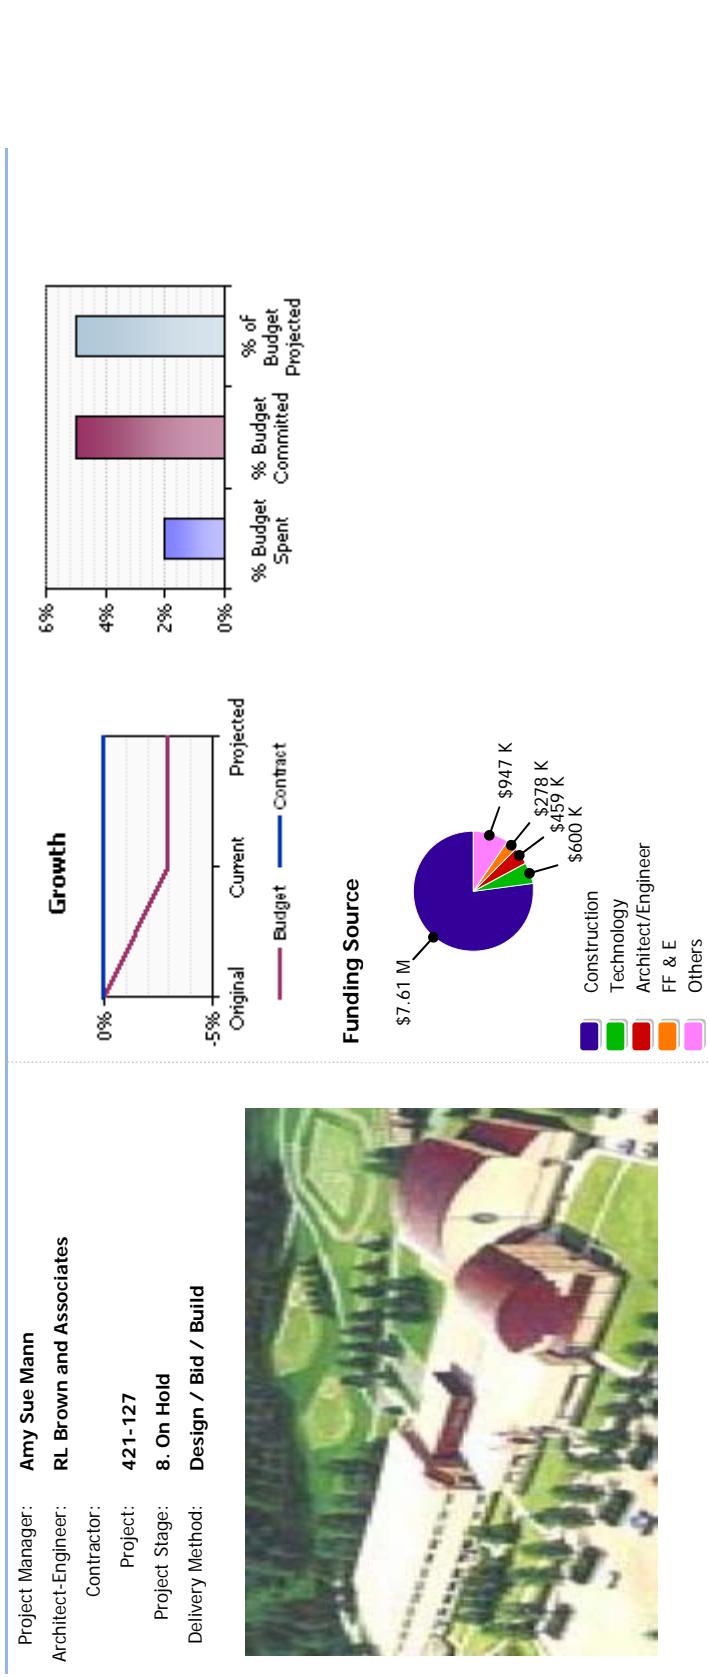

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
CIT Managed												
Architect/Engineer: 7400-7101	\$458,927	\$458,927	\$371,250			\$371,250	\$25,988	\$314,438		\$87,677	\$458,927	
Surveying: 7100-7102	\$30,000	\$68,850	\$98,850	\$57,069		\$57,069				\$41,781	\$98,850	
Construction Testing: 7100-7103	\$72,486		\$72,486	\$5,250		\$5,250				\$67,236	\$72,486	
Other Consultants: 7100-7105	\$39,500		\$39,500	\$14,436		\$14,436	\$7,171	\$2,500		\$25,064	\$39,500	
Management Fees: 7200-7201	\$289,500	(\$289,500)										
Construction: 7300-7301	\$7,605,868		\$7,605,868							\$7,605,868	\$7,605,868	
Construction Technology: 7300-7301.22	\$94,000		\$94,000							\$94,000	\$94,000	
Miscellaneous: 7300-7302	\$156,098		\$156,098							\$156,098	\$156,098	

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
Security: 7400-7401	\$75,000		\$75,000							\$75,000	\$75,000	
Utilities: 7500-7501	\$125,000		\$125,000							\$125,000	\$125,000	
Moving / Relocation: 7500-7502	\$100,000		\$100,000							\$100,000	\$100,000	
Contingency: 9999-9999	\$348,750	(\$162,850)	\$185,900							\$85,900	\$185,900	
CIT Managed Subtotal	\$9,301,129	(\$289,500)	\$9,011,629	\$448,005			\$448,005	\$95,478	\$316,938	\$8,563,624	\$9,011,629	
DCSS Managed												
F&E: 7700-7504	\$277,650		\$277,650	\$17,634		\$17,634				\$260,016	\$277,650	(-\$0)
Technology: 7800-7801	\$600,000		\$600,000							\$600,000	\$600,000	
DCSS Managed Subtotal	\$877,650		\$877,650	\$17,634		\$17,634				\$860,016	\$877,650	(-\$0)
Project Total	\$10,178,779	(\$289,500)	\$9,889,279	\$465,639		\$465,639	\$113,112	\$316,938		\$9,423,640	\$9,889,279	(-\$0)

Program\DeKalb County\421 SPLOST III\Elementary Schools\McLendon ES - HVAC & ADA

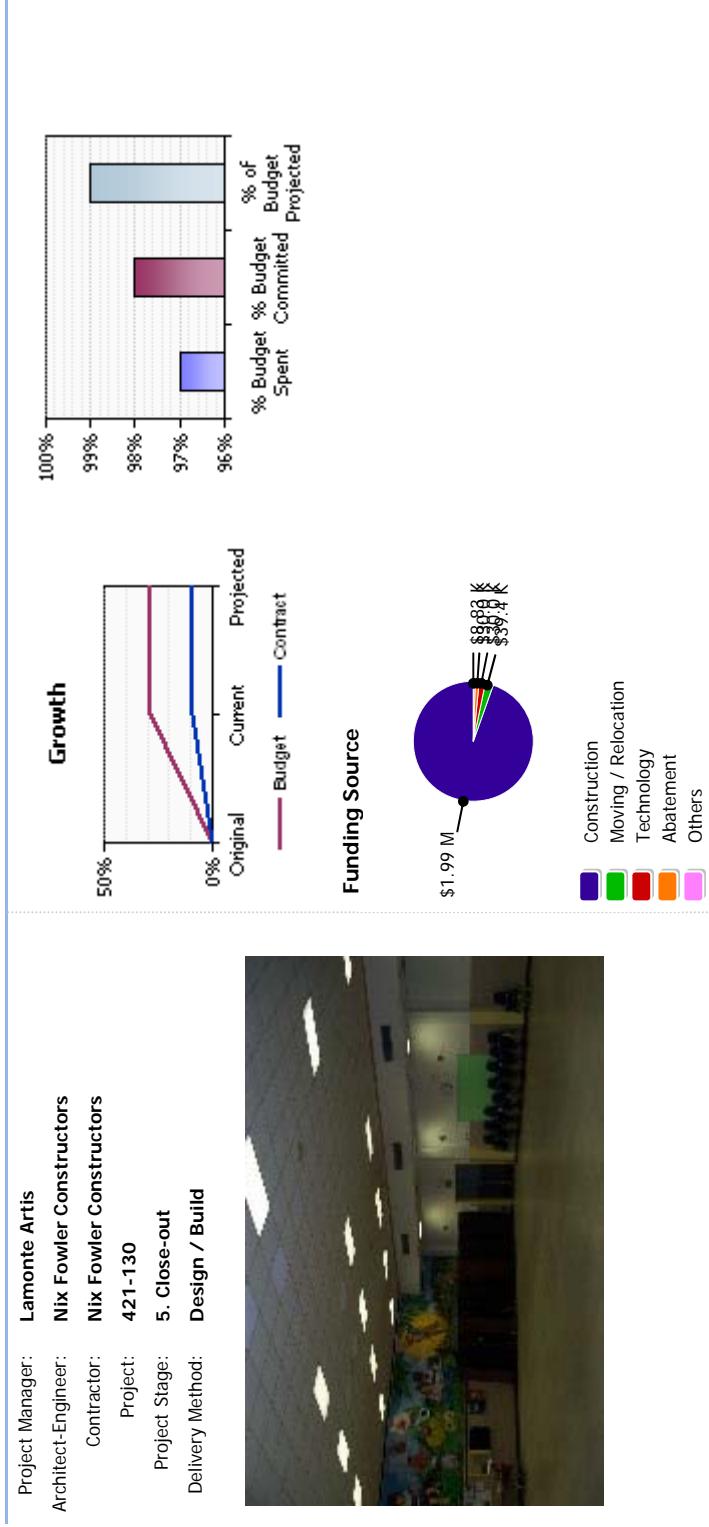

Scope of Work:

- Scope of work consists of HVAC, ceiling and lighting replacement, as well as interior and exterior ADA accessibility upgrades.

Remarks:


- This project is substantially complete. Contractor is performing punchlist items. The contractor has submitted closeout documents for review by DCSS.

Cost Status by Budget Category:

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
CIT Managed												
Architect/Engineer: 7100-7101	\$79,517	(\$79,517)										
Construction Testing: 7100-7103	\$14,087	(\$14,087)										
Abatement: 7100-7104	\$30,000		\$30,000	\$28,056			\$28,056	\$27,499	\$557			
Other Consultants: 7100-7105	\$13,522	(\$13,522)										
Management Fees: 7200-7201	\$28,996	(\$28,996)										
Construction: 7300-7301	\$1,257,672	\$732,517	\$1,990,189	\$1,787,008	\$164,673	\$1,951,681	\$1,814,540	(\$1,623)	\$15,916	\$10,000	\$1,977,597	\$12,592
Miscellaneous: 7300-7302	\$65,788	(\$63,000)	\$2,788	\$250		\$250	\$250			\$2,500	\$2,750	\$38
Security: 7400-7401	\$10,000	(\$10,000)		\$7,542		\$7,542	\$7,542				\$7,542	(\$7,542)
Utilities: 7500-7501	\$25,000	(\$25,000)										
Moving / Relocation: 7500-7502	\$50,000	(\$50,000)	\$10,631	\$39,369	\$39,451	\$39,451	\$39,451	(\$0)			\$39,451	(\$32)
Contingency: 9999-9999	\$83,044	(\$80,000)								\$3,000	\$3,000	\$44

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
CIT Managed Subtotal	\$1,627,626	\$437,764	\$2,065,390	\$1,862,306	\$164,673	\$2,026,979	\$1,889,282	(\$1,066)	\$15,916	\$15,500	\$2,058,395	\$6,995
DCSS Managed												
FF&E: 7700-7504	\$3,000	\$3,000	\$2,623			\$2,623	\$2,623	\$0			\$2,623	\$377
Technology: 7800-7801	\$30,000	\$30,000	\$22,391			\$22,391	\$18,255	\$4,136		\$7,600	\$29,991	\$9
DCSS Managed Subtotal	\$33,000	\$33,000	\$25,014			\$25,014	\$20,877	\$4,137		\$7,600	\$32,614	\$386
Project Total	\$1,627,626	\$470,764	\$2,098,390	\$1,887,320	\$164,673	\$2,051,993	\$1,910,159	\$3,070	\$15,916	\$23,100	\$2,091,009	\$7,381


Program\DeKalb County\421 SPLOST III\High Schools\McNair HS - SPLOST II Deferred

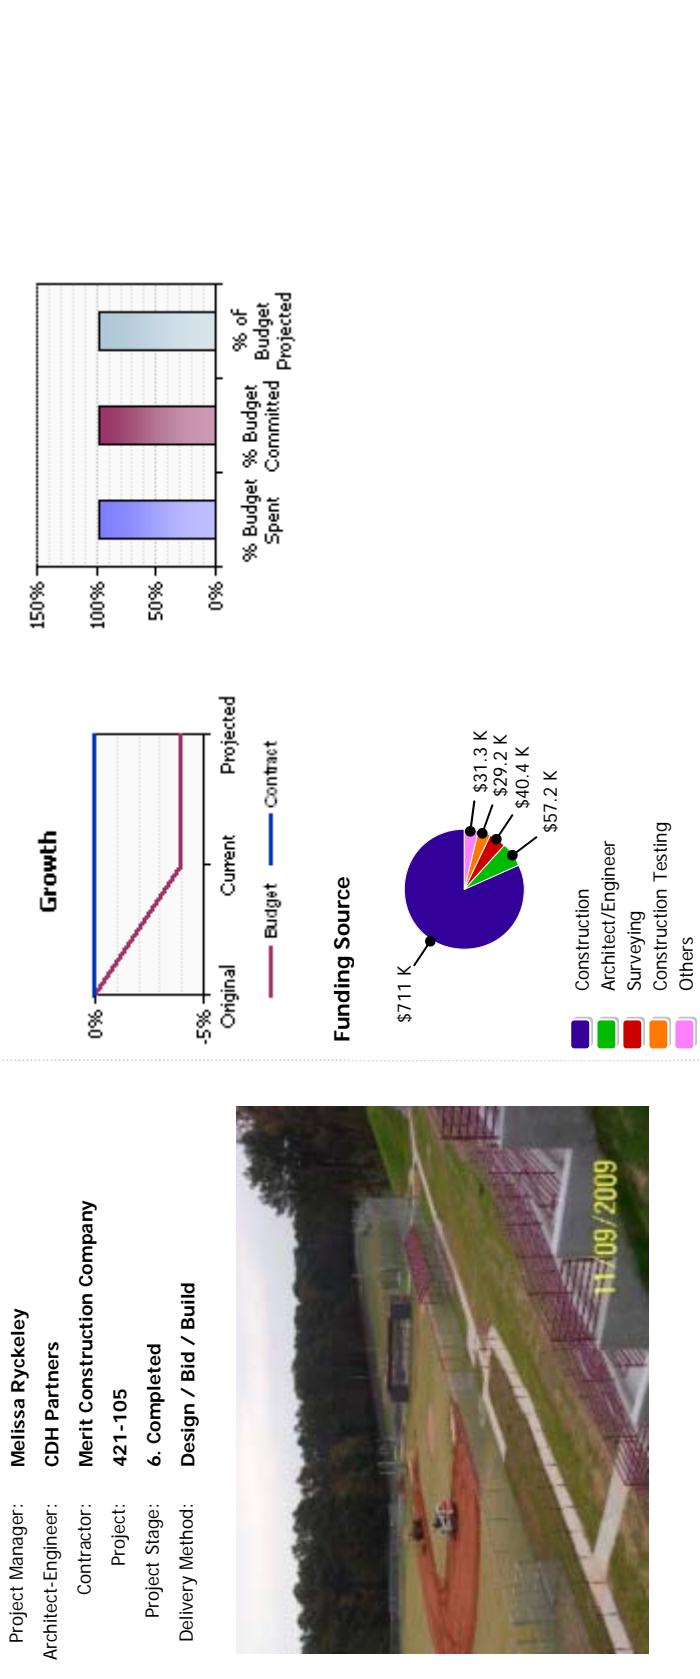



Program\DeKalb County\421 SPLOST III Elementary Schools\Midvale ES - HVAC, Roof, ADA

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
Contingency: 9999.9999	\$131,070	(\$131,070)										
CIT Managed Subtotal	\$2,564,393	\$485,812	\$3,050,205	\$2,918,564	\$71,919	\$2,990,482	\$2,901,323	\$71,592		\$58,983	\$3,049,465	\$740
DCSS Managed												
Technology: 7800-7801	\$20,000	\$20,000	\$16,637		\$16,637	\$8,267	\$8,371				\$16,637	\$3,363
DCSS Managed Subtotal	\$20,000	\$20,000	\$16,637		\$16,637	\$8,267	\$8,371				\$16,637	\$3,363
Project Total	\$2,564,393	\$505,812	\$3,070,205	\$2,935,201	\$71,919	\$3,007,120	\$2,909,590	\$79,962		\$58,983	\$3,066,103	\$4,102

Program\DeKalb County\421 SPLOST IMPLEMENTATION Schools\Midway ES - Roof


Project Manager:	Yolanda Brown	Growth					
Architect-Engineer:	PCI Group, Inc						
Contractor:	Klein Contracting Corporation						
Project:	421-214						
Project Stage:	6. Completed						
Delivery Method:	Design / Bid / Build						
							
							
							
							
Scope of Work:							
<ul style="list-style-type: none"> The installation of a new energy star roofing system. The roofing system is a smooth white modified bitumen system. 							
Remarks:							
<ul style="list-style-type: none"> Construction was completed June 2010. 							
Cost Status by Budget Category:							
Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract			
CIT Managed							
Architect/Engineer: 7100-7101	\$45,265	(\$28,365)	\$16,900	\$16,900			
Construction Testing: 7100-7103	\$1,500	(\$1,500)		\$16,900			
Abatement: 7100-7104		\$7,050	\$7,050	\$7,050			
Other Consultants: 7100-7105	\$3,537	(\$394)	\$3,143	\$3,143			
Construction: 7300-7301	\$763,062	(\$243,447)	\$519,615	\$519,615			
Miscellaneous: 7300-7302	\$1,500	(\$1,152)	\$348	\$348			
Contingency: 9999-9999	\$42,182	(\$42,182)					
CIT Managed Subtotal	\$857,046	(\$309,990)	\$547,056	\$547,056			
Project Total	\$957,046	(\$309,990)	\$547,056	\$547,056			
CIT Managed Total	\$857,046	(\$309,990)	\$547,056	\$547,056			

Program\DeKalb County\421 SPLOST III\High Schools\Miller Grove HS - Addition


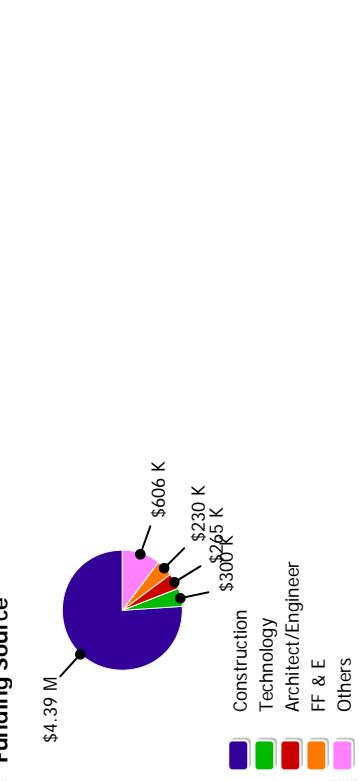
<p>Project Manager: Robert Mitchell</p> <p>Architect-Engineer: Mangley, Spangler, & Smith Architects</p> <p>Contractor:</p> <p>Project: 421-128</p> <p>Project Stage: 2. Design</p> <p>Delivery Method: Design / Bid / Build</p>	 <p>Growth</p> <p>Original Current Projected</p> <p>% Budget Spent % Budget Committed % of Budget Projected</p>	 <p>Funding Source</p> <p>\$4.39 M</p> <ul style="list-style-type: none"> Construction: \$300K Technology: \$230K Architect/Engineer: \$245K FF & E: \$606K Others: \$10K 	<p>Scope of Work:</p> <ul style="list-style-type: none"> This scope includes the addition of 16 classrooms as well as sitework, furniture, fixture and equipment improvements. <p>Remarks:</p> <ul style="list-style-type: none"> DCSS waiting for design changes/modifications from the Architect 	<p>Cost Status by Budget Category:</p> <table border="1"> <thead> <tr> <th>Budget Category</th><th>Original Budget</th><th>Budget Revision</th><th>Current Budget</th><th>Original Contract</th><th>Executed Changes</th><th>Current Contract</th><th>Paid To Date</th><th>Contract Balance</th><th>CORS</th><th>ETC Forecast</th><th>Estimate At Completion</th><th>Uncommitted</th></tr> </thead> <tbody> <tr> <td>CIT Managed</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr> <tr> <td>Architect/Engineer: 7100-7101</td><td>\$265,017</td><td>\$265,017</td><td>\$210,000</td><td>\$21,000</td><td>\$189,000</td><td>\$19,319</td><td>\$1</td><td></td><td></td><td>\$55,017</td><td>\$265,017</td></tr> <tr> <td>Surveying: 7100-7102</td><td>\$25,000</td><td>\$11,600</td><td>\$36,600</td><td>\$22,362</td><td>\$22,362</td><td></td><td></td><td></td><td></td><td>\$14,238</td><td>\$36,600</td></tr> <tr> <td>Construction Testing: 7100-7103</td><td>\$44,783</td><td></td><td>\$44,783</td><td></td><td></td><td></td><td></td><td></td><td></td><td>\$44,783</td><td>\$44,783</td></tr> <tr> <td>Other Consultants: 7100-7105</td><td>\$16,600</td><td></td><td>\$16,600</td><td>\$9,801</td><td>\$9,801</td><td></td><td></td><td></td><td></td><td>\$6,799</td><td>\$16,600</td></tr> <tr> <td>Management Fees: 7200-7201</td><td>\$81,600</td><td>(\$81,600)</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr> <tr> <td>Construction: 7300-7301</td><td>\$4,391,945</td><td></td><td>\$4,391,945</td><td></td><td></td><td></td><td></td><td></td><td></td><td>\$4,391,945</td><td>\$4,391,945</td></tr> <tr> <td>Construction Technology: 7300-7301.22</td><td></td><td>\$60,000</td><td>\$60,000</td><td></td><td></td><td></td><td></td><td></td><td></td><td>\$60,000</td><td>\$60,000</td></tr> <tr> <td>Miscellaneous: 7300-7302</td><td>\$90,142</td><td></td><td>\$90,142</td><td></td><td></td><td></td><td></td><td></td><td></td><td>\$90,142</td><td>\$90,142</td></tr> <tr> <td>Security: 7400-7401</td><td>\$50,000</td><td></td><td>\$50,000</td><td></td><td></td><td></td><td></td><td></td><td></td><td>\$50,000</td><td>\$50,000</td></tr> </tbody> </table>	Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORS	ETC Forecast	Estimate At Completion	Uncommitted	CIT Managed													Architect/Engineer: 7100-7101	\$265,017	\$265,017	\$210,000	\$21,000	\$189,000	\$19,319	\$1			\$55,017	\$265,017	Surveying: 7100-7102	\$25,000	\$11,600	\$36,600	\$22,362	\$22,362					\$14,238	\$36,600	Construction Testing: 7100-7103	\$44,783		\$44,783							\$44,783	\$44,783	Other Consultants: 7100-7105	\$16,600		\$16,600	\$9,801	\$9,801					\$6,799	\$16,600	Management Fees: 7200-7201	\$81,600	(\$81,600)										Construction: 7300-7301	\$4,391,945		\$4,391,945							\$4,391,945	\$4,391,945	Construction Technology: 7300-7301.22		\$60,000	\$60,000							\$60,000	\$60,000	Miscellaneous: 7300-7302	\$90,142		\$90,142							\$90,142	\$90,142	Security: 7400-7401	\$50,000		\$50,000							\$50,000	\$50,000
Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORS	ETC Forecast	Estimate At Completion	Uncommitted																																																																																																																														
CIT Managed																																																																																																																																										
Architect/Engineer: 7100-7101	\$265,017	\$265,017	\$210,000	\$21,000	\$189,000	\$19,319	\$1			\$55,017	\$265,017																																																																																																																															
Surveying: 7100-7102	\$25,000	\$11,600	\$36,600	\$22,362	\$22,362					\$14,238	\$36,600																																																																																																																															
Construction Testing: 7100-7103	\$44,783		\$44,783							\$44,783	\$44,783																																																																																																																															
Other Consultants: 7100-7105	\$16,600		\$16,600	\$9,801	\$9,801					\$6,799	\$16,600																																																																																																																															
Management Fees: 7200-7201	\$81,600	(\$81,600)																																																																																																																																								
Construction: 7300-7301	\$4,391,945		\$4,391,945							\$4,391,945	\$4,391,945																																																																																																																															
Construction Technology: 7300-7301.22		\$60,000	\$60,000							\$60,000	\$60,000																																																																																																																															
Miscellaneous: 7300-7302	\$90,142		\$90,142							\$90,142	\$90,142																																																																																																																															
Security: 7400-7401	\$50,000		\$50,000							\$50,000	\$50,000																																																																																																																															

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORS	Forecast	ETC Forecast	Estimate At Completion	Uncommitted
Utilities: 7500-7501	\$100,000		\$100,000							\$100,000	\$100,000		
Moving / Relocation: 7500-7502	\$75,000		\$75,000							\$75,000	\$75,000		
Contingency: 9999-9999	\$204,000	(\$71,600)	\$132,400							\$132,400	\$132,400		
CIT Managed Subtotal	\$5,344,087	(\$81,600)	\$5,262,487	\$242,163		\$242,163	\$50,055	\$189,066		\$5,020,324	\$5,262,487		
DCSS Managed													
FF&E: 7700-7504	\$230,400		\$230,400							\$230,400	\$230,400		
Technology: 7800-7801	\$300,000		\$300,000							\$300,000	\$300,000		
DCSS Managed Subtotal	\$530,400		\$530,400							\$530,400	\$530,400		
Project Total	\$5,874,487	(\$81,600)	\$5,792,887	\$242,163		\$242,163	\$50,055	\$189,066		\$5,550,724	\$5,792,887		


Program\DeKalb County\421 SPLIT III\Elementary Schools\Montgomery ES - HVAC

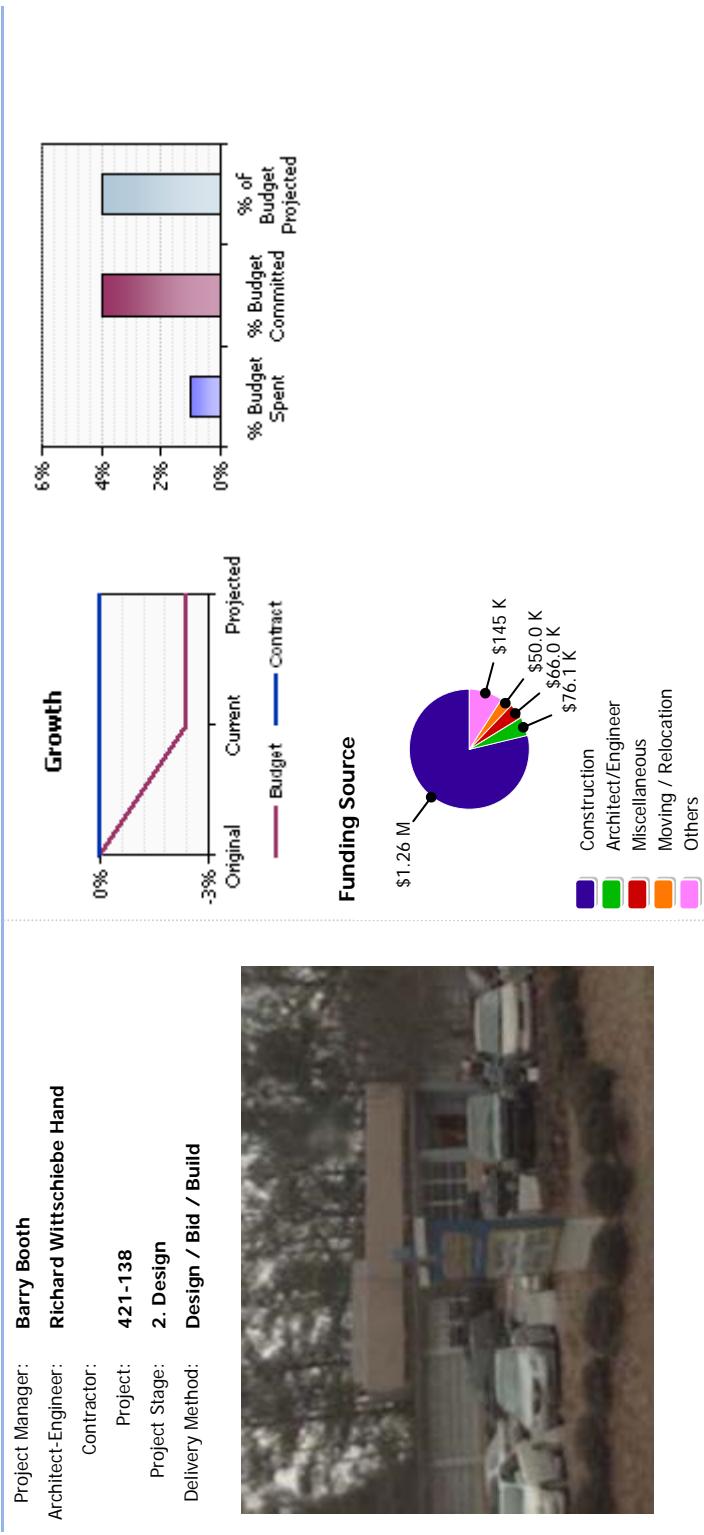

Program\DeKalb County\421 SPLOST III\Elementary Schools\Murphrey Candler ES - Roof

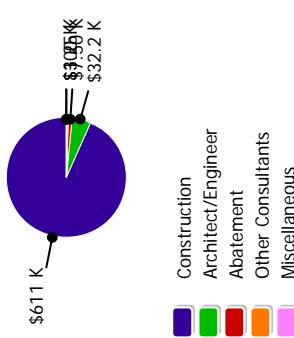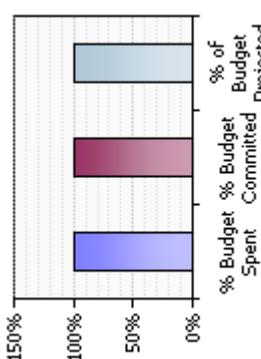Project Manager:	Yolanda Brown	Growth											
Architect-Engineer:	Merik Marketing, Inc.												
Contractor:	Pinkston-Hollar												
Project:	421-202												
Project Stage:	6. Completed												
Delivery Method:	Design / Bid / Build												
No Photo Available		 <p>Funding Source</p> <table> <tr> <td>Construction</td> <td>\$611 K</td> </tr> <tr> <td>Architect/Engineer</td> <td>\$310.5 K</td> </tr> <tr> <td>Abatement</td> <td>\$32.2 K</td> </tr> <tr> <td>Other Consultants</td> <td></td> </tr> <tr> <td>Miscellaneous</td> <td></td> </tr> </table>		Construction	\$611 K	Architect/Engineer	\$310.5 K	Abatement	\$32.2 K	Other Consultants		Miscellaneous	
Construction	\$611 K												
Architect/Engineer	\$310.5 K												
Abatement	\$32.2 K												
Other Consultants													
Miscellaneous													
 <p>Growth</p>													
Scope of Work:	<ul style="list-style-type: none"> Full Roof Replacement project with the installation of a new modified buttermen roof system, a new recovery modified buttermen roof membrane and the replacement of the fascia panels. It includes a five year roofing contractor's warranty and a 20 year roofing manufacturer's warranty. 												
Remarks:	<ul style="list-style-type: none"> This project was completed December 2008. 												
Cost Status by Budget Category:													
Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted	
CIT Managed													
Architect/Engineer: 7100-7101	\$50,513	(\$18,363)	\$32,150	\$32,150			\$32,150	\$32,150				\$32,150	
Abatement: 7100-7104		\$7,500	\$7,500	\$7,500			\$7,500	\$7,500				\$7,500	
Other Consultants: 7100-7105		\$3,246	\$3,246	\$3,246			\$3,246	\$3,246				\$3,246	
Management Fees: 7200-7201	\$17,181	(\$17,181)											
Construction: 7300-7301	\$791,362	(\$180,017)	\$611,345	\$602,450	\$8,895	\$611,345	\$611,345					\$611,345	
Miscellaneous: 7300-7302		\$100	\$100		\$100		\$100	\$100				\$100	
Contingency: 9999.9999	\$45,214	(\$45,214)											
CIT Managed Subtotal	\$904,270	(\$249,929)	\$654,341	\$645,446	\$8,895	\$654,341	\$654,341	\$654,341				\$654,341	
Project Total	\$904,270	(\$249,929)	\$654,341	\$645,446	\$8,895	\$654,341	\$654,341	\$654,341				\$654,341	


Program\DeKalb County\421 SPLOST III\Elementary Schools\Nancy Creek (Kittridge) ES - Roof

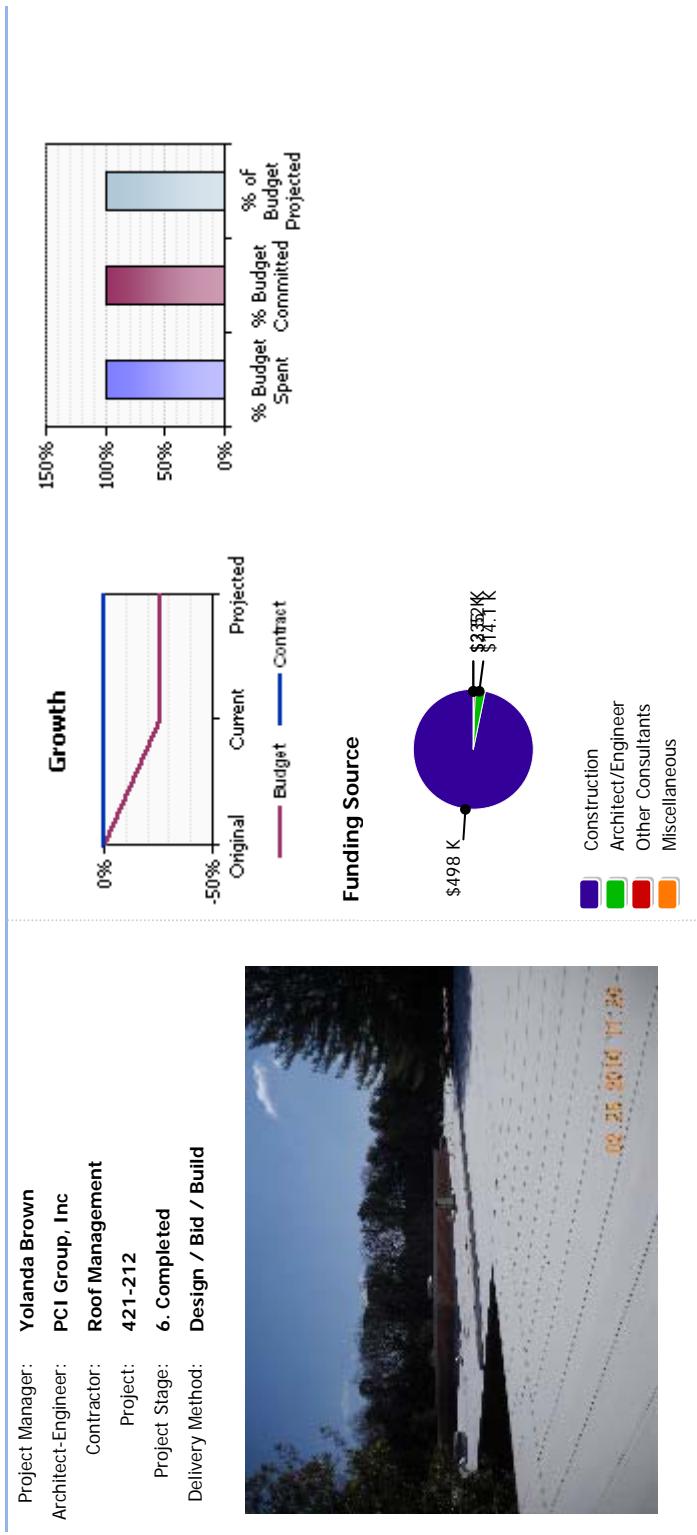

Cost Status by Budget Category:



Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	ETC Completion	Estimate At Uncommitted
CIIT Managed												
Architect/Engineer: 7100-7101	\$39,116	(\$24,991)	\$14,125	\$13,800		\$13,800	\$13,525	\$275		\$325	\$14,125	
Other Consultants: 7100-7105	\$2,321	\$2,321	\$2,321	\$2,321		\$2,321	\$2,521	\$2,521			\$2,521	
Management Fees: 7200-7201	\$13,305	(\$13,305)										
Construction: 7300-7301	\$612,813	(\$114,354)	\$498,459	\$498,459	(\$1,875)	\$496,584	\$496,583	\$1		\$1,875	\$498,459	
Miscellaneous: 7300-7302	\$335	\$335					\$335	\$335			\$335	
Contingency: 9999-9999	\$35,012	(\$35,012)										
CIIT Managed Subtotal	\$700,246	(\$184,806)	\$515,440	\$515,115	(\$1,875)	\$513,240	\$512,964	\$276		\$2,200	\$515,440	
Project Total	\$700,246	(\$184,806)	\$515,440	\$515,115	(\$1,875)	\$513,240	\$512,964	\$276		\$2,200	\$515,440	

Program\DeKalb County\421 SPLOST III\High Schools\Redan HS - Roof, HVAC, Career Tech, ADA

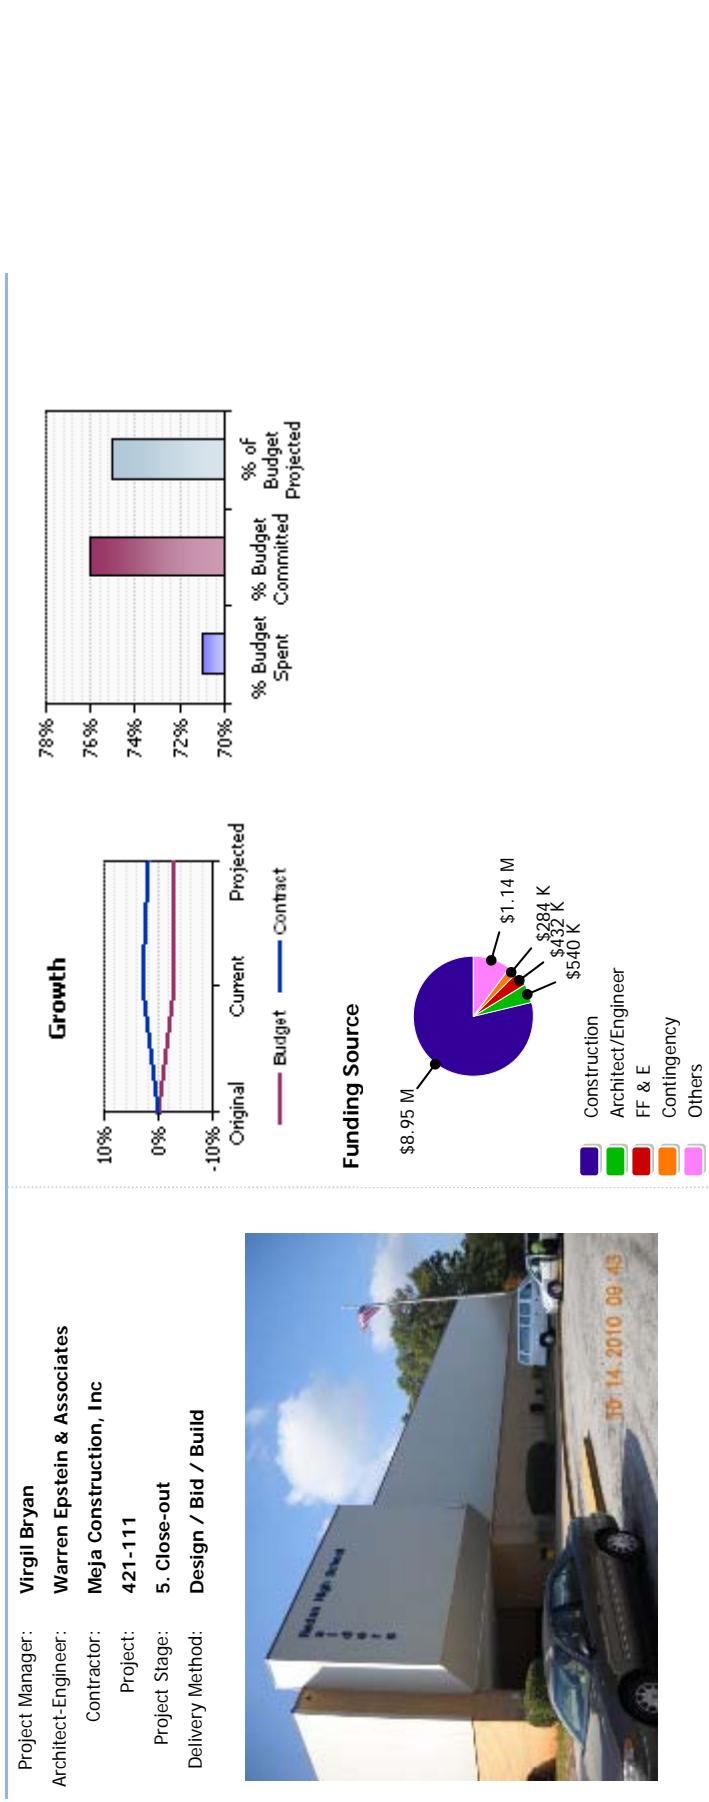


Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	ETC At Completion	Uncommitted
Utilities: 7500-7501	\$135,000		\$135,000	\$175,000	\$115,262	\$114,360	\$257		\$135,000	\$135,000		
Moving / Relocation: 7500-7502	\$175,000		\$175,000	\$100,000	\$4,680	\$4,680	\$4,258	\$422	\$59,000	\$174,262	\$738	
Trailers: 7600-7503	\$250,000	(\$150,000)	\$100,000	\$199,000	\$233,616				\$95,300	\$99,980	\$20	
Contingency: 9999-9999	\$482,616	(\$199,000)	\$10,761,359	\$7,924,104	\$251,910	\$8,176,014	\$7,048,698	\$1,065,448	(\$73,786)	\$133,000	\$133,000	
CIT Managed Subtotal	\$11,231,962	(\$470,603)							\$2,583,650	\$10,685,878	\$75,481	
DCSS Managed												
FF & E: 7700-7504	\$282,120	\$150,000	\$432,120	\$266,375	\$266,375	\$266,375	\$0		\$165,745	\$432,120	\$0	
Technology: 7800-7801	\$150,000		\$150,000	\$152,467	\$152,467	\$105,036	\$47,431		\$152,467	(\$2,467)		
DCSS Managed Subtotal	\$432,120	\$150,000	\$582,120	\$418,842	\$418,842	\$371,411	\$47,432	\$165,745	\$564,587	(\$2,467)		
Project Total	\$11,664,082	(\$320,603)	\$11,343,479	\$8,342,946	\$251,910	\$8,594,857	\$7,420,109	\$1,112,880	(\$73,786)	\$2,749,395	\$11,270,465	\$73,014

Program\DeKalb County\421 SPLOST III\Elementary Schools\Rockbridge ES - HVAC & ADA

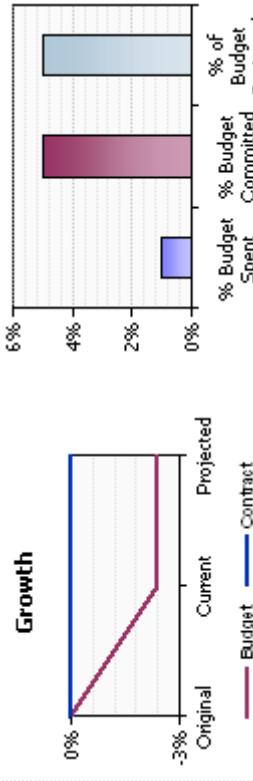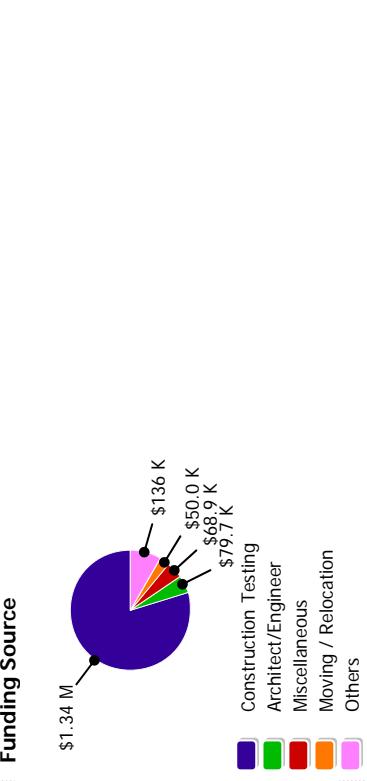
<p>Project Manager: Brad Jacobs Architect-Engineer: Epstein Group Contractor: 421-133 Project Stage: 2. Design Delivery Method: Design / Bid / Build</p> 	<p>Growth</p>  <p>Funding Source</p>  <table border="1"> <thead> <tr> <th>Category</th> <th>Amount (\$)</th> </tr> </thead> <tbody> <tr> <td>Contract</td> <td>\$79.7K</td> </tr> <tr> <td>Budget</td> <td>\$68.9K</td> </tr> <tr> <td>Others</td> <td>\$50.0K</td> </tr> <tr> <td>Moving / Relocation</td> <td>\$136K</td> </tr> <tr> <td>Architect/Engineer</td> <td>\$68.9K</td> </tr> <tr> <td>Construction Testing</td> <td>\$79.7K</td> </tr> <tr> <td>Miscellaneous</td> <td>\$50.0K</td> </tr> </tbody> </table>	Category	Amount (\$)	Contract	\$79.7K	Budget	\$68.9K	Others	\$50.0K	Moving / Relocation	\$136K	Architect/Engineer	\$68.9K	Construction Testing	\$79.7K	Miscellaneous	\$50.0K	<p>Cost Status by Budget Category:</p> <table border="1"> <thead> <tr> <th>Budget Category</th> <th>Original Budget</th> <th>Budget Revision</th> <th>Current Budget</th> <th>Original Contract</th> <th>Executed Changes</th> <th>Current Contract</th> <th>Paid To Date</th> <th>Contract Balance</th> <th>CORs</th> <th>ETC Forecast</th> <th>ETC Estimate At Completion</th> <th>Uncommitted</th> </tr> </thead> <tbody> <tr> <td>CIT Managed</td> <td></td> </tr> <tr> <td>Architect/Engineer: 7100-7101</td> <td>\$79,662</td> <td></td> <td>\$79,662</td> <td>\$75,229</td> <td></td> <td>\$11,284</td> <td>\$56,422</td> <td></td> <td></td> <td>\$4,433</td> <td>\$79,662</td> <td></td> </tr> <tr> <td>Construction Testing: 7100-7103</td> <td>\$13,983</td> <td></td> <td>\$13,983</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>\$13,983</td> <td>\$13,983</td> <td></td> </tr> <tr> <td>Other Consultants: 7100-7105</td> <td>\$14,124</td> <td></td> <td>\$14,124</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>\$14,124</td> <td>\$14,124</td> <td></td> </tr> <tr> <td>Management Fees: 7200-7201</td> <td>\$30,375</td> <td>(\$30,375)</td> <td></td> </tr> <tr> <td>Construction Technology: 7300-7301-22</td> <td>\$1,322,526</td> <td></td> </tr> <tr> <td>Construction Technology: 7300-7301-22</td> <td>\$40,000</td> <td></td> <td>\$40,000</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> </tr> <tr> <td>Miscellaneous: 7300-7302</td> <td>\$68,938</td> <td></td> </tr> <tr> <td>Security: 7400-7401</td> <td>\$10,000</td> <td></td> <td>\$10,000</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> </tr> <tr> <td>Utilities: 7500-7501</td> <td>\$25,000</td> <td></td> <td>\$25,000</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> </tr> <tr> <td>Moving / Relocation: 7500-7502</td> <td>\$50,000</td> <td></td> <td>\$50,000</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> </tr> <tr> <td>Contingency: 9999-9999</td> <td>\$86,916</td> <td>(\$40,000)</td> <td>\$46,916</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> </tr> <tr> <td></td> </tr> </tbody> </table> <p>Scope of Work:</p> <ul style="list-style-type: none"> HVAC, Ceiling and Lighting replacement and other improvements including new generator, parking lot lighting, grease trap, and cooler / freezer boxes. <p>Remarks:</p> <ul style="list-style-type: none"> Preliminary Design underway. 	Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	ETC Estimate At Completion	Uncommitted	CIT Managed													Architect/Engineer: 7100-7101	\$79,662		\$79,662	\$75,229		\$11,284	\$56,422			\$4,433	\$79,662		Construction Testing: 7100-7103	\$13,983		\$13,983							\$13,983	\$13,983		Other Consultants: 7100-7105	\$14,124		\$14,124							\$14,124	\$14,124		Management Fees: 7200-7201	\$30,375	(\$30,375)											Construction Technology: 7300-7301-22	\$1,322,526												Construction Technology: 7300-7301-22	\$40,000		\$40,000										Miscellaneous: 7300-7302	\$68,938												Security: 7400-7401	\$10,000		\$10,000										Utilities: 7500-7501	\$25,000		\$25,000										Moving / Relocation: 7500-7502	\$50,000		\$50,000										Contingency: 9999-9999	\$86,916	(\$40,000)	\$46,916																						
Category	Amount (\$)																																																																																																																																																																																																							
Contract	\$79.7K																																																																																																																																																																																																							
Budget	\$68.9K																																																																																																																																																																																																							
Others	\$50.0K																																																																																																																																																																																																							
Moving / Relocation	\$136K																																																																																																																																																																																																							
Architect/Engineer	\$68.9K																																																																																																																																																																																																							
Construction Testing	\$79.7K																																																																																																																																																																																																							
Miscellaneous	\$50.0K																																																																																																																																																																																																							
Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	ETC Estimate At Completion	Uncommitted																																																																																																																																																																																												
CIT Managed																																																																																																																																																																																																								
Architect/Engineer: 7100-7101	\$79,662		\$79,662	\$75,229		\$11,284	\$56,422			\$4,433	\$79,662																																																																																																																																																																																													
Construction Testing: 7100-7103	\$13,983		\$13,983							\$13,983	\$13,983																																																																																																																																																																																													
Other Consultants: 7100-7105	\$14,124		\$14,124							\$14,124	\$14,124																																																																																																																																																																																													
Management Fees: 7200-7201	\$30,375	(\$30,375)																																																																																																																																																																																																						
Construction Technology: 7300-7301-22	\$1,322,526																																																																																																																																																																																																							
Construction Technology: 7300-7301-22	\$40,000		\$40,000																																																																																																																																																																																																					
Miscellaneous: 7300-7302	\$68,938																																																																																																																																																																																																							
Security: 7400-7401	\$10,000		\$10,000																																																																																																																																																																																																					
Utilities: 7500-7501	\$25,000		\$25,000																																																																																																																																																																																																					
Moving / Relocation: 7500-7502	\$50,000		\$50,000																																																																																																																																																																																																					
Contingency: 9999-9999	\$86,916	(\$40,000)	\$46,916																																																																																																																																																																																																					

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
CIT Managed Subtotal	\$1,701,524	(\$30,375)	\$1,671,149	\$75,229		\$75,229	\$11,284	\$56,422		\$1,595,920	\$1,671,149	
Project Total	\$1,701,524	(\$30,375)	\$1,671,149	\$75,229		\$75,229	\$11,284	\$56,422		\$1,595,920	\$1,671,149	

Program\DeKalb County\421 SPLOST III\Elementary Schools\Sagamore Hills ES - Roof

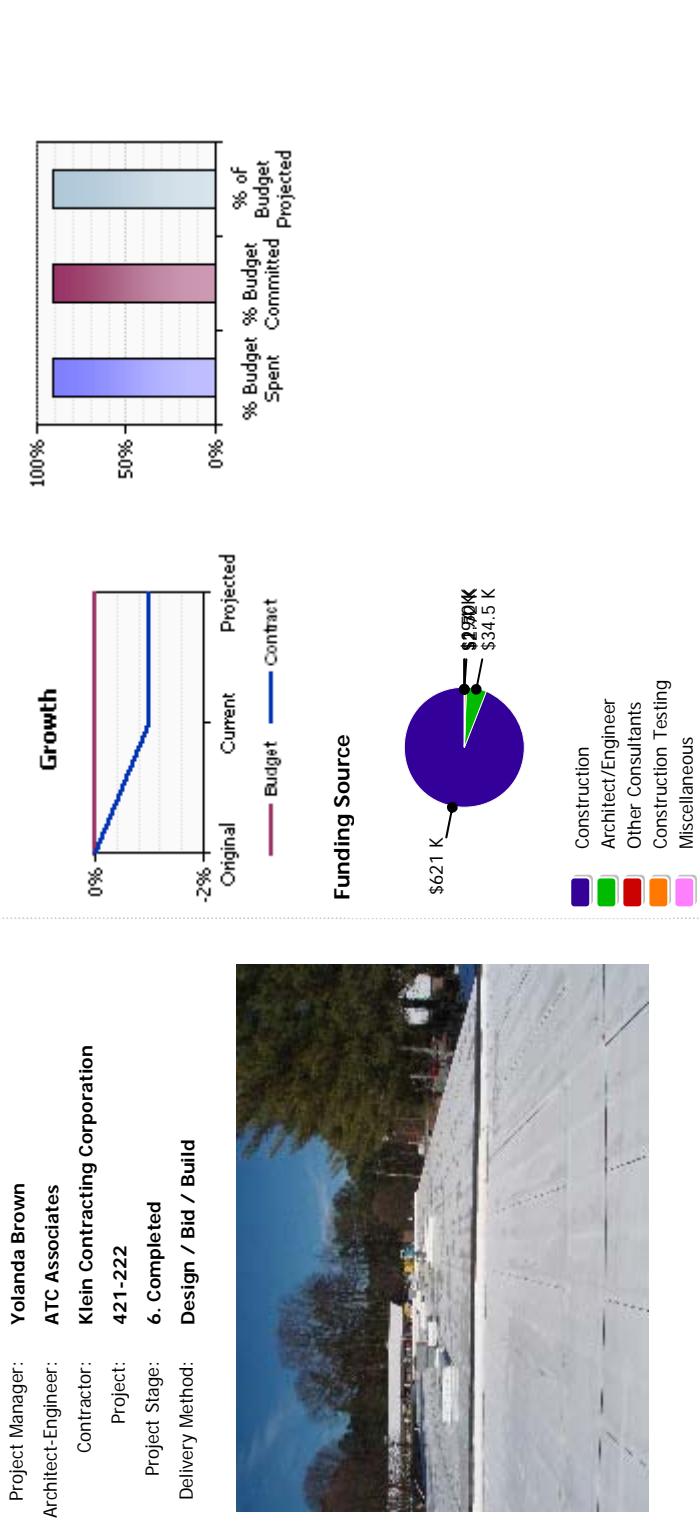

Program\DeKalb County\421 SPLOST III\Other Facilities\Sam Moss Service Center - HVAC and Roof

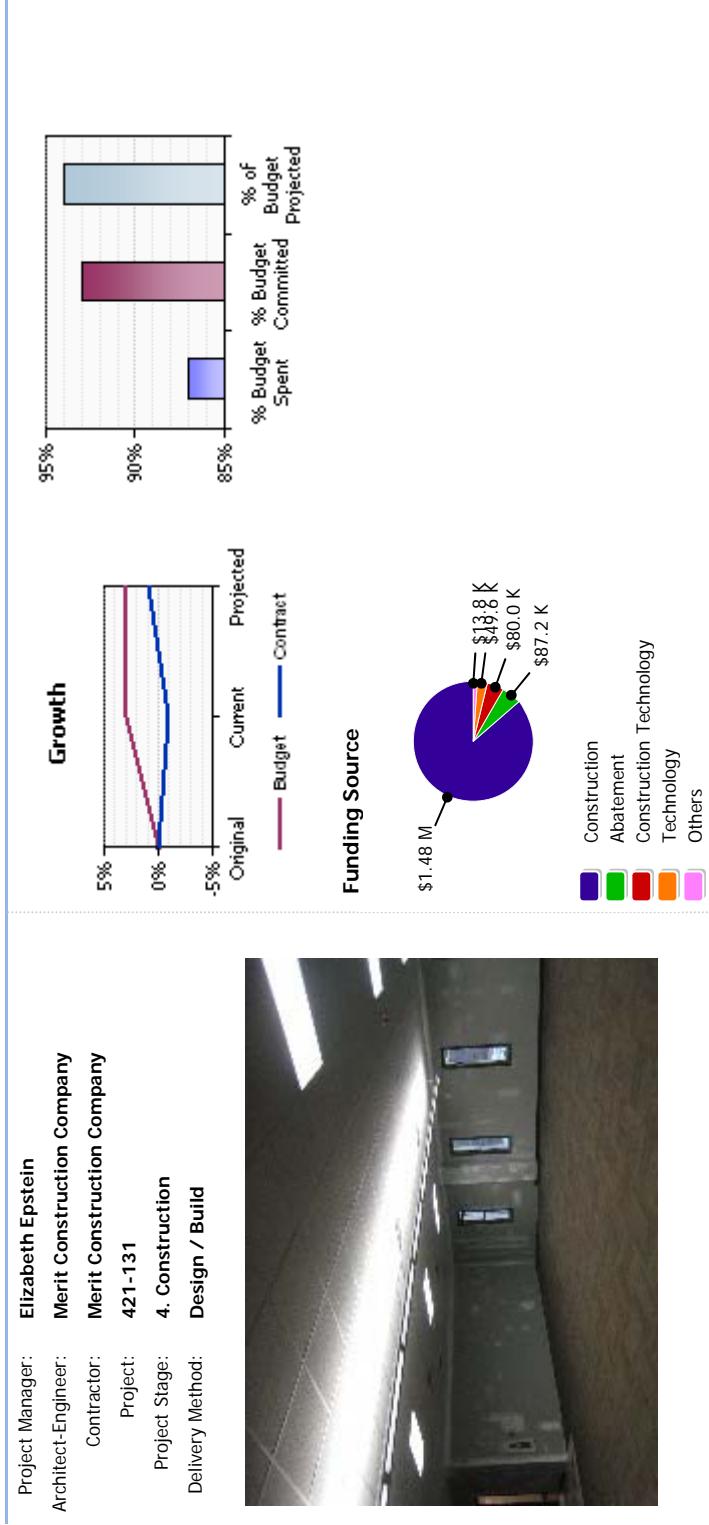

Scope of Work:


- Interior renovation of existing office area, to be completed in phases. Replacement of the HVAC system, ceilings, and lighting, as well as relocation of interior partitions. Work includes painting interior walls, new ceilings and new flooring in the office and administrative areas of the building.
- Completion of installation of wireless network access points (AP's) for entire building was achieved 4/5/11, and network is fully operational.Consolidation of MIS equipment previously located in Phase 4 into the main server room constructed in Phase 1 has been completed. Demolition and abatement of former MIS server room was completed 4/20. Revised floor plans were approved by DeKalb County planning and fire marshal on April 15. Framing of new walls started on April 28 and were completed mid May.

Remarks:

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORS Forecast	ETC Forecast	Estimate At Completion	Uncommitted
CIT Managed												
Architect/Engineer: 7100-7101	\$87,696	(\$80,196)	\$7,500	\$8,000		\$8,000	\$8,000				\$8,000	(\$500)
Construction Testing: 7100-7103	\$15,232	(\$15,232)										
Abatement: 7100-7104	\$8,000	\$79,200	\$87,200	\$72,180		\$72,180	\$0				\$72,180	\$15,020
Other Consultants: 7100-7105	\$16,324	(\$16,000)	\$324	\$120		\$120					\$204	\$324
Management Fees: 7200-7201	\$27,930	(\$27,930)										
Construction: 7300-7301	\$1,416,462	\$59,396	\$1,475,858	\$1,439,765	(\$9,186)	\$1,430,578	\$1,326,932	\$103,646	\$21,336	\$10,000	\$1,451,914	\$23,944
Construction Technology: 7300-7301-22	\$80,000	\$80,000	\$18,749	\$18,749		\$18,749					\$287,49	\$51,251
Trailers: 7600-7503	\$6,000	\$6,000	\$2,925	\$2,925		\$2,925					\$3,075	\$6,000


Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORS	ETC Forecast	Estimate At Completion	Uncommitted
Contingency: 9999.9999	\$82,718	(\$82,718)										
CIT Managed Subtotal	\$1,654,362	\$2,520	\$1,656,882	\$1,541,739	(\$9,186)	\$1,532,552	\$1,428,906	\$103,647	\$21,336	\$13,279	\$1,567,167	\$89,715
DCSS Managed												
Technology: 7800-7801	\$49,550	\$49,550	\$48,793			\$48,793	\$48,793				\$48,793	\$757
DCSS Managed Subtotal	\$49,550	\$49,550	\$48,793			\$48,793	\$48,793				\$48,793	\$757
Project Total	\$1,654,362	\$52,070	\$1,706,432	\$1,590,532	(\$9,186)	\$1,581,345	\$1,477,699	\$103,647	\$21,336	\$13,279	\$1,615,960	\$90,472

Program\DeKalb County\421 SPLOST III\Site Improvements\Site Improvements 1 (321)\Security Lighting

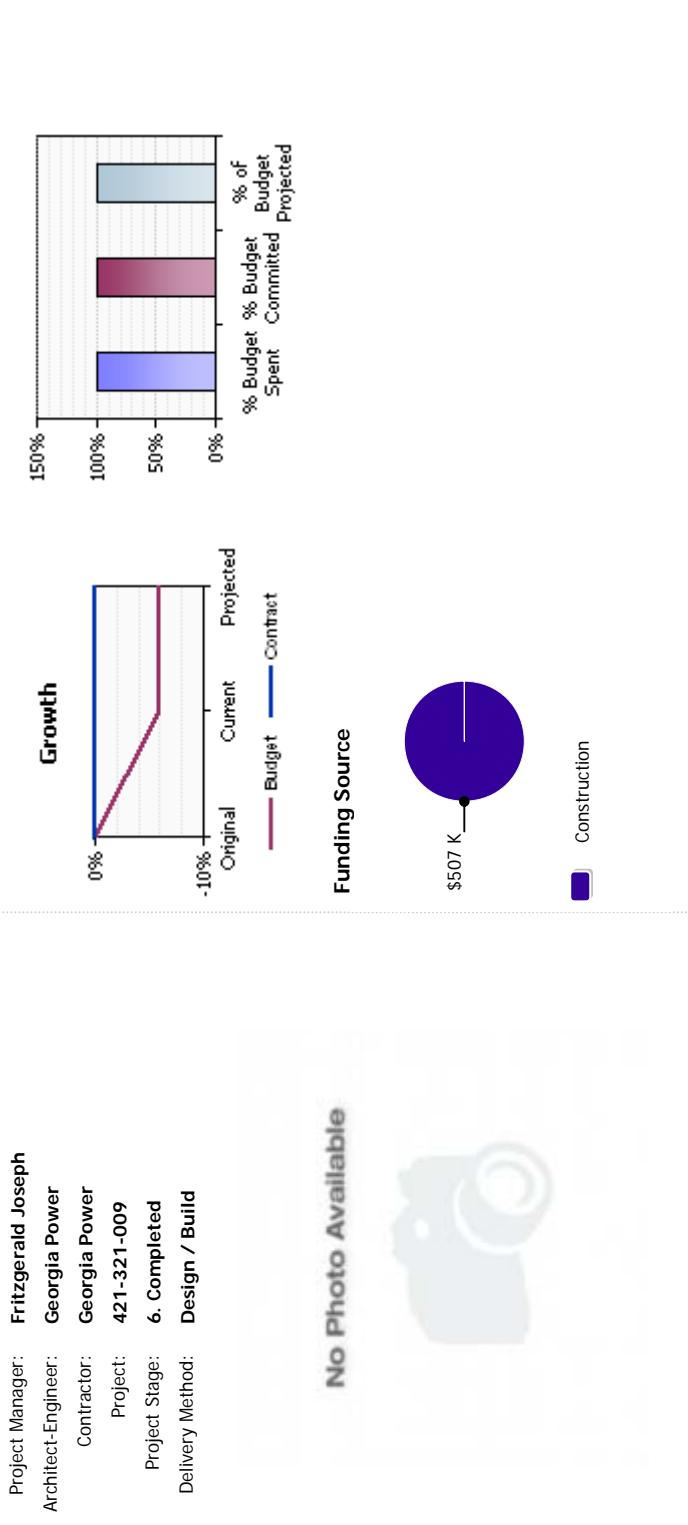

Cost Status by Budget Category:													
Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	ETC Completion	Estimate At Completion	Uncommitted
CIT Managed													
Construction: 7300-7301	\$537,360	(\$30,820)	\$506,540	\$506,540		\$506,540	\$506,540					\$506,540	
CIT Managed Subtotal	\$537,360	(\$30,820)	\$506,540	\$506,540		\$506,540	\$506,540					\$506,540	
Project Total	\$537,360	(\$30,820)	\$506,540	\$506,540		\$506,540	\$506,540					\$506,540	

Program\DeKalb County\421 SPLOST III\Local School Requests\LSPR 2 (341)\Security Upgrade Systems

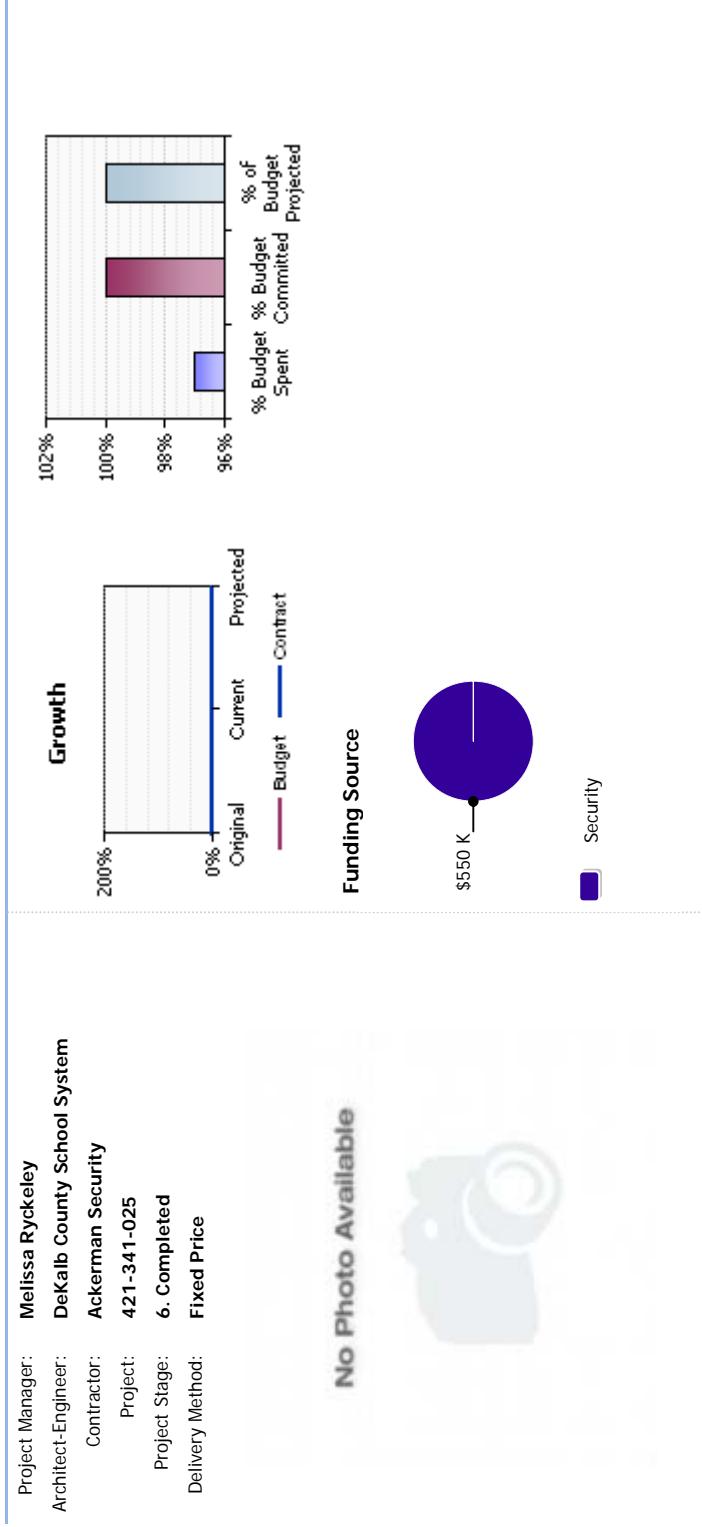

Scope of Work:

- Access control points for various schools and installation of AIPHONE systems at 61 elementary schools and centers.


Remarks:

- WA#1 is 100% complete-
Allgood ES, Flat Rock ES, Oak Grove ES, Princeton ES, Student Relations, East Campus, Livsey ES, Peachtree MS, Lithonia HS, Woodridge ES, Austin ES, Woodward ES, WA#2 is 100% complete-
Bob Mathis ES, Briar Vista ES, Briar Lake ES, Brookett ES, Carey Reynolds ES Montclair ES, Columbia ES, Dresden ES, Coralwood CTR, Dunaire ES, Eagle Woods CTR, E L Bouie ES
WA#3 is 100% complete-
E.L. Miller ES, Evansdale ES, Fernbank Science CTR, Flatshoals ES, Hambrick ES, Henderson MS, Henderson Mill ES, Huntley Hills ES, Idlewood ES, Indian Creek ES, International CTR, Jolly ES,
Kingsley ES, Kittridge Magnet ES, WA#4 is 100% complete-
Gresham ES, Clifton ES, Kelley Lake ES, Stone Mtn ES, Knollwood ES, Laurel Ridge ES, Marbut Theme ES, Meadowview ES, Medlock ES, Stone View ES, Midvale ES, Midway ES, Montgomery ES, Narvie J Harris ES,
WA#5 is 100% complete-
OakView ES, Panola Way ES, Snapfinger ES, Peachcrest ES, Pine Ridge ES, Rainbow ES, Robert Shaw Theme ES, Rockbridge ES, Rowland ES, Sagamore Hills ES, Shadow Rock CTR, Stephenson HS, Shamrock MS, Smokerise ES,
WA#6 is 100% complete-
Terry Mill/DESA ES, Toney ES, Vanderlyn ES, Wadsworth ES, Warren Tech CTR, WBBC Wynbrooke ES, Eagle Woods CTR, DSA HS, Montclair ES, Flat Rock ES, Princeton ES,
Ashford Park ES, Hawthorne ES, International CTR, WA#7 100% complete-
Freeman A & B, Columbia HS, McClendon ES, Salem ES, Chesnut Charter ES, Redan ES Arabia Mtn, Drivers ED N, McNair ES, Sam Moss CTR, Clarkston HS, Redan HS Chapel Hill ES, Chapel Hill MS, Oakcliff ES,
Atherton, Browns Mill, Drivers ED S, McNair HS, Sky Haven ES, Heritage CTR, Rock Chapel ES, Cedar Grove MS, Druid Hills HS, Miller Grove HS, Stone Mill ES, Hightower ES, Tucker HS, Forrest Hills ES, Glen Haven ES, WBBC,

Cost Status by Budget Category:


Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	ETC At Completion	Estimate At Uncommitted
CIT Managed												
Security: 7400-7401	\$550,000		\$550,000	\$550,000		\$550,000	\$535,775	\$14,225			\$550,000	
CIT Managed Subtotal	\$550,000		\$550,000	\$550,000		\$550,000	\$535,775	\$14,225			\$550,000	
Project Total	\$550,000		\$550,000	\$550,000		\$550,000	\$535,775	\$14,225			\$550,000	

Program\DeKalb County\421 SPLOST III\Middle Schools\Sequoyah MS - Roof

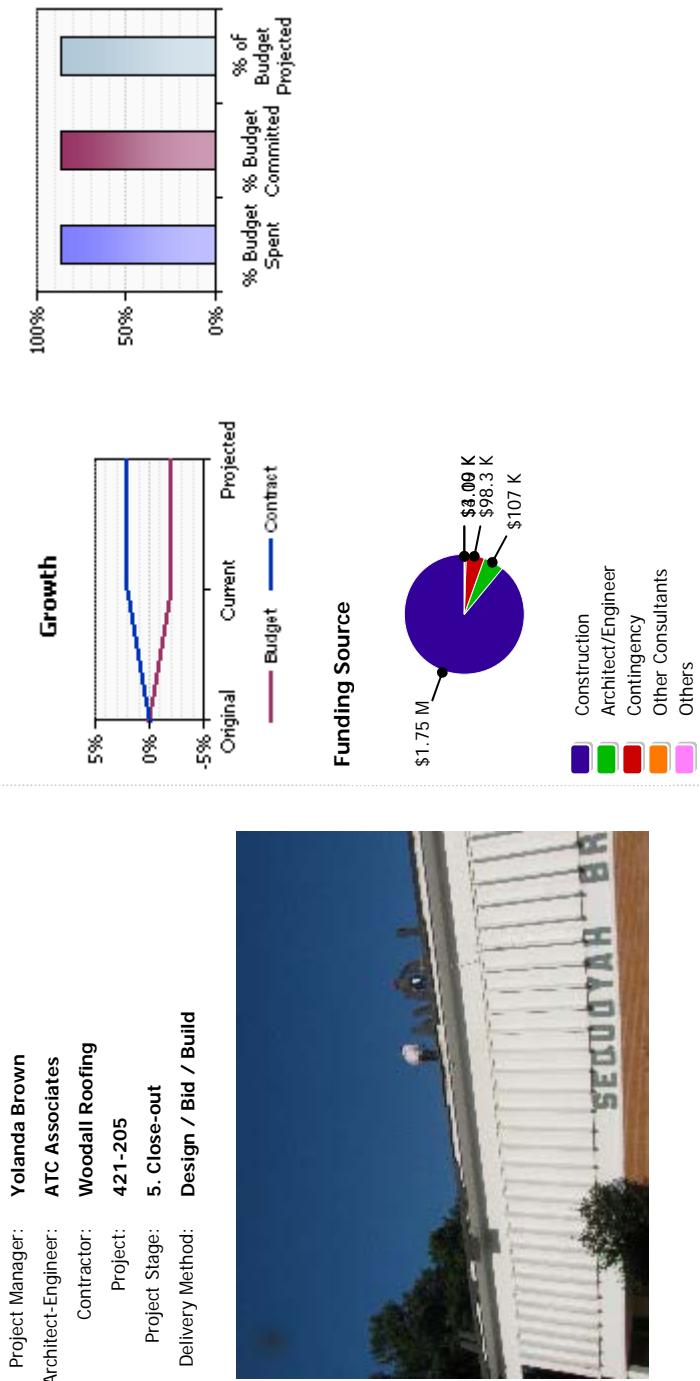

Cost Status by Budget Category:		Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORS	ETC Forecast	Estimate At Completion	Uncommitted
CIT Managed														
Architect/Engineer: 7100-7101	\$111,539	(\$4,186)	\$107,353		\$21,962			\$21,962	(\$0)		\$85,000	\$106,962	\$391	
Construction Testing: 7100-7103		\$1,500	\$1,117		\$1,117			\$1,117	\$0		\$333	\$1,500		
Other Consultants: 7100-7105	\$4,186	\$4,186	\$3,725		\$3,725			\$3,725			\$461		\$4,186	
Management Fees: 7200-7201	\$37,938	(\$37,938)	\$1,747,435	(\$1,500)	\$1,745,935	\$1,638,000	\$34,485	\$1,672,485	\$1,522,942		\$70,000	\$1,742,485	\$3,450	
Construction: 7300-7301	\$1,747,435		\$1,500		\$1,500	\$348		\$348			\$1,152	\$1,500		
Miscellaneous: 7300-7302														
Contingency: 9999-9999	\$99,838	(\$1,500)	\$98,338								\$98,000	\$98,000		
CIT Managed Subtotal	\$1,996,750	(\$37,938)	\$1,958,812	\$1,665,152	\$34,485	\$1,699,637	\$1,550,094	\$0	\$254,996	\$1,954,633	\$4,179			
Project Total	\$1,996,750	(\$37,938)	\$1,958,812	\$1,665,152	\$34,485	\$1,699,637	\$1,550,094	\$0	\$254,996	\$1,954,633	\$4,179			

Program\DeKalb County\421 SPLOST III\Elementary Schools\Sky Haven ES - Roof

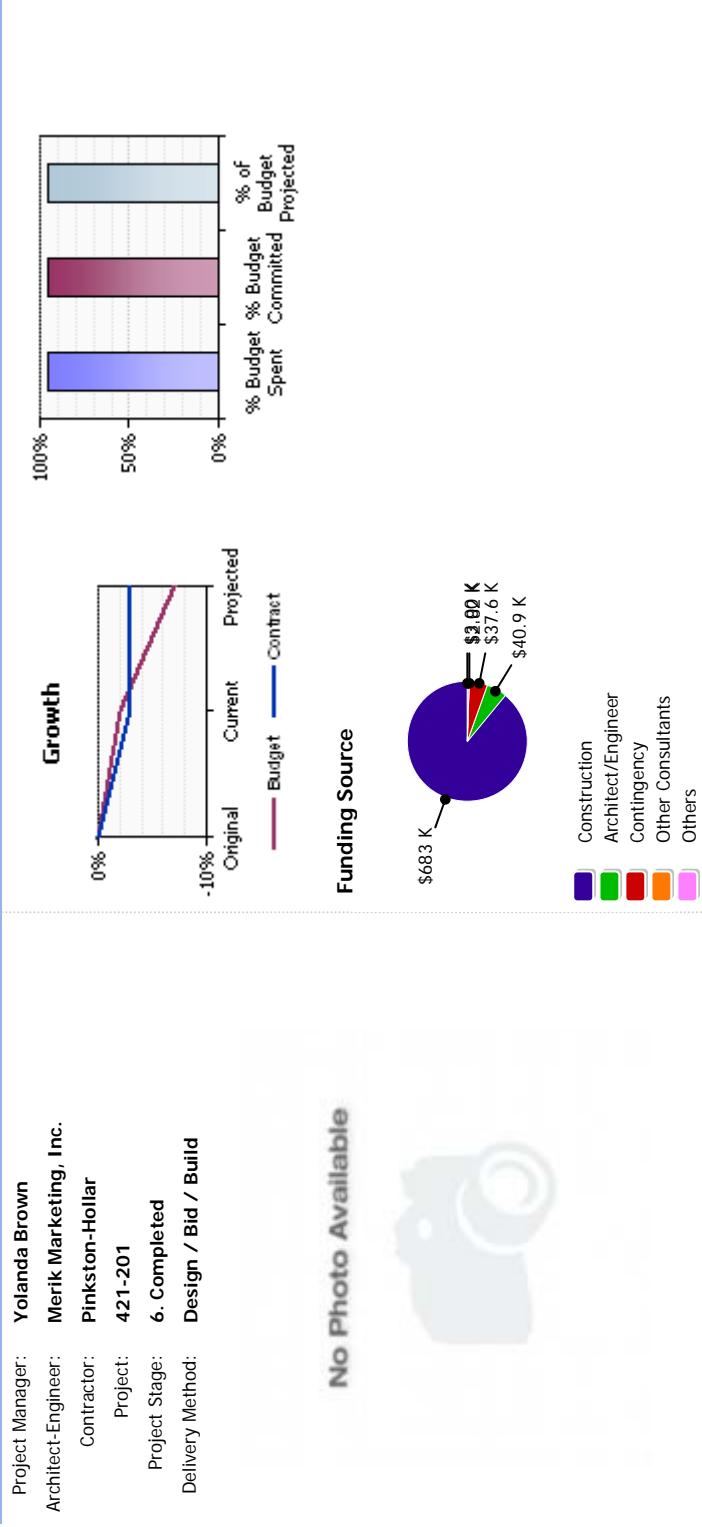


Cost Status by Budget Category:

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
CIT Managed												
Architect/Engineer: 7100-7101	\$43,720	(\$2,819)	\$40,901	\$28,100		\$28,100	\$28,100			\$28,100	\$12,801	
Construction Testing: 7100-7103	\$1,500	\$1,500	\$923			\$923	\$923			\$923	\$577	
Other Consultants: 7100-7105	\$2,819	\$2,819	\$2,819			\$2,819	\$2,819			\$2,819		
Management Fees: 7200-7201	\$14,867	(\$14,867)										
Construction: 7300-7301	\$684,757	(\$1,500)	\$683,257	\$719,157	(\$22,701)	\$692,156	\$2			\$696,456	(\$13,199)	
Miscellaneous: 7300-7302	\$1,500	\$1,500	\$100			\$100				\$100	\$1,400	
Contingency: 9999-9999	\$39,124	(\$1,500)	\$37,624							\$14,000	\$14,000	\$23,624
CIT Managed Subtotal	\$782,468	(\$14,867)	\$767,601	\$751,098	(\$22,701)	\$728,397	\$2	\$724,097	\$14,000	\$742,397	\$25,204	
Project Total	\$782,468	(\$14,867)	\$767,601	\$751,098	(\$22,701)	\$728,397	\$2	\$724,097	\$14,000	\$742,397	\$25,204	


Program\DeKalb County\421 SPLOST III\Elementary Schools\Snapfinger ES - Roof



Program\DeKalb County\421 SPLIT III\Elementary Schools\Stone Mill ES - HVAC



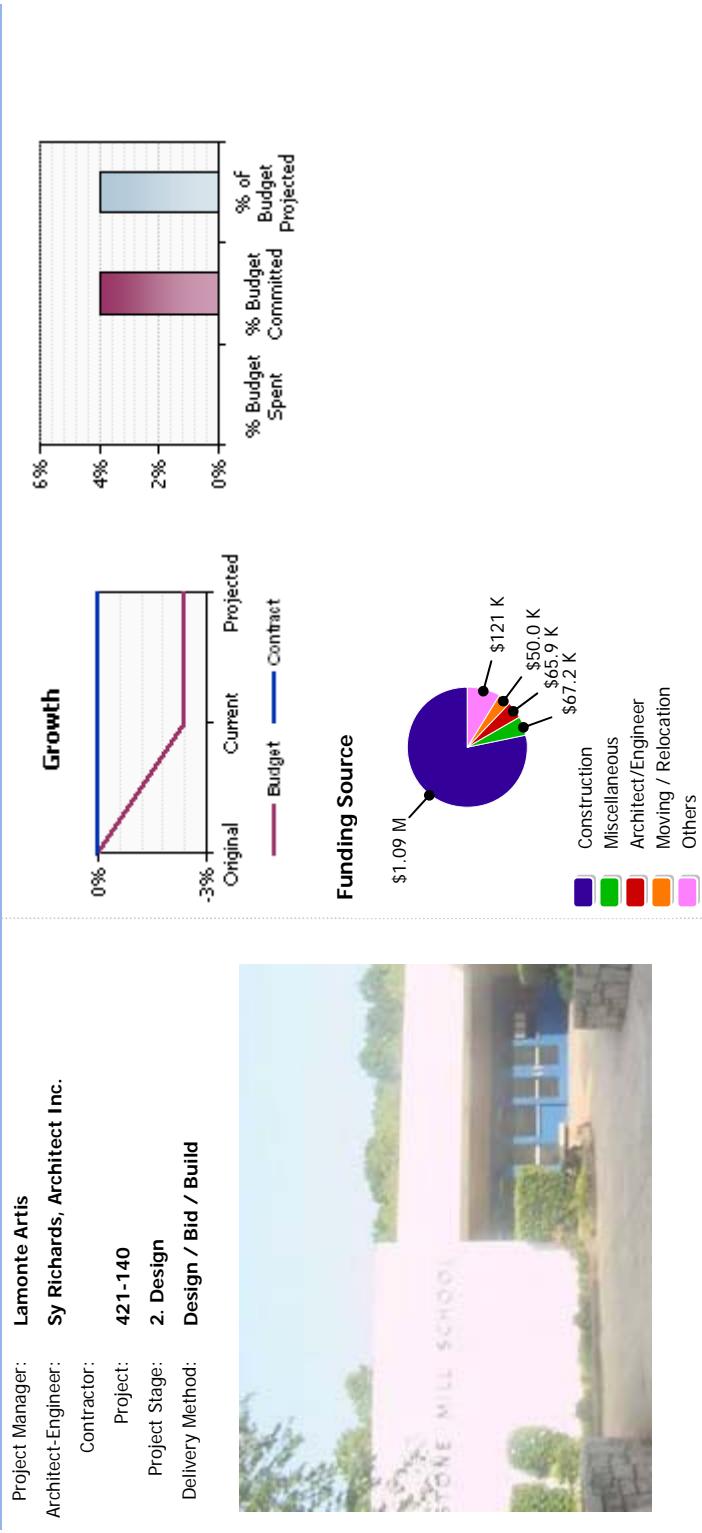


Program\DeKalb County\421 SPLOST III\Elementary Schools\Stone Mountain ES - HVAC & ADA

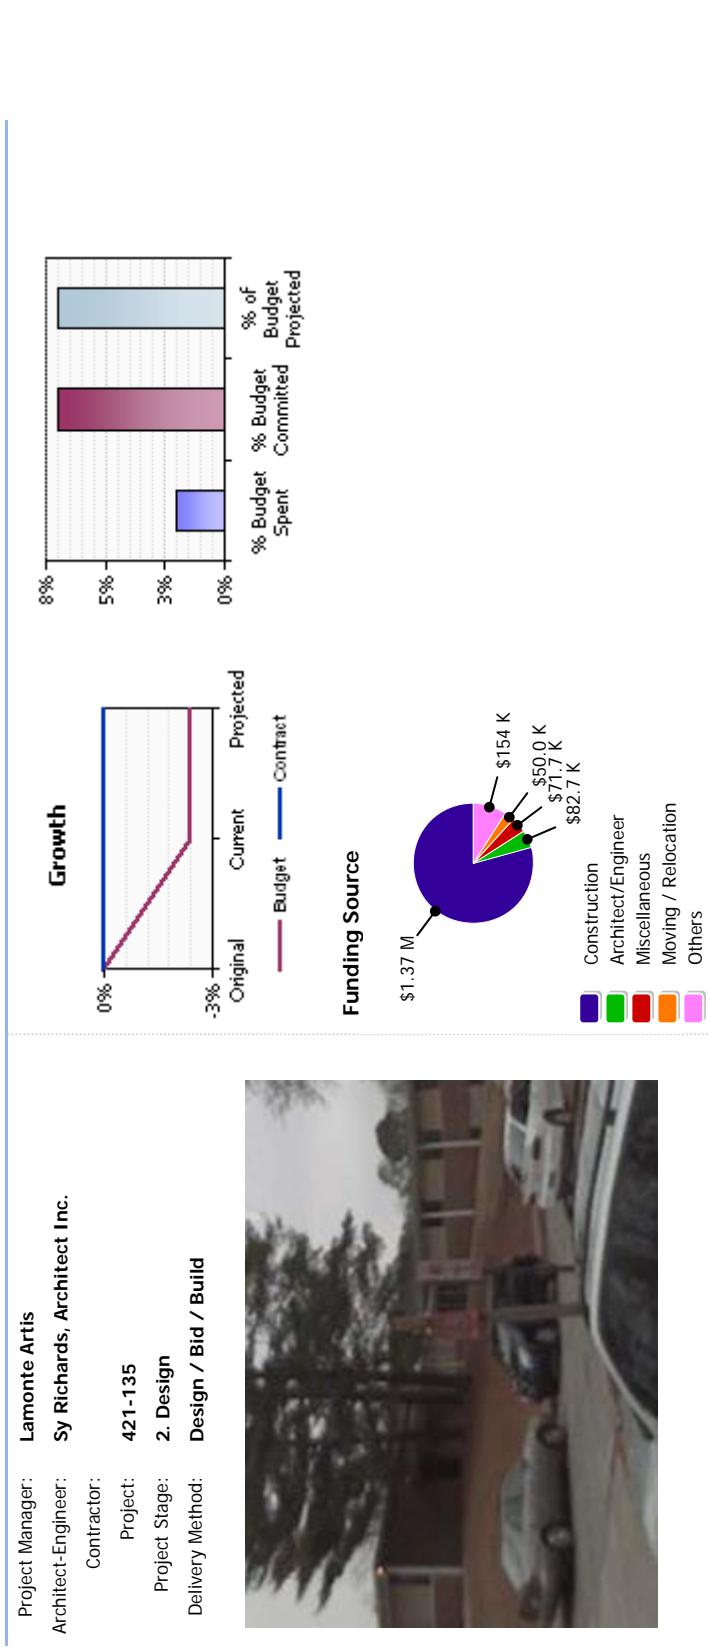

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
CIT Managed Subtotal	\$1,762,775	(\$31,727)	\$1,731,048	\$116,240		\$116,240		\$33,206	\$83,034		\$1,614,808	\$1,731,048
Project Total	\$1,762,775	(\$31,727)	\$1,731,048	\$116,240		\$116,240		\$33,206	\$83,034		\$1,614,808	\$1,731,048

Program\DeKalb County\421 SPLOST III\High Schools\Stone Mountain HS - HVAC, Roof

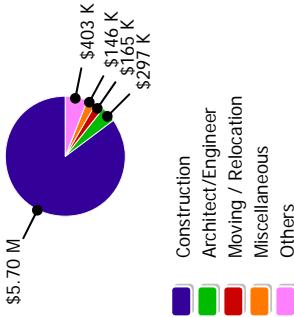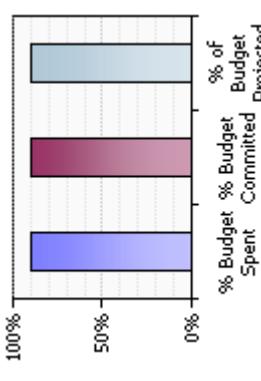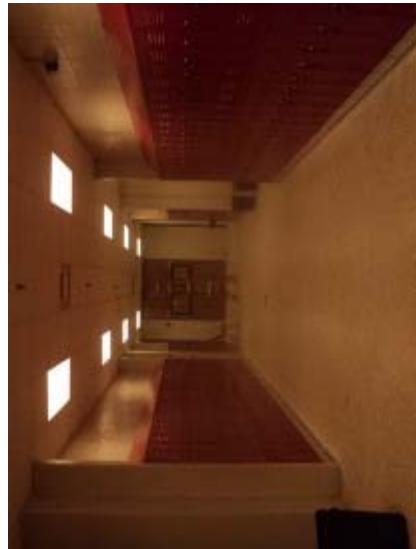Project Manager:	Wade Richardson	Growth																																																																																																																																																														
Architect-Engineer:	Leopard Johnson & Associates																																																																																																																																																															
Contractor:	Merit Construction Company																																																																																																																																																															
Project:	421-110																																																																																																																																																															
Project Stage:	5. Close-out																																																																																																																																																															
Delivery Method:	Design / Bid / Build																																																																																																																																																															
Funding Source																																																																																																																																																																
																																																																																																																																																																
																																																																																																																																																																
																																																																																																																																																																
<p>Scope of Work:</p> <ul style="list-style-type: none"> The scope includes the replacement of the HVAC system, interior lighting system, fire alarm system, and ceilings. The roof will also be replaced and a new emergency generator will be installed. 																																																																																																																																																																
<p>Remarks:</p> <ul style="list-style-type: none"> The project is in the close-out stage. 																																																																																																																																																																
<p>Cost Status by Budget Category:</p> <table border="1"> <thead> <tr> <th>Budget Category</th> <th>Original Budget</th> <th>Budget Revision</th> <th>Current Budget</th> <th>Original Contract</th> <th>Executed Changes</th> <th>Current Contract</th> <th>Paid To Date</th> <th>Contract Balance</th> <th>CORs</th> <th>ETC Forecast</th> <th>ETC</th> <th>Estimate At Completion</th> <th>Uncommitted</th> </tr> </thead> <tbody> <tr> <td>CIT Managed</td> <td></td> </tr> <tr> <td>Architect/Engineer: 7100-7101</td> <td>\$322,300</td> <td>(\$25,000)</td> <td>\$297,300</td> <td>\$135,500</td> <td>\$51,040</td> <td>\$186,540</td> <td>\$182,934</td> <td>\$481</td> <td></td> <td>\$110,760</td> <td>\$297,300</td> <td></td> </tr> <tr> <td>Surveying: 7100-7102</td> <td>\$28,000</td> <td>\$28,000</td> <td>\$27,300</td> <td>\$27,300</td> <td></td> <td>\$27,300</td> <td>\$27,300</td> <td></td> <td></td> <td>\$700</td> <td>\$28,000</td> <td></td> </tr> <tr> <td>Construction Testing: 7100-7103</td> <td>\$37,582</td> <td>(\$32,000)</td> <td>\$5,382</td> <td>\$5,143</td> <td></td> <td>\$5,143</td> <td>\$3,615</td> <td>\$1,237</td> <td></td> <td>\$439</td> <td>\$5,582</td> <td></td> </tr> <tr> <td>Abatement: 7100-7104</td> <td>\$20,000</td> <td>\$60,000</td> <td>\$80,000</td> <td>\$69,438</td> <td></td> <td>\$69,438</td> <td>\$65,517</td> <td>\$0</td> <td></td> <td>\$10,562</td> <td>\$80,000</td> <td>\$0</td> </tr> <tr> <td>Other Consultants: 7100-7105</td> <td>\$37,961</td> <td>(\$15,000)</td> <td>\$22,961</td> <td>\$7,591</td> <td></td> <td>\$7,591</td> <td>\$7,591</td> <td></td> <td></td> <td>\$15,370</td> <td>\$22,961</td> <td></td> </tr> <tr> <td>Management Fees: 7200-7201</td> <td>\$117,971</td> <td>(\$117,971)</td> <td></td> </tr> <tr> <td>Construction: 7300-7301</td> <td>\$5,187,833</td> <td>\$515,211</td> <td>\$5,703,044</td> <td>\$5,131,046</td> <td>\$357,461</td> <td>\$5,488,507</td> <td>\$4,815,760</td> <td>\$12,036</td> <td></td> <td>\$214,000</td> <td>\$5,702,507</td> <td>\$537</td> </tr> <tr> <td>Construction Technology: 7300-7301.22</td> <td>\$30,000</td> <td></td> <td>\$30,000</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>\$10,000</td> <td>\$10,000</td> <td></td> </tr> <tr> <td>Miscellaneous: 7300-7302</td> <td>\$174,867</td> <td>(\$147,000)</td> <td>\$22,867</td> <td>\$12,061</td> <td></td> <td>\$12,061</td> <td>\$5,243</td> <td>\$13</td> <td></td> <td>\$5,806</td> <td>\$17,867</td> <td></td> </tr> <tr> <td>Security: 7400-7401</td> <td>\$30,000</td> <td>\$40,000</td> <td>\$70,000</td> <td>\$24,185</td> <td></td> <td>\$24,185</td> <td>\$24,185</td> <td></td> <td></td> <td>\$45,000</td> <td>\$45,000</td> <td>\$815</td> </tr> </tbody> </table>			Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	ETC	Estimate At Completion	Uncommitted	CIT Managed														Architect/Engineer: 7100-7101	\$322,300	(\$25,000)	\$297,300	\$135,500	\$51,040	\$186,540	\$182,934	\$481		\$110,760	\$297,300		Surveying: 7100-7102	\$28,000	\$28,000	\$27,300	\$27,300		\$27,300	\$27,300			\$700	\$28,000		Construction Testing: 7100-7103	\$37,582	(\$32,000)	\$5,382	\$5,143		\$5,143	\$3,615	\$1,237		\$439	\$5,582		Abatement: 7100-7104	\$20,000	\$60,000	\$80,000	\$69,438		\$69,438	\$65,517	\$0		\$10,562	\$80,000	\$0	Other Consultants: 7100-7105	\$37,961	(\$15,000)	\$22,961	\$7,591		\$7,591	\$7,591			\$15,370	\$22,961		Management Fees: 7200-7201	\$117,971	(\$117,971)											Construction: 7300-7301	\$5,187,833	\$515,211	\$5,703,044	\$5,131,046	\$357,461	\$5,488,507	\$4,815,760	\$12,036		\$214,000	\$5,702,507	\$537	Construction Technology: 7300-7301.22	\$30,000		\$30,000							\$10,000	\$10,000		Miscellaneous: 7300-7302	\$174,867	(\$147,000)	\$22,867	\$12,061		\$12,061	\$5,243	\$13		\$5,806	\$17,867		Security: 7400-7401	\$30,000	\$40,000	\$70,000	\$24,185		\$24,185	\$24,185			\$45,000	\$45,000	\$815
Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	ETC	Estimate At Completion	Uncommitted																																																																																																																																																			
CIT Managed																																																																																																																																																																
Architect/Engineer: 7100-7101	\$322,300	(\$25,000)	\$297,300	\$135,500	\$51,040	\$186,540	\$182,934	\$481		\$110,760	\$297,300																																																																																																																																																					
Surveying: 7100-7102	\$28,000	\$28,000	\$27,300	\$27,300		\$27,300	\$27,300			\$700	\$28,000																																																																																																																																																					
Construction Testing: 7100-7103	\$37,582	(\$32,000)	\$5,382	\$5,143		\$5,143	\$3,615	\$1,237		\$439	\$5,582																																																																																																																																																					
Abatement: 7100-7104	\$20,000	\$60,000	\$80,000	\$69,438		\$69,438	\$65,517	\$0		\$10,562	\$80,000	\$0																																																																																																																																																				
Other Consultants: 7100-7105	\$37,961	(\$15,000)	\$22,961	\$7,591		\$7,591	\$7,591			\$15,370	\$22,961																																																																																																																																																					
Management Fees: 7200-7201	\$117,971	(\$117,971)																																																																																																																																																														
Construction: 7300-7301	\$5,187,833	\$515,211	\$5,703,044	\$5,131,046	\$357,461	\$5,488,507	\$4,815,760	\$12,036		\$214,000	\$5,702,507	\$537																																																																																																																																																				
Construction Technology: 7300-7301.22	\$30,000		\$30,000							\$10,000	\$10,000																																																																																																																																																					
Miscellaneous: 7300-7302	\$174,867	(\$147,000)	\$22,867	\$12,061		\$12,061	\$5,243	\$13		\$5,806	\$17,867																																																																																																																																																					
Security: 7400-7401	\$30,000	\$40,000	\$70,000	\$24,185		\$24,185	\$24,185			\$45,000	\$45,000	\$815																																																																																																																																																				

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
Utilities: 7500-7501	\$75,000	(\$45,000)	\$30,000	\$1,620		\$1,620		\$1	\$28,380	\$30,000		
Moving / Relocation: 7500-7502	\$125,000	\$40,000	\$165,000	\$80,576		\$80,576	\$72,203	(\$3,604)	\$84,424	\$165,000	\$0	
Trailers: 7600-7503	\$250,000	(\$238,500)	\$11,500	\$11,500		\$11,500	\$10,514	\$841		\$11,500		
Contingency: 9999-9999	\$335,711	\$15,000	(\$320,711)	\$6,486,254	\$5,505,960	\$408,501	\$5,914,461	\$11,005	\$540,441	\$6,454,902	\$31,352	
DCSS Managed Subtotal	\$6,714,225	(\$227,971)										
DCSS Managed												
FF&E: 7700-7504	\$100,000	\$100,000	\$48,942		\$48,942				\$51,058	\$100,000	(\$0)	
Technology: 7800-7801	\$10,000	\$10,000	\$2,842		\$2,842		\$2,796	\$46	\$7,158	\$10,000		
DCSS Managed Subtotal	\$110,000	\$110,000	\$51,784				\$51,784	\$5,738	\$58,216	\$110,000	(\$0)	
Project Total	\$6,714,225	(\$117,971)	\$6,596,254	\$5,557,744	\$408,501	\$5,966,245	\$5,266,601	\$11,051	\$598,657	\$6,564,902	\$31,352	

Program\DeKalb County\421 SPLOST III\High Schools\SW DeKalb HS - SPLOST II Deferred, ADA

Project Manager: Wade Richardson
Architect-Engineer: CDH Partners
Contractor: 421-102
Project: 421-102
Project Stage: 2. Design
Delivery Method: Design / Bid / Build

Growth

Original Current Projected

— Budget — Contract

Funding Source

\$17.6 M \$1.90 M \$674 K \$1.07 M \$1.07 M

Construction Architect/Engineer Contingency Technology Others

Southwest DeKalb High School

Projected Budget vs Actual Spent

Category	Actual Spent (%)	Budget (%)	Projected (%)
Construction	~10%	~10%	~10%
Architect/Engineer	~5%	~5%	~5%
Contingency	~1%	~1%	~1%
Technology	~1%	~1%	~1%
Others	~1%	~1%	~1%

Scope of Work:

- The SPLOST II scope of work included locker room renovations, a new multipurpose building, new roads, parking lot paving, resurfacing the tennis court and baseball/football/soccer field which has all been completed.

In July, 2009, under SPLOST III, the DeKalb County Board of Education approved an additional \$20.2 million in funding for a new 31-classroom addition, pursuant to the CIP Mid-Program Assessment Report.


Demand:

- The multi-purpose building construction is complete and the associated contracts have been closed.

Cost Status by Budget Category:

Budget Category		Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORS	ETC Forecast	Estimate At Completion	Uncommitted
Construction: 7300-7301		\$1,371,400	\$16,227,508	\$17,598,908	\$1,384,133	\$83,351	\$1,467,484	\$1,449,416	\$18,068	\$16,131,424	\$17,598,908		
Construction Technology: 7300-7301.22			\$30,000	\$30,000						\$30,000	\$30,000		
Miscellaneous: 7300-7302		\$173,350	\$375,449	\$548,799	\$345		\$345		\$22,200	\$22,180	\$20	\$548,454	
Security: 7400-7401		\$10,000	\$87,200	\$97,200								\$75,000	\$97,200
Utilities: 7500-7501			\$125,000	\$125,000								\$125,000	\$125,000
Moving / Relocation: 7500-7502		\$30,000	\$100,000	\$130,000	\$670		\$670					\$129,000	\$129,670
Contingency: 9999-9999		\$91,175	\$976,325	\$1,067,500								\$1,067,500	\$330
CTI Managed Subtotal		\$1,852,225	\$19,146,134	\$20,998,409	\$2,185,899	\$184,785	\$2,370,684	\$1,718,486	\$611,928		\$18,627,395	\$20,998,079	\$330
DCSS Managed													
FF&E: 7700-7504		\$31,760	\$606,049	\$637,809	\$3,030		\$3,030					\$637,779	
Technology: 7800-7801		\$260,000	\$414,032	\$674,032	\$254,913		\$254,913					\$419,119	
DCSS Managed Subtotal		\$291,760	\$1,020,081	\$1,311,841	\$257,943		\$257,943					\$1,053,898	
Project Total		\$2,144,035	\$20,166,215	\$22,310,250	\$2,443,842	\$184,785	\$2,628,627	\$1,976,429	\$611,928		\$19,681,293	\$22,309,920	\$330


Program\DeKalb County\421 SPLOST III\Elementary Schools\Terry Mill ES (DESA) - Roof

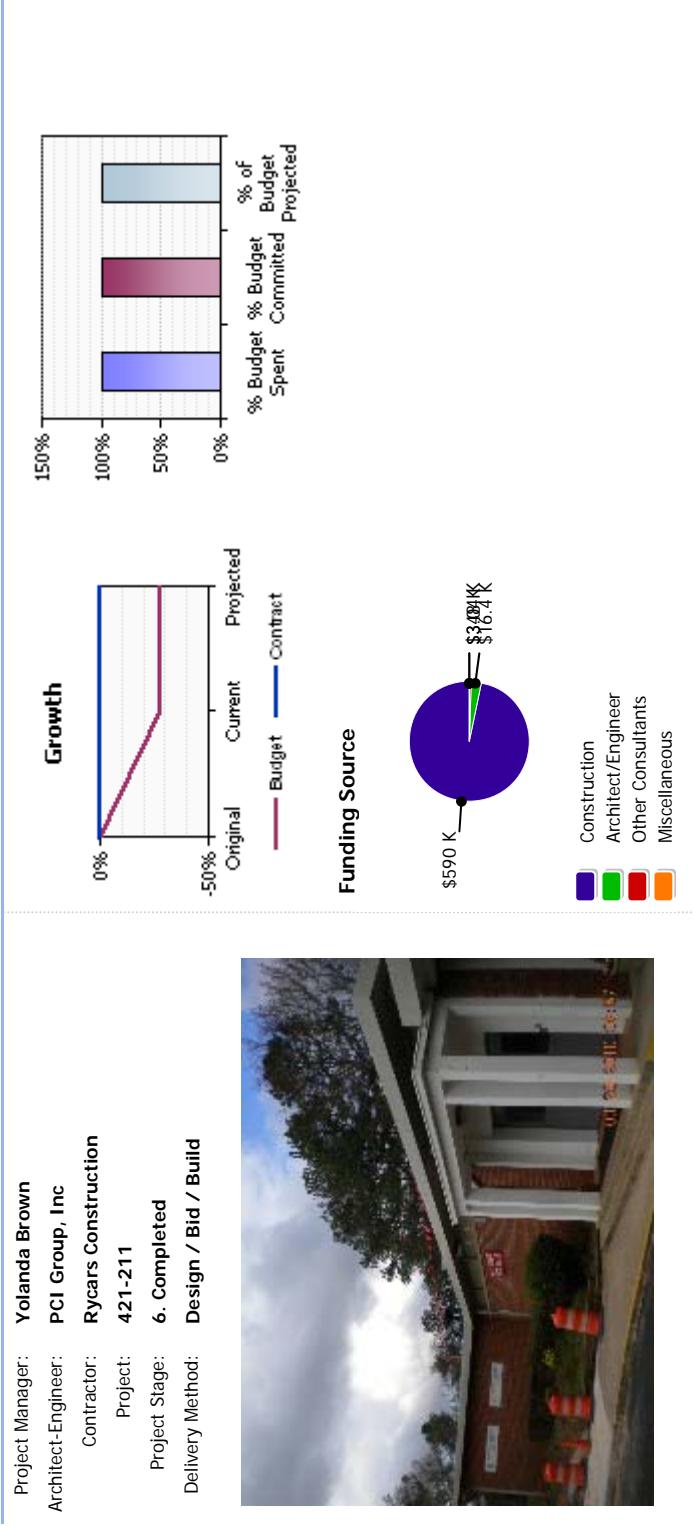

Cost Status by Budget Category:						
Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract
CIT Managed						
Architect/Engineer: 7100-7101	\$47,329	(\$30,929)	\$16,400	\$16,400		\$16,400
Other Consultants: 7100-7105		\$3,037	\$3,037	\$3,037		\$3,037
Management Fees: 7200-7201	\$16,098	(\$16,098)				
Construction: 7300-7301	\$741,480	(\$71,078)	\$590,402	\$592,902	(\$2,500)	\$590,402
Miscellaneous: 7300-7302		\$348	\$348			
Contingency: 9999.9999	\$42,364	(\$42,364)				
CIT Managed Subtotal	\$847,271	(\$237,084)	\$610,187	\$612,687	(\$2,500)	\$610,187
Project Total	\$847,271	(\$237,084)	\$610,187	\$612,687	(\$2,500)	\$610,187

Estimate At Completion

Program\DeKalb County\421 SPLOST III\High Schools\Towers HS - SPLOST II Deferred

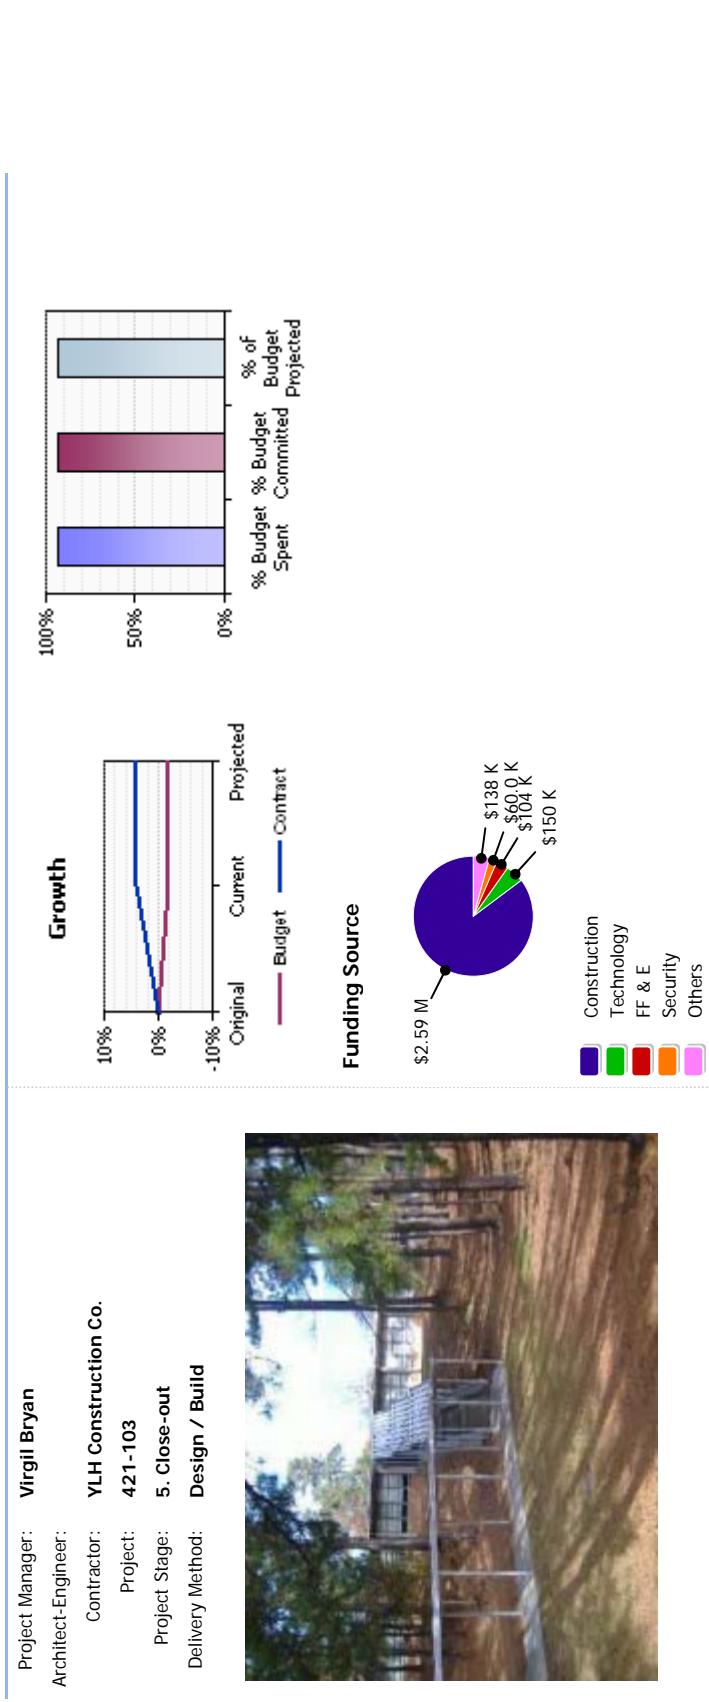

Scope of Work:

- The scope includes a 3 Classroom Suite Career Technology addition and bus loop renovation. Existing square footage is 170,679.
- 02/17/11: The addition has been turned over to the school and in use. Close-out is in progress. The temporary exit from the cafeteria is being reviewed for conversion to a permanent exit for trash removal/compactor access.

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
Moving / Relocation: 7500-7502	\$50,000	(\$40,000)	\$10,000	\$1,600		\$1,600	\$1,916	(\$316)			\$1,600	\$8,400
Trailers: 7600-7503	\$100,000	(\$94,000)	\$6,000	\$6,000		\$6,000	\$6,000				\$6,000	
Contingency: 9999-9999	\$128,000	(\$118,000)	\$10,000									\$10,000
CIT Managed Subtotal	\$2,844,000	(\$51,200)	\$2,792,800	\$2,567,084	\$102,723	\$2,669,807	\$2,668,095	\$1,712	(\$1,060)	\$31,000	\$2,699,747	\$93,053
DCSS Managed												
FF&E: 7700-7504	\$103,600		\$103,600	\$76,829		\$76,829					\$26,270	\$103,099
Technology: 7800-7801	\$150,000		\$150,000	\$100,989		\$100,989					\$25,000	\$125,989
DCSS Managed Subtotal	\$253,600		\$253,600	\$177,818		\$177,818					\$51,270	\$229,088
Project Total	\$3,097,600	(\$51,200)	\$3,046,400	\$2,744,902	\$102,723	\$2,847,625	\$2,845,913	\$1,712	(\$1,060)	\$82,270	\$2,928,835	\$117,565

Program\DeKalb County\421 SPLOST III\High Schools\Tucker HS - New Replacement High School

Project Manager: Amy Sue Mann
Architect-Engineer: Milton Pace Architects
Contractor: Turner Construction
Project: 421-108
Project Stage: 5. Close-out
Delivery Method: CM @ Risk

Growth

Funding Source

Site Photograph

The dashboard displays the following information:

- Project Status:** A bar chart comparing % Budget Spent (dark blue), % Budget Committed (light blue), and % of Budget Projected (lightest blue). The bars are nearly at 100%.
- Growth:** A line graph showing Actual Growth (red line) and Projected Growth (blue line) over time. Both lines start near -25%, drop sharply to 0% by week 10, and then rise to approximately 25% by week 20.
- Funding Source:** A pie chart showing the distribution of \$54.2 M across five categories: Construction (purple), Architect/Engineer (green), Technology (yellow), FF & E (orange), and Others (pink).
- Site Photograph:** An aerial view of the construction site, showing several large buildings with blue roofs and surrounding infrastructure.

Scope of Work:


- The new facility will be built in two phases around the existing school. Phase 1 includes a two story building fronting LaVista Road which will house academic classrooms and the 9th Grade Academy. Additionally, a four story general classroom wing with administrative offices and a media center and a three story parking deck will be constructed. Phase 2 consists of the Career Technology Labs, Auditorium, Fine Arts and Gymnasium facilities. Site work for the new fields will also be completed in this phase.
 - Remarks:
 - The conversion of the Tucker Middle School Softball field for high school competition softball use and additional work at the baseball field to replace items originally constructed by the Booster Club, but not included in the original project, will be completed over the summer 2011. This project is in close out. Budget Reallocation in place for July 2011

Cost Status by Budget Category:

Cost Status by Budget Category							
Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date
CIT Managed							
Architect/Engineer: 7100-7101	\$3,035,428	(\$500,000)	\$2,535,428	\$2,066,346	\$363,835	\$2,430,181	\$2,375,371
Surveying: 7100-7102	\$15,000	\$21,000	\$36,000	\$18,709		\$18,709	\$18,709
Construction Testing: 7100-7103	\$225,000	\$105,900	\$330,900	\$316,509		\$316,509	\$303,823
Abatement: 7100-7104	\$100,000	\$60,000	\$160,000	\$135,532		\$135,532	(\$836)
Other Consultants: 7100-7105	\$365,000	(\$300,000)	\$65,000				\$134,242
Management Fees: 7200-7201	\$1,365,000	(\$1,365,000)					\$1,290
Construction: 7200-7202	\$1,530,466	\$2,270,000	\$54,230,466	\$48,133,948	\$6,555,142	\$54,689,090	\$49,184,562
Miscellaneous: 7200-7203	\$712,050	\$712,050					

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
Security: 7400-7401	\$200,000	(\$167,000)	\$33,000	\$29,147		\$29,147	\$29,147			\$3,800	\$32,947	\$53
Utilities: 7500-7501	\$200,000	\$200,000	\$200,000	\$111,527		\$111,527	\$31,707	(\$0)		\$88,000	\$199,527	\$473
Moving / Relocation: 7500-7502	\$250,000	\$250,000	\$250,000	\$63,560		\$63,560	\$62,227	(\$12)	\$5,313	\$181,000	\$249,873	\$127
Trailers: 7600-7503	\$2,000,000	(\$2,000,000)										
Contingency: 9999-9999	\$4,075,000	(\$3,778,085)	\$296,915									
CIT Managed Subtotal	\$64,072,944	(\$5,466,085)	\$58,606,859	\$50,900,969	\$6,918,977	\$57,819,946	\$52,153,434	\$1,151,311	\$11,813	\$1,230,100	\$59,061,859	\$15 (\$455,000)
DCSS Managed												
Land: 7100-7150	\$276,085	\$276,085	\$276,084			\$276,084					\$276,084	\$2
FF&E: 7700-7504	\$1,007,072	\$225,000	\$1,232,072	\$1,171,167		\$1,171,167					\$60,900	\$1,232,067
Technology: 7800-7801	\$1,250,000	\$1,250,000	\$1,115,214			\$1,115,214					\$134,780	\$1,249,994
DCSS Managed Subtotal	\$2,257,072	\$501,085	\$2,758,157	\$2,562,464		\$2,562,464					\$195,680	\$2,758,144
Project Total	\$66,330,016	(\$4,965,000)	\$61,365,016	\$53,463,433	\$6,918,977	\$60,382,410	\$54,716,076	\$1,151,132	\$11,813	\$1,425,780	\$61,820,003	(\$454,987)

Program\DeKalb County\421 SPLOST III\Elementary Schools\Vanderlyn ES - HVAC, Roof, ADA

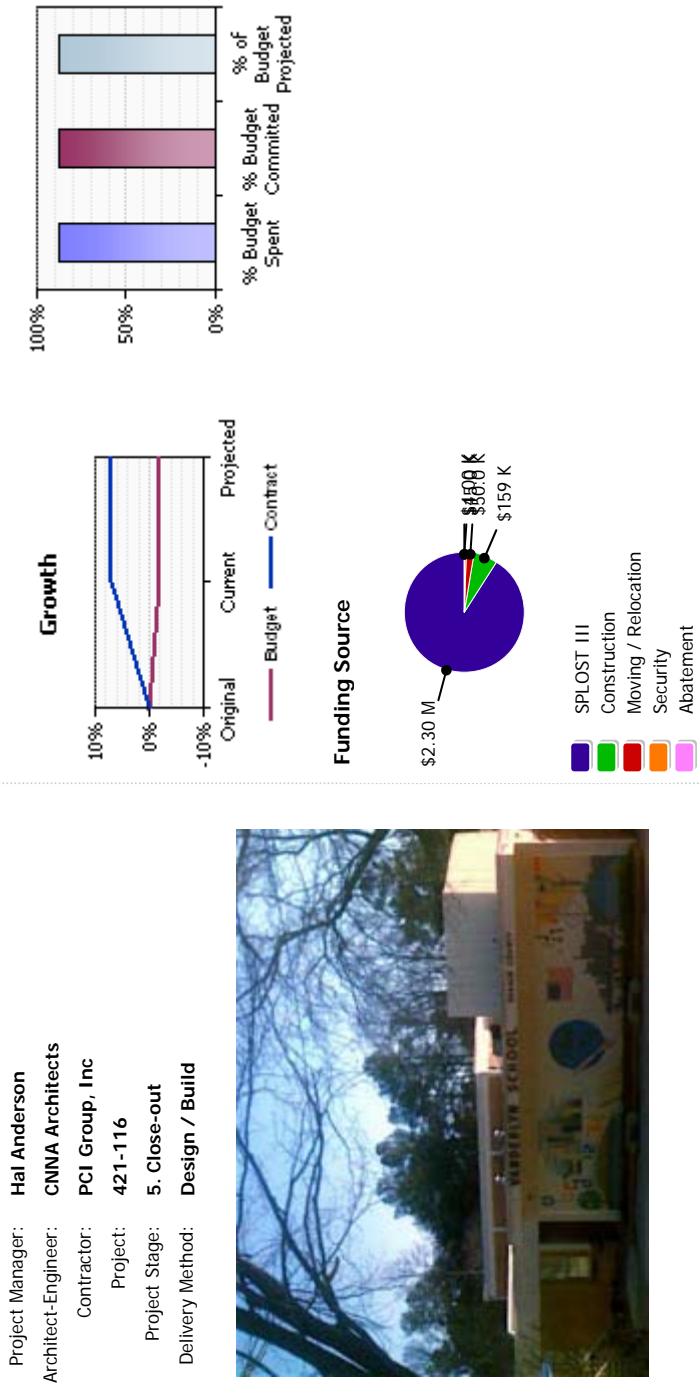


Cost Status by Budget Category:


Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORS	ETC Forecast	Estimate At Completion	Uncommitted
CIT Managed												
Architect/Engineer: 7100-7101	\$114,000	(\$114,000)										
Construction Testing: 7100-7103	\$14,236		\$14,236	\$2,525		\$2,525				\$11,711		\$14,236
Abatement: 7100-7104	\$6,000	\$4,000	\$10,000	\$5,671		\$5,668	\$3			\$4,329		\$10,000
Other Consultants: 7100-7105	\$9,500		\$9,500	\$2,477		\$2,477				\$7,023		\$9,500
Management Fees: 7200-7201	\$42,730	(\$42,730)										
Construction: 7300-7301	\$1,894,009	\$159,000	\$2,053,009	\$1,829,026	\$129,933	\$1,958,959	\$1,929,558	\$372		\$94,000		\$2,052,959
Miscellaneous: 7300-7302	\$66,499		\$66,499	\$464		\$464	\$64			\$66,035		\$66,499
Security: 7400-7401	\$10,000	\$15,000	\$25,000	\$22,694		\$22,694	\$15,247			\$2,306		\$25,000
Utilities: 7500-7501	\$25,000		\$25,000							\$25,000		\$25,000
Moving / Relocation: 7500-7502	\$50,000		\$50,000	\$31,351		\$31,351				\$18,600		\$49,951
Contingency: 9999-9999	\$119,347	(\$64,000)	\$55,347							\$55,347		\$49

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
CIT Managed Subtotal	\$2,351,321	(\$42,730)	\$2,308,591	\$1,894,208	\$129,933	\$2,024,141	\$1,987,290	\$375	\$284,351	\$2,308,492	\$99	
Project Total	\$2,351,321	(\$42,730)	\$2,308,591	\$1,894,208	\$129,933	\$2,024,141	\$1,987,290	\$375	\$284,351	\$2,308,492	\$99	

Program\DeKalb County\421 SPLOST III\Elementary Schools\Wadsworth ES - Roof


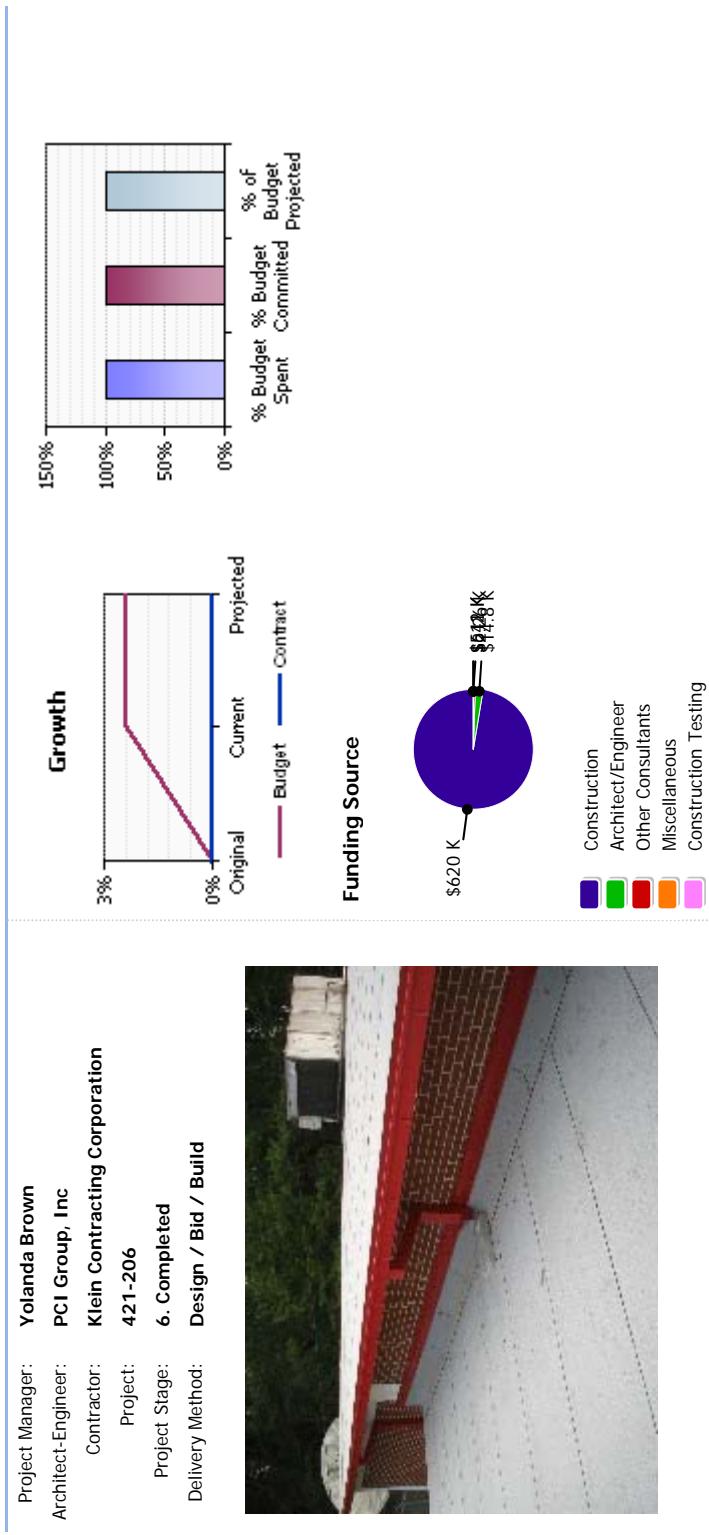


Program\DeKalb County\421 SPLOST III\Other Facilities\Warren Tech - HVAC

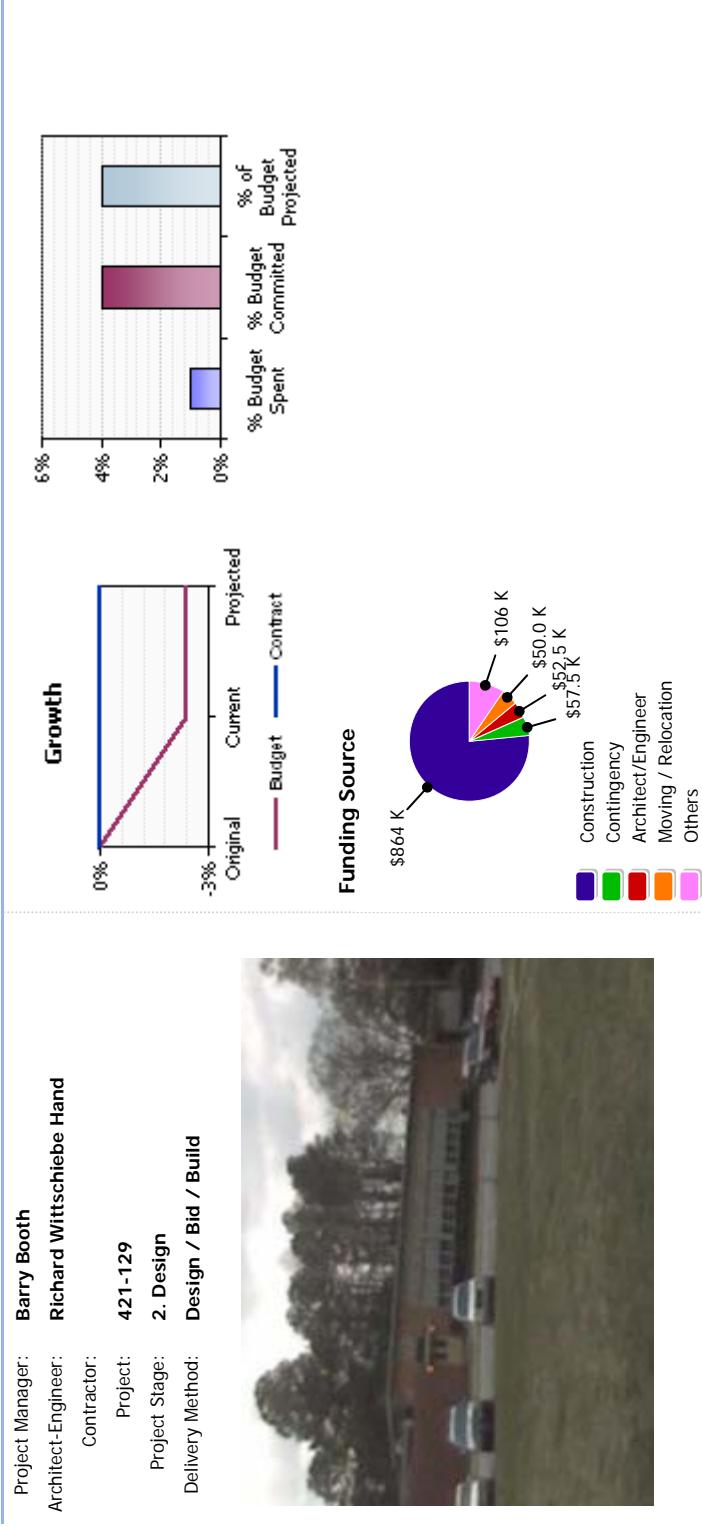

Cost Status by Budget Category:												
Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORS	ETC Forecast	Estimate At Completion	Uncommitted
CIT Managed												
Architect/Engineer: 7100-7101	\$52,455	\$46,863										
Surveying: 7100-7102	\$19,779	\$19,779										
Other Consultants: 7100-7105	\$9,877	\$9,877										
Management Fees: 7200-7201	\$20,157	(\$20,157)										
Construction: 7300-7301	\$864,458	\$864,458										
Miscellaneous: 7300-7302	\$41,125	\$41,125										
Security: 7400-7401	\$10,000	\$10,000										
Utilities: 7500-7501	\$25,000	\$25,000										
Moving / Relocation: 7500-7502	\$50,000	\$50,000										
Contingency: 9999-9999	\$57,518	\$57,518										
CIT Managed Subtotal	\$1,150,369	(\$20,157)	\$1,130,212	\$46,863								
Project Total	\$1,150,369	(\$20,157)	\$1,130,212	\$46,863	\$9,373	\$37,490	\$1,083,349	\$1,130,212	\$1,083,349	\$1,130,212		

Program\DeKalb County\421 SPLOST III\Other Facilities\William Bradley Bryant Center

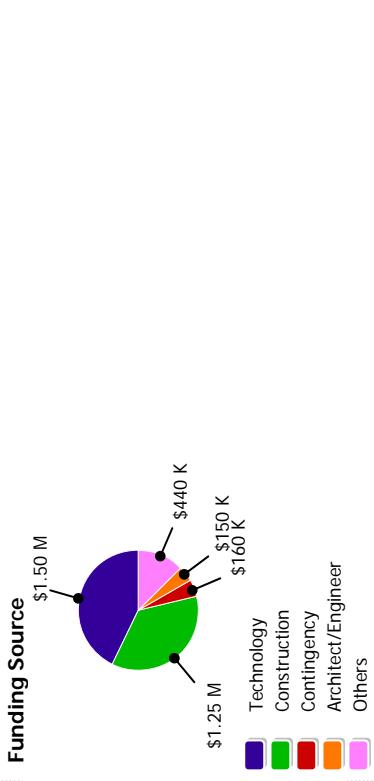Project Manager:	Brad Jacobs	Growth												
Architect-Engineer:														
Contractor:														
Project:	421-228													
Project Stage:	3. Procurement													
Delivery Method:	Design / Bid / Build													
		 <p>A line graph titled 'Growth' showing projected growth over time. The Y-axis ranges from 0% to 150% in increments of 50%. The X-axis shows 'Original', 'Current', and 'Projected' stages. A blue line starts at 0% for 'Original' and rises to 200% for 'Projected'.</p>												
		 <p>A pie chart titled 'Funding Source' showing the breakdown of the budget. The total budget is \$1.50M.</p> <table border="1"> <thead> <tr> <th>Funding Category</th> <th>Budget Allocation (\$)</th> </tr> </thead> <tbody> <tr> <td>Technology</td> <td>\$1.25 M</td> </tr> <tr> <td>Construction</td> <td>\$160 K</td> </tr> <tr> <td>Contingency</td> <td>\$150 K</td> </tr> <tr> <td>Architect/Engineer</td> <td>\$440 K</td> </tr> <tr> <td>Others</td> <td>\$160 K</td> </tr> </tbody> </table>	Funding Category	Budget Allocation (\$)	Technology	\$1.25 M	Construction	\$160 K	Contingency	\$150 K	Architect/Engineer	\$440 K	Others	\$160 K
Funding Category	Budget Allocation (\$)													
Technology	\$1.25 M													
Construction	\$160 K													
Contingency	\$150 K													
Architect/Engineer	\$440 K													
Others	\$160 K													
		 <p>A photograph of the William Bradley Bryant Center building, a modern facility with large windows and a glass entrance, situated in a landscaped area with trees and a parking lot.</p>												

Scope of Work:

- Scope of work includes:
 - renovations to the front offices to accommodate MIS personnel, to be relocated from vacated Admin Building A
 - Increase in the size of electrical service to the building to accommodate relocated data equipment.
 - Conversion of the existing cafeteria into the new MIS Data Center
 - Relocation of data equipment from Building A to WBBC, as well as infrastructure / fiber optic relocations.
 - Parking lot improvements
 - Improvements to interior finishes

Remarks:


- Design complete. RFP for construction has been issued, with a June, 2011 contract award anticipated.

Cost Status by Budget Category:

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
CIT Managed												
Architect/Engineer: 7100-7101	\$150,000		\$150,000				\$4,950	\$4,950		\$150,000	\$150,000	
Surveying: 7100-7102	\$10,000		\$10,000	\$4,950						\$5,050	\$10,000	
Construction Testing: 7100-7103	\$35,000		\$35,000	\$5,337			\$5,337	\$2,600	\$2,737	\$29,663	\$35,000	\$0
Abatement: 7100-7104	\$20,000		\$20,000							\$20,000	\$20,000	
Construction: 7300-7301	\$1,250,000		\$1,250,000							\$1,250,000	\$1,250,000	

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
Miscellaneous: 7300-7302	\$75,000	\$75,000	\$75,000	\$232		\$232	\$406	(\$174)		\$74,768	\$75,000	
Security: 7400-7401	\$25,000		\$25,000							\$25,000	\$25,000	
Utilities: 7500-7501	\$75,000		\$75,000							\$75,000	\$75,000	
Moving / Relocation: 7500-7502	\$100,000		\$100,000							\$100,000	\$100,000	
Contingency: 9999-9999	\$160,000		\$160,000							\$160,000	\$160,000	
CLT Managed Subtotal	\$1,900,000		\$1,900,000	\$10,519		\$10,519	\$7,956	\$2,563		\$1,889,481	\$1,900,000	\$0
DCSS Managed												
FF&E: 7700-7504	\$100,000		\$100,000							\$100,000	\$100,000	
Technology: 7800-7801	\$1,500,000		\$1,500,000							\$1,500,000	\$1,500,000	
DCSS Managed Subtotal	\$1,600,000		\$1,600,000	\$3,500,000	\$10,519	\$10,519	\$7,956	\$2,563		\$1,600,000	\$1,600,000	
Project Total	\$3,500,000									\$3,489,481	\$3,500,000	\$0


Program\DeKalb County\421 SPL OST III\Elementary Schools\Woodridge ES - Roof

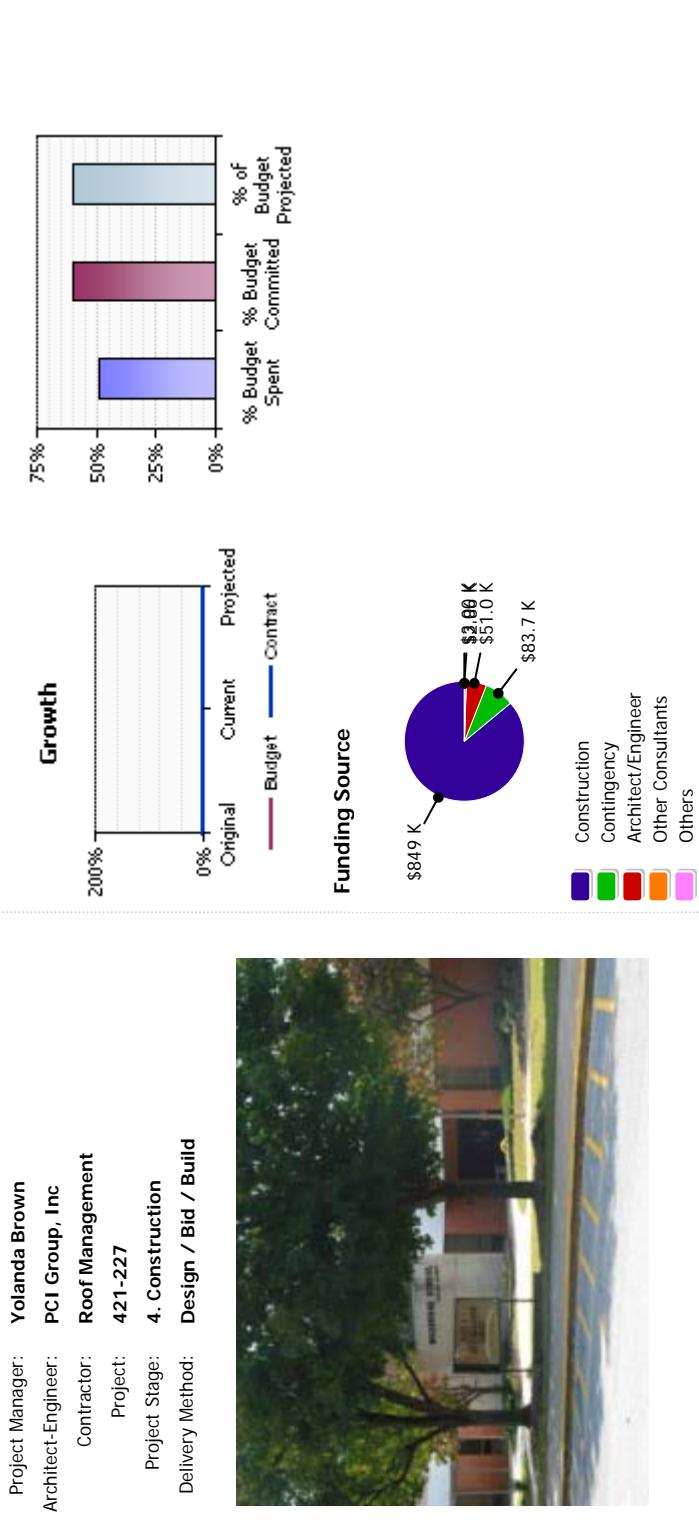

Cost Status by Budget Category:

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORS	ETC Forecast	Estimate At Completion	Uncommitted
CIT Managed												
Architect/Engineer: 7100-7101	\$50,968		\$50,968	\$22,000			\$22,000	\$14,200	\$7,800		\$28,968	\$50,968
Construction Testing: 7100-7103	\$1,500		\$1,500								\$1,500	\$1,500
Other Consultants: 7100-7105	\$2,856		\$2,856								\$2,856	\$2,856
Consulting: 7300-7301	\$849,473		\$849,473	\$571,474		\$571,474	\$469,179	\$102,295			\$277,999	\$849,473
Miscellaneous: 7300-7302	\$1,500		\$1,500	\$348		\$348	\$348				\$1,152	\$1,500
Contingency: 9999-9999	\$83,703		\$83,703								\$83,703	\$83,703
CIT Managed Subtotal	\$990,000		\$990,000	\$593,822		\$593,822	\$483,727	\$110,095			\$396,178	\$990,000
Project Total	\$990,000		\$990,000	\$593,822		\$593,822	\$483,727	\$110,095			\$396,178	\$990,000

Program\DeKalb County\421 SPLOST III\Elementary Schools\Woodward ES - HVAC, Roof

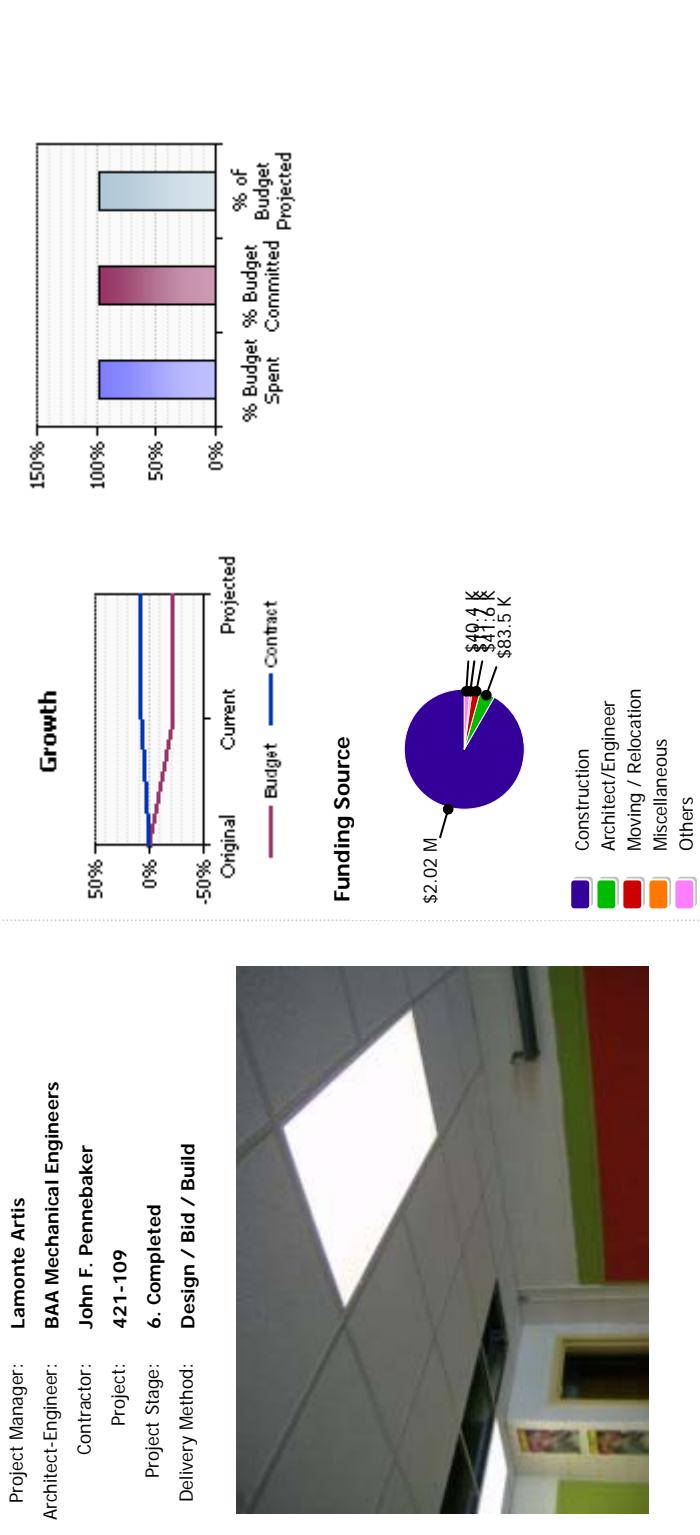

Scope of Work:

- The scope consists of HVAC, ceiling and lighting replacement. The multipurpose/gym building is not included in this scope (other than new fire alarm system) because it is a relatively new addition to the facility.

Remarks:

- This project has been completed.

Cost Status by Budget Category:

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
CIT Managed												
Architect/Engineer: 7100-7101	\$143,505	(\$60,000)	\$83,505	\$68,250		\$68,250						
Construction Testing: 7100-7103	\$17,260	(\$17,260)										
Abatement: 7100-7104	\$10,000	\$646	\$10,646	\$7,676		\$7,676						
Other Consultants: 7100-7105	\$17,434	(\$10,000)	\$7,434									
Management Fees: 7200-7201	\$52,921	(\$52,921)										
Construction: 7300-7301	\$2,324,598	(\$300,000)	\$2,024,598	\$1,875,000	\$143,219	\$2,018,219						
Miscellaneous: 7300-7302	\$80,312	(\$68,600)	\$11,712	\$3,680		\$3,680						
Security: 7400-7401	\$10,000		\$10,000	\$9,995		\$9,995						
Utilities: 7500-7501	\$25,000	(\$25,000)										
Moving / Relocation: 7500-7502	\$50,000	(\$8,417)	\$41,583	\$41,583		\$41,583						

Budget Category	Original Budget	Budget Revision	Current Budget	Original Contract	Executed Changes	Current Contract	Paid To Date	Contract Balance	CORs	ETC Forecast	Estimate At Completion	Uncommitted
Contingency: 9999-9999	\$143,738	(\$135,000)	\$8,738								\$8,738	
CLT Managed Subtotal	\$2,874,768	(\$676,552)	\$2,198,216	\$2,006,183	\$143,219	\$2,149,402	\$2,149,402				\$2,149,402	
DCSS Managed											\$48,814	
Technology: 7800-7801	\$3,600	\$3,600	\$2,047			\$2,047	\$2,047				\$1,553	
DCSS Managed Subtotal	\$3,600	\$3,600	\$2,047			\$2,047	\$2,047				\$1,553	
Project Total	\$2,874,768	(\$672,952)	\$2,201,816	\$2,008,231	\$143,219	\$2,151,450	\$2,151,450				\$50,366	

SPLOST III Capital Improvement Program

Project Bid List

Monthly Status Report

ACTIVE BID ITEMS

No.	Project	Scope	Bid Type	Issue	Pre Bid/ Proposal	Time	Questions Due	Issue Addendum #1	Final	Due Date	Due Time	Agenda Mo.	Comments	Project Manager
419-002-003	Arabia Mountain HS	Storage Facility	TB Prequalified	6/8/2011	10:00 AM	6/24/2011	TBD	6/27/2011	6/30/2011	12:00 PM	August	Public Opening (Budget Under \$50K)		Robert Mitchell
421-123	DSA at Avondale HS	HVAC Modifications	TB Prequalified	6/9/2011	10:00 AM	6/14/2011	TBD	6/17/2011	6/21/2011	2:00 PM	N/A	Public Opening (Budget Under \$50K)		Wade Richardson
N/A	Meadowview ES	Plumbing Fixtures (Labor Only)	TB Prequalified	6/10/2011	N/A	6/15/2011	TBD	6/16/2011	6/17/2011	2:00 PM	N/A	Budget under \$25K		Larry Williams

PENDING BID ITEMS

No.	Project	Scope	Bid Type	Release Draft	Status	Comments	Project Manager	Solicitor	A/E Firm
421-341-027	Wadsworth Magnet ES	Minor HVAC, Ceiling & Lighting Replacement	A/E RFP	6/16/2011	Scope Development		Melissa Ryckley	Joshua Williams	N/A
421-341-043	Allgood ES	Kitchen Renovation	A/E RFP	6/16/2011	Scope Development		Robert Mitchell	Joshua Williams	N/A
421-341-039	Clifton ES	Ceiling Tile Replacement	A/E RFP	6/16/2011	Scope Development		Melissa Ryckley	Joshua Williams	N/A
421-303-011	Hawthorne ES	ADA Modifications	TB	6/23/2011			Bernard Levert	Joshua Williams	The Epstein Group
N/A	Prequalification	Various	RFO	TBD	Preparing Docs	Solicitation planned for Summer 2011	Joshua Williams	Joshua Williams	N/A
421-117	Chamblee HS	Traffic Study	RFP	TBD			Amy Sue Mann	Joshua Williams	N/A
421-118	Cedar Grove HS	Restroom Upgrades	A/E RFP	TBD	Scope Development	Pending Board approval of additional allocation of funds	Carlton Parker	Joshua Williams	N/A
421-123	Avondale HS	Renovations	GC RFP	TBD	Scope Development	CANCELLED	Vigil Bryant	Joshua Williams	N/A
421-302-003	Group B-3	ADA Modifications	A/E RFP	TBD	Under Evaluation	Pending results from Student Services	Bernard Levert	Liz Epstein	N/A
421-303	Group C	ADA Modifications	A/E RFP	TBD	Under Evaluation	Pending results from Student Services	Bernard Levert	Liz Epstein	N/A
421-304	Group D	ADA Modifications	A/E RFP	TBD	Under Evaluation	Pending results from Student Services	Bernard Levert	Liz Epstein	N/A
421-305	Group E	ADA Modifications	A/E RFP	TBD	Under Evaluation	Pending results from Student Services	Bernard Levert	Liz Epstein	N/A
421-102	Southwest DeKalb	Addition	GC RFP	TBD	Scope Development	30% Construction Documents	Wade Richardson	Joshua Williams	CDH Partners
421-111	Redan HS	Renovations	GC RFP	TBD	Scope Development	35% Construction Documents	Wade Richardson	Joshua Williams	Richard Wittsiebie
421-127	MLK Jr. HS	Addition	GC RFP	TBD	Scope Development	On Hold	Amy Sue Mann	Joshua Williams	R.L. Brown
421-128	Miller Grove HS	Addition	GC RFP	TBD	Scope Development	30% Construction Documents	Robert Mitchell	Joshua Williams	Manley Spangler Smith
421-226	Old Chamblee MS	Roof Replacement	A/E RFP	TBD	Draft Complete	On Hold	Yolanda Brewer	Joshua Williams	N/A

CLOSED BIDS

No.	Project	Scope	Bid Type	Dates	Time	Questions Due	Issue Addendum	Due Date	Due Time	Agenda Mo.	Comments	Project Manager	
421-117	Chamblee HS	Replacement High School	CM/GC @ Risk RFP	2/17/2011	10:00 AM	3/14/2011	TBD	3/17/2011	10:00 AM	April	Contract Executed	Amy Sue Mann	
421-341-0420	Chamblee MS	Painting Various Areas	ITB	2/17/2011	10:00 AM	3/16/2011	TBD	3/21/2011	1:00 PM	April	CANCELLED	Melissa Ryckley	
410-364	WBBC	Front Office Renovation	GC RFP	3/24/2011	4/19/2011	10:00 AM	4/25/2011	TBD	4/28/2011	2:00 PM	June	Pending Contract Execution	Brad Jacobs
410-364-001	WBBC	Data Center Racks, Power Distribution and Cooling Systems	GC RFP	3/24/2011	4/20/2011	10:00 AM	4/26/2011	TBD	4/29/2011	2:00 PM	June	Pending Contract Execution	Leon Glasser/Tony Hunter
421-123	Avondale HS	Roof Replacement	Hard Bid Prequalified	3/24/2011	4/21/2011	10:00 AM	4/27/2011	TBD	5/2/2011	2:00 PM	June	CANCELLED	Wade Richardson
421-321-015	Emergency Generators	(Redan ES and Rainbow ES)	ITB	4/5/2011	4/19/2011	2:00 PM	4/27/2011	TBD	5/2/2011	3:00 PM	June	Pending Contract Execution	Larry Williams
421-132	Knollwood ES	HVAC & ADA Modifications	A/E RFP	4/21/2011	4/28/2011	10:00 AM	5/5/2011	TBD	5/9/2011	12:00 PM	June	Pending Contract Execution	Robert Mitchell
421-110	Stone Mountain HS	Career Technology Lab Renovation	ITB Prequalified	5/5/2011	5/31/2011	10:00 AM	6/6/2011	TBD	6/9/2011	2:00 PM	N/A	Pending Contract Execution	Wade Richardson
421-125	Lakeside HS	Construction Material Testing Services	RFP	5/20/2011	5/25/2011	1:00 PM	6/1/2011	TBD	6/3/2011	6/7/2011	12:00 PM	Evaluation Complete	Hal Anderson
421-132	Knollwood ES	Media Center HVAC, Ceiling & Lighting Replacement	ITB Prequalified				Liz solicited through an informal bid process due to projected budget being under \$100K threshold as per Board's Purchasing Policy DUE.			June COW Meeting	Pending Contract Execution	Liz Epstein	



Budget Reallocations for This Period

Cost Code	Code Description	Code Type	Current Budget	Change	Revised Budget
421.71.50.00.1117421.752.0000	Chamblee HS	Land	\$2,500,000.00	\$500,000.00	\$3,000,000.00
421.73.01.00.1117421.752.0000	Chamblee HS	Construction	\$3,972,232.00	(\$700,000.00)	\$3,272,232.00
421.75.03.00.1117421.752.0000	Chamblee HS	Trailers	\$0.00	\$200,000.00	\$200,000.00
421.74.01.00.1119421.752.0000	Druid Hills HS	Security	\$45,000.00	\$20,868.00	\$65,868.00
421.73.02.00.1119421.752.0000	Druid Hills HS	Miscellaneous	\$270,000.00	(\$20,868.00)	\$249,132.00
421.73.01.00.125421.752.0000	Lakeside HS	Construction	\$20,401,171.00	\$450,000.00	\$20,851,171.00
421.99.99.00.125421.752.0000	Lakeside HS	Project Contingency	\$503,825.00	(\$450,000.00)	\$53,825.00
421.73.01.00.341421.752.0000	Local School Request/LSPR2	Construction	\$4,936,091.00	(\$75,000.00)	\$4,861,091.00
421.75.02.00.341421.752.0000	Local School Request/LSPR2	Moving/Relocation	\$5,000.00	\$75,000.00	\$80,000.00
421.73.02.00.110421.752.0000	Stone Mountain HS	Miscellaneous	\$87,867.00	(\$75,000.00)	\$12,867.00
421.99.99.00.110421.752.0000	Stone Mountain HS	ProjectContingency	\$79,711.00	(\$39,711.00)	\$40,000.00
421.71.02.00.110421.752.0000	Stone Mountain HS	Surveying	\$38,000.00	(\$10,000.00)	\$28,000.00
421.71.03.00.110421.752.0000	Stone Mountain HS	Construction Testing	\$27,582.00	(\$7,000.00)	\$20,582.00
421.71.04.00.110421.752.0000	Stone Mountain HS	Abatement	\$175,000.00	(\$30,000.00)	\$145,000.00
421.73.01.00.110421.752.0000	Stone Mountain HS	Construction	\$5,387,833.00	(\$20,000.00)	\$5,367,833.00
421.75.03.00.110421.752.0000	Stone Mountain HS	Trailers	\$50,000.00	(\$18,500.00)	\$31,500.00
421.73.01.00.110421.752.0000	Stone Mountain HS	Construction	\$5,557,833.00	\$165,211.00	\$5,723,044.00
421.71.01.00.110421.752.0000	Stone Mountain HS	Architect/Engineer	\$272,300.00	\$50,000.00	\$322,300.00
421.71.05.00.110421.752.0000	Stone Mountain HS	Other Consultants	\$37,961.00	(\$15,000.00)	\$22,961.00
Total:			\$44,347,406.00	\$0.00	\$44,347,406.00
